


STORMWATER POLLUTION PREVENTION PLAN

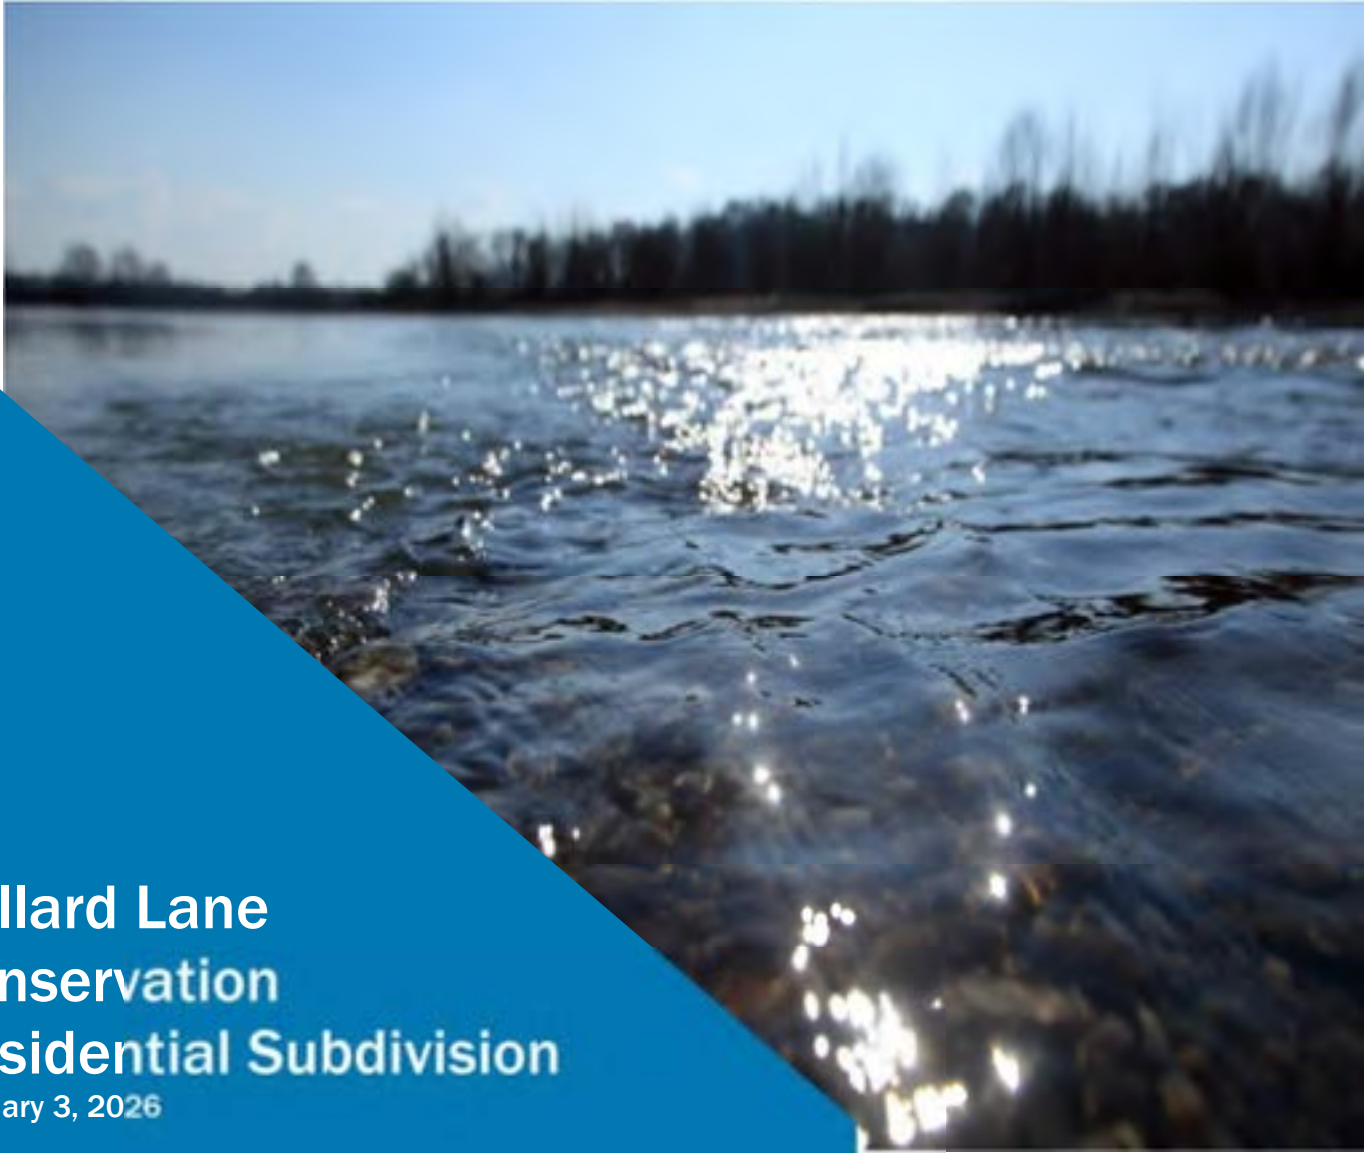

Bullard Lane Conservation Residential Subdivision

February 3, 2026

PREPARED FOR:
Saratoga Landworks, LLC
144 Pelcher Road
Broadalbin, NY 12025



Bullard Lane Conservation Residential Subdivision SWPPP

Table of Contents

1.0	EXECUTIVE SUMMARY	5
1.1	RESPONSIBILITIES OF THE PARTICIPANTS.....	5
1.2	PARTICIPANT CONTACT INFORMATION.....	11
2.0	SITE DESCRIPTION	11
2.1	LOCATION	12
2.3	SOILS AND GROUNDWATER.....	12
2.4	LAND COVER.....	12
2.5	WETLANDS.....	12
2.6	SURFACE WATERS.....	12
2.7	RAINFALL DATA	13
2.8	EXISTING LAND USE.....	13
3.0	PERMIT ELIGIBILITY	13
3.1	STATE HISTORIC PRESERVATION OFFICE	13
3.2	THREATENED AND ENDANGERED SPECIES	13
4.0	PROJECT DESCRIPTION	13
5.0	METHODOLOGY	14
6.0	PROCESS FOR STORMWATER SITE PLANNING AND PRACTICE SELECTION.....	15
6.1	SITE PLANNING.....	15
6.2	DETERMINE THE WATER QUALITY VOLUME AND MINIMUM REDUCTION VOLUME	18
6.3	RUNOFF REDUCTION BY APPLYING GREEN INFRASTRUCTURE TECHNIQUES AND STANDARD SMPs WITH RRV CAPACITY.....	19
6.4	RUNOFF REDUCTION TECHNIQUE EVALUATION.....	20
6.5	STANDARD STORMWATER MANAGEMENT PRACTICES TO TREAT WATER QUALITY VOLUME NOT ADDRESSED BY GREEN INFRASTRUCTURE TECHNIQUES.....	22
7.0	HYDROLOGIC AND HYDRAULIC ANALYSIS	22
7.1	EXISTING PRE-DEVELOPMENT CONDITIONS.....	23
7.2	PROPOSED POST-DEVELOPMENT WATERSHED CONDITIONS.....	24
7.3	PROPOSED WATER QUANTITY AND QUALITY CONTROLS.....	25
8.0	CLIMATE CHANGE CONSIDERATIONS	29
8.1	PHYSICAL RISKS DUE TO CLIMATE CHANGE	29
9.0	PERMANENT STORMWATER MANAGEMENT SYSTEM FEATURES	30
9.1	CONVEYANCE PIPING	30
9.2	STORMWATER MANAGEMENT SYSTEM.....	31
10.0	STORMWATER EROSION AND SEDIMENT CONTROLS.....	31
10.1	EROSION AND SEDIMENT CONTROLS	32
10.2	OTHER POLLUTANT CONTROLS.....	32



10.3	BEST MANAGEMENT PRACTICES.....	34
11.0	CONSTRUCTION SEQUENCE SCHEDULING	35
12.0	IMPLEMENTING THE SWPPP	36
12.1	EMPLOYEE TRAINING	36
12.2	SITE INSPECTIONS.....	36
12.3	MAINTENANCE.....	37
12.4	PROGRESS REPORTS AND SUMMARIES.....	38
12.5	CERTIFICATION	38
12.6	NYSDEC WINTER SITE STABILIZATION/SITE INSPECTIONS FOR CONSTRUCTION SITES.....	38
13.0	POST CONSTRUCTION OPERATION AND MAINTENANCE.....	40
13.1	OPERATION AND MAINTENANCE PLAN/REPORT	40
14.0	CONCLUSION	40

APPENDICIES

Appendix A: Owner & Contractor Certification Forms

Appendix B: Site Location/Drainage Area/Drainage Pattern Maps

Appendix C: Pre-Development and Post-Development Run-off Calculations

Appendix D: Calculations- Storm Management, Green Infrastructure, Pipe Sizing

Appendix E: Grading/Drainage/Sediment, Erosion Control Plan, and Landscaping Plan

Appendix F: NYSDEC SPDES General Permit GP-0-25-001

Appendix G: Construction Phase Inspection Report (Sample Form)

Appendix H: MS4 Acceptance Form

Appendix I: Notice of Intent (NOI)

Appendix J: Notice of Termination (NOT) Documentation

Appendix K: Deep Ripping and Decompaction

Appendix L: Permit Eligibility

Appendix M: Stormwater Management Practice Operation & Maintenance Manual



1.0 Executive Summary

This Water Quality and Quantity Plan and Stormwater Pollution Prevention Plan (SWPPP) has been prepared pursuant to the Environmental Protection Agency's (EPA) and the New York State Department of Environmental Conservation's (NYSDEC) Phase II Storm Water Regulations. All responsible parties as defined below are responsible for executing the SWPPP and for complying with the requirements set forth in the EPA's National Pollution Discharge Elimination System (NPDES) General Permit, the NYSDEC's State Pollution Discharge Elimination System (SPDES) General Permit GP-0-25-001, and any local governing agencies having jurisdiction with regard to erosion and sediment control.

This SWPPP has been prepared in accordance with Stormwater Management Planning techniques and Green Infrastructure Practices required by the most current version of the New York State Stormwater Management Design Manual (Design Manual). These planning techniques and practices emphasize a holistic approach to resource protection, water quality treatment, flow volume control, maintenance cost reduction, and the dynamics of stormwater science. According to the Design Manual, the green infrastructure approach for stormwater management reduces a site's impact on the aquatic ecosystem through the use of site planning techniques, runoff reduction techniques, and certain standard stormwater management practices.

The purpose of the Water Quality and Quantity Plan and the SWPPP described herein is to provide for the detention of high intensity storms (up to the 100-year storm) and the passive water quality treatment of low intensity storms. These controls and treatments will be achieved using appropriate temporary and permanent features such as drainage ditches, conveyance channels, conveyance piping, green infrastructure, and earth formed stormwater management basins. The goal is to limit the post-development storm water discharge rate to that of the pre-development flows and prevent discharge of pollutants into receiving waters.

This SWPPP has been prepared in accordance with the most current effluent limitations applicable to discharges from construction activities. The stormwater discharges outlined in this report will achieve, at a minimum, the effluent limitations outlined in Part II.B.1 (a)-(e) of NYSDEC's SPDES GP-0-25-001.

Additionally, this Plan outlines methods that Owners and Contractors can use to adjust construction practices in a way that will retain surface water quality and prevent sediment laden runoff from entering wetlands, streams, rivers, lakes and then ultimately to estuaries or other sensitive environments. This plan describes methods for stormwater management and runoff management during the construction phase and summarizes responsible stormwater pollution prevention practices that can be phased into everyday activities post construction.

1.1 Responsibilities of the Participants

All responsible parties shall comply with the measures set forth in this SWPPP and in accordance with the NYSDEC General Permit. The following outlines the responsibilities of all participants:

Owner/Operator/Permittee

The following is a summary of the Owner's responsibilities:



-
1. Satisfy the requirements of the State Environmental Quality Review Act when SEQR is applicable and where required, all necessary Department permits subject to the Uniform Procedures Act (UPA).
 2. An owner or operator of a construction activity that is not subject to the requirements of a regulated, traditional land use control MS4 must first develop a SWPPP in accordance with all applicable requirements of this permit and then submit a completed eNOI form electronically to the NYSDEC in order to be authorized to discharge under this permit. The eNOI form shall be one which is associated with this permit, signed in accordance with Part I.D of GP-0-25-001.
 3. An owner or operator of a construction activity that is subject to the requirements of a regulated, traditional land use control MS4 must first develop a SWPPP in accordance with all applicable requirements of this permit and then have its SWPPP reviewed and accepted by the MS4 prior to submitting the eNOI to the Department. The owner or operator shall have the “MS4 SWPPP Acceptance” form signed by the principal executive officer or ranking elected official from the regulated, traditional land use control MS4, or by a duly authorized representative of that person, and then upload that form to the eNOI prior to submittal of the eNOI to the NYSDEC.
 4. Read and understand the Electronic Notice of Intent (eNOI) and the SWPPP to make sure they are in accordance with the requirements of the General Permit. Certify the eNOI and the SWPPP by signing the Owner/Operator Certification statement contained in the NOI.
 5. The owner shall have the SWPPP preparer sign the “SWPPP Preparer Certification” form contained in the eNOI. The form shall then be uploaded to the eNOI prior to submittal of the eNOI to the NYSDEC.
 6. The owner/Operator shall sign the “Owner/Operator Certification” form contained in the eNOI. The form shall then be uploaded to the eNOI prior to submitting the eNOI to the NYSDEC. The eNOI should then be submitted electronically to the NYSDEC using the NYSDEC approved form.
 7. As of the date the eNOI is submitted to the Department, the owner or operator shall make the eNOI and SWPPP available for review and copying in accordance with the requirements in Part VII.H. of this permit.
 8. Ensure the provisions of the SWPPP are implemented from the commencement of construction activity until final stabilization and the Notice of Termination (NOT) has been submitted to the NYSDEC.
 9. Identify the contractor(s) and/or subcontractors(s) involved with construction activity that disturbs site soils prior to commencement of construction. Require all contractor(s) and/or subcontractor(s) fully implement the SWPPP and adhere to requirements set forth in the General Permit by having them sign the “contractor certification” in Appendix A. Each of these contractors and subcontractors shall have at least one trained individual from their company that will be responsible for implementation of the SWPPP and be on site when soil disturbing activities are occurring.
 10. Maintain a copy of the General Permit (GP-0-25-001), NOI, NOI Acknowledgement Letter, SWPPP, MS4 SWPPP Acceptance form, Contractor Certification(s), and inspection reports for the duration of construction activity until a NOT is filed with the NYSDEC. These documents should be kept in a secure location on site accessible during normal working hours.



-
11. Obtain the services of a qualified inspector to conduct regular on-site inspections for general compliance with the SWPPP and the SPDES General permit at least once every seven (7) calendar days.
 12. Obtain prior written authorization from the NYSDEC or MS4 if construction activity will disturb greater than five (5) acres of soil at any one time. A copy of this authorization should be kept on site. For as long as there is greater than five acres of soil disturbance, inspections shall be conducted twice every seven days with a minimum of two days separation. When soil disturbance has been temporarily or permanently suspended in these areas, stabilization measures shall be applied within seven days. A phasing plan defining maximum disturbance and required cuts and fills shall be developed as well as any additional site-specific practices needed to protect water quality.
 13. For construction activities that are subject to the requirements of a regulated, traditional land use control MS4, the owner or operator shall notify the MS4 in writing of any planned amendments or modifications to the post-construction stormwater management practice component of the SWPPP required by Part III.A. 5 of this permit. Unless otherwise notified by the MS4, the owner or operator shall have the SWPPP amendments or modifications reviewed and accepted by the MS4 prior to commencing construction of the post-construction stormwater management practice.
 14. Upon project completion and when the site has reached final stabilization, the Owner shall request termination of coverage under GP 0-25-001 by submitting and completing an Electronic Notice of Termination (eNOT) form electronically to the NYSDEC using the NYSDEC approved form.
 15. Retain all site records and documentation including project plans and reports, the SWPPP, SWPPP inspection reports and all records of data used to complete the NOI for a minimum of five (5) years from the date the site reached final stabilization.
 16. It is the responsibility of the owner or operator to provide documentation supporting the determination of permit eligibility with regard to Park I.D.10 (Historic Places). At a minimum, the supporting documentation shall include: information on whether the stormwater discharge or construction activities would have an effect on a property that is listed or eligible for listing on the State or National Register of Historic Places, results of historic places screening determinations conducted, a description of measures necessary to avoid or minimize adverse impacts on places listed or eligible for listing, or where effects may occur, any written agreements that the owner or operator has made with the OPRHP or other governmental agency to mitigate those effects, or local land use approvals evidencing the same.
 17. It is the responsibility of the owner or operator to provide documentation supporting the determination of permit eligibility with regard to construction activities that may adversely affect an endangered or threatened species unless the owner or (Part I.F.4) 10 operator has obtained a permit issued pursuant to 6 NYCRR Part 182 for the project or the Department has issued a letter of non-jurisdiction for the project. All documentation necessary to demonstrate eligibility shall be maintained on site in accordance with Part II.D.2 of this permit;



Notice to Purchaser and Developers

This SWPPP provides guidance to comply with the New York State Pollutant Discharge Elimination System (SPDES) for stormwater discharges associated with construction activities (GP-0-25-001). The Notice of Intent (eNOI) submitted to New York State to obtain permit coverage identifies the owner/operator of the land who is responsible for compliance with the General Permit and the project SWPPP.

If a separate party (herein referred to as the Purchaser) purchases land from the permitted owner/operator, and disturbs soil as part of the residential subdivision, the owner/operator has the obligation to ensure that the Purchaser's construction complies with the General Permit and the project SWPPP. Any amendments made to this SWPPP due to alteration of the scope of the project, or needed amendments due to compliance with a New York State revision to the General Permit are also the responsibility of the owner/operator.

When property ownership changes or when there is a change in operational control over the construction plans and specifications, the original owner or operator must follow the guidelines outlined in Part 1. G of GP-0-25-001.

Once the new owner or operator obtains permit coverage, the original owner or operator shall then submit a completed eNOT with the name and permit identification number of the new owner or operator to the Department. If the original owner or operator maintains ownership of a portion of the construction activity and will disturb soil, they must maintain their coverage under the permit.

Permit coverage for the new owner or operator will be effective as of the date the new owner receives the letter of acknowledgement (LOA) from the NYSDEC.

Owner's Engineer

The following is a summary of the Engineer's responsibilities:

1. Prepare this SWPPP using good Engineering practices, best management practices, and in compliance with NYSDEC Stormwater Regulations under General Permit (GP-0-25-001) and the "New York Standards and Specifications for Erosion and Sediment Control".
2. Prepare the NOI for the Owner to submit to the NYSDEC. The SWPPP preparer shall sign the "SWPPP Preparer Certification" contained in the NOI.
3. Update the SWPPP each time there is a significant modification to the design or construction which may have a significant effect on the potential for discharge of pollutants into receiving waters.

Contractors and Sub Contractors

The following is a summary of responsibilities for Contractors and/or subcontractors involved with construction activities that disturb soils on site:

1. Certify that the SWPPP has been read and understood by signing the Contractor Certification statement contained in Appendix A of this report.
2. In addition to providing the certification statement above, the certification page must also identify the specific elements of the SWPPP that each contractor and subcontractor will be responsible for and include the name and title of the person providing the signature; the name and title of the trained contractor responsible for SWPPP implementation; the name, address and telephone



number of the contracting firm; the address (or other identifying description) of the site; and the date the certification statement is signed. The owner or operator shall attach the certification statement(s) to the copy of the SWPPP that is maintained at the construction site. If new or additional contractors are hired to implement measures identified in the SWPPP after construction has commenced, they must also sign the certification statement and provide the information listed above.

3. Fully implement the SWPPP and the requirements set forth in the SPDES General Permit.
4. Conduct inspections on a regular basis of the erosion and sedimentation controls installed at the site. Responsible for installing, constructing, repairing, inspecting, and maintaining the erosion and sediment control practices. Each of these contractors and subcontractors shall have at least one trained individual from their company that will be responsible for implementation of the SWPPP and be on site when soil disturbing activities are occurring. This person shall be known as the trained contractor. The owner or operator shall ensure that at least one trained contractor is on site on a daily basis when soil disturbances are being performed.

Site Inspector

The owner or operator shall have a qualified inspector conduct site inspections in conformance with the general permit.

The following is a summary of the Site Inspector's responsibilities:

1. Inspections should be completed only by a "qualified inspector". Definition of qualified inspector is:

A qualified inspector means a person that is knowledgeable in the principles and practices of erosion and sediment control, such as a licensed Professional Engineer, Certified Professional in Erosion and Sediment Control (CPESC), Registered Landscape Architect, New York State Erosion and Sediment Control Certificate Program holder or other Department endorsed individual(s). It can also mean someone working under the direct supervision of, and at the same company as, the licensed Professional Engineer or Registered Landscape Architect, provided that person has training in the principles and practices of erosion and sediment control. Training in the principles and practices of erosion and sediment control means that the individual working under the direct supervision of the licensed Professional Engineer or Registered Landscape Architect has received four (4) hours of Department endorsed training in proper erosion and sediment control principles from a Soil and Water Conservation District, or other Department endorsed entity. After receiving the initial training, the individual working under the direct supervision of the licensed Professional Engineer or Registered Landscape Architect shall receive four (4) hours of training every three (3) years. It can also mean a person that meets the Qualified Professional qualifications in addition to the Qualified Inspector qualifications.

2. Conduct on-site inspections at least once every seven (7) calendar days for general compliance with the SWPPP and the NYSDEC SPDES General Permit. Inspection reports will be provided to the Owner and all contractors and subcontractors involved with earth disturbing activities within one business day of the field inspection. The inspector shall sign the certifying statements contained at the end of the inspection reports. See section 9.2 of this SWPPP for further detail concerning inspections as well as winter shutdown inspection requirements. The inspection reports shall include and/or address the following:

- Permit identification number



-
- The date and time of the inspection
 - Name and title of person(s) performing inspection;
 - Description of the weather and soil conditions at the time of the inspection;
 - Description of the condition of the runoff at all points of discharge from the construction site. This must include identification of any discharges of sediment from the construction site. Include discharges from conveyance systems (i.e. pipes, culverts, ditches, etc.) and overland flow.
 - A description of the condition of all surface waters of the State located within, or immediately adjacent to, the property boundaries of the construction site which receive runoff from disturbed areas. This must include identification of any discharges of sediment to the surface waters of the State;
 - Identification of all erosion and sediment control practices that need repair or maintenance;
 - Identification of all erosion and sediment control practices that were not installed properly or are not functioning as designed and require reinstallation or replacement.
 - Description and sketch of disturbed areas with active soil disturbance activity, areas that have been disturbed but are inactive at the time of the inspection, and areas that have been stabilized (temporary and or/ final) since the last inspection;
 - Total area of soil disturbance (acres) at the time of inspection of the following:
 - Total area with active soil disturbance (not requiring either temporary stabilization or final stabilization)
 - Total area with inactive soil disturbance (requiring either temporary stabilization or final stabilization)
 - Total area that has achieved temporary stabilization; and
 - Total area that has achieved final stabilization
 - Must identify the current stage of construction of all post-construction stormwater management practices and identification of all construction activity on site that is not in conformance with the SWPPP and technical standards.
 - Corrective actions that must be taken to install, repair, replace or maintain erosion and sediment control practices; and to correct deficiencies identified with the construction of the post-construction stormwater management practices;
 - Identification and status of all corrective actions that were required by previous inspection;
 - Digital photographs, with date stamp, that clearly show the condition of all practices that have been identified as needing corrective actions. The qualified inspector shall attach paper color copies of the digital photographs to the inspection report being maintained onsite within seven (7) calendar days of the date of the inspection. The



qualified inspector shall also take digital photographs, with date stamp, that clearly show the condition of the practice(s) after the corrective action has been completed. The qualified inspector shall attach paper color copies of the digital photographs to the inspection report that documents the completion of the corrective action work within seven (7) calendar days of that inspection.

3. At a minimum, the qualified inspector shall inspect all erosion and sediment control practices to ensure integrity and effectiveness, all post-construction stormwater management practices under construction to ensure that they are constructed in conformance with the SWPPP, all areas of disturbance that have not achieved final stabilization, all points of discharge to natural surface waterbodies located within, or immediately adjacent to, the property boundaries of the construction site, and all points of discharge from the construction site.
4. Review the SWPPP logbook on a periodic basis to ensure compliance and update as necessary.
5. When construction is complete, provide the Owner with a final site assessment verifying that the site has undergone final stabilization and met all requirements of the SWPPP and the General Permit. When the site has undergone final stabilization, prepare the eNOT and sign the “Final Stabilization” and “Post-Construction Stormwater Management Practice” certification statement. The eNOT must then be submitted electronically to the NYSDEC.

For construction activities that are subject to the requirements of a regulated, traditional land use control MS4, the owner or operator shall also have the MS4 sign the “MS4 Acceptance” statement on the eNOT. The owner or operator shall have the principal executive officer, ranking elected official, or duly authorized representative from the regulated, traditional land use control MS4, sign the “MS4 Acceptance” statement. The MS4 official, by signing this statement, has determined that it is acceptable for the owner or operator to submit the eNOT in accordance with the requirements of the general permit. The MS4 can make this determination by performing a final site inspection themselves or by accepting the qualified inspector’s final site inspection certification(s).

1.2 Participant Contact Information

Owner/Operator	Engineering Firm	Contractor’s & Sub Contractors
Saratoga Landworks, LLC 144 Pelcher Road Broadalbin, NY 12025	Lansing Engineering, P.C. 2452 State Route 9, Suite 301 Malta, New York 12020 (518) 899-5243	TBD

2.0 Site Description

This section briefly describes existing and proposed hydrologic and hydraulic conditions at and around the project site as they relate to surface water management planning considerations. Subsequent sections contain a description of the manner in which site runoff will be managed to minimize effects on areas adjacent to the site.



2.1 Location

The proposed Bullard Lane Conservation Residential Subdivision is located on approximately 72.73 acres of land located along the south side of Bullard Lane in the Town of Wilton, NY. The project site has a tax map identification number of 141.-2-5.2.

2.1 Topography

Existing site topography is moderately level to moderately steep. Based on topographic survey information, the project site generally slopes toward the north and south to the existing wetlands located in the central portion of the parcel area.

2.3 Soils and Groundwater

According to maps from the Natural Resources Conservation Service (NRCS) of Saratoga County, the onsite soils are classified as follows.

- *Oakville Loamy Fine Sand, OaA/OaB/OaC*, – This is a very deep, predominantly well drained soil formed in water sorted sand. It is located on glacial outwash plains, lake plains, and beach ridges. The permeability rapid throughout the mineral soil. The soil has very slow surface runoff. The depth to the water table is expected to be generally between 3 and 6 feet. Depth to bedrock is generally greater than 60 inches. The soil has a slight erosion hazard. (Hydrologic Soil Type A)

Onsite soil tests were conducted on 12/23/2025 by Lansing Engineering, PC. The tests included deep hole soil observations. The on-site soil tests indicated the site consisted of sand consistent with the NRCS soil description with groundwater observed generally greater than 7 feet below the ground surface. As a result, the soils have been modeled as a Hydrologic Soil Type A. A summary of the deep hole tests and locations is provided on the Existing Conditions Map included in Appendix B of this report.

2.4 Land Cover

The existing land cover consists of predominantly mature woods. A small portion of the area has been cleared during the construction of the neighboring residential subdivision to the west. Additionally, a small portion of existing roadway is located in the northern limits of the project site.

2.5 Wetlands

The project contains NYSDEC regulated wetlands and associated 100-ft buffers. The wetlands have been delineated by a wetland scientist at Gilbert VanGuilder Land Surveyor, PLLC and are identified on the project site plans.

2.6 Surface Waters

The project site does not contain any surface waters.



2.7 Rainfall Data

Rainfall data utilized in the modeling and the analysis was obtained from a joint venture between the Northeast Regional Climate Center (NRCC) and the Natural Resources Conservation Service (NRCS) and can be found at the website: precip@cornell.edu. The data used is specific to this project and various 24-hour storm events are presented below. This data has also been used to create site specific Intensity-Duration-Frequency (IDF) curves that have been used for this analysis.

24-Hour Storm Event	24-hour rainfall
1 year	2.25
10 year	3.75
25 year	4.62
100 year	6.33

Data for the 90% average annual stormwater runoff volume (P) was obtained from Figure 4.1 of the “New York State Stormwater Management Design Manual” and is equal to one inch (1.15”).

2.8 Existing Land Use

Existing land use consists of the dense vacant woods with a small portion of existing impervious in the northern portion of the project site.

3.0 Permit Eligibility

This section briefly describes the project’s GP-0-25-001 permit eligibility in regard to State Historic Preservation Office (OPRHP) and threatened and endangered species.

3.1 State Historic Preservation Office

Hartgen Archeological Associates has been obtained to the applicant to coordinate with the NYSOPRHP. The no effect letter is included in Appendix L of this report.

3.2 Threatened and Endangered Species

The NYSDEC Environmental Assessment Form mapper has indicated the potential for the Frosted Elfin and Karner Blue Butterfly on the project site. Gilbert VanGuilder Land Surveyors has been retained by the applicant to conduct a habitat study on the project site. A copy of the study is included in Appendix L of this report.

4.0 Project Description

The applicant proposes the construction of a 25-lot conservation residential subdivision. Access to the site will be provided via a new curb cut along Bullard Lane and a new roadway approximately 2,252 linear feet in length.

The anticipated impermeable surfaces include paved road areas, driveways, and structure rooftops. Stormwater from the impermeable surfaces will be directed towards green infrastructure practices as well as an open drainage stormwater conveyance system and further to a stormwater basin to the greatest



extent possible. The stormwater from the basin will then be stored, treated and released and discharged via infiltration into the existing ground or towards existing drainage pathways on the project site. Storm events greater than the 100-year storm will be directed to discharge to an existing drainage corridor. The project design will ensure that the soils, wetlands, and groundwater table will be protected.

Stormwater management areas will be constructed to treat and control stormwater runoff. The systems have been sized to ensure that adequate storage capacity exists to properly treat and store runoff associated with the 1, 10, 25, and 100 year design storm events.

5.0 Methodology

This SWPPP utilizes several Stormwater Management Planning techniques and Green Infrastructure Practices. This approach to stormwater management emphasizes a holistic approach to resource protection, water quality treatment, flow volume control, maintenance cost reduction, and the dynamics of stormwater science. The primary goal is to reduce a site's impact on the aquatic ecosystem using site planning techniques, runoff reduction techniques, and certain standard stormwater management practices.

According to the most recent version of the New York State Stormwater Design Manual (NYSSDM), the term green infrastructure includes a wide array of practices at multiple scales to manage and treat stormwater, maintain and restore natural hydrology and ecological function by infiltration, evapotranspiration, capture and reuse of stormwater, and establishment of natural vegetative features. On the local scale, green infrastructure consists of site and neighborhood specific practices and runoff reduction techniques. When implemented throughout a development and watershed, green infrastructure can: reduce runoff volume, peak flow, and flow duration, slow down the flow to increase the time of concentration, improve groundwater recharge, protect downstream water resources, including wetlands, reduce downstream flooding and property damage, reduce incidence of combined sewer overflow, provide water quality improvements/reduced treatment costs, reduce thermal pollution, and improve wildlife habitat.

The methodology for implementing green infrastructure techniques as well as designing the stormwater management and erosion and sedimentation control structures for this project is summarized as follows:

The Six Step Process for Stormwater Site Planning and Practice Selection

- 1.0 Planning the site in accordance with local laws and ordinances to preserve natural resources, utilize site hydrology and reduce impervious cover.
- 2.0 Initial calculation of the water quality volume for the site.
- 3.0 Incorporation of green infrastructure techniques and standard stormwater management practices (SMPs) with Runoff Reduction Volume (RRv) capacity to reduce 100% of the WQv calculated in step 2. If this is not possible, an explanation as to why the green infrastructure techniques were not feasible and specific site limitations will be provided.
- 4.0 Determine the minimum Runoff Reduction Volume (RRv) required.
- 5.0 Use of standard SMPs, where applicable, to treat the portion of water quality volume not addressed by green infrastructure techniques and standard SMPs with RRv capacity,



-
- 6.0 Design of volume and peak rate control practices where required.
- 6.1 Evaluate the hydrologic condition of the tributary area using the USDA-SCS Technical Release No. 20 (June 1986) Methods.
 - 6.2 Determine peak flows from each watershed, for various storm events, using the Autodesk Storm and Sanitary Analysis computer program.
 - 6.3 Determine the water quality volume, channel protection volume, overbank flood protection volume and extreme storm flood protection volume for each drainage area that requires mitigation. Design the stormwater systems for each drainage area with structures that store and discharge the previously mentioned volumes at the required rates.
 - 6.4 Perform stormwater system routings for the stormwater management using the Autodesk Storm and Sanitary Analysis computer program if necessary. Examine and compare the output for peak elevations and peak outflows for both pre and post-development conditions.
 - 6.5 Design the stormwater system, in accordance with the "New York State Stormwater Management Design Manual", July 2024, prepared by the Maryland's Center for Watershed Protection for the New York State Department of Environmental Conservation.
 - 6.6 Design the erosion and sedimentation control structures, and prepare engineering calculations for the design of channels and conveyance piping in accordance with the "New York Standards and Specifications for Erosion and Sediment Control.

6.0 Process for Stormwater Site Planning and Practice Selection

6.1 Site Planning

The first step in developing a comprehensive stormwater management plan using green infrastructure is to avoid or minimize land disturbance by preserving natural resources and utilizing the hydrology of the site. An existing conditions map was prepared identifying the natural resource areas and drainage patterns prior to designing the site layout. The map includes but is not limited to wetlands (state and federally regulated), waterways (major, perennial, intermittent, or springs), buffer areas (stream, wetland and forest), floodplains, forest, critical areas, topography, soils (hydrologic soil group, highly erodible soils, etc.), and significant geologic features including bedrock. This map is shown in Appendix B and addressed in the Erosion and Sediment Control Plan.

Preservation of Natural Features

Utilizing the Natural Resource Areas and Drainage Pattern Map, a strategy for protecting and enhancing natural resources was created. This strategy involves preserving natural features prior to site layout, utilizing natural features to preserve the natural hydrology, maintaining natural drainage design points, maximizing retention of forest cover and undisturbed soils, avoiding erodible soils on steep slopes and limiting mass grading of sites. Preservation of natural features includes techniques to foster the identification and preservation of natural areas that can be used in the protection of water, habitat and



vegetative resources. The following planning practices to protect natural features have been considered and where possible, applied to the proposed development.

Preservation of Undisturbed Areas: Preservation of undisturbed areas have been included in this project and includes the deed restricted NYSDEC 100’ wetland adjacent areas as well as proposed deed restricted areas to be dedicated to the Town of Wilton.

Preservation of Buffers: Preservation of buffers have been included for the proposed development and consist of the preservation of the NYSDEC 100’ wetland adjacent areas.

Reduction of Clearing and Grading: Clearing shall be limited to only what is necessary for the construction of the buildings, parking lots and required stormwater management features. A limit of disturbance will be established based on the maximum disturbance zone for all development activities that considers equipment needs and construction techniques.

Locating Development in Less Sensitive Areas: The project has been designed with the conscious effort to not impact any wetlands or buffers.

Open Space Design: The project utilizes a cluster design to provide more open space and conservation areas.

Soil Restoration: Soil restoration will be completed in areas that require extensive grading and will be performed during the construction phase of the project. According to the New York State Stormwater Design Manual, soil restoration is a required practice applied across areas of a development site where soils have been disturbed and will be vegetated in order to recover the original properties and porosity of the soil. Soil restoration is applied in the cleanup, restoration, and landscaping phase of construction followed by the permanent establishment of an appropriate, deep-rooted groundcover to help maintain the restored soil structure. A simple maintenance agreement will be included identifying where this technique has been applied and will be conserved and who is responsible.

Soil restoration includes mechanical decompaction, compost amendment or both. The following table (from the New York State Stormwater Design Manual) describes various soil disturbance activities related to land development, soil types and the requirements for soil restoration for each activity.

Soil Restoration Requirements			
Type of Soil Disturbance	Soil Restoration Requirement		Comments / Examples
No Soil Disturbance	Restoration not permitted		Preservation of natural features
Minimal soil disturbance	Restoration not required		Clearing and Grubbing
Areas where topsoil is stripped only – no change in grade	HSG A&B	HSG C&D***	Protect area from any ongoing construction activities
	Apply 6 inches of topsoil	Aerate*and apply 6” of topsoil	
Areas of cut or fill	HSG A&B	HSG C&D	
	Aerate*and apply 6” of topsoil	Apply full soil restoration**	
Heavy traffic areas on site (especially in a zone 5-25 feet around buildings but not within a 5 foot perimeter around foundation walls.	Apply Full Soil Restoration (decompaction and compost enhancement)		



Areas where Runoff Reduction and/or infiltration practices are applied	Restoration not required, but may be applied to enhance the reduction specified for appropriate practices	Keep construction equipment from crossing these areas. To protect newly installed practice from any ongoing construction activities construct a single phase operation fence area
Redevelopment projects	Soil restoration is required on redevelopment projects in areas where existing impervious area will be converted to pervious area.	

*Aeration includes the use of machines such as tractor-drawn implements with coulters making a narrow slit in the soil, a roller with many spikes making indentations in the soil, or prongs which function like a mini-subsoiler.

** "Please see Deep Ripping and De-compaction, DEC 2008" which is found in Appendix K.

*** This project is situated on D type soils
(HSG = hydrologic soil group)

Soil restoration will help return the soil to its original state prior to development. This planning technique will increase rainwater absorption therefore increasing temporary water storage in the soil, filtering out water pollutants, reducing stormwater runoff through infiltration and evapotranspiration and promoting healthy plant growth with a reduced need for irrigation, pesticides and fertilizers.

Reduction of Impervious Cover

The next step is to reduce the impacts of the development by reducing the impervious cover. This strategy involves reducing roadways, sidewalks, driveways, cul-de-sacs, building footprints and parking areas. Impervious surfaces can significantly disrupt the natural rhythm of the hydrologic cycle. Since they do not allow stormwater to percolate into the soil, infiltration, evapotranspiration and groundwater recharge is decreased. These surfaces also increase the rate at which runoff and associated pollutants are conveyed to the nearest water body, which can compromise water quality and may result in a higher frequency of flooding and accelerated stream erosion. The following planning practices to reduce impervious cover have been considered and where possible, applied to the proposed development.

Roadway Reduction: Roadways for this project have been reduced to the minimum extent possible allowed by the Town of Wilton.

Sidewalk Reduction: This practice is not applicable as the project does not include sidewalks.

Driveway Reduction: The driveways for this project have been designed to the minimum extent possible allowed by the Town of Wilton.

Building Reduction: This practice of reducing the building footprint was utilized to reduce the area of the buildings to the maximum extent possible while still making the project feasible. The buildings have been designed to be as efficient with space as possible while still achieving the required use needs.

Parking Reduction: This planning practice was not applicable as this is single family construction and parking is located in the driveways.

By protecting natural resources and utilizing the hydrology of the site, every attempt has been made to preserve the natural conditions of the site, minimize runoff and maintain the preconstruction hydrology.



Careful consideration has been made to preserve undisturbed areas and buffers, reduce clearing and grading, locate development in less sensitive areas, and restore soils.

The proposed project has a minimal impervious area for a project of this size and use. Impervious areas are limited to building, access driveways, parking areas, and sidewalks. All reasonable opportunities for preserving natural conditions of the site have been employed by the project to preserve the natural conditions of the site to minimize the runoff and maintain the pre-construction hydrology.

6.2 Determine the Water Quality Volume and Minimum Reduction Volume

The total project area (developed area) is approximately 72.73 acres. Of the 72.73 acres, 3.39± acres is new impervious development. A total of 0.50± acres of impervious is existing as mentioned above. As stated in Section 9.2.1 of the New York State Stormwater Design Manual, 25% of the existing, disturbed impervious area and 100% of the new development Water Quality Volume must be treated. The project development does not include disturbance of any existing impervious areas. Therefore, approximately 3.39 of impervious has been considered for WQv treatment. As stated in Section 9.2.1 of the New York State Stormwater Design Manual, RRV is required for the increase in impervious area only. Therefore, a total of 3.39± acres of impervious has been considered for green infrastructure minimum runoff reduction calculations.

Following a review of existing topography and site conditions, eight (8) drainage areas and eight (8) distinct design points have been defined for the subject site and the stormwater management analysis. A detailed description of this design points can be found in section 7.1 & 7.2 of this report. The water quality volume (WQv) and Minimum Reduction Volume for the project has been calculated as follows:

Water Quality Volume:

$$WQv = \frac{P \times Rv \times A}{12}$$

Where:

Rv = 0.05 + 0.009(I); I = percent impervious

P (inch) = 90% Rainfall Event

A = Site Area

$$WQv = \frac{1.15 \times 0.092 \times 72.73}{12} = 0.641 \text{ ac-ft}$$

The Water Quality Volume for the project is 0.641 ac-ft or 27,917 cf of stormwater.

Minimum RRV required:

$$RRv = \frac{P \times Rv \times S \times A}{12}$$

Where:

P = 90% rainfall event (inches)

Rv = 0.05 + 0.009(I) where I is 100% impervious

S = Soil Factor (weighted average of all soils)

A = Total New Impervious Area

$$\text{Minimum RRV required} = \frac{(1.15 \times 0.95 \times 0.55 \times 3.39)}{12} = 0.170 \text{ ac-ft}$$

Minimum RRV required = 0.170 acre-feet



6.3 Runoff Reduction by Applying Green Infrastructure Techniques and Standard SMPs with RRv Capacity

The Runoff Reduction Volume (RRv) results in a reduction of the total WQv through implementation of green infrastructure techniques. Runoff reduction shall be achieved by infiltration, groundwater recharge, reuse, recycle, evaporation/transpiration of 100 percent of the post development water quality volumes to replicate pre-development hydrology by maintaining pre-construction infiltration, peak runoff flow, discharge volume, as well as minimizing concentrated flow by using runoff control techniques to provide treatment in a distributed manner before runoff reaches the collection system. Green infrastructure techniques shall be employed to reduce the required WQv. Green infrastructure techniques are grouped into two categories. They include:

- Practices resulting in a reduction of contributing area, and
- Practices resulting in a reduction of contributing volume

All of the green infrastructure planning and design options have been evaluated to determine the feasibility of the runoff reduction option for use on the project site. If the option is not feasible for the project site, a description has been provided indicating why the green infrastructure option was not feasible. Implementation of green infrastructure cannot be considered infeasible unless physical constraints, hydraulic conditions, soil testing, existing and proposed slopes (detailed contour), or other existing technical limitations are objectively documented.

The following chart (from the NYSSSDM) outlines the green infrastructure techniques that are acceptable for runoff reduction that must be evaluated for feasibility for the project.

Green Infrastructure Techniques Acceptable for Runoff Reduction		
Group	Practice	Description
Runoff Reduction Techniques	Conservation of natural areas	Retain the pre-development hydrologic and water quality characteristics of undisturbed natural areas, stream and wetland buffers by restoring and/or permanently conserving these areas on a site.
	Sheetflow to riparian buffers or filter strips	Undisturbed natural areas such as forested conservation areas and stream buffers or vegetated filter strips and riparian buffers can be used to treat and control stormwater runoff from some areas of a development project.
	Vegetated open swale	The natural drainage paths, or properly designed vegetated channels, can be used instead of constructing underground storm sewers or concrete open channels to increase time of concentration, reduce the peak discharge, and provide infiltration
	Tree planting/tree box	Plant or conserve trees to reduce stormwater runoff, increase nutrient uptake, and provide bank stabilization. Trees can be used for applications such as landscaping, stormwater management practice areas, conservation areas and erosion and sediment control.
	Disconnection of rooftop runoff	Direct runoff from residential rooftop areas and upland overland runoff flow to designated pervious areas to reduce runoff volumes and rates.
	Stream daylighting for redevelopment projects	Stream daylight previously culverted / piped streams to restore natural habitats, better attenuate runoff by increasing the storage size, promoting infiltration, and help reduce pollutant loads.
	Rain Garden	Manage and treat small volumes of stormwater runoff using a conditioned planting soil bed and planting materials to filter runoff stored within a shallow depression.



	Green roof	Capture runoff by a layer of vegetation and soil installed atop a conventional flat or sloped roof. The rooftop vegetation allows evaporation and evapotranspiration processes to reduce volume and discharge rate of runoff entering conveyance system.
	Stormwater planter	Small landscaped stormwater treatment devices that can be designed as infiltration or filtering practices. Stormwater planters use soil infiltration and biogeochemical processes to decrease stormwater quantity and improve water quality
	Rain tank / Cistern	Capture and store stormwater runoff to be used for irrigation systems or filtered and reused for non-contact activities
	Porous Pavement	Pervious types of pavements that provide an alternative to conventional paved surfaces, designed to infiltrate rainfall through the surface, thereby reducing stormwater runoff from a site and providing some pollutant uptake in the underlying soils.

6.4 Runoff Reduction Technique Evaluation

The runoff reduction techniques offered in the NYSDEC Stormwater Design Manual have been reviewed to determine the suitability of the site for use. The feasible runoff reduction practices are shown in the project plans. Additionally, a summary of the individual runoff reduction and total runoff reduction volume and the impact it will have on the total WQv is included after the description and evaluation of each practice.

Conservation of Natural Areas: Conservation of Natural Areas have been proposed for this project. A total of 29.22 acres will be included in a deed restricted conservation easement. Of the 29.22 acres, 6.61 acres consists of NYSDEC Wetlands. As such, a total of 22.61 acres has been utilized for runoff reduction purposes.

Sheet Flow to Riparian Buffers or Filter Strips: This green infrastructure practice helps treat and control stormwater runoff from developed areas. Providing sheet flow to filter strips will promote groundwater recharge, reduce pollutant loading, increase infiltration and help to maintain pre- and post-hydrologic conditions. Filter strips have not been proposed as the proposed project does not allow for the required minimum filter strip width.

Vegetated Swale: According to the New York State Stormwater Design Manual, a vegetative swale is a maintained, turf lined swale specifically designed to convey stormwater at a low velocity, promoting natural treatment and infiltration. Where drainage area, topography, soils, slope and safety issues permit, vegetated swales can be used in the street right-of-way and on developed sites to convey and treat stormwater from roadways and other impervious surfaces. Vegetated swales have been proposed for this project to convey stormwater. However, no green infrastructure credit has been accounted for by this practice as other green infrastructure practices have been utilized.

Tree Planting / Tree Pit: Conservation of existing trees shall be utilized by the project. This practice helps to reduce stormwater runoff through rainfall interception and evapotranspiration. Other benefits include providing wildlife habitat, promoting shade, creating natural buffers, increasing nutrient uptake, and aiding infiltration. Tree Plantings have not been included in the green infrastructure calculations as other green practices have been utilized.

Disconnection of Rooftop Runoff: Disconnection of Rooftop Runoff will not be proposed for this project due to the feasibility and size of the commercial buildings being proposed.

Stream Daylighting: The stream daylighting technique is typically used for retrofit or redevelopment projects and therefore is not applicable to this project.

Rain Gardens: According to the New York State Stormwater Design Manual, the rain garden is a stormwater management practice intended to manage and treat small volumes of stormwater runoff from impervious surfaces using a conditioned planting soil bed and planting materials to filter runoff stored within a shallow depression. This practice is most commonly used in residential land use settings and is appropriate for townhomes and single-family homes. Rain gardens have not been proposed for this project due to the maintenance requirements that would be placed on the individual homeowners.

Green Roofs: Green roofs are not considered to be feasible for the project based upon structural requirements that would be imposed upon the proposed building and due to safety concerns for the future owners / tenants. Also, extreme weather and potential heavy snow loads during winter months make this practice undesirable.

Stormwater Planters: According to the New York State Stormwater Design Manual, stormwater planters, much like rain gardens, use soil infiltration and biogeochemical processes to decrease stormwater quantity and improve stormwater quality. Stormwater planters have not been proposed for this project as other green infrastructure techniques have been utilized.

Rain Barrels and Cisterns: Rain barrels and cisterns have not been proposed for this project as other green infrastructure techniques have been utilized.

Porous Pavement: According to the New York State Stormwater Design Manual, porous pavement provides an alternative to conventional paved surfaces. It is designed to infiltrate rainfall directly through the surface, thereby reducing stormwater runoff. In addition, porous pavement provides some pollutant uptake in the underlying soils thus improving the water quality. Porous pavement has not been proposed for this project due to the presence of seasonably high groundwater.

Bio-retention infiltration: According to the New York State Stormwater Design Manual, bio-retention is a stormwater management practice intended to manage and treat stormwater runoff from impervious surfaces using a conditioned planting soil bed and planting materials to filter runoff stored within a shallow depression. This practice is most commonly used in residential and commercial land use settings and is appropriate for townhomes, parking lots and commercial buildings. A bio-retention area has not been proposed.

The required WQv that shall be treated for the project is calculated in Section 6.2 and is approximately 0.641 ac-ft or 27,917 cf of stormwater for the project. The required minimum runoff reduction requirements have been calculated in Section 6.2 and is approximately 0.025 ac-ft. The proposed runoff reduction volumes utilizing green infrastructure techniques have been calculated and are shown in Appendix D at the end of this report. A summary of the calculation results are as follows:

The original WQv=	0.641 ac-ft
The minimum required RRv =	0.170 ac-ft
<u>Area Reduction Practices</u>	
Conservation of natural areas=	22.61 ac
Riparian buffers / filter strips =	0.00 ac
Tree Planting/tree preservation=	0.00 ac
Total Area Reduction=	22.61 ac



Runoff Reduction volume= 0.363 ac-ft

Practices with RRv Capacity

Rooftop Disconnection	N/A
Infiltration	0.334 ac-ft
Porous Pavement	N/A
Dry Swale	N/A
Green Roof	N/A
Rain Garden	N/A
Stormwater Planters	N/A
Cisterns/Rain Barrels	N/A
Bioretention (Filtration)	N/A
Infiltration Trenches	0.058 ac-ft

Runoff Reduction volume= 0.392 ac-ft

Total Runoff Reduction Volume	0.755 ac-ft
Total WQv Reduced	0.755 ac-ft
Total WQv to be Treated by Standard Practices	0.000 ac-ft

The total runoff reduction volume of 0.755 ac-ft for the project site is greater than the water quality volume of 0.641 ac-ft. Approximately 118% of the water quality volume has been reduced using green infrastructure practices. Additionally, all new impervious areas are treated by proposed infiltration practices.

6.5 Standard Stormwater Management Practices to Treat Water quality Volume not Addressed by Green Infrastructure Techniques

All the green infrastructure practices have been evaluated and included in the design where possible. The RRv requirement has been satisfied and the SWPPP complies with the required sizing criteria. A description of the stormwater management basin is included in Section 7.3.

7.0 Hydrologic and Hydraulic Analysis

The amount of stormwater runoff generated from the subject parcels after development is completed should not be greater than the stormwater runoff generated prior to development. To ensure the pre-development stormwater discharge is less than or equal to post-development stormwater discharge, the 1- year, 10-year, 25-year and 100-year storm events were considered for the design of the stormwater management plan.

The first step in completing the watershed model is to determine the contributing drainage areas for both the pre-development and post-development conditions. The times of concentration and runoff curve numbers (CN) were then calculated for each watershed area. This data was then entered into the HydroCAD computer program. HydroCAD, developed by Applied Microcomputer Systems of Chocorua, New Hampshire, is a Computer-Aided-Design (CAD) program for analyzing the hydrologic and hydraulic characteristics of a given watershed and associated stormwater management facilities. HydroCAD is used to calculate peak runoff flows and to create hydrographs for the four storms evaluated for both pre-development and post development conditions.



7.1 Existing Pre-Development Conditions

Following a review of existing topography and site conditions, eight (8) subcatchment and eight (8) design points have been identified for the subject site and the stormwater management analysis. The analysis area includes the developed portions of the parcel with a total of 72.73 acres.

Design Point 1 is located at the existing low area located at the northwestern corner of the project area boundary. The drainage area to Design Point 1 (Subcatchment 1) has a contributing area of approximately 3.54-acres. The existing cover within the subcatchment includes existing impervious area, grassed lawn, and woods. Stormwater originating from Subcatchment 1 predominantly flows overland to the west to the existing low area at Design Point 1.

Design Point 2 is located at the existing wetland complex in the northeastern portion of the project area. The drainage to Design Point 2 (Subcatchment 2) has a contributing area of approximately 8.10-acres. The existing cover within the subcatchment includes existing impervious area, grassed lawn, and woods. Stormwater originating from Subcatchment 2 predominantly flows overland to the east to the existing wetland complex at Design Point 2.

Design Point 3 is located at an existing low area located in the northwestern portion of the project area. The drainage to Design Point 3 (Subcatchment 3) has a contributing area of approximately 9.53-acres. The existing cover within the subcatchment consists of dense woods. Stormwater originating from Subcatchment 3 flows overland from all directions to the existing low area at Design Point 3.

Design Point 4 is located at the existing wetland complex in the central portion of the project area. The drainage to Design Point 4 (Subcatchment 4) has a contributing area of approximately 18.52-acres and consists of dense woods. Stormwater originating from Subcatchment 4 flows overland from all directions to the existing wetland complex at Design Point 4.

Design Point 5 is located at an existing drainage course along the western project area boundary. The drainage to Design Point 5 (Subcatchment 5) has a contributing area of approximately 4.47-acres and consists of dense woods and a small grass area. Stormwater originating from Subcatchment 5 flows overland from east to the west and continues offsite following the existing drainage course at Design Point 5.

Design Point 6 is located at an existing wetland complex in the central portion of the project area. The drainage to Design Point 6 (Subcatchment 6) has a contributing area of approximately 12.94-acres and consists of dense woods. Stormwater originating from Subcatchment 6 flows overland from all directions to the existing wetland complex at Design Point 6.

Design Point 7 is located at an existing low area along the western project area boundary in the southwestern corner of the parcel. The drainage to Design Point 7 (Subcatchment 7) has a contributing area of approximately 5.27-acres and consists of dense woods and a small grass area. Stormwater originating from Subcatchment 7 flows overland from east to the west to the existing low area at Design Point 7.

Design Point 8 is located at an existing low area in the southern portion of the project area. The drainage to Design Point 8 (Subcatchment 8) has a contributing area of approximately 10.36-acres and consists of dense woods. Stormwater originating from Subcatchment 8 flows overland from north to south to and existing low area at Design Point 8.



7.2 Proposed Post-Development Watershed Conditions

Under proposed conditions, the Design Points remain in the same general location. Due to the proposed development the site has been divided into additional subcatchments to most accurately depict the developed conditions. The post-development stormwater analysis includes the identified subcatchments.

Subcatchment 1A encompasses approximately 0.55 acres located in the northwestern portion of the project area. The subcatchment includes grass and woods. Stormwater originating from Subcatchment 1A generally flows overland to the west to the existing low point at Design Point 1.

Subcatchment 1B encompasses approximately 2.54 acres located in the northern portion of the project area. This subcatchment includes grass, woods, existing impervious surfaces, and proposed impervious surfaces from the development. Stormwater originating from Subcatchment 1B will flow overland where it is conveyed to Infiltration Trench #1 where it will be treated and infiltrated into the existing ground.

Subcatchment 2A encompasses approximately 8.10 acres located in the northeastern portion of the project area. This subcatchment includes grass, woods, and existing impervious surfaces. Stormwater originating from Subcatchment 2A generally flows overland to the north and east to the existing wetland complex at Design Point 2.

Subcatchment 2B encompasses approximately 13.32 acres located in the central portion of the project area. This subcatchment includes grass, woods, and impervious surfaces from the proposed development. Stormwater originating from Subcatchment 2B will flow overland to the proposed open drainage conveyance swale system where it is conveyed to Infiltration Basin #1 where it will be treated and infiltrated into the existing ground.

Subcatchment 3A encompasses approximately 2.10 acres located in the northwestern portion of the project area. This subcatchment includes grassed lawn and woods. Stormwater originating from Subcatchment 3A will flow overland to the west to the existing low area at Design Point 3.

Subcatchment 4A encompasses approximately 16.72 acres located in the central portion of the project area. This subcatchment includes grassed lawn and woods. Stormwater originating from Subcatchment 4A will flow overland from all directions to the existing wetland complex at Design Point 4.

Subcatchment 5A encompasses approximately 1.79 acres located in the western portion of the project area. This subcatchment includes grassed lawn and woods. Stormwater originating from Subcatchment 5A will flow overland to the west where it continues offsite following the existing drainage course at Design Point 5.

Subcatchment 6A encompasses approximately 11.98 acres located in the southeastern portion of the project area. This subcatchment includes grassed lawn and woods. Stormwater originating from Subcatchment 6A will flow overland from all directions to the existing wetland complex at Design Point 6.

Subcatchment 7A encompasses approximately 5.27 acres located in the southwestern corner of the project parcel. This subcatchment includes grassed lawn and woods. Stormwater originating from Subcatchment 7A will flow overland to the west to the existing low area at Design Point 7.



Subcatchment 8A encompasses approximately 10.36 acres located in the southern portion of the project area. This subcatchment includes existing woods. Stormwater originating from Subcatchment 8A will flow overland from the north to the south where it is collected at an existing low area at Design Point 8.

The pre-development and post-development peak discharge rates at the identified Design Points for the 1, 10, 25, and 100-year storms **prior** to mitigation are as follows:

	1-YR	10-YR	25-YR	100-YR
PRE-DEVELOPMENT	cfs	cfs	cfs	cfs
DESIGN POINT 1	0.00	0.02	0.11	0.94
DESIGN POINT 2	0.00	0.02	0.09	1.23
DESIGN POINT 3	0.00	0.00	0.06	0.94
DESIGN POINT 4	0.00	0.00	0.12	2.17
DESIGN POINT 5	0.00	0.00	0.03	0.53
DESIGN POINT 6	0.00	0.00	0.08	1.33
DESIGN POINT 7	0.00	0.00	0.03	0.62
DESIGN POINT 8	0.00	0.00	0.06	1.15
POST-DEVELOPMENT	Cfs	cfs	cfs	cfs
DESIGN POINT 1	0.00	0.21	0.64	2.39
DESIGN POINT 2	0.06	2.58	6.32	16.24
DESIGN POINT 3	0.00	0.00	0.06	0.94
DESIGN POINT 4	0.00	0.00	0.10	1.96
DESIGN POINT 5	0.00	0.00	0.01	0.28
DESIGN POINT 6	0.00	0.00	0.07	1.23
DESIGN POINT 7	0.00	0.00	0.03	0.62
DESIGN POINT 8	0.00	0.00	0.06	1.15

These post development volume and discharge values represent the post development condition without any designed stormwater management areas in relation to existing conditions. The post-development stormwater discharge must be mitigated.

7.3 Proposed Water Quantity and Quality Controls

The post development runoff rates for the developed site are higher than the pre-development rates; therefore, mitigation is required to properly regulate post development runoff. The area that the post-development hydrograph exceeds the pre-development hydrograph equals the volume of water that needs to be mitigated by implementing stormwater management basins.

The proposed stormwater management system for this site has been designed with provisions to store and treat the water quality volume, channel protection volume, overbank flood protection volume and extreme storm flood protection volume for the developed portions of the project parcel. The proposed stormwater management systems have been included with the proposed development considering various site constraints and the Town of Wilton regulations.

Stormwater Infiltration Basin #1

In order to reduce post-development discharge rates below pre-development discharge rates and to provide water quality treatment, a stormwater infiltration basin has been included in the design of the project. The infiltration basin is located in the northeastern portion of the developed site. This practice has been chosen due to project area existing soil conditions and the need to provide runoff reduction. The New York State Stormwater Management Design Manual requires the infiltration basin variation I-2 to receive a maximum of 25 acres on contributing area. This system will collect and treat stormwater runoff from approximately 13.32 acres of the developed portions of the site. The infiltration basin will be pre-treated by a forebay prior to stormwater entering the infiltration basin area. Stormwater will be directed to the infiltration basin where it will be stored and infiltrate into the existing ground.

Stormwater Infiltration Basin #1 is located in the northeastern portion of the project site. The infiltration basin has been designed with a bottom of basin elevation of 323.50' which provides 2' of separation from the bottom of the basin to groundwater. This system collects and treats the stormwater from approximately 13.32 acres of the developed portions of the site. Stormwater Infiltration Basin #1 has been modeled with a conservative infiltration rate of 3.5 inches/hour to account for potential future sedimentation inside the infiltration basin. Actual soil tests indicate that the infiltration rate of the soil in this area is 7 inches/hour.

The water quality volume (WQv) is designed to improve water quality sizing to capture and treat 90% of the average annual stormwater runoff volume. The water quality volume is directly related to the amount of impervious cover created at the site. The WQv is 0.334 ac-ft for the Stormwater Infiltration Basin #1. The NYSDEC Stormwater Design Manual indicates that 25% of the WQv is to be pretreated for soil percolation rates of 7 inches per hour. Pretreatment is provided by a forebay and includes 3,821 cf of volume storage which is greater than the required 3,635 cf. This pretreatment will prolong the life of the infiltration basin.

The stream channel protection volume requirements are designed to protect stream channels from erosion. In New York State this goal is accomplished by providing 24-hour extended detention of the one-year, 24-hour storm event. The entire stream channel protection volume will be stored and infiltrated by Stormwater Infiltration Basin #1.

The primary purpose of the overbank flood control sizing is to prevent an increase in the frequency and magnitude of out-of-bank flooding generated by urban development. Overbank control requires storage to attenuate the post-development 10-year, 24-hour peak discharge rate to pre-development rates. The entire overbank flood control volume will be stored and infiltrated by Stormwater Infiltration Basin #1.

The intent of the extreme flood criterion is to prevent the increased risk of flood damage from large storm events, maintain the boundaries of the pre-development 100-year floodplain and protect the physical integrity of stormwater management practices. Extreme flood protection requires storage to attenuate the post-development 100-year, 24-hour peak discharge rate to pre-development rates. The entire extreme flood protection volume will be stored and infiltrated by Stormwater Infiltration Basin #1.

A rating table (stage/storage/discharge) was then developed for the proposed infiltration basin based on the geometry of the system, characteristics of the water quality volume, channel protection volume, overbank flood protection volume and extreme storm flood protection volume for each drainage area. The proposed infiltration basin has been designed to include an emergency overflow spillway for storms greater than the 100-year storm event.



Stormwater Infiltration Basin #1:

Peak Inflows	Peak Infiltration	High Water Elevation	Freeboard
Q ₁ = 0.03 cfs	Q ₁ = 0.03 cfs	323.50'	2.50'
Q ₁₀ = 1.59 cfs	Q ₁₀ = 1.36 cfs	323.54'	2.46'
Q ₂₅ = 4.71 cfs	Q ₁₀ = 1.46 cfs	323.85'	2.15'
Q ₁₀₀ = 15.11 cfs	Q ₁₀₀ = 1.80 cfs	324.90'	1.10'

- Basin Bottom = 323.50', Top of Bank = 326.00', Emergency Spillway = 325.00'

Stormwater Infiltration Trench #1

In order to reduce post-development discharge rates below pre-development discharge rates and to provide water quality treatment, a stormwater infiltration trench has been included in the design of the project. The infiltration trench is located in the northwestern corner of the developed site. This practice has been chosen due to project area existing soil conditions and the need to provide runoff reduction. The New York State Stormwater Management Design Manual requires the infiltration trench variation I-1 to receive a maximum of 5 acres on contributing area. This system will collect and treat stormwater runoff from approximately 2.54 acres of the developed portions of the site. The infiltration trench will be pretreated by grass filter strips prior to stormwater entering the infiltration trench area. Stormwater will be directed to the infiltration trench where it will be stored and infiltrate into the existing ground.

Stormwater Infiltration Trench #1 is located in the northwestern corner of the project site. The infiltration trench has been designed with a bottom of trench elevation of 321.00' which provides 2' of separation from the bottom of the trench to groundwater. This system collects and treats the stormwater from approximately 2.54 acres of the developed portions of the site. Stormwater Infiltration Trench #1 has been modeled with a conservative infiltration rate of 15 inches/hour to account for potential future sedimentation inside the infiltration trench. Actual soil tests indicate that the infiltration rate of the soil in this area is 33 inches/hour.

The water quality volume (WQv) is designed to improve water quality sizing to capture and treat 90% of the average annual stormwater runoff volume. The water quality volume is directly related to the amount of impervious cover created at the site. The WQv is 0.058 ac-ft for the Stormwater Infiltration Trench #1. The NYSDEC Stormwater Design Manual indicates that 50% of the WQv is to be pretreated for soil percolation rates of 33 inches per hour. Pretreatment is provided by grass filter strips a minimum of 15' in length. This pretreatment will prolong the life of the infiltration trench.

The stream channel protection volume requirements are designed to protect stream channels from erosion. In New York State this goal is accomplished by providing 24-hour extended detention of the one-year, 24-hour storm event. The entire stream channel protection volume will be stored and infiltrated by Stormwater Infiltration Trench #1.

The primary purpose of the overbank flood control sizing is to prevent an increase in the frequency and magnitude of out-of-bank flooding generated by urban development. Overbank control requires storage to attenuate the post-development 10-year, 24-hour peak discharge rate to pre-development rates. The entire overbank flood control volume will be stored and infiltrated by Stormwater Infiltration Trench #1.

The intent of the extreme flood criterion is to prevent the increased risk of flood damage from large storm events, maintain the boundaries of the pre-development 100-year floodplain and protect the physical integrity of stormwater management practices. Extreme flood protection requires storage to attenuate



the post-development 100-year, 24-hour peak discharge rate to pre-development rates. The entire extreme flood protection volume will be stored and infiltrated by Stormwater Infiltration Trench #1.

A rating table (stage/storage/discharge) was then developed for the proposed infiltration trench based on the geometry of the system, characteristics of the water quality volume, channel protection volume, overbank flood protection volume and extreme storm flood protection volume for each drainage area.

Stormwater Infiltration Trench #1:

Peak Inflows	Peak Infiltration	High Water Elevation	Freeboard
Q ₁ = 0.00 cfs	Q ₁ = 0.00 cfs	322.00'	4.00'
Q ₁₀ = 0.21 cfs	Q ₁₀ = 0.21 cfs	322.01'	3.99'
Q ₂₅ = 0.64 cfs	Q ₁₀ = 0.65 cfs	322.03'	3.97'
Q ₁₀₀ = 2.37 cfs	Q ₁₀₀ = 1.48 cfs	323.99'	2.01'

- Trench Stone Bottom = 322.00', Top of Trench Stone = 324.00', Top of Swale Area = 326.00' (Freeboard measured from top of swale)

The proposed stormwater flows will not adversely affect the downstream receiving waters. A comparison of pre-and post-development discharge after installation of mitigation is shown below:

	1-YR	10-YR	25-YR	100-YR
PRE-DEVELOPMENT	cfs	cfs	cfs	cfs
DESIGN POINT 1	0.00	0.02	0.11	0.94
DESIGN POINT 2	0.00	0.02	0.09	1.23
DESIGN POINT 3	0.00	0.00	0.06	0.94
DESIGN POINT 4	0.00	0.00	0.12	2.17
DESIGN POINT 5	0.00	0.00	0.03	0.53
DESIGN POINT 6	0.00	0.00	0.08	1.33
DESIGN POINT 7	0.00	0.00	0.03	0.62
DESIGN POINT 8	0.00	0.00	0.06	1.15
POST-DEVELOPMENT	Cfs	cfs	cfs	cfs
DESIGN POINT 1	0.00	0.00	0.00	0.08
DESIGN POINT 2	0.00	0.02	0.09	1.14
DESIGN POINT 3	0.00	0.00	0.06	0.94
DESIGN POINT 4	0.00	0.00	0.10	1.96
DESIGN POINT 5	0.00	0.00	0.01	0.28
DESIGN POINT 6	0.00	0.00	0.07	1.23
DESIGN POINT 7	0.00	0.00	0.03	0.62
DESIGN POINT 8	0.00	0.00	0.06	1.15

Post development peak stormwater discharge is less than or equal to pre-development peak stormwater discharge for all storm events analyzed. The stormwater management systems have been sized to provide sufficient capacity to treat up to and including the 100-year storm event. Emergency overflows have been included in the design to release storms greater than the 100-year storm. The excess stormwater from these extremely rare events will flow through the overflow and overland to the existing drainage course.

8.0 Climate Change Considerations

This section describes the design considerations associated with this project in respect to climate change.

8.1 Physical Risks Due to Climate Change

This project has taken steps to limit the physical risks due to climate change into account through site planning, location, elevation, and sizing of the stormwater systems. The following provides greater details on how each of the preceding items has been considered with respect to climate change:

Overall Site Planning:

- *Increasing Temperature:* The overall site plan has been designed to limit the potential impacts of increasing temperature by limiting the impervious surfaces to only what is necessary for the project to remain functional. This will reduce the heat-island effect for the overall site.
- *Increasing Precipitation:* The overall site plan has been designed to limit the effects of possible future increasing precipitation by providing positive drainage away from all proposed buildings and structures. Additionally, impervious surfaces have been limited to only what is necessary for the project to remain functional.
- *Increasing Variability in Precipitation, including chance of draught:* The overall site plan has been designed to limit the possible effects of variability in precipitation, including the chance of draught by ensuring proper drainage and incorporating drought resistant plantings where appropriate.
- *Increasing frequency and severity of flooding:* The overall site plan has been designed to limit the possible effects of increasing frequency and severity of flooding by ensuring key features of the project such as buildings and access points are out of the flood plain. Stormwater management systems have also been designed with excess capacity.
- *Rising Sea Level:* The overall site plan will not be affected by the potential rise in sea levels as the project is situated well above projected sea level increases.
- *Increase in Storm Surge:* The overall site plan will not be affected by the possible increase in storm surge as the project is not located near a large enough body of water that could produce a storm surge.
- *Shifting Ecology:* The overall project site plan has been evaluated and protects against the potential for shifting ecology by locating the development in less sensitive areas and preserving natural features to the greatest extent possible.

Location, Elevation, and Sizing of Control Measures and Practices, Conveyance Systems, and Detention Systems:

- *Increasing Temperature:* Location, elevation, and sizing of control measures and practices, conveyance systems, and detention systems have been designed to limit the potential impacts of increasing temperature by designing these systems and components



in a manner that promotes infiltration to the greatest extent possible. This process will then reduce the evaporation on site due to potential increases in temperature.

- *Increasing Precipitation:* Location, elevation, and sizing of control measures and practices, conveyance systems, and detention systems have been designed to limit the effects of possible future increasing precipitation by providing additional capacity on the systems and components as well as overflow contingencies should any of the systems become overwhelmed.
- *Increasing Variability in Precipitation, including chance of draught:* Location, elevation, and sizing of control measures and practices, conveyance systems, and detention systems have been designed to limit the possible effects of variability in precipitation, including the chance of draught by promoting infiltration conveyance systems and drought resistant plantings with deep roots to the greatest extent possible.
- *Increasing frequency and severity of flooding:* Location, elevation, and sizing of control measures and practices, conveyance systems, and detention systems have been designed to limit the possible effects of increasing frequency and severity of flooding by ensuring the site includes overflow contingencies for extreme storm events as well as locating the storm system components above any flood plain.
- *Rising Sea Level:* Location, elevation, and sizing of control measures and practices, conveyance systems, and detention systems will not be affected by the potential rise in sea levels as the project is situated well above projected sea level increases.
- *Increase in Storm Surge:* Location, elevation, and sizing of control measures and practices, conveyance systems, and detention systems will not be affected by the possible increase in storm surge as the project is not located near a large enough body of water that could produce a storm surge.
- *Shifting Ecology:* Location, elevation, and sizing of control measures and practices, conveyance systems, and detention systems has been designed to protect against the potential for shifting ecology by locating the storm system components in less sensitive areas while incorporating natural features to the greatest extent possible.

9.0 Permanent Stormwater Management System Features

This section describes the permanent features of the Stormwater Management System for proposed development, including storm sewer piping and stormwater basins. In all instances, the structures associated with the stormwater management system have been sized to accommodate peak flows from the 10-year design storm event.

See the Construction Plans for the location, size, quantity and details of the permanent stormwater management features.

9.1 Conveyance Piping

Storm runoff from developed areas will be conveyed to the stormwater basin by means of storm sewers. In general, piping is designed such that:



-
- All conveyance piping is sized to accommodate the peak flow from the 10-year 24-hour design storm.
 - Flow capacity is sufficient to convey runoff to the receiving basin or ditch without overflowing the ditch or drop inlet at the entrance of the culvert.
 - All storm drainage pipes are designed such that the projected velocities from the design storm are greater than three feet per second, and
 - Strength is sufficient to withstand the soil cover and vehicle loads.

9.2 Stormwater Management System

The following design criteria shall apply to the design of storm drainage facilities:

- All storm drainage facilities shall be designed based on a ten-year (10) storm frequency.
- Peak runoff rates from the project site after development shall not exceed pre-development peak runoff rates.
- Adequate storage facilities shall be provided for the site to store the additional runoff volume due to development of the project site for a ten-year, twenty-five-year and one-hundred-year storm frequency.
- Provisions, such as overflow studies shall be made for protection against property damage and loss of life for more severe storms (100-year storm).

10.0 Stormwater Erosion and Sediment Controls

Several types of permanent and temporary storm water pollutant controls are required to be installed and implemented pre-construction, during construction and post-construction as shown on the Construction Plans and per the NYSDEC SPDES General Permit. Guidelines and recommendations can be found in the “New York Standards and Specifications for Urban Erosion and Sediment Control.”

The permanent storm water management system has been designed to accommodate peak storm flows utilizing drainage ditches, conveyance channels, piping and a stormwater management basin. These permanent features should be installed and constructed as shown on the Construction Plans.

Selection of temporary storm water controls will be on an “as needed basis” and will depend on the specific conditions of the site. Since site characteristics can change significantly during construction, it is important to monitor the site regularly to ensure the proper selection and implementation of the necessary controls. These controls include, but are not limited to silt fence, drainage swales, check dams, hay bales, stone construction entrances, sediment traps and seed and mulch.



10.1 Erosion and Sediment Controls

Temporary Stabilization

Silt fences, drainage swales, check dams, stabilized stone construction entrances, sediment traps and seed and mulch and other controls will be utilized as temporary surface water management features. Silt fence will be used as necessary to reduce the sediment load in the receiving drainage ditches. In addition, silt fencing will be placed on the downslope sides of all disturbed areas (5 ft.) from the toe of the slope until more permanent drainage and erosion control structures are established. Check dams will be placed along the permanent drainage ditches in which vegetation is being established. Stone check dams will be placed in ditches to control flow velocity and reduce sedimentation. See the Construction Plans for the location, size, quantity, and details of the temporary stormwater management features. Steep slopes and exposed soils should be stabilized with silt fences, mulching blankets, geotextiles, geosynthetic drainage netting, seed and mulch, or any other stabilization measure shall be used that will significantly reduce the risk of erosion. Stabilization measures must be initiated by the end of the next business day and completed within fourteen (14) days from the date of the current soil disturbance activity ceased.

Permanent Stabilization

Permanent stormwater management features as described above include drainage ditches, conveyance channels, piping and stormwater management basin. In all instances, the structures associated with the stormwater management system have been sized to accommodate peak flows from the appropriate storm events as required by the Town of Wilton. All lawns, basins and swales will be permanently seeded and mulched and maintained as necessary to prevent overgrowth.

10.2 Other Pollutant Controls

Paints and Solvents

During construction, temporary structures such as construction trailers may be moved on site to store items such as paints, solvents and gasoline pertinent to the continuation of construction activities. The intention of these structures is to shelter potential contaminants from stormwater and reduce the potential of toxic chemicals from entering the stormwater runoff due to construction activities.

Solvents and detergents may be stored on-site that will be used for regular cleaning and maintenance of construction vehicles or temporary structures. Solvents shall be used in cleaning machinery pursuant to 6 NYCRR Part 750. After use, solvents shall be disposed of in approved containers and removed from site at scheduled intervals. Vehicle wash water that contains detergents must be disposed of into the sanitary sewer.

Fuels

Fuel for construction equipment shall either be obtained from a licensed distributor of petroleum products or from an approved above ground storage tank on site. A distributor may be contracted to arrive on site periodically and fill all equipment as necessary. All distributors of petroleum products must have adequate liability insurance to mitigate and clean up any spills that occur on site as well as obtain appropriate permits and licenses from the NYSDEC. All above ground storage tanks with a combined capacity of 1,100 gallons shall be installed pursuant to 6 NYCRR Part 614 Standards for New and Substantially Modified Petroleum Storage Facilities.



Fuel from construction vehicles may come into contact with stormwater when vehicles are stored outside. Good housekeeping and preventative maintenance procedures shall be implemented to ensure fuel spills and leaks are minimized during refueling and storage. Any small-scale fuel or oil spills must be remedied immediately, and contaminated soils shall be disposed of appropriately. The designated spill prevention and response team shall handle large-scale gasoline spills.

Oil and other petroleum products may be stored on site in limited quantities to ensure the continued operation of construction equipment in the event a scheduled delivery is unavailable. Items shall be stored in their original containers within temporary structures and shall not be exposed to stormwater. Used oil and petroleum products shall be stored in approved containers until recycled or disposed of at an approved disposal facility.

Temporary Facilities

Temporary sanitary facilities may be located on site for construction workers. This facility shall be in an accessible and visible location. Such a facility shall be leak and tip proof. A waste management company may be contracted to arrive on site and provide the routine pumping and sanitization of the facility. Such a company shall have adequate liability insurance to mitigate and clean up any spills that occur on site as well as appropriate permits and licenses from the NYSDEC.

Dust Control

Construction traffic must enter and exit the site at the stabilized construction entrance. The purpose is to trap dust and mud that would otherwise be carried off-site by construction traffic. Water trucks will be used as needed during construction to reduce dust generated on the site. Dust control must be provided by the General Contractor to a degree that is acceptable to the Owner, and in compliance with applicable local and state dust control regulations.

Solid Waste

No solid materials, including building materials and concrete washout wastewater, are allowed to be discharged from the site with storm water. All solid waste, including disposable materials incidental to the major construction activities, must be collected and placed in containers. The containers will be emptied periodically by a contract trash disposal service and hauled away from the site.

Thermal Pollution

Stormwater that meets roadways, driveways, parking lots or other impermeable surfaces may increase in temperature during warm weather. If stormwater is discharged into surface water bodies, the temperature of the water body may also increase, potentially threatening plant and animal species sensitive to temperature changes as well as providing an environment that may cause nuisance species to flourish.

After development is complete, impervious areas shall be graded to channel water to catch basins and culverts, which in turn convey stormwater to the stormwater management basins. All stormwaters shall be stored and treated within the basin before it is released to downstream water bodies. Prior to release the stormwater will be retained in the stormwater management area and during the retention time the stormwater will be cooled by the ambient temperature of the earth. Treatment of the stormwater in the basin will reduce any threat of raising the temperature of any downstream waterbodies.



10.3 Best Management Practices

Throughout construction, care shall be taken to ensure sediment does not enter surface water bodies and chemicals do not enter stormwater, potentially contaminating surface and groundwater supplies. The following Best Management Practices (BMP) shall be observed to maintain responsible environmental practices on the construction site.

Good Housekeeping

Good housekeeping is essential to reducing the risk of contaminating runoff waters during every stage of construction. The General Contractor shall ensure supervisors train each employee in good housekeeping practices as they pertain to the implementation of this SWPPP.

Immediately following mobilization, the General Contractor shall take an inventory of all equipment and containers containing hazardous or toxic materials and submit this inventory to the Owner to keep on-site with this Stormwater Pollution Prevention Plan. This inventory shall be updated regularly to reflect changes in the quantity or type of hazardous and toxic materials stored on site. In the event of a spill, the Spill Response Team can refer to the inventory if the contents of the spill are unknown.

All equipment shall be operational while it is stored on site. Inspections shall be conducted regularly to ensure all equipment is free of leaks and that oil and grease are not in contact with soils or stormwater. Portable equipment such as chain saws, drills as well as hand tools must be placed within a trailer or under cover at the end of each workday.

A storage area shall be designated on-site where all hazardous or toxic materials are stored. Each employee shall return the materials to the designated storage area following use. Chemicals, including oil, grease, solvents and detergents shall be stored on-site in approved containers only. Used chemicals shall be disposed of in refuse containers and removed periodically. Containers shall be regularly inspected to ensure the integrity of the container and seals to prevent leaks.

A scheduled clean-up shall occur at the end of each workweek. During this clean up, empty containers of solvents, oils, grease, paints and detergents shall be disposed of, containers of gasoline shall be placed in trailers where they are not in contact with stormwater and the inventory shall be updated. Empty containers shall not be permitted on the ground.

Preventative Maintenance

All on-site vehicles must be inspected regularly for oil and grease leaks. All leaks shall be repaired immediately upon obtaining the appropriate equipment. If the leak cannot be fixed immediately, it shall be temporarily mitigated to prevent the flow of contaminants onto the soil and potentially into the stormwater. If necessary, the reservoir will be drained to stop the flow of contaminants, or the vehicle will be moved under cover. Drip pans shall be used when performing any maintenance or cleaning on construction vehicles.

Spill Prevention and Response

The safety of employees and neighbors shall be of utmost concern when hazardous or toxic chemicals are stored or utilized on-site. Materials Safety Data Sheets (MSDS) shall be obtained for all toxic or hazardous



substances that are stored on-site to provide employees with a valuable database in assessing risk in the event of a spill.

Any above ground storage tanks on site shall be installed pursuant to 6 NYCRR Part 614. According to the New York State “Minimum Standards for New and Substantially Modified Above Ground Storage Facilities”, all tanks installed must meet or exceed the design criteria in one or more of the following design or manufacturing standards: UL No. 142, UL No. 58, API Standard No. 650, API Standard No. 620, CAN4-S601-M84 or CAN4-S630-M84. Tanks constructed of wood, concrete, aluminum, fiberglass reinforced plastic as well as riveted or bolted steel tanks are not permitted. All tanks must have installed leak detection systems, secondary containment, corrosion protection, and undergo periodic monitoring pursuant to all Part 614 requirements.

Should a spill occur, trained individuals shall be always on-call to mitigate the potential negative effects of a spill. The General Contractor shall have trained employees knowledgeable in the location of sorbent, brooms, rags and mops in the event of a small-scale spill. An inventory of equipment and its location shall be posted in a visible location as well as kept in proximity to this Pollution Prevention Plan. If the General Contractor does not have Hazardous Materials trained employees on site, a firm that specializes in handling spills, soil and water contamination shall be called.

After a spill occurs, all personnel not trained in hazardous materials spill response shall be asked to evacuate the immediate area. The New York State NYSDEC of Environmental Conservation (NYSDEC) Spill Response Team shall be called at 1-(800)-457-7362 to investigate the spill and determine if additional actions should be taken to ensure the safety of personnel and nearby residents. Should any employee have a suspected injury, a local emergency squad must be contacted immediately.

11.0 Construction Sequence Scheduling

A phased construction sequence schedule of the project will limit the acreage of exposed soils at any given time to less than five (5) acres. Limiting the exposed soils will reduce the amount of sediment in runoff water and ultimately preserve the quality of surface waters. The construction phasing method selected is designed to combine development with responsible land management as well as protection of sensitive environments both within the proposed development and the surrounding area. Temporary and permanent stabilization methods will be implemented before construction begins and will be continuously modified throughout the project to provide the best methods for stormwater management and pollution prevention. For more details pertaining to construction sequence, please refer to the “NYSDEC Instruction Manual for Stormwater Construction Permit” pages 23-26.

Phasing of activities is as follows:

Pre-Construction Activities

- Identify all natural resources and mark and protect them as necessary i.e trees, vegetation, wetlands.
- Identify on-site and downstream surface water bodies and install controls to protect them from sedimentation.
- Establish temporary stone construction entrance pads to capture mud and debris from the tires of construction vehicles.
- Install perimeter sediment controls such as silt fence as shown on the project plans.
- All earth disturbance during this phase should be limited to work necessary to install erosion and sedimentation controls.



During Construction Activities

- Install principal sediment basin as shown on the project plans.
- Install runoff and drainage controls as shown on the project plans and as necessary. These controls should reduce run-off flow rates and velocities as well as divert off site and clean run-off.
- Stabilize the conveyance system i.e., ditches, swales, berms etc. by seeding, mulching, installing rock check dams.
- Utilize practices to infiltrate the run-off as much as possible when applicable.
- Stabilize all run-off outlets as shown on the project plans and as necessary.
- Limit soil disturbance to small areas and preserve as much of the existing vegetation as practical.
- Earth disturbance should be limited to 5 acres without prior approval from the NYSDEC.
- All topsoil stockpiles should be staged in an area away from surface waters and storm drains and should be protected and stabilized.
- Earth disturbance is not allowed in established buffers, within any regulated distance from wetlands, within the high-water line of a body of water affected by tidal action or other such protected zones.
- At any location where surface run-off from disturbed or graded areas may flow off-site, sedimentation control measures must be installed to prevent sedimentation from being transported.
- Regular inspections and maintenance should be performed as described in the following section.
- The infiltration trenches shall not be utilized as sediment control devices during site construction and shall not be constructed until all the contributing drainage area has been completely stabilized.

Post-Construction Activities

- Identify the permanent structural or non-structural practices that will remain on the site.
- Provide an Operation & Maintenance (O&M) manual to the new Owner who is expected to conduct the necessary O&M over the life of the structures as described in Section 10.0 of this report.

12.0 Implementing the SWPPP

12.1 Employee Training

All employees on-site shall be aware of the stipulations outlined in this SWPPP as it pertains to their everyday activities. All employees must be able to recognize potential problems and could provide either temporary or permanent stabilization measures, as appropriate, to mitigate stormwater runoff before problems occur. The NYSDEC periodically holds workshops on erosion and sediment control. It is recommended that on-site personnel attend these workshops for training current and up to date. Contact the NYSDEC for more information.

12.2 Site Inspections

The Owner must have a qualified professional assess the site prior to the commencement of construction and certify in an inspection report that the appropriate erosion and sediment controls described in this SWPPP have been adequately installed or implemented to ensure overall preparedness of the site for the commencement of construction. A qualified professional is defined as a Professional Engineer or Landscape Architect licensed to practice in New York State or is a Certified Professional in Erosion and Sediment Control (CPESC). For sites where disturbances are limited to less than five acres, regular inspection of construction activities by the qualified professional are required at least once every 7 days



to ensure deficiencies regarding erosion and sedimentation are reported and corrected. Inspection reports will be provided to the Owner and all contractors and subcontractors involved with earth disturbing activities within one business day of the field inspection. The inspector shall sign the certifying statements contained at the end of the inspection reports. The inspection reports must be in accordance with Part IV. C.4 and 6 of GP-0-25-001.

At a minimum, the qualified inspector shall inspect all erosion and sediment control practices to ensure integrity and effectiveness, all post-construction stormwater management practices under construction to ensure that they are constructed in conformance with the SWPPP, all areas of disturbance that have not achieved final stabilization, all points of discharge to natural surface waterbodies located within, or immediately adjacent to, the property boundaries of the construction site, and all points of discharge from the construction site.

For sites where disturbances are greater than five acres, regular inspection of construction activities by the qualified professional are required every 3 days to ensure deficiencies regarding erosion and sedimentation are reported and corrected. It is the responsibility of the Contractor to continuously monitor construction activities to ensure the measures outlined in this report are being implemented.

Areas which have not been fully stabilized, areas used for materials storage and all structural control measures must be inspected once every seven calendar days to monitor erosion and assess the risk of sedimentation. The Owner or Contractor shall be responsible for monitoring precipitation amounts. Precipitation must be obtained from a reliable meteorological data source, or a rain gauge can be installed on site. If a rain gauge is installed, it should be monitored after each storm event.

Each year, a thorough site evaluation shall be performed to determine the continued applicability of the permit, and assess the need to make any changes that have not already been reflected in this SWPPP. The SWPPP shall be reviewed to evaluate its overall effectiveness in preventing sediment laden stormwater runoff. Temporary and permanent stabilization methods shall be assessed, and new methods shall be established, should any method be determined to be inadequate.

A copy of the SWPPP must be maintained on site at all times in the field log book. The Owner must maintain a record of all inspection reports with the on-site SWPPP. The SWPPP and inspection reports must be maintained on-site and be made available to the permitting authority upon request.

12.3 Maintenance

It shall be necessary to maintain all temporary controls installed as well as vegetative measures across the site. Maintenance shall also be necessary to ensure the permanent structural features, such as the stormwater management basins and conveyance piping remain optimally functional and continue to reduce the risk of sediment loading of surface water bodies. All controls shall be repaired or replaced as necessary and as noted on the inspection reports as prepared by the Owner's Engineer.

During construction, maintenance of these stabilization measures shall be the responsibility of the General Contractor or appropriate Sub Contractors. Vegetative plantings must not be allowed to become overgrown. Vegetation shall be removed should it be ineffective and be replaced with a variety of grasses, trees and shrubs more suitable for preventing stormwater runoff. Silt fences must be inspected regularly to ensure that they are still effective and their capability to reduce stormwater runoff has not been reduced due to prolonged sun exposure.



Piping and catch basin sumps shall be cleaned out periodically to prevent the collection of sediment that will reduce the maximum flow. Sediment must be removed from sediment basins, infiltration basins or traps whenever their capacity has been reduced by 50 percent of their design capacity. Within the stormwater management basin, as maintenance occurs the elevation of the basin will be pumped down via a portable pump until the elevation permits maintenance to occur.

Guidelines and recommendations for installation and maintenance practices can be found in the “New York Standards and Specifications Erosion and Sediment Control” handbook.

12.4 Progress Reports and Summaries

Progress reports shall be completed by the General Contractor and all Sub Contractors weekly to document any conditions, which may affect adherence to the construction schedule and may ultimately result in changes to the stormwater pollution prevention plan.

Each progress report must contain the project, date, weather conditions and a brief description of progress made throughout the week, including the use of temporary and permanent stabilization measures on all exposed soils. The progress reports shall be filed with this SWPPP in the on-site logbook.

Additionally, as described in Section 1.1 of this report, the Owner’s Engineer will prepare weekly inspection reports. These reports should be maintained on-site with the SWPPP in accordance with GP-0-25-001.

12.5 Certification

Prior to starting construction, the Owner must certify that to the best of their knowledge this SWPPP was prepared in accordance with the requirements in the NYSDEC SPDES General Permit and that it meets all federal, state and local erosion and sediment control requirements. The certifying statement is presented in Appendix A of this report.

The General Contractor and all appropriate Sub Contractors are responsible for reading and understanding the SWPPP and are also required to certify the SWPPP by signing the certifying statement presented in Appendix A of this report.

All inspection reports are to be certified by an authorized person who has responsibility for the overall operation of the site such as a project manager or site superintendent. Certification of these documents is executed by signing the certifying statements presented at the end of the inspection reports.

12.6 NYSDEC Winter Site Stabilization/Site Inspections for Construction Sites

A temporary site specific, enhanced erosion and sediment control plan must be developed and implemented should construction occur during winter/frozen ground conditions with soil exposure between November 15th and April 1st. The following requirements do not supersede any other requirements of this SWPPP as they apply to non-frozen ground conditions.

- Prepare a snow management plan with adequate storage for snow and control of melt water, requiring cleared snow to be stored in a manner not affecting ongoing construction activities.
- Enlarge and stabilize access points to provide for snow management and stockpiling. Snow management activities must not destroy or degrade installed erosion and sediment control



practices.

- A minimum 25 foot buffer shall be maintained from all perimeter controls such as silt fence. Mark silt fence with tall stakes that are visible above the snow pack.
- Edges of disturbed areas that drain to a waterbody within 100 feet will have 2 rows of silt fence, 5 feet apart, installed on the contour.
- Drainage structures must be kept open and free of snow and ice dams. All debris, ice dams, or debris from plowing operations, that restrict the flow of runoff and meltwater, shall be removed.
- Sediment barriers must be installed at all appropriate perimeter and sensitive locations. Silt fence and other practices requiring earth disturbance must be installed before the ground freezes.
- Soil stockpiles must be protected by the use of established vegetation, anchored straw mulch, rolled stabilization matting, or other durable covering. A barrier must be installed at least 15 feet from the toe of the stockpile to prevent soil migration and to capture loose soil.
- In areas where soil disturbance activity has temporarily or permanently ceased, the application of soil stabilization measures should be initiated by the end of the next business day and completed within three (3) days. Rolled erosion control blankets must be used on all slopes 3 horizontal to 1 vertical or steeper.
- If straw mulch alone is used for temporary stabilization, it shall be applied at double the standard rate of 2 tons per acre, making the application rate 4 tons per acre. Other manufactured mulches should be applied at double the manufacturer's recommended rate.
- To ensure adequate stabilization of disturbed soil in advance of a melt event, areas of disturbed soil should be stabilized at the end of each work day unless:
 - work will resume within 24 hours in the same area and no precipitation is forecast or;
 - the work is in disturbed areas that collect and retain runoff, such as open utility trenches, foundation excavations, or water management areas.
- Use stone paths to stabilize access perimeters of buildings under construction and areas where construction vehicle traffic is anticipated. Stone paths should be a minimum 10 feet in width but wider as necessary to accommodate equipment.

During the winter season, if a site has been stabilized and soil disturbing activities have been suspended for the winter, weekly inspections can be reduced to once a month. If the soil disturbance is completely suspended and the site is properly stabilized an owner/operator may reduce the self-inspection frequency, but shall maintain a minimum of monthly inspections in all situations (even when there is total winter shutdown).

To be allowed to reduce inspection frequencies, the operator must complete stabilization activities (perimeter controls, traps, barriers etc.) before proper installation is precluded by snow cover or frozen ground. If vegetation is desired, seeding, planting, and/or sodding must be scheduled to avoid die-off from fall frosts and allow for proper germination/establishment.

Frozen ground, winter conditions and equipment can affect erosion and sediment control practices. Check for damage during monthly inspections and repair as necessary. This is especially important during thaws



and prior to spring rain events. Weekly inspections must resume no later than March 15 or as directed by the Department.

13.0 Post Construction Operation and Maintenance

13.1 Operation and Maintenance Plan/Report

A site-specific long-term operation and maintenance manual shall be prepared in accordance with the latest NYSSDM. The plan/report shall be conveyed to the owner prior to the start of construction.

14.0 Conclusion

Lansing Engineering has designed a Stormwater Management Plan for the Bullard Lane Conservation Residential Subdivision project that reduces and/or eliminates the impacts of the proposed development by controlling and treating stormwater through the use of drainage ditches and channels, storm sewer piping, and stormwater management systems. The stormwater management systems will function adequately and will not adversely affect adjacent or downstream properties provided it is constructed and maintained as outlined in this plan and as shown on the site plans.





Appendix A:
Owner & Contractor Certification Forms

STORMWATER POLLUTION PREVENTION PLAN

CONTRACTOR CERTIFICATION

Signatory requirements as per NYSDEC SPDES General Permit for Stormwater Discharges from Construction Activities Permit No. GP-0-25-001 Part III.A.6

"I hereby certify under penalty of law that I understand and agree to comply with the terms and conditions of the SWPPP and agree to implement any corrective actions identified by the qualified inspector during a site inspection. I also understand that the owner or operator must comply with the terms and conditions of the most current version of the New York State Pollutant Discharge Elimination System ("SPDES") general permit for stormwater discharges from construction activities and that it is unlawful for any person to cause or contribute to a violation of water quality standards. Furthermore, I am aware that there are significant penalties for submitting false information that I do not believe to be true, including the possibility of fine and imprisonment for knowing violations"

Project Name and/or Address

Contractor Company Name

Address

Phone Number

email

Trained Contractor *

Title

Authorized Representative

Title

Authorized Representative Signature

Date

Please identify the specific elements of the SWPPP you will be responsible for: (Use additional sheets if required)

*A **Trained Contractor** as defined in Appendix A of the General Permit- means an employee from the contracting (construction) company, identified in Part III.A.6., that has received four (4) hours of Department endorsed training in proper erosion and sediment control principles from a Soil and Water Conservation District, or other Department endorsed entity. After receiving the initial training, the trained contractor shall receive four (4) hours of training every three (3) years.



Owner/Operator Certification Form

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(In accordance with CGP Part I.D.2.b. or Part I.F.2. and 3., the completed form must be attached to the eNOI or the Request to Continue Coverage, and submitted to NYSDEC electronically.)

Project/Site Name: _____

eNOI Submission ID: _____

eNOI Submitted by: **Owner/Operator** **SWPPP Preparer** **Other**

Certification Statement - Owner/Operator

I hereby certify that I read, and will comply with, the GP-0-25-001 permit requirements. I understand that authorization to discharge under the permit for the project/site named above is dependent on receipt of a Letter of Authorization (LOA) or a Letter of Continued Coverage (LOCC) from the New York State Department of Environmental Conservation (NYSDEC) in accordance with CGP Part I.D.3.b. or Part I.F.4. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

Owner/Operator First Name

MI

Owner/Operator Last Name

Signature

Date




Appendix B:

Site Location/Drainage Area/Drainage Pattern Maps





SITE LOCATION MAP



PRELIMINARY / NOT FOR CONSTRUCTION

UNAUTHORIZED ALTERATION OR
ADDITION TO THIS DOCUMENT
IS A VIOLATION OF THE
NYS EDUCATION LAW.
COPYRIGHT LANSING
ENGINEERING, PC.

BULLARD LANE RESIDENTIAL SUBDIVISION BULLARD LANE, TOWN OF WILTON, SARATOGA COUNTY, NEW YORK



LANSING
ENGINEERING

2452 STATE ROUTE 9 SUITE 301
MALTA, NY 12020
(518) 899-5243

CIVIL - TRANSPORTATION - ENVIRONMENTAL - LAND SURVEYING


SITE LOCATION MAP

PROJ. NO: 1061.01
SCALE: AS SHOWN
DATE: 2/03/2025


SLM-1
SHEET 1 OF 1

SOIL APPRAISAL - DEEP HOLE TESTS - PERFORMED 12/23/2025 BY LANSING ENGINEERING & WITNESSED BY SCDPH	
TEST PIT #1 0'-18" TOPSOIL & ORGANICS 18"-10" MEDIUM BROWN SAND NO MOTTLING OR GROUNDWATER OBSERVED	TEST PIT #16 0'-20" TOPSOIL & ORGANICS 20"-8" MEDIUM BROWN ORANGE SAND 8"-10.5" MEDIUM GREY SATURATED SAND MOTTLING @ 8" SATURATED @ 9", NO GROUNDWATER OBSERVED
TEST PIT #3 0'-14" TOPSOIL & ORGANICS 14"-6.5" MEDIUM BROWN ORANGE SAND 6.5"-7.5" MEDIUM GREY SATURATED SAND MOTTLING @ 6" SATURATED @ 7.5", NO GROUNDWATER OBSERVED	TEST PIT #17 0'-12" TOPSOIL & ORGANICS 12"-6" MEDIUM ORANGE SAND 6"-8" FINE BROWN SAND 8"-10.5" MEDIUM GREY SAND MOTTLING @ 8.5" NO GROUNDWATER OBSERVED
TEST PIT #4 0'-8" TOPSOIL & ORGANICS 8"-48" MEDIUM BROWN SAND 48"-76" MEDIUM GRAY SAND MOTTLING @ 48" GROUNDWATER OBSERVED @ 76"	TEST PIT #18 0'-16" TOPSOIL & ORGANICS 16"-5" MEDIUM ORANGE SAND 5"-7" FINE ORANGE SAND 7"-9.5" MEDIUM GREY SAND MOTTLING @ 7" NO GROUNDWATER OBSERVED
TEST PIT #5 0'-16" TOPSOIL & ORGANICS 16"-5" MEDIUM ORANGE SAND 5"-9" GREY FINE SAND MOTTLING @ 5.5" GROUNDWATER OBSERVED @ 9"	TEST PIT #19 0'-16" TOPSOIL & ORGANICS 16"-10" MEDIUM BROWN SAND NO MOTTLING NO GROUNDWATER OBSERVED
TEST PIT #6 0'-10" TOPSOIL & ORGANICS 10"-5" MEDIUM BROWN SAND 5"-10" GREY FINE SAND MOTTLING @ 5" SATURATED @ 7", GROUNDWATER OBSERVED @ 9"	TEST PIT #20 0'-16" TOPSOIL & ORGANICS 16"-9" MEDIUM BROWN SAND NO MOTTLING NO GROUNDWATER OBSERVED
TEST PIT #7 0'-12" TOPSOIL & ORGANICS 12"-8" MEDIUM BROWN SAND 8"-10" SATURATED MEDIUM GREY SAND MOTTLING @ 8" SATURATED @ 8", NO GROUNDWATER OBSERVED	TEST PIT #21 0'-16" TOPSOIL & ORGANICS 16"-44" FINE BROWN SAND 44"-6.5" MEDIUM GREY SATURATED SAND MOTTLING @ 44" SATURATED @ 5", GROUNDWATER OBSERVED @ 6.5"
TEST PIT #8 0'-5" TOPSOIL & ORGANICS 5"-8.5" MEDIUM BROWN SAND NO MOTTLING OR GROUNDWATER OBSERVED	TEST PIT #22 0'-8" TOPSOIL & ORGANICS 8"-40" MEDIUM BROWN SAND 40"-100" MEDIUM GREY SATURATED SAND MOTTLING @ 40" SATURATED @ 5", NO GROUNDWATER OBSERVED
TEST PIT #9 0'-12" TOPSOIL & ORGANICS 12"-10.5" MEDIUM BROWN SAND NO MOTTLING OR GROUNDWATER OBSERVED	TEST PIT #23 0'-14" TOPSOIL & ORGANICS 14"-10" MEDIUM BROWN SAND NO MOTTLING NO GROUNDWATER OBSERVED
TEST PIT #10 0'-8" TOPSOIL & ORGANICS 8"-9.5" MEDIUM BROWN SAND NO MOTTLING OR GROUNDWATER OBSERVED	TEST PIT #24 0'-14" TOPSOIL & ORGANICS 14"-9" MEDIUM BROWN SAND NO MOTTLING NO GROUNDWATER OBSERVED
TEST PIT #11 0'-8" TOPSOIL & ORGANICS 8"-9" MEDIUM BROWN SAND NO MOTTLING OR GROUNDWATER OBSERVED	TEST PIT #25 0'-9" TOPSOIL & ORGANICS 9"-9" MEDIUM BROWN SAND NO MOTTLING NO GROUNDWATER OBSERVED
TEST PIT #12 0'-13" TOPSOIL & ORGANICS 13"-9.5" MEDIUM BROWN SAND NO MOTTLING OR GROUNDWATER OBSERVED	TEST PIT #26 0'-16" TOPSOIL & ORGANICS 16"-44" MEDIUM BROWN SAND 44"-7" MEDIUM GREY SATURATED SAND MOTTLING @ 44" GROUNDWATER OBSERVED @ 64"
TEST PIT #13 0'-14" TOPSOIL & ORGANICS 14"-8" MEDIUM BROWN SAND NO MOTTLING OR GROUNDWATER OBSERVED	TEST PIT #27 0'-24" TOPSOIL & ORGANICS 24"-4" FINE BROWN SAND 4"-5" MEDIUM GREY SATURATED SAND MOTTLING @ 40" GROUNDWATER OBSERVED @ 5"
TEST PIT #14 0'-10" TOPSOIL & ORGANICS 10"-9" MEDIUM BROWN SAND NO MOTTLING OR GROUNDWATER OBSERVED	TEST PIT #28 0'-16" TOPSOIL & ORGANICS 16"-54" MEDIUM BROWN SAND 54"-68" MEDIUM GREY SATURATED SAND MOTTLING @ 54" SATURATED @ 68", GROUNDWATER OBSERVED @ 6.5"
TEST PIT #15 0'-18" TOPSOIL & ORGANICS 18"-9" MEDIUM BROWN SAND NO MOTTLING OR GROUNDWATER OBSERVED	TEST PIT #29 0'-12" TOPSOIL & ORGANICS 12"-0" MEDIUM ORANGE SAND 0"-8" MEDIUM GREY SATURATED SAND MOTTLING @ 40" SATURATED @ 72", GROUNDWATER OBSERVED @ 96"

PERCOLATION TEST PERFORMED ON 12/23/25 & 12/26/25 BY LANSING ENGINEERING	
PERCOLATION TEST LOCATIONS	PERCOLATION RATE
PT1 @ 3' DEPTH	1.1 MIN./IN
PT3 @ 3' DEPTH	2.5 MIN./IN
PT4 @ 3' DEPTH	5.1 MIN./IN
PT5 @ 3' DEPTH	6.1 MIN./IN
PT6 @ 3' DEPTH	3.1 MIN./IN
PT7 @ 3' DEPTH	1.6 MIN./IN
PT8 @ 3' DEPTH	2.7 MIN./IN
PT9 @ 3' DEPTH	2.7 MIN./IN
PT10 @ 3' DEPTH	2.0 MIN./IN
PT11 @ 3' DEPTH	1.5 MIN./IN
PT12 @ 3' DEPTH	1.8 MIN./IN
PT13 @ 3' DEPTH	1.5 MIN./IN
PT14 @ 3' DEPTH	1.7 MIN./IN
PT15 @ 3' DEPTH	1.7 MIN./IN
PT16 @ 3' DEPTH	3.9 MIN./IN
PT17 @ 3' DEPTH	1.5 MIN./IN
PT18 @ 3' DEPTH	1.5 MIN./IN
PT19 @ 3' DEPTH	2.5 MIN./IN
PT20 @ 3' DEPTH	1.3 MIN./IN
PT21 @ 3' DEPTH	4.2 MIN./IN
PT22 @ 3' DEPTH	3.0 MIN./IN
PT23 @ 3' DEPTH	2.8 MIN./IN
PT24 @ 3' DEPTH	1.8 MIN./IN
PT25 @ 3' DEPTH	1.8 MIN./IN
PT26 @ 3' DEPTH	15.1 IN./HR
PT27 @ 3' DEPTH	5.9 IN./HR
PT28 @ 3' DEPTH	22.5 IN./HR
PT29 @ 3' DEPTH	7.0 IN./HR

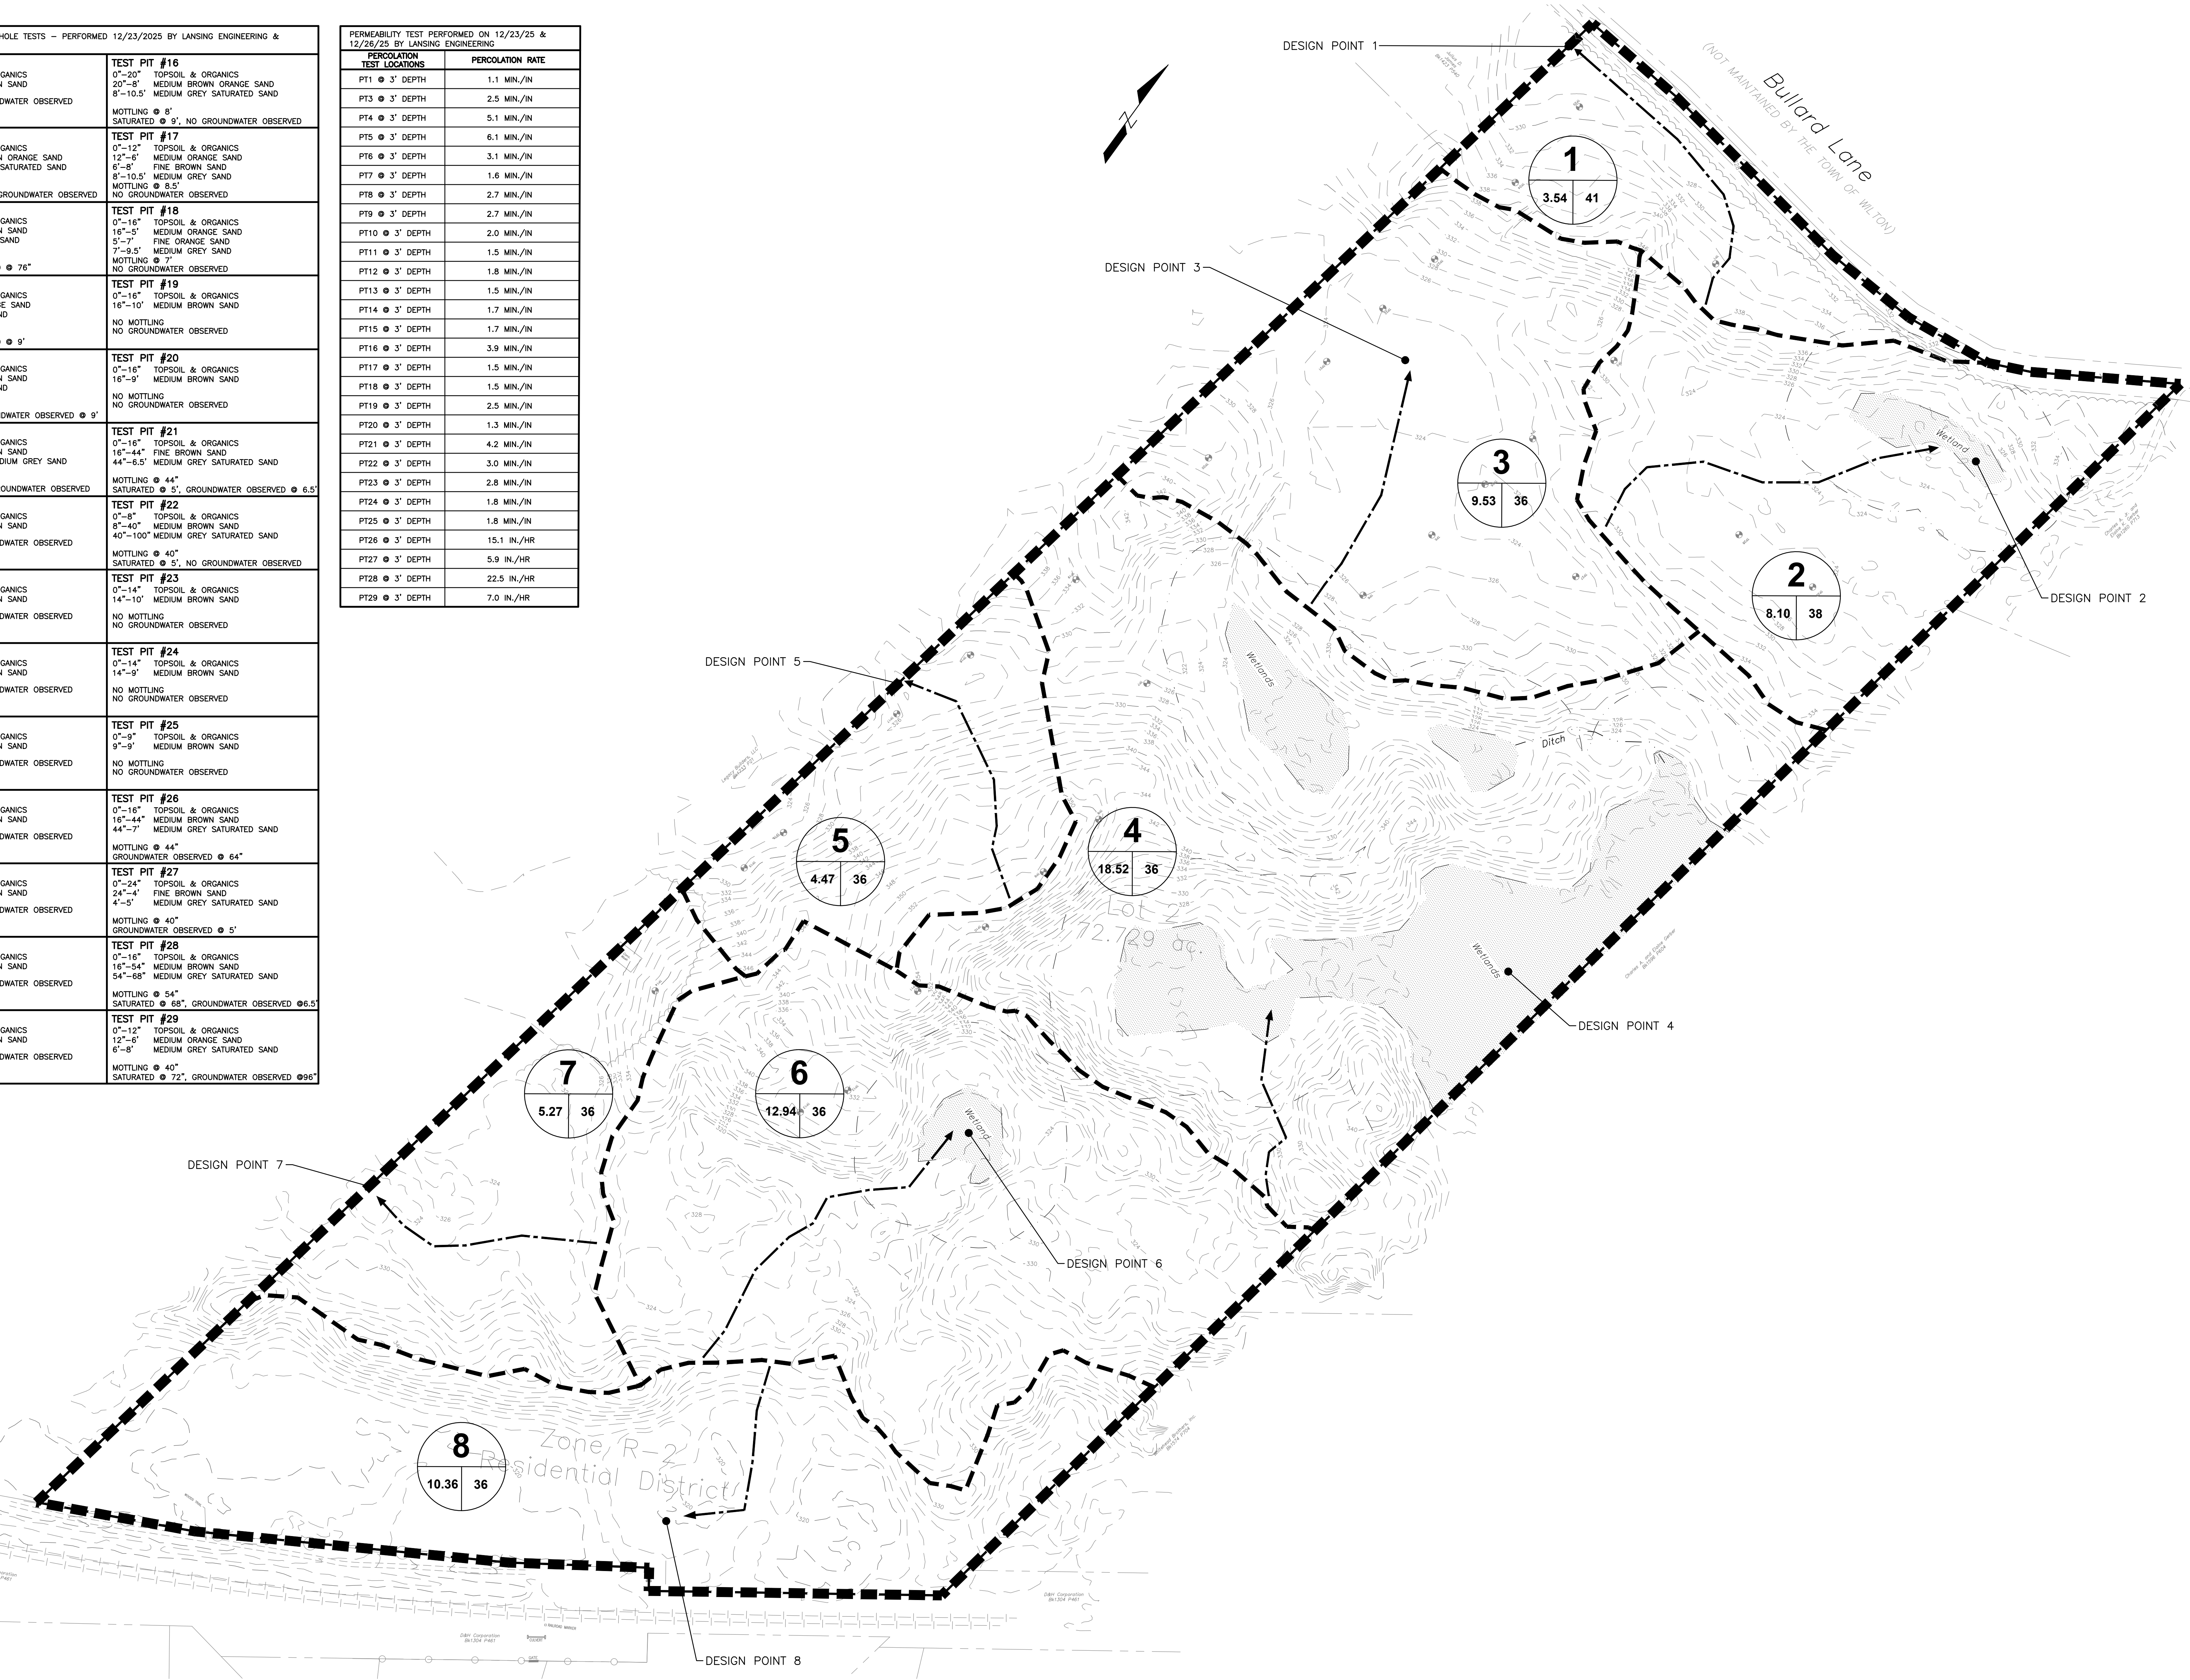

EXISTING CONDITIONS PLAN



UNAUTHORIZED ADDITION TO THIS LOCATION OF THE INSIGHT LANSING ENGINEERING, P.C.



CIVIL / TRANSPORTATION / ENVIRONMENTAL / LAND SURVEYING

DATE: REVISIONS: RECORD / DESCRIPTION:


BULLARD LANE RESIDENTIAL SUBDIVISION
 BULLARD LANE, TOWN OF WILTON, SARATOGA COUNTY, NEW YORK

PRELIMINARY / NOT FOR CONSTRUCTION

LANSING ENGINEERING
 885 WEST 14TH STREET
 WILTON, NY 12149
 (518) 838-8848

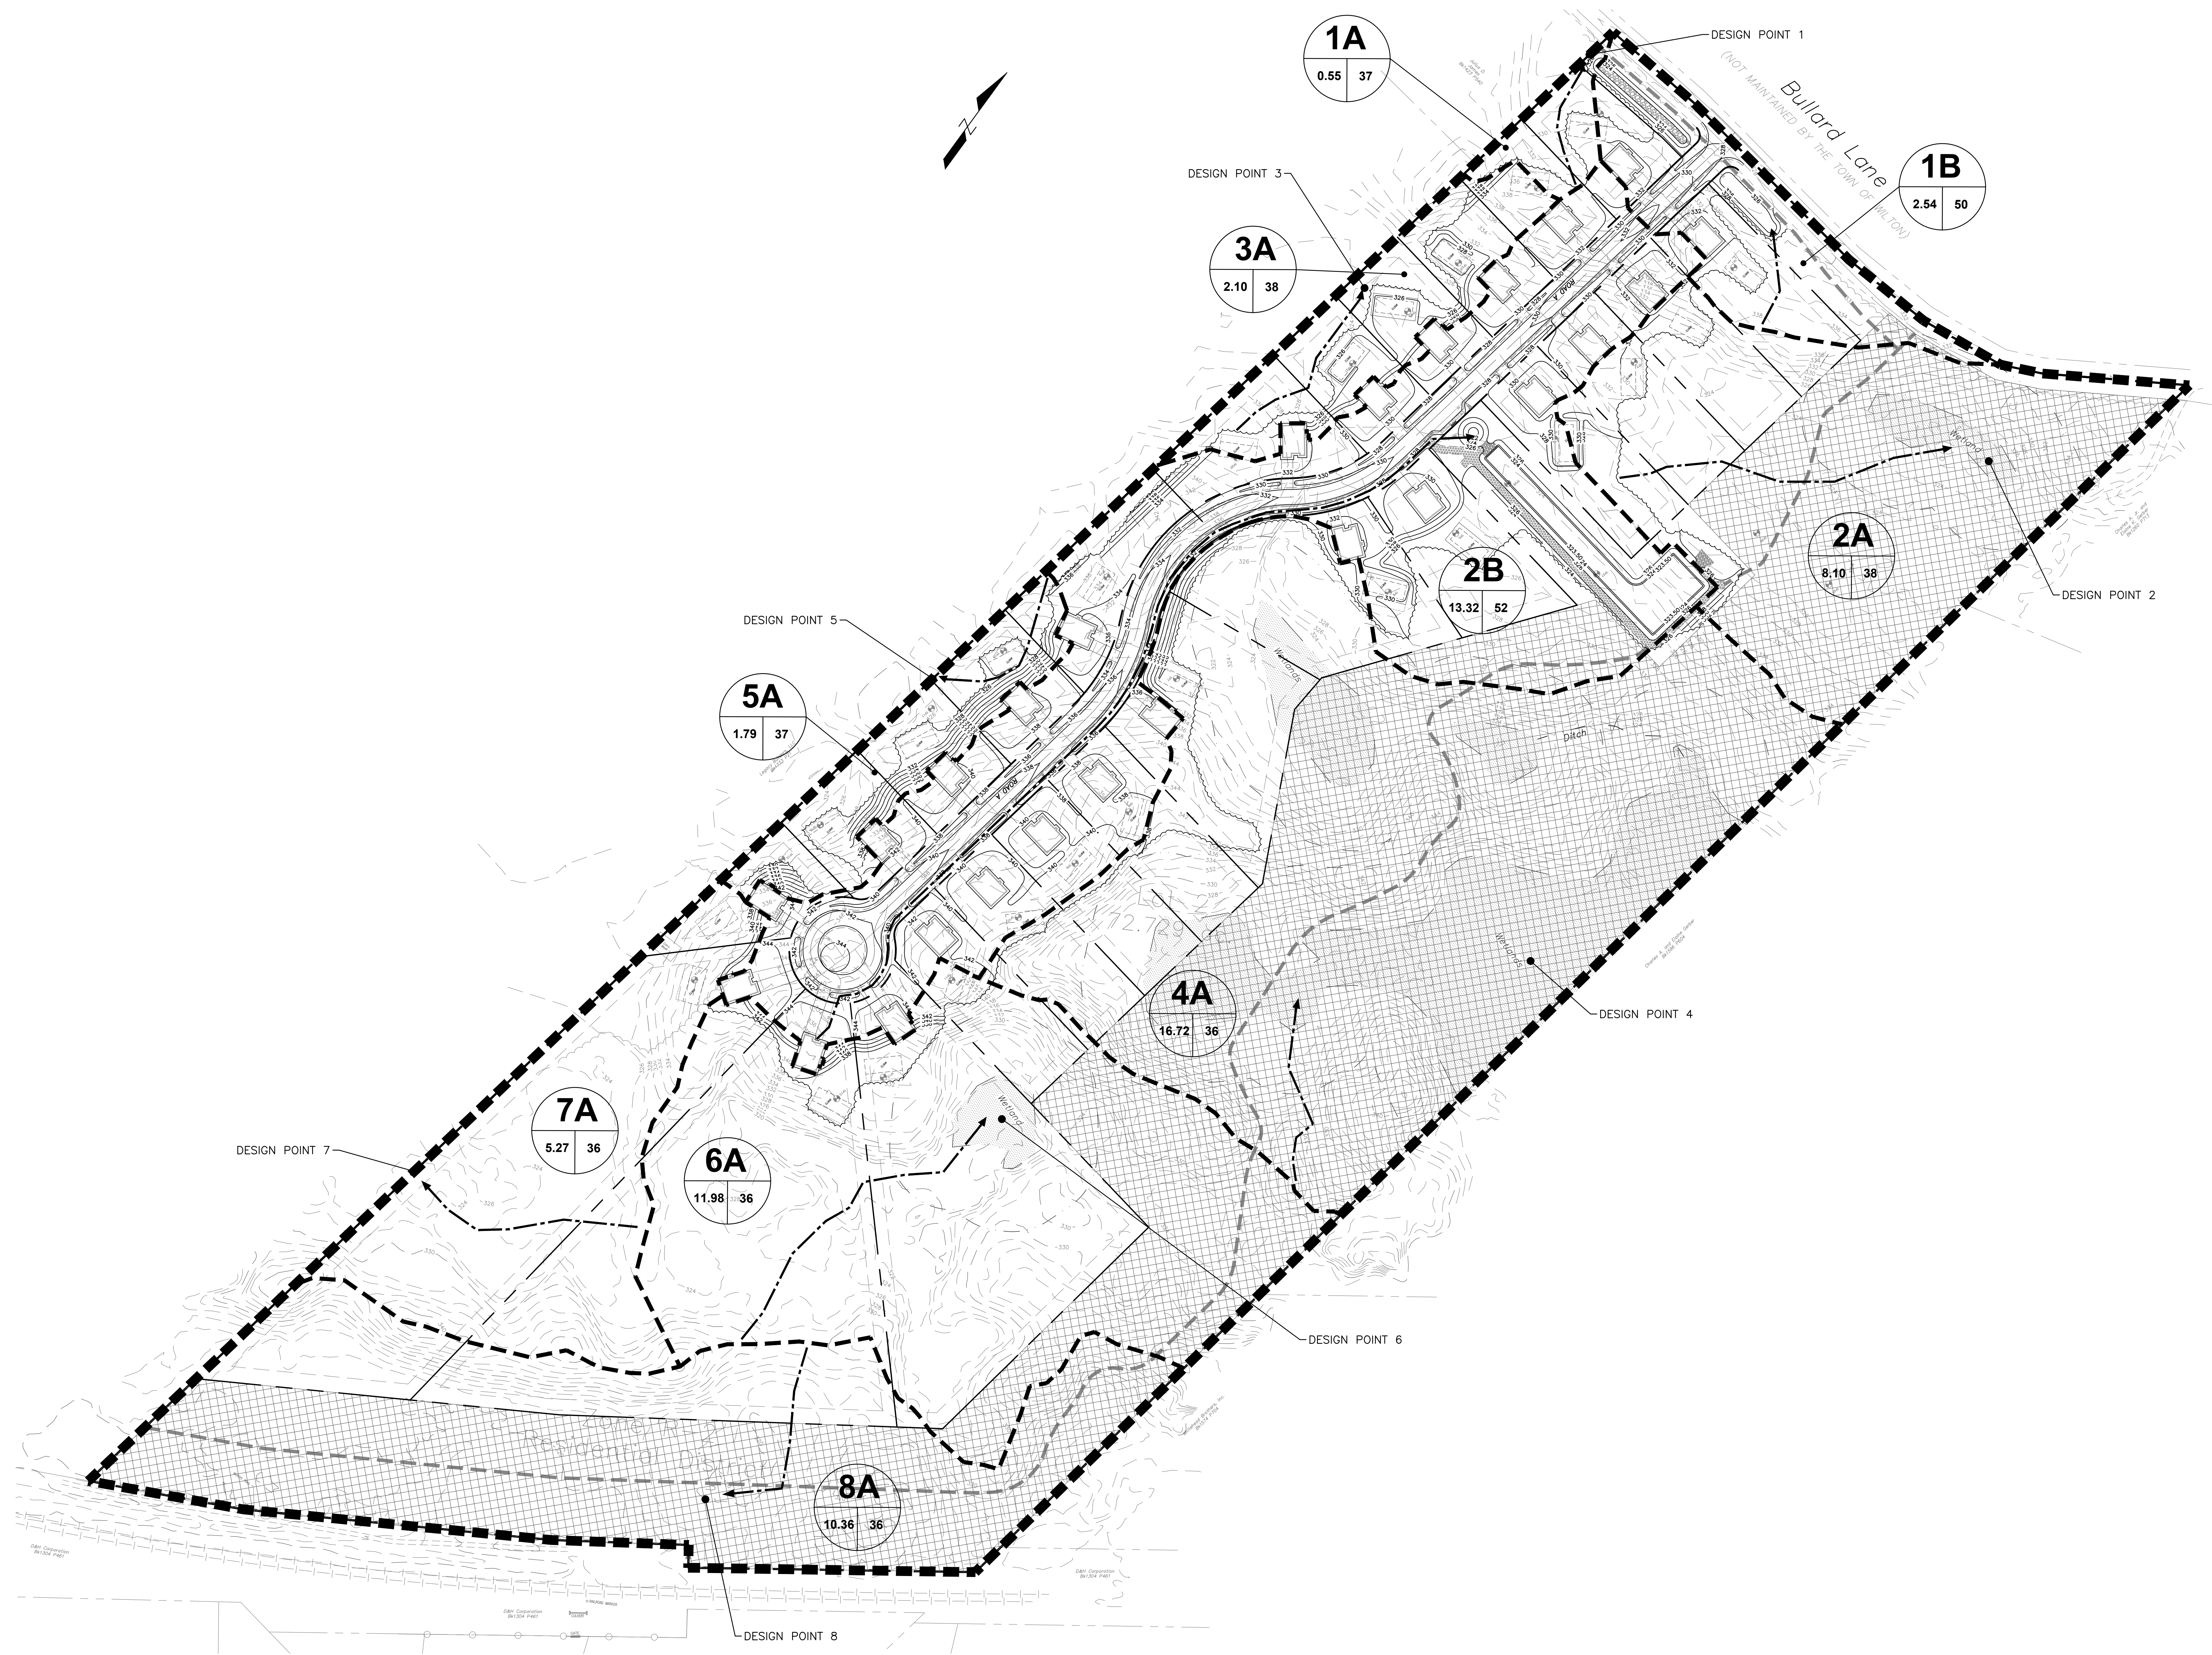

PROPOSED CONDITIONS PLAN



BULLARD LANE RESIDENTIAL SUBDIVISION
 BULLARD LANE, TOWN OF WILTON, SARATOGA COUNTY, NEW YORK

PRELIMINARY / NOT FOR CONSTRUCTION

LANSING
 ENGINEERING

CIVIL, TRANSPORTATION, ENVIRONMENTAL, LAND SURVEYING

PROJECT NO: 1061.01
 SCALE: AS SHOWN
 DATE: 2/03/2026




PC-1
 SHEET 2 OF 2



Appendix C:

Pre-Development and Post-Development Run-off Calculations



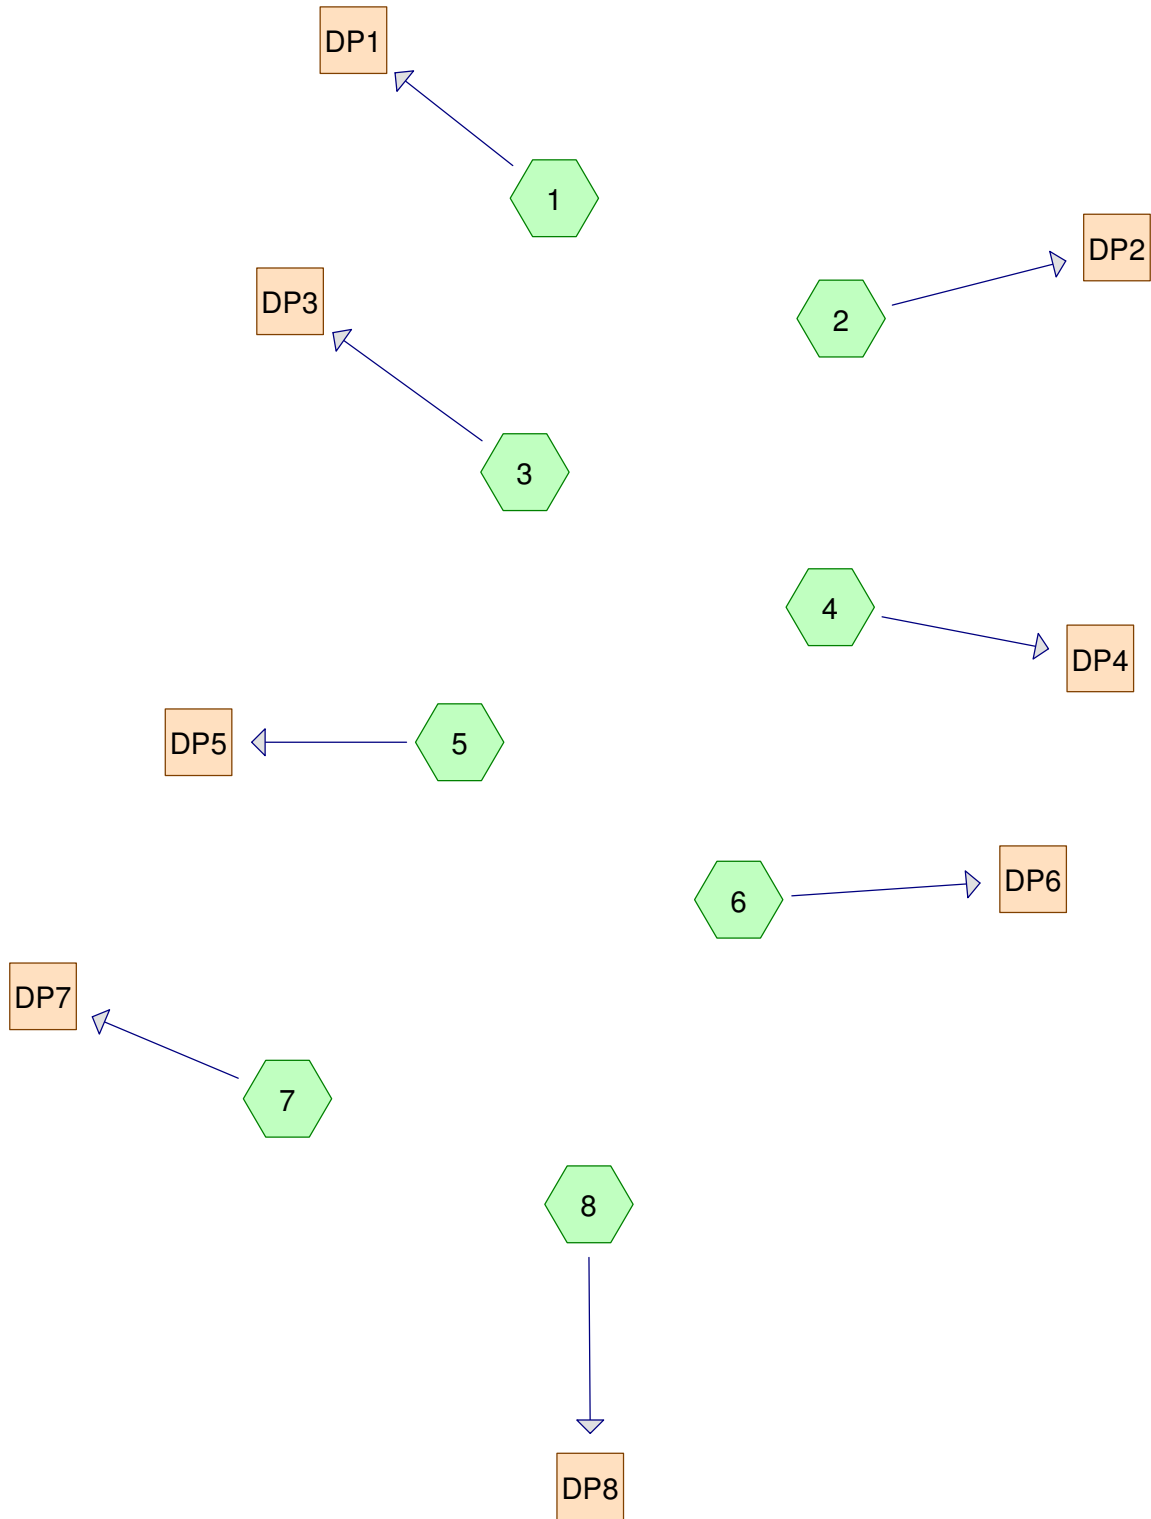

Routing Diagram for EXISTING CONDITIONS
 Prepared by Lansing Eng, Printed 2/3/2026
 HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

EXISTING CONDITIONS

Prepared by Lansing Eng

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Printed 2/3/2026

Page 2

Project Notes

Defined 9 rainfall events from NY - Bullard Lane IDF

Copied 9 events from NY - Bullard Lane 24-hr S1 storm

EXISTING CONDITIONS

Rainfall Events Listing (selected events)

Event#	Event Name	Storm Type	Curve	Mode	Duration (hours)	B/B	Depth (inches)	AMC
1	1-yr	NY - Bullard Lane 24-hr S1	1-yr	Default	24.00	1	2.25	2
2	10-yr	NY - Bullard Lane 24-hr S1	10-yr	Default	24.00	1	3.75	2
3	25-yr	NY - Bullard Lane 24-hr S1	25-yr	Default	24.00	1	4.62	2
4	100-yr	NY - Bullard Lane 24-hr S1	100-yr	Default	24.00	1	6.33	2

EXISTING CONDITIONS

Prepared by Lansing Eng
HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Printed 2/3/2026

Page 4

Area Listing (all nodes)

Area (acres)	CN	Description (subcatchment-numbers)
1.440	39	>75% Grass cover, Good, HSG A (1, 2, 5, 7)
0.500	98	Paved parking, HSG A (1, 2)
70.790	36	Woods, Fair, HSG A (1, 2, 3, 4, 5, 6, 7, 8)
72.730	36	TOTAL AREA

EXISTING CONDITIONS

Prepared by Lansing Eng
HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Printed 2/3/2026

Page 5

Soil Listing (all nodes)

Area (acres)	Soil Group	Subcatchment Numbers
72.730	HSG A	1, 2, 3, 4, 5, 6, 7, 8
0.000	HSG B	
0.000	HSG C	
0.000	HSG D	
0.000	Other	
72.730		TOTAL AREA

EXISTING CONDITIONS

Ground Covers (all nodes)

HSG-A (acres)	HSG-B (acres)	HSG-C (acres)	HSG-D (acres)	Other (acres)	Total (acres)	Ground Cover	Subcatchment Numbers
1.440	0.000	0.000	0.000	0.000	1.440	>75% Grass cover, Good	1, 2, 5, 7
0.500	0.000	0.000	0.000	0.000	0.500	Paved parking	1, 2
70.790	0.000	0.000	0.000	0.000	70.790	Woods, Fair	1, 2, 3, 4, 5, 6, 7, 8
72.730	0.000	0.000	0.000	0.000	72.730	TOTAL AREA	

EXISTING CONDITIONS

Prepared by Lansing Eng
HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Printed 2/3/2026

Page 7

Time span=5.00-20.00 hrs, dt=0.05 hrs, 301 points
Runoff by SCS TR-20 method, UH=SCS, Weighted-CN
Reach routing by Stor-Ind+Trans method - Pond routing by Stor-Ind method

Subcatchment 1: Runoff Area=3.540 ac 7.63% Impervious Runoff Depth=0.00"
Flow Length=504' Tc=27.5 min CN=41 Runoff=0.00 cfs 0.000 af

Subcatchment 2: Runoff Area=8.100 ac 2.84% Impervious Runoff Depth=0.00"
Flow Length=570' Tc=31.7 min CN=38 Runoff=0.00 cfs 0.000 af

Subcatchment 3: Runoff Area=9.530 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=386' Tc=29.7 min CN=36 Runoff=0.00 cfs 0.000 af

Subcatchment 4: Runoff Area=18.520 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=298' Tc=17.9 min CN=36 Runoff=0.00 cfs 0.000 af

Subcatchment 5: Runoff Area=4.470 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=407' Tc=17.7 min CN=36 Runoff=0.00 cfs 0.000 af

Subcatchment 6: Runoff Area=12.940 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=550' Tc=26.6 min CN=36 Runoff=0.00 cfs 0.000 af

Subcatchment 7: Runoff Area=5.270 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=350' Tc=17.5 min CN=36 Runoff=0.00 cfs 0.000 af

Subcatchment 8: Runoff Area=10.360 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=305' Tc=21.2 min CN=36 Runoff=0.00 cfs 0.000 af

Reach DP1: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Reach DP2: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Reach DP3: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Reach DP4: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Reach DP5: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Reach DP6: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Reach DP7: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Reach DP8: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

EXISTING CONDITIONS

NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 8

Total Runoff Area = 72.730 ac Runoff Volume = 0.000 af Average Runoff Depth = 0.00"
99.31% Pervious = 72.230 ac 0.69% Impervious = 0.500 ac

EXISTING CONDITIONS

Prepared by Lansing Eng
 HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Printed 2/3/2026

Page 9

Summary for Subcatchment 1:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
 Routed to Reach DP1 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Area (ac)	CN	Description
0.270	98	Paved parking, HSG A
0.380	39	>75% Grass cover, Good, HSG A
2.890	36	Woods, Fair, HSG A
3.540	41	Weighted Average
3.270		92.37% Pervious Area
0.270		7.63% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
16.5	100	0.0500	0.10		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
11.0	404	0.0150	0.61		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
27.5	504	Total			

Summary for Subcatchment 2:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
 Routed to Reach DP2 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Area (ac)	CN	Description
0.230	98	Paved parking, HSG A
0.200	39	>75% Grass cover, Good, HSG A
7.670	36	Woods, Fair, HSG A
8.100	38	Weighted Average
7.870		97.16% Pervious Area
0.230		2.84% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
18.0	100	0.0400	0.09		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
13.7	470	0.0130	0.57		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
31.7	570	Total			

EXISTING CONDITIONS

Prepared by Lansing Eng
 HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Printed 2/3/2026

Page 10

Summary for Subcatchment 3:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
 Routed to Reach DP3 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Area (ac)	CN	Description
9.530	36	Woods, Fair, HSG A
9.530		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
20.2	100	0.0300	0.08		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
9.5	286	0.0100	0.50		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
29.7	386	Total			

Summary for Subcatchment 4:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
 Routed to Reach DP4 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Area (ac)	CN	Description
18.520	36	Woods, Fair, HSG A
18.520		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
3.5	198	0.0350	0.94		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.9	298	Total			

Summary for Subcatchment 5:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
 Routed to Reach DP5 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

EXISTING CONDITIONS

NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 11

Area (ac)	CN	Description
4.440	36	Woods, Fair, HSG A
0.030	39	>75% Grass cover, Good, HSG A
4.470	36	Weighted Average
4.470		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
13.7	100	0.0800	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
4.0	307	0.0650	1.27		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.7	407	Total			

Summary for Subcatchment 6:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
 Routed to Reach DP6 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Area (ac)	CN	Description
12.940	36	Woods, Fair, HSG A
12.940		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
12.2	450	0.0150	0.61		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
26.6	550	Total			

Summary for Subcatchment 7:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
 Routed to Reach DP7 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Area (ac)	CN	Description
0.830	39	>75% Grass cover, Good, HSG A
4.440	36	Woods, Fair, HSG A
5.270	36	Weighted Average
5.270		100.00% Pervious Area

EXISTING CONDITIONS

NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 12

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
11.6	100	0.1200	0.14		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
5.9	250	0.0200	0.71		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.5	350	Total			

Summary for Subcatchment 8:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
Routed to Reach DP8 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Area (ac)	CN	Description
10.360	36	Woods, Fair, HSG A
10.360		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
6.8	205	0.0100	0.50		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
21.2	305	Total			

Summary for Reach DP1:

Inflow Area = 3.540 ac, 7.63% Impervious, Inflow Depth = 0.00" for 1-yr event
Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP2:

Inflow Area = 8.100 ac, 2.84% Impervious, Inflow Depth = 0.00" for 1-yr event
Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

EXISTING CONDITIONS

NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 13

Summary for Reach DP3:

Inflow Area = 9.530 ac, 0.00% Impervious, Inflow Depth = 0.00" for 1-yr event
Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP4:

Inflow Area = 18.520 ac, 0.00% Impervious, Inflow Depth = 0.00" for 1-yr event
Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP5:

Inflow Area = 4.470 ac, 0.00% Impervious, Inflow Depth = 0.00" for 1-yr event
Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP6:

Inflow Area = 12.940 ac, 0.00% Impervious, Inflow Depth = 0.00" for 1-yr event
Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP7:

Inflow Area = 5.270 ac, 0.00% Impervious, Inflow Depth = 0.00" for 1-yr event
Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP8:

Inflow Area = 10.360 ac, 0.00% Impervious, Inflow Depth = 0.00" for 1-yr event
Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

EXISTING CONDITIONS

Prepared by Lansing Eng

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Printed 2/3/2026

Page 14

Time span=5.00-20.00 hrs, dt=0.05 hrs, 301 points
Runoff by SCS TR-20 method, UH=SCS, Weighted-CN
Reach routing by Stor-Ind+Trans method - Pond routing by Stor-Ind method

Subcatchment 1:	Runoff Area=3.540 ac 7.63% Impervious Runoff Depth>0.03" Flow Length=504' Tc=27.5 min CN=41 Runoff=0.02 cfs 0.008 af
Subcatchment 2:	Runoff Area=8.100 ac 2.84% Impervious Runoff Depth>0.00" Flow Length=570' Tc=31.7 min CN=38 Runoff=0.02 cfs 0.003 af
Subcatchment 3:	Runoff Area=9.530 ac 0.00% Impervious Runoff Depth=0.00" Flow Length=386' Tc=29.7 min CN=36 Runoff=0.00 cfs 0.000 af
Subcatchment 4:	Runoff Area=18.520 ac 0.00% Impervious Runoff Depth=0.00" Flow Length=298' Tc=17.9 min CN=36 Runoff=0.00 cfs 0.000 af
Subcatchment 5:	Runoff Area=4.470 ac 0.00% Impervious Runoff Depth=0.00" Flow Length=407' Tc=17.7 min CN=36 Runoff=0.00 cfs 0.000 af
Subcatchment 6:	Runoff Area=12.940 ac 0.00% Impervious Runoff Depth=0.00" Flow Length=550' Tc=26.6 min CN=36 Runoff=0.00 cfs 0.000 af
Subcatchment 7:	Runoff Area=5.270 ac 0.00% Impervious Runoff Depth=0.00" Flow Length=350' Tc=17.5 min CN=36 Runoff=0.00 cfs 0.000 af
Subcatchment 8:	Runoff Area=10.360 ac 0.00% Impervious Runoff Depth=0.00" Flow Length=305' Tc=21.2 min CN=36 Runoff=0.00 cfs 0.000 af
Reach DP1:	Inflow=0.02 cfs 0.008 af Outflow=0.02 cfs 0.008 af
Reach DP2:	Inflow=0.02 cfs 0.003 af Outflow=0.02 cfs 0.003 af
Reach DP3:	Inflow=0.00 cfs 0.000 af Outflow=0.00 cfs 0.000 af
Reach DP4:	Inflow=0.00 cfs 0.000 af Outflow=0.00 cfs 0.000 af
Reach DP5:	Inflow=0.00 cfs 0.000 af Outflow=0.00 cfs 0.000 af
Reach DP6:	Inflow=0.00 cfs 0.000 af Outflow=0.00 cfs 0.000 af
Reach DP7:	Inflow=0.00 cfs 0.000 af Outflow=0.00 cfs 0.000 af
Reach DP8:	Inflow=0.00 cfs 0.000 af Outflow=0.00 cfs 0.000 af

EXISTING CONDITIONS

NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 15

Total Runoff Area = 72.730 ac Runoff Volume = 0.011 af Average Runoff Depth = 0.00"
99.31% Pervious = 72.230 ac 0.69% Impervious = 0.500 ac

EXISTING CONDITIONS

Prepared by Lansing Eng
 HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Printed 2/3/2026

Page 16

Summary for Subcatchment 1:

Runoff = 0.02 cfs @ 19.10 hrs, Volume= 0.008 af, Depth> 0.03"
 Routed to Reach DP1 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Area (ac)	CN	Description
0.270	98	Paved parking, HSG A
0.380	39	>75% Grass cover, Good, HSG A
2.890	36	Woods, Fair, HSG A
3.540	41	Weighted Average
3.270		92.37% Pervious Area
0.270		7.63% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
16.5	100	0.0500	0.10		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
11.0	404	0.0150	0.61		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
27.5	504	Total			

Summary for Subcatchment 2:

Runoff = 0.02 cfs @ 20.00 hrs, Volume= 0.003 af, Depth> 0.00"
 Routed to Reach DP2 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Area (ac)	CN	Description
0.230	98	Paved parking, HSG A
0.200	39	>75% Grass cover, Good, HSG A
7.670	36	Woods, Fair, HSG A
8.100	38	Weighted Average
7.870		97.16% Pervious Area
0.230		2.84% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
18.0	100	0.0400	0.09		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
13.7	470	0.0130	0.57		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
31.7	570	Total			

EXISTING CONDITIONS

Prepared by Lansing Eng
 HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Printed 2/3/2026

Page 17

Summary for Subcatchment 3:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
 Routed to Reach DP3 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Area (ac)	CN	Description
9.530	36	Woods, Fair, HSG A
9.530		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
20.2	100	0.0300	0.08		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
9.5	286	0.0100	0.50		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
29.7	386	Total			

Summary for Subcatchment 4:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
 Routed to Reach DP4 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Area (ac)	CN	Description
18.520	36	Woods, Fair, HSG A
18.520		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
3.5	198	0.0350	0.94		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.9	298	Total			

Summary for Subcatchment 5:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
 Routed to Reach DP5 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

EXISTING CONDITIONS

NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 18

Area (ac)	CN	Description
4.440	36	Woods, Fair, HSG A
0.030	39	>75% Grass cover, Good, HSG A
4.470	36	Weighted Average
4.470		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
13.7	100	0.0800	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
4.0	307	0.0650	1.27		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.7	407	Total			

Summary for Subcatchment 6:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
 Routed to Reach DP6 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Area (ac)	CN	Description
12.940	36	Woods, Fair, HSG A
12.940		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
12.2	450	0.0150	0.61		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
26.6	550	Total			

Summary for Subcatchment 7:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
 Routed to Reach DP7 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Area (ac)	CN	Description
0.830	39	>75% Grass cover, Good, HSG A
4.440	36	Woods, Fair, HSG A
5.270	36	Weighted Average
5.270		100.00% Pervious Area

EXISTING CONDITIONS

NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 19

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
11.6	100	0.1200	0.14		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
5.9	250	0.0200	0.71		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.5	350	Total			

Summary for Subcatchment 8:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
Routed to Reach DP8 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Area (ac)	CN	Description
10.360	36	Woods, Fair, HSG A
10.360		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
6.8	205	0.0100	0.50		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
21.2	305	Total			

Summary for Reach DP1:

Inflow Area = 3.540 ac, 7.63% Impervious, Inflow Depth > 0.03" for 10-yr event
Inflow = 0.02 cfs @ 19.10 hrs, Volume= 0.008 af
Outflow = 0.02 cfs @ 19.10 hrs, Volume= 0.008 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP2:

Inflow Area = 8.100 ac, 2.84% Impervious, Inflow Depth > 0.00" for 10-yr event
Inflow = 0.02 cfs @ 20.00 hrs, Volume= 0.003 af
Outflow = 0.02 cfs @ 20.00 hrs, Volume= 0.003 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

EXISTING CONDITIONS

NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 20

Summary for Reach DP3:

Inflow Area = 9.530 ac, 0.00% Impervious, Inflow Depth = 0.00" for 10-yr event
Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP4:

Inflow Area = 18.520 ac, 0.00% Impervious, Inflow Depth = 0.00" for 10-yr event
Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP5:

Inflow Area = 4.470 ac, 0.00% Impervious, Inflow Depth = 0.00" for 10-yr event
Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP6:

Inflow Area = 12.940 ac, 0.00% Impervious, Inflow Depth = 0.00" for 10-yr event
Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP7:

Inflow Area = 5.270 ac, 0.00% Impervious, Inflow Depth = 0.00" for 10-yr event
Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP8:

Inflow Area = 10.360 ac, 0.00% Impervious, Inflow Depth = 0.00" for 10-yr event
Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

EXISTING CONDITIONS

Prepared by Lansing Eng
HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Printed 2/3/2026

Page 21

Time span=5.00-20.00 hrs, dt=0.05 hrs, 301 points
Runoff by SCS TR-20 method, UH=SCS, Weighted-CN
Reach routing by Stor-Ind+Trans method - Pond routing by Stor-Ind method

Subcatchment 1:	Runoff Area=3.540 ac 7.63% Impervious Runoff Depth>0.14" Flow Length=504' Tc=27.5 min CN=41 Runoff=0.11 cfs 0.040 af
Subcatchment 2:	Runoff Area=8.100 ac 2.84% Impervious Runoff Depth>0.07" Flow Length=570' Tc=31.7 min CN=38 Runoff=0.09 cfs 0.045 af
Subcatchment 3:	Runoff Area=9.530 ac 0.00% Impervious Runoff Depth>0.03" Flow Length=386' Tc=29.7 min CN=36 Runoff=0.06 cfs 0.027 af
Subcatchment 4:	Runoff Area=18.520 ac 0.00% Impervious Runoff Depth>0.03" Flow Length=298' Tc=17.9 min CN=36 Runoff=0.12 cfs 0.053 af
Subcatchment 5:	Runoff Area=4.470 ac 0.00% Impervious Runoff Depth>0.03" Flow Length=407' Tc=17.7 min CN=36 Runoff=0.03 cfs 0.013 af
Subcatchment 6:	Runoff Area=12.940 ac 0.00% Impervious Runoff Depth>0.03" Flow Length=550' Tc=26.6 min CN=36 Runoff=0.08 cfs 0.036 af
Subcatchment 7:	Runoff Area=5.270 ac 0.00% Impervious Runoff Depth>0.03" Flow Length=350' Tc=17.5 min CN=36 Runoff=0.03 cfs 0.015 af
Subcatchment 8:	Runoff Area=10.360 ac 0.00% Impervious Runoff Depth>0.03" Flow Length=305' Tc=21.2 min CN=36 Runoff=0.06 cfs 0.030 af
Reach DP1:	Inflow=0.11 cfs 0.040 af Outflow=0.11 cfs 0.040 af
Reach DP2:	Inflow=0.09 cfs 0.045 af Outflow=0.09 cfs 0.045 af
Reach DP3:	Inflow=0.06 cfs 0.027 af Outflow=0.06 cfs 0.027 af
Reach DP4:	Inflow=0.12 cfs 0.053 af Outflow=0.12 cfs 0.053 af
Reach DP5:	Inflow=0.03 cfs 0.013 af Outflow=0.03 cfs 0.013 af
Reach DP6:	Inflow=0.08 cfs 0.036 af Outflow=0.08 cfs 0.036 af
Reach DP7:	Inflow=0.03 cfs 0.015 af Outflow=0.03 cfs 0.015 af
Reach DP8:	Inflow=0.06 cfs 0.030 af Outflow=0.06 cfs 0.030 af

EXISTING CONDITIONS

NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 22

Total Runoff Area = 72.730 ac Runoff Volume = 0.259 af Average Runoff Depth = 0.04"
99.31% Pervious = 72.230 ac 0.69% Impervious = 0.500 ac

EXISTING CONDITIONS

Prepared by Lansing Eng
 HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Printed 2/3/2026

Page 23

Summary for Subcatchment 1:

Runoff = 0.11 cfs @ 12.86 hrs, Volume= 0.040 af, Depth> 0.14"
 Routed to Reach DP1 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Area (ac)	CN	Description
0.270	98	Paved parking, HSG A
0.380	39	>75% Grass cover, Good, HSG A
2.890	36	Woods, Fair, HSG A
3.540	41	Weighted Average
3.270		92.37% Pervious Area
0.270		7.63% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
16.5	100	0.0500	0.10		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
11.0	404	0.0150	0.61		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
27.5	504	Total			

Summary for Subcatchment 2:

Runoff = 0.09 cfs @ 15.06 hrs, Volume= 0.045 af, Depth> 0.07"
 Routed to Reach DP2 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Area (ac)	CN	Description
0.230	98	Paved parking, HSG A
0.200	39	>75% Grass cover, Good, HSG A
7.670	36	Woods, Fair, HSG A
8.100	38	Weighted Average
7.870		97.16% Pervious Area
0.230		2.84% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
18.0	100	0.0400	0.09		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
13.7	470	0.0130	0.57		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
31.7	570	Total			

EXISTING CONDITIONS

Prepared by Lansing Eng
 HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Printed 2/3/2026

Page 24

Summary for Subcatchment 3:

Runoff = 0.06 cfs @ 18.88 hrs, Volume= 0.027 af, Depth> 0.03"
 Routed to Reach DP3 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Area (ac)	CN	Description
9.530	36	Woods, Fair, HSG A
9.530		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
20.2	100	0.0300	0.08		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
9.5	286	0.0100	0.50		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
29.7	386	Total			

Summary for Subcatchment 4:

Runoff = 0.12 cfs @ 18.68 hrs, Volume= 0.053 af, Depth> 0.03"
 Routed to Reach DP4 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Area (ac)	CN	Description
18.520	36	Woods, Fair, HSG A
18.520		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
3.5	198	0.0350	0.94		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.9	298	Total			

Summary for Subcatchment 5:

Runoff = 0.03 cfs @ 18.80 hrs, Volume= 0.013 af, Depth> 0.03"
 Routed to Reach DP5 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

EXISTING CONDITIONS

NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 25

Area (ac)	CN	Description
4.440	36	Woods, Fair, HSG A
0.030	39	>75% Grass cover, Good, HSG A
4.470	36	Weighted Average
4.470		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
13.7	100	0.0800	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
4.0	307	0.0650	1.27		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.7	407	Total			

Summary for Subcatchment 6:

Runoff = 0.08 cfs @ 18.96 hrs, Volume= 0.036 af, Depth> 0.03"
 Routed to Reach DP6 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Area (ac)	CN	Description
12.940	36	Woods, Fair, HSG A
12.940		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
12.2	450	0.0150	0.61		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
26.6	550	Total			

Summary for Subcatchment 7:

Runoff = 0.03 cfs @ 18.73 hrs, Volume= 0.015 af, Depth> 0.03"
 Routed to Reach DP7 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Area (ac)	CN	Description
0.830	39	>75% Grass cover, Good, HSG A
4.440	36	Woods, Fair, HSG A
5.270	36	Weighted Average
5.270		100.00% Pervious Area

EXISTING CONDITIONS

NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 26

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
11.6	100	0.1200	0.14		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
5.9	250	0.0200	0.71		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.5	350	Total			

Summary for Subcatchment 8:

Runoff = 0.06 cfs @ 18.83 hrs, Volume= 0.030 af, Depth> 0.03"
Routed to Reach DP8 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Area (ac)	CN	Description
10.360	36	Woods, Fair, HSG A
10.360		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
6.8	205	0.0100	0.50		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
21.2	305	Total			

Summary for Reach DP1:

Inflow Area = 3.540 ac, 7.63% Impervious, Inflow Depth > 0.14" for 25-yr event
Inflow = 0.11 cfs @ 12.86 hrs, Volume= 0.040 af
Outflow = 0.11 cfs @ 12.86 hrs, Volume= 0.040 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP2:

Inflow Area = 8.100 ac, 2.84% Impervious, Inflow Depth > 0.07" for 25-yr event
Inflow = 0.09 cfs @ 15.06 hrs, Volume= 0.045 af
Outflow = 0.09 cfs @ 15.06 hrs, Volume= 0.045 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

EXISTING CONDITIONS

Prepared by Lansing Eng
HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Printed 2/3/2026
Page 27

Summary for Reach DP3:

Inflow Area = 9.530 ac, 0.00% Impervious, Inflow Depth > 0.03" for 25-yr event
Inflow = 0.06 cfs @ 18.88 hrs, Volume= 0.027 af
Outflow = 0.06 cfs @ 18.88 hrs, Volume= 0.027 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP4:

Inflow Area = 18.520 ac, 0.00% Impervious, Inflow Depth > 0.03" for 25-yr event
Inflow = 0.12 cfs @ 18.68 hrs, Volume= 0.053 af
Outflow = 0.12 cfs @ 18.68 hrs, Volume= 0.053 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP5:

Inflow Area = 4.470 ac, 0.00% Impervious, Inflow Depth > 0.03" for 25-yr event
Inflow = 0.03 cfs @ 18.80 hrs, Volume= 0.013 af
Outflow = 0.03 cfs @ 18.80 hrs, Volume= 0.013 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP6:

Inflow Area = 12.940 ac, 0.00% Impervious, Inflow Depth > 0.03" for 25-yr event
Inflow = 0.08 cfs @ 18.96 hrs, Volume= 0.036 af
Outflow = 0.08 cfs @ 18.96 hrs, Volume= 0.036 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP7:

Inflow Area = 5.270 ac, 0.00% Impervious, Inflow Depth > 0.03" for 25-yr event
Inflow = 0.03 cfs @ 18.73 hrs, Volume= 0.015 af
Outflow = 0.03 cfs @ 18.73 hrs, Volume= 0.015 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP8:

Inflow Area = 10.360 ac, 0.00% Impervious, Inflow Depth > 0.03" for 25-yr event
Inflow = 0.06 cfs @ 18.83 hrs, Volume= 0.030 af
Outflow = 0.06 cfs @ 18.83 hrs, Volume= 0.030 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

EXISTING CONDITIONS

Prepared by Lansing Eng
HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Printed 2/3/2026

Page 28

Time span=5.00-20.00 hrs, dt=0.05 hrs, 301 points
Runoff by SCS TR-20 method, UH=SCS, Weighted-CN
Reach routing by Stor-Ind+Trans method - Pond routing by Stor-Ind method

Subcatchment 1:	Runoff Area=3.540 ac 7.63% Impervious Runoff Depth>0.55" Flow Length=504' Tc=27.5 min CN=41 Runoff=0.94 cfs 0.161 af
Subcatchment 2:	Runoff Area=8.100 ac 2.84% Impervious Runoff Depth>0.38" Flow Length=570' Tc=31.7 min CN=38 Runoff=1.23 cfs 0.258 af
Subcatchment 3:	Runoff Area=9.530 ac 0.00% Impervious Runoff Depth>0.29" Flow Length=386' Tc=29.7 min CN=36 Runoff=0.94 cfs 0.228 af
Subcatchment 4:	Runoff Area=18.520 ac 0.00% Impervious Runoff Depth>0.29" Flow Length=298' Tc=17.9 min CN=36 Runoff=2.17 cfs 0.449 af
Subcatchment 5:	Runoff Area=4.470 ac 0.00% Impervious Runoff Depth>0.29" Flow Length=407' Tc=17.7 min CN=36 Runoff=0.53 cfs 0.108 af
Subcatchment 6:	Runoff Area=12.940 ac 0.00% Impervious Runoff Depth>0.29" Flow Length=550' Tc=26.6 min CN=36 Runoff=1.33 cfs 0.310 af
Subcatchment 7:	Runoff Area=5.270 ac 0.00% Impervious Runoff Depth>0.29" Flow Length=350' Tc=17.5 min CN=36 Runoff=0.62 cfs 0.128 af
Subcatchment 8:	Runoff Area=10.360 ac 0.00% Impervious Runoff Depth>0.29" Flow Length=305' Tc=21.2 min CN=36 Runoff=1.15 cfs 0.250 af
Reach DP1:	Inflow=0.94 cfs 0.161 af Outflow=0.94 cfs 0.161 af
Reach DP2:	Inflow=1.23 cfs 0.258 af Outflow=1.23 cfs 0.258 af
Reach DP3:	Inflow=0.94 cfs 0.228 af Outflow=0.94 cfs 0.228 af
Reach DP4:	Inflow=2.17 cfs 0.449 af Outflow=2.17 cfs 0.449 af
Reach DP5:	Inflow=0.53 cfs 0.108 af Outflow=0.53 cfs 0.108 af
Reach DP6:	Inflow=1.33 cfs 0.310 af Outflow=1.33 cfs 0.310 af
Reach DP7:	Inflow=0.62 cfs 0.128 af Outflow=0.62 cfs 0.128 af
Reach DP8:	Inflow=1.15 cfs 0.250 af Outflow=1.15 cfs 0.250 af

EXISTING CONDITIONS

NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 29

Total Runoff Area = 72.730 ac Runoff Volume = 1.891 af Average Runoff Depth = 0.31"
99.31% Pervious = 72.230 ac 0.69% Impervious = 0.500 ac

EXISTING CONDITIONS

NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 30

Summary for Subcatchment 1:

Runoff = 0.94 cfs @ 12.62 hrs, Volume= 0.161 af, Depth> 0.55"
 Routed to Reach DP1 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Area (ac)	CN	Description
0.270	98	Paved parking, HSG A
0.380	39	>75% Grass cover, Good, HSG A
2.890	36	Woods, Fair, HSG A
3.540	41	Weighted Average
3.270		92.37% Pervious Area
0.270		7.63% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
16.5	100	0.0500	0.10		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
11.0	404	0.0150	0.61		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
27.5	504	Total			

Summary for Subcatchment 2:

Runoff = 1.23 cfs @ 12.75 hrs, Volume= 0.258 af, Depth> 0.38"
 Routed to Reach DP2 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Area (ac)	CN	Description
0.230	98	Paved parking, HSG A
0.200	39	>75% Grass cover, Good, HSG A
7.670	36	Woods, Fair, HSG A
8.100	38	Weighted Average
7.870		97.16% Pervious Area
0.230		2.84% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
18.0	100	0.0400	0.09		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
13.7	470	0.0130	0.57		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
31.7	570	Total			

EXISTING CONDITIONS

Prepared by Lansing Eng
 HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Printed 2/3/2026

Page 31

Summary for Subcatchment 3:

Runoff = 0.94 cfs @ 12.77 hrs, Volume= 0.228 af, Depth> 0.29"
 Routed to Reach DP3 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Area (ac)	CN	Description
9.530	36	Woods, Fair, HSG A
9.530		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
20.2	100	0.0300	0.08		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
9.5	286	0.0100	0.50		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
29.7	386	Total			

Summary for Subcatchment 4:

Runoff = 2.17 cfs @ 12.62 hrs, Volume= 0.449 af, Depth> 0.29"
 Routed to Reach DP4 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Area (ac)	CN	Description
18.520	36	Woods, Fair, HSG A
18.520		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
3.5	198	0.0350	0.94		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.9	298	Total			

Summary for Subcatchment 5:

Runoff = 0.53 cfs @ 12.62 hrs, Volume= 0.108 af, Depth> 0.29"
 Routed to Reach DP5 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

EXISTING CONDITIONS

NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 32

Area (ac)	CN	Description
4.440	36	Woods, Fair, HSG A
0.030	39	>75% Grass cover, Good, HSG A
4.470	36	Weighted Average
4.470		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
13.7	100	0.0800	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
4.0	307	0.0650	1.27		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.7	407	Total			

Summary for Subcatchment 6:

Runoff = 1.33 cfs @ 12.73 hrs, Volume= 0.310 af, Depth> 0.29"
 Routed to Reach DP6 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Area (ac)	CN	Description
12.940	36	Woods, Fair, HSG A
12.940		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
12.2	450	0.0150	0.61		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
26.6	550	Total			

Summary for Subcatchment 7:

Runoff = 0.62 cfs @ 12.61 hrs, Volume= 0.128 af, Depth> 0.29"
 Routed to Reach DP7 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Area (ac)	CN	Description
0.830	39	>75% Grass cover, Good, HSG A
4.440	36	Woods, Fair, HSG A
5.270	36	Weighted Average
5.270		100.00% Pervious Area

EXISTING CONDITIONS

NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 33

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
11.6	100	0.1200	0.14		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
5.9	250	0.0200	0.71		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.5	350	Total			

Summary for Subcatchment 8:

Runoff = 1.15 cfs @ 12.66 hrs, Volume= 0.250 af, Depth> 0.29"
Routed to Reach DP8 :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Area (ac)	CN	Description
10.360	36	Woods, Fair, HSG A
10.360		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
6.8	205	0.0100	0.50		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
21.2	305	Total			

Summary for Reach DP1:

Inflow Area = 3.540 ac, 7.63% Impervious, Inflow Depth > 0.55" for 100-yr event
Inflow = 0.94 cfs @ 12.62 hrs, Volume= 0.161 af
Outflow = 0.94 cfs @ 12.62 hrs, Volume= 0.161 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP2:

Inflow Area = 8.100 ac, 2.84% Impervious, Inflow Depth > 0.38" for 100-yr event
Inflow = 1.23 cfs @ 12.75 hrs, Volume= 0.258 af
Outflow = 1.23 cfs @ 12.75 hrs, Volume= 0.258 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

EXISTING CONDITIONS

Prepared by Lansing Eng
HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Printed 2/3/2026
Page 34

Summary for Reach DP3:

Inflow Area = 9.530 ac, 0.00% Impervious, Inflow Depth > 0.29" for 100-yr event
Inflow = 0.94 cfs @ 12.77 hrs, Volume= 0.228 af
Outflow = 0.94 cfs @ 12.77 hrs, Volume= 0.228 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP4:

Inflow Area = 18.520 ac, 0.00% Impervious, Inflow Depth > 0.29" for 100-yr event
Inflow = 2.17 cfs @ 12.62 hrs, Volume= 0.449 af
Outflow = 2.17 cfs @ 12.62 hrs, Volume= 0.449 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP5:

Inflow Area = 4.470 ac, 0.00% Impervious, Inflow Depth > 0.29" for 100-yr event
Inflow = 0.53 cfs @ 12.62 hrs, Volume= 0.108 af
Outflow = 0.53 cfs @ 12.62 hrs, Volume= 0.108 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP6:

Inflow Area = 12.940 ac, 0.00% Impervious, Inflow Depth > 0.29" for 100-yr event
Inflow = 1.33 cfs @ 12.73 hrs, Volume= 0.310 af
Outflow = 1.33 cfs @ 12.73 hrs, Volume= 0.310 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP7:




Inflow Area = 5.270 ac, 0.00% Impervious, Inflow Depth > 0.29" for 100-yr event
Inflow = 0.62 cfs @ 12.61 hrs, Volume= 0.128 af
Outflow = 0.62 cfs @ 12.61 hrs, Volume= 0.128 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP8:

Inflow Area = 10.360 ac, 0.00% Impervious, Inflow Depth > 0.29" for 100-yr event
Inflow = 1.15 cfs @ 12.66 hrs, Volume= 0.250 af
Outflow = 1.15 cfs @ 12.66 hrs, Volume= 0.250 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

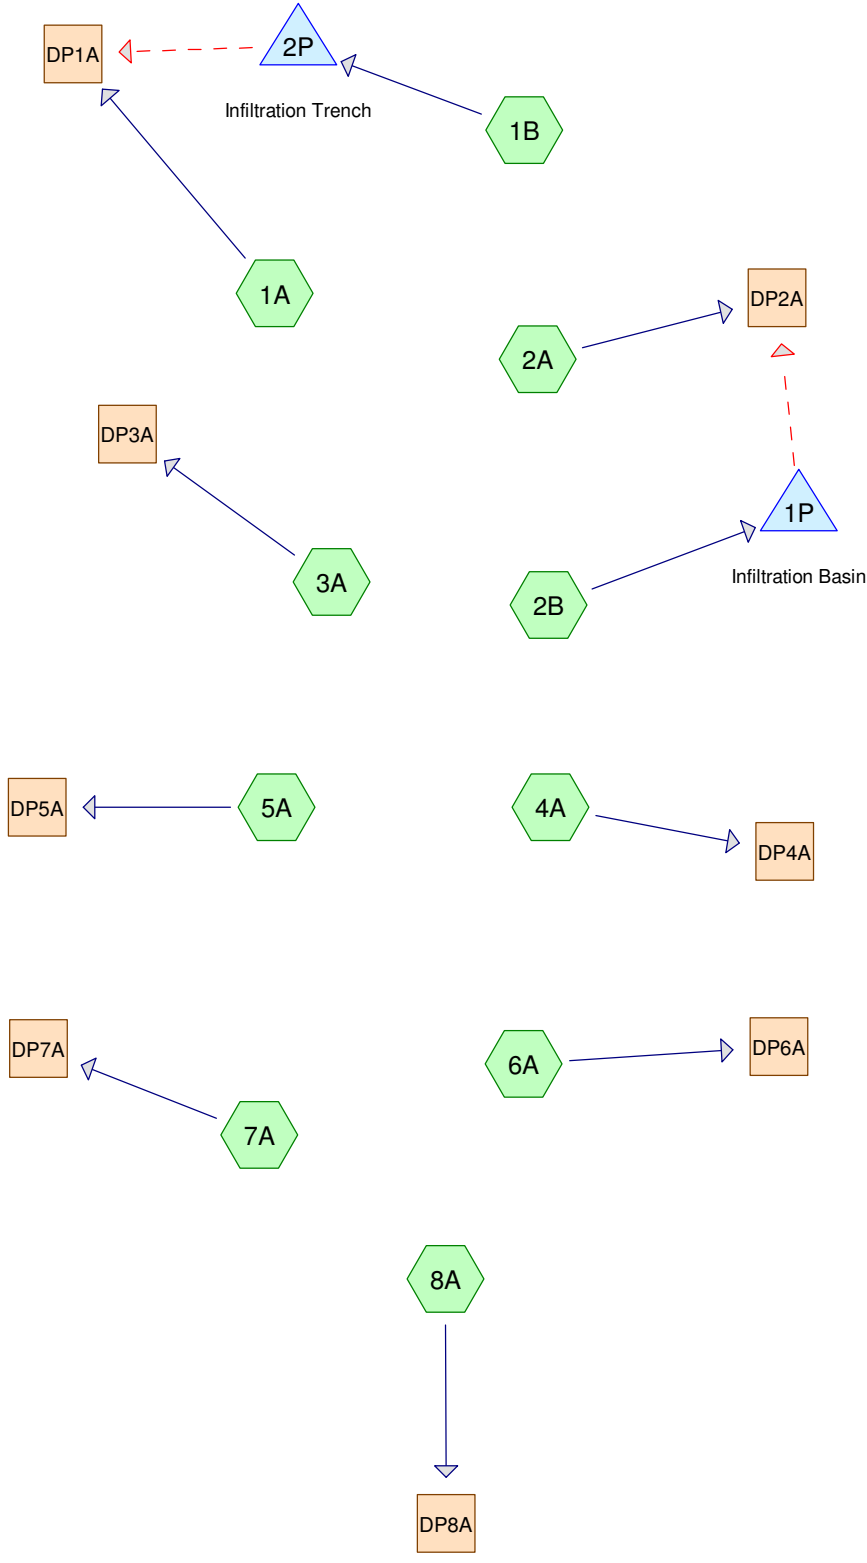

Routing Diagram for PROPOSED CONDITIONS
 Prepared by Lansing Eng, Printed 2/3/2026
 HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

PROPOSED CONDITIONS

Prepared by Lansing Eng
HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Printed 2/3/2026

Page 2

Project Notes

Defined 9 rainfall events from NY - Bullard Lane IDF
Copied 9 events from NY - Bullard Lane 24-hr S1 storm

PROPOSED CONDITIONS

Prepared by Lansing Eng
HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Printed 2/3/2026

Page 3

Rainfall Events Listing (selected events)

Event#	Event Name	Storm Type	Curve	Mode	Duration (hours)	B/B	Depth (inches)	AMC
1	1-yr	NY - Bullard Lane 24-hr S1	1-yr	Default	24.00	1	2.25	2
2	10-yr	NY - Bullard Lane 24-hr S1	10-yr	Default	24.00	1	3.75	2
3	25-yr	NY - Bullard Lane 24-hr S1	25-yr	Default	24.00	1	4.62	2
4	100-yr	NY - Bullard Lane 24-hr S1	100-yr	Default	24.00	1	6.33	2

PROPOSED CONDITIONS

Prepared by Lansing Eng
HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Printed 2/3/2026
Page 4

Area Listing (all nodes)

Area (acres)	CN	Description (subcatchment-numbers)
15.390	39	>75% Grass cover, Good, HSG A (1A, 1B, 2A, 2B, 3A, 4A, 5A, 6A, 7A)
3.360	98	Paved parking, HSG A (2A, 2B)
0.270	98	Paved parking, HSG A (Existing) (1B)
0.260	98	Paved parking, HSG A (New) (1B)
53.450	36	Woods, Fair, HSG A (1A, 1B, 2A, 2B, 3A, 4A, 5A, 6A, 7A, 8A)
72.730	40	TOTAL AREA

PROPOSED CONDITIONS

Prepared by Lansing Eng
HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Printed 2/3/2026
Page 5

Soil Listing (all nodes)

Area (acres)	Soil Group	Subcatchment Numbers
72.730	HSG A	1A, 1B, 2A, 2B, 3A, 4A, 5A, 6A, 7A, 8A
0.000	HSG B	
0.000	HSG C	
0.000	HSG D	
0.000	Other	
72.730		TOTAL AREA

PROPOSED CONDITIONS

Ground Covers (all nodes)

HSG-A (acres)	HSG-B (acres)	HSG-C (acres)	HSG-D (acres)	Other (acres)	Total (acres)	Ground Cover	Subcatchment Numbers
15.390	0.000	0.000	0.000	0.000	15.390	>75% Grass cover, Good	1A, 1B, 2A, 2B, 3A, 4A, 5A, 6A, 7A
3.890	0.000	0.000	0.000	0.000	3.890	Paved parking	1B, 2A, 2B
53.450	0.000	0.000	0.000	0.000	53.450	Woods, Fair	1A, 1B, 2A, 2B, 3A, 4A, 5A, 6A, 7A, 8A
72.730	0.000	0.000	0.000	0.000	72.730	TOTAL AREA	

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 7

Time span=5.00-20.00 hrs, dt=0.05 hrs, 301 points
Runoff by SCS TR-20 method, UH=SCS, Weighted-CN
Reach routing by Stor-Ind+Trans method - Pond routing by Stor-Ind method

Subcatchment 1A: Runoff Area=0.550 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=150' Tc=15.2 min CN=37 Runoff=0.00 cfs 0.000 af

Subcatchment 1B: Runoff Area=2.540 ac 20.87% Impervious Runoff Depth>0.00"
Flow Length=150' Tc=15.2 min CN=50 Runoff=0.00 cfs 0.000 af

Subcatchment 2A: Runoff Area=8.100 ac 2.84% Impervious Runoff Depth=0.00"
Flow Length=533' Tc=38.2 min CN=38 Runoff=0.00 cfs 0.000 af

Subcatchment 2B: Runoff Area=13.320 ac 23.50% Impervious Runoff Depth>0.01"
Flow Length=1,509' Tc=14.0 min CN=52 Runoff=0.03 cfs 0.008 af

Subcatchment 3A: Runoff Area=2.100 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=302' Tc=19.2 min CN=38 Runoff=0.00 cfs 0.000 af

Subcatchment 4A: Runoff Area=16.720 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=298' Tc=17.9 min CN=36 Runoff=0.00 cfs 0.000 af

Subcatchment 5A: Runoff Area=1.790 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=269' Tc=14.5 min CN=37 Runoff=0.00 cfs 0.000 af

Subcatchment 6A: Runoff Area=11.980 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=550' Tc=26.6 min CN=36 Runoff=0.00 cfs 0.000 af

Subcatchment 7A: Runoff Area=5.270 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=350' Tc=17.5 min CN=36 Runoff=0.00 cfs 0.000 af

Subcatchment 8A: Runoff Area=10.360 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=305' Tc=21.2 min CN=36 Runoff=0.00 cfs 0.000 af

Reach DP1A: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Reach DP2A: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Reach DP3A: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Reach DP4A: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Reach DP5A: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Reach DP6A: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 8

Reach DP7A:

Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Reach DP8A:

Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Pond 1P: Infiltration Basin

Peak Elev=323.50' Storage=9 cf Inflow=0.03 cfs 0.008 af
Discarded=0.03 cfs 0.008 af Secondary=0.00 cfs 0.000 af Outflow=0.03 cfs 0.008 af

Pond 2P: Infiltration Trench

Peak Elev=322.00' Storage=0 cf Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Total Runoff Area = 72.730 ac Runoff Volume = 0.008 af Average Runoff Depth = 0.00"
94.65% Pervious = 68.840 ac 5.35% Impervious = 3.890 ac

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 9

Summary for Subcatchment 1A:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"

Routed to Reach DP1A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Area (ac)	CN	Description
0.170	39	>75% Grass cover, Good, HSG A
0.380	36	Woods, Fair, HSG A
0.550	37	Weighted Average
0.550		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
0.8	50	0.0400	1.00		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
15.2	150	Total			

Summary for Subcatchment 1B:

Runoff = 0.00 cfs @ 20.00 hrs, Volume= 0.000 af, Depth> 0.00"

Routed to Pond 2P : Infiltration Trench

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Area (ac)	CN	Description
* 0.270	98	Paved parking, HSG A (Existing)
* 0.260	98	Paved parking, HSG A (New)
1.210	39	>75% Grass cover, Good, HSG A
0.800	36	Woods, Fair, HSG A
2.540	50	Weighted Average
2.010		79.13% Pervious Area
0.530		20.87% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
0.8	50	0.0400	1.00		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
15.2	150	Total			

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 10

Summary for Subcatchment 2A:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"

Routed to Reach DP2A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Area (ac)	CN	Description
0.230	98	Paved parking, HSG A
0.770	39	>75% Grass cover, Good, HSG A
7.100	36	Woods, Fair, HSG A
8.100	38	Weighted Average
7.870		97.16% Pervious Area
0.230		2.84% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
23.8	100	0.0200	0.07		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
14.4	433	0.0100	0.50		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
38.2	533	Total			

Summary for Subcatchment 2B:

Runoff = 0.03 cfs @ 20.00 hrs, Volume= 0.008 af, Depth> 0.01"

Routed to Pond 1P : Infiltration Basin

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Area (ac)	CN	Description
3.130	98	Paved parking, HSG A
8.430	39	>75% Grass cover, Good, HSG A
1.760	36	Woods, Fair, HSG A
13.320	52	Weighted Average
10.190		76.50% Pervious Area
3.130		23.50% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
8.9	78	0.0510	0.15		Sheet Flow, Grass: Dense n= 0.240 P2= 2.61"
5.1	1,431	0.0100	4.65	74.42	Channel Flow, Area= 16.0 sf Perim= 28.0' r= 0.57' n= 0.022 Earth, clean & straight
14.0	1,509	Total			

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 11

Summary for Subcatchment 3A:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"

Routed to Reach DP3A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Area (ac)	CN	Description
0.910	36	Woods, Fair, HSG A
1.190	39	>75% Grass cover, Good, HSG A
2.100	38	Weighted Average
2.100		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
15.3	100	0.0600	0.11		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
3.9	202	0.0300	0.87		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
19.2	302	Total			

Summary for Subcatchment 4A:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"

Routed to Reach DP4A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Area (ac)	CN	Description
15.420	36	Woods, Fair, HSG A
1.300	39	>75% Grass cover, Good, HSG A
16.720	36	Weighted Average
16.720		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
3.5	198	0.0350	0.94		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.9	298	Total			

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 12

Summary for Subcatchment 5A:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"

Routed to Reach DP5A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Area (ac)	CN	Description
0.950	36	Woods, Fair, HSG A
0.840	39	>75% Grass cover, Good, HSG A
1.790	37	Weighted Average
1.790		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
12.5	100	0.1000	0.13		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
2.0	169	0.0400	1.40		Shallow Concentrated Flow, Short Grass Pasture Kv= 7.0 fps
14.5	269	Total			

Summary for Subcatchment 6A:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"

Routed to Reach DP6A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Area (ac)	CN	Description
11.330	36	Woods, Fair, HSG A
0.650	39	>75% Grass cover, Good, HSG A
11.980	36	Weighted Average
11.980		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
12.2	450	0.0150	0.61		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
26.6	550	Total			

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 13

Summary for Subcatchment 7A:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
Routed to Reach DP7A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Area (ac)	CN	Description
0.830	39	>75% Grass cover, Good, HSG A
4.440	36	Woods, Fair, HSG A
5.270	36	Weighted Average
5.270		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
11.6	100	0.1200	0.14		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
5.9	250	0.0200	0.71		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.5	350	Total			

Summary for Subcatchment 8A:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"
Routed to Reach DP8A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Area (ac)	CN	Description
10.360	36	Woods, Fair, HSG A
10.360		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
6.8	205	0.0100	0.50		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
21.2	305	Total			

Summary for Reach DP1A:

Inflow Area = 0.550 ac, 0.00% Impervious, Inflow Depth = 0.00" for 1-yr event
Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 14

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP2A:

Inflow Area =	8.100 ac,	2.84% Impervious,	Inflow Depth = 0.00"	for 1-yr event
Inflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af
Outflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP3A:

Inflow Area =	2.100 ac,	0.00% Impervious,	Inflow Depth = 0.00"	for 1-yr event
Inflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af
Outflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP4A:

Inflow Area =	16.720 ac,	0.00% Impervious,	Inflow Depth = 0.00"	for 1-yr event
Inflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af
Outflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP5A:

Inflow Area =	1.790 ac,	0.00% Impervious,	Inflow Depth = 0.00"	for 1-yr event
Inflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af
Outflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP6A:

Inflow Area =	11.980 ac,	0.00% Impervious,	Inflow Depth = 0.00"	for 1-yr event
Inflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af
Outflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP7A:

Inflow Area =	5.270 ac,	0.00% Impervious,	Inflow Depth = 0.00"	for 1-yr event
Inflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af
Outflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af, Atten= 0%, Lag= 0.0 min

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 15

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP8A:

Inflow Area = 10.360 ac, 0.00% Impervious, Inflow Depth = 0.00" for 1-yr event
 Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
 Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Pond 1P: Infiltration Basin

Inflow Area = 13.320 ac, 23.50% Impervious, Inflow Depth > 0.01" for 1-yr event
 Inflow = 0.03 cfs @ 20.00 hrs, Volume= 0.008 af
 Outflow = 0.03 cfs @ 20.00 hrs, Volume= 0.008 af, Atten= 0%, Lag= 0.0 min
 Discarded = 0.03 cfs @ 20.00 hrs, Volume= 0.008 af
 Secondary = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
 Routed to Reach DP2A :

Routing by Stor-Ind method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 Peak Elev= 323.50' @ 20.00 hrs Surf.Area= 16,614 sf Storage= 9 cf

Plug-Flow detention time= 5.1 min calculated for 0.008 af (98% of inflow)
 Center-of-Mass det. time= 2.2 min (1,084.9 - 1,082.7)

Volume	Invert	Avail.Storage	Storage Description
#1	323.50'	54,184 cf	Custom Stage Data (Prismatic) Listed below (Recalc)

Elevation (feet)	Surf.Area (sq-ft)	Inc.Store (cubic-feet)	Cum.Store (cubic-feet)
323.50	16,612	0	0
324.00	18,596	8,802	8,802
326.00	26,786	45,382	54,184

Device	Routing	Invert	Outlet Devices
#1	Discarded	323.50'	3.500 in/hr Exfiltration over Surface area
#2	Secondary	325.00'	10.0' long x 10.0' breadth Broad-Crested Rectangular Weir Head (feet) 0.20 0.40 0.60 0.80 1.00 1.20 1.40 1.60 Coef. (English) 2.49 2.56 2.70 2.69 2.68 2.69 2.67 2.64

Discarded OutFlow Max=1.35 cfs @ 20.00 hrs HW=323.50' (Free Discharge)
 ↑—1=Exfiltration (Exfiltration Controls 1.35 cfs)

Secondary OutFlow Max=0.00 cfs @ 5.00 hrs HW=323.50' (Free Discharge)
 ↑—2=Broad-Crested Rectangular Weir (Controls 0.00 cfs)

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 1-yr Rainfall=2.25"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 16

Summary for Pond 2P: Infiltration Trench

Inflow Area = 2.540 ac, 20.87% Impervious, Inflow Depth > 0.00" for 1-yr event
 Inflow = 0.00 cfs @ 20.00 hrs, Volume= 0.000 af
 Outflow = 0.00 cfs @ 20.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min
 Discarded = 0.00 cfs @ 20.00 hrs, Volume= 0.000 af

Routing by Stor-Ind method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 Peak Elev= 322.00' @ 20.00 hrs Surf.Area= 2,413 sf Storage= 0 cf

Plug-Flow detention time= 0.8 min calculated for 0.000 af (99% of inflow)
 Center-of-Mass det. time= 0.3 min (1,147.7 - 1,147.4)

Volume	Invert	Avail.Storage	Storage Description
#1	322.00'	1,930 cf	Custom Stage Data (Prismatic) Listed below (Recalc) 4,826 cf Overall x 40.0% Voids
#2	324.00'	7,290 cf	Custom Stage Data (Prismatic) Listed below (Recalc)
		9,220 cf	Total Available Storage

Elevation (feet)	Surf.Area (sq-ft)	Inc.Store (cubic-feet)	Cum.Store (cubic-feet)
322.00	2,413	0	0
324.00	2,413	4,826	4,826

Elevation (feet)	Surf.Area (sq-ft)	Inc.Store (cubic-feet)	Cum.Store (cubic-feet)
324.00	2,413	0	0
326.00	4,877	7,290	7,290

Device	Routing	Invert	Outlet Devices
#1	Discarded	322.00'	15.000 in/hr Exfiltration over Surface area

Discarded OutFlow Max=0.84 cfs @ 20.00 hrs HW=322.00' (Free Discharge)
 ↑**1=Exfiltration** (Exfiltration Controls 0.84 cfs)

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 17

Time span=5.00-20.00 hrs, dt=0.05 hrs, 301 points
Runoff by SCS TR-20 method, UH=SCS, Weighted-CN
Reach routing by Stor-Ind+Trans method - Pond routing by Stor-Ind method

Subcatchment 1A: Runoff Area=0.550 ac 0.00% Impervious Runoff Depth>0.00"
Flow Length=150' Tc=15.2 min CN=37 Runoff=0.00 cfs 0.000 af

Subcatchment 1B: Runoff Area=2.540 ac 20.87% Impervious Runoff Depth>0.20"
Flow Length=150' Tc=15.2 min CN=50 Runoff=0.21 cfs 0.043 af

Subcatchment 2A: Runoff Area=8.100 ac 2.84% Impervious Runoff Depth>0.00"
Flow Length=533' Tc=38.2 min CN=38 Runoff=0.02 cfs 0.003 af

Subcatchment 2B: Runoff Area=13.320 ac 23.50% Impervious Runoff Depth>0.26"
Flow Length=1,509' Tc=14.0 min CN=52 Runoff=1.59 cfs 0.291 af

Subcatchment 3A: Runoff Area=2.100 ac 0.00% Impervious Runoff Depth>0.00"
Flow Length=302' Tc=19.2 min CN=38 Runoff=0.00 cfs 0.001 af

Subcatchment 4A: Runoff Area=16.720 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=298' Tc=17.9 min CN=36 Runoff=0.00 cfs 0.000 af

Subcatchment 5A: Runoff Area=1.790 ac 0.00% Impervious Runoff Depth>0.00"
Flow Length=269' Tc=14.5 min CN=37 Runoff=0.00 cfs 0.000 af

Subcatchment 6A: Runoff Area=11.980 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=550' Tc=26.6 min CN=36 Runoff=0.00 cfs 0.000 af

Subcatchment 7A: Runoff Area=5.270 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=350' Tc=17.5 min CN=36 Runoff=0.00 cfs 0.000 af

Subcatchment 8A: Runoff Area=10.360 ac 0.00% Impervious Runoff Depth=0.00"
Flow Length=305' Tc=21.2 min CN=36 Runoff=0.00 cfs 0.000 af

Reach DP1A: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Reach DP2A: Inflow=0.02 cfs 0.003 af
Outflow=0.02 cfs 0.003 af

Reach DP3A: Inflow=0.00 cfs 0.001 af
Outflow=0.00 cfs 0.001 af

Reach DP4A: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Reach DP5A: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Reach DP6A: Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 18

Reach DP7A:

Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Reach DP8A:

Inflow=0.00 cfs 0.000 af
Outflow=0.00 cfs 0.000 af

Pond 1P: Infiltration Basin

Peak Elev=323.54' Storage=620 cf Inflow=1.59 cfs 0.291 af
Discarded=1.36 cfs 0.289 af Secondary=0.00 cfs 0.000 af Outflow=1.36 cfs 0.289 af

Pond 2P: Infiltration Trench

Peak Elev=322.01' Storage=10 cf Inflow=0.21 cfs 0.043 af
Outflow=0.21 cfs 0.043 af

Total Runoff Area = 72.730 ac Runoff Volume = 0.338 af Average Runoff Depth = 0.06"
94.65% Pervious = 68.840 ac 5.35% Impervious = 3.890 ac

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 19

Summary for Subcatchment 1A:

Runoff = 0.00 cfs @ 20.00 hrs, Volume= 0.000 af, Depth> 0.00"

Routed to Reach DP1A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Area (ac)	CN	Description
0.170	39	>75% Grass cover, Good, HSG A
0.380	36	Woods, Fair, HSG A
0.550	37	Weighted Average
0.550		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
0.8	50	0.0400	1.00		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
15.2	150	Total			

Summary for Subcatchment 1B:

Runoff = 0.21 cfs @ 12.56 hrs, Volume= 0.043 af, Depth> 0.20"

Routed to Pond 2P : Infiltration Trench

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Area (ac)	CN	Description
* 0.270	98	Paved parking, HSG A (Existing)
* 0.260	98	Paved parking, HSG A (New)
1.210	39	>75% Grass cover, Good, HSG A
0.800	36	Woods, Fair, HSG A
2.540	50	Weighted Average
2.010		79.13% Pervious Area
0.530		20.87% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
0.8	50	0.0400	1.00		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
15.2	150	Total			

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 20

Summary for Subcatchment 2A:

Runoff = 0.02 cfs @ 20.00 hrs, Volume= 0.003 af, Depth> 0.00"

Routed to Reach DP2A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Area (ac)	CN	Description
0.230	98	Paved parking, HSG A
0.770	39	>75% Grass cover, Good, HSG A
7.100	36	Woods, Fair, HSG A
8.100	38	Weighted Average
7.870		97.16% Pervious Area
0.230		2.84% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
23.8	100	0.0200	0.07		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
14.4	433	0.0100	0.50		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
38.2	533	Total			

Summary for Subcatchment 2B:

Runoff = 1.59 cfs @ 12.46 hrs, Volume= 0.291 af, Depth> 0.26"

Routed to Pond 1P : Infiltration Basin

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Area (ac)	CN	Description
3.130	98	Paved parking, HSG A
8.430	39	>75% Grass cover, Good, HSG A
1.760	36	Woods, Fair, HSG A
13.320	52	Weighted Average
10.190		76.50% Pervious Area
3.130		23.50% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
8.9	78	0.0510	0.15		Sheet Flow, Grass: Dense n= 0.240 P2= 2.61"
5.1	1,431	0.0100	4.65	74.42	Channel Flow, Area= 16.0 sf Perim= 28.0' r= 0.57' n= 0.022 Earth, clean & straight
14.0	1,509	Total			

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 21

Summary for Subcatchment 3A:

Runoff = 0.00 cfs @ 20.00 hrs, Volume= 0.001 af, Depth> 0.00"

Routed to Reach DP3A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Area (ac)	CN	Description
0.910	36	Woods, Fair, HSG A
1.190	39	>75% Grass cover, Good, HSG A
2.100	38	Weighted Average
2.100		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
15.3	100	0.0600	0.11		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
3.9	202	0.0300	0.87		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
19.2	302	Total			

Summary for Subcatchment 4A:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"

Routed to Reach DP4A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Area (ac)	CN	Description
15.420	36	Woods, Fair, HSG A
1.300	39	>75% Grass cover, Good, HSG A
16.720	36	Weighted Average
16.720		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
3.5	198	0.0350	0.94		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.9	298	Total			

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 22

Summary for Subcatchment 5A:

Runoff = 0.00 cfs @ 20.00 hrs, Volume= 0.000 af, Depth> 0.00"

Routed to Reach DP5A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Area (ac)	CN	Description
0.950	36	Woods, Fair, HSG A
0.840	39	>75% Grass cover, Good, HSG A
1.790	37	Weighted Average
1.790		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
12.5	100	0.1000	0.13		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
2.0	169	0.0400	1.40		Shallow Concentrated Flow, Short Grass Pasture Kv= 7.0 fps
14.5	269	Total			

Summary for Subcatchment 6A:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"

Routed to Reach DP6A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Area (ac)	CN	Description
11.330	36	Woods, Fair, HSG A
0.650	39	>75% Grass cover, Good, HSG A
11.980	36	Weighted Average
11.980		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
12.2	450	0.0150	0.61		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
26.6	550	Total			

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 23

Summary for Subcatchment 7A:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"

Routed to Reach DP7A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Area (ac)	CN	Description
0.830	39	>75% Grass cover, Good, HSG A
4.440	36	Woods, Fair, HSG A
5.270	36	Weighted Average
5.270		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
11.6	100	0.1200	0.14		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
5.9	250	0.0200	0.71		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.5	350	Total			

Summary for Subcatchment 8A:

Runoff = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Depth= 0.00"

Routed to Reach DP8A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Area (ac)	CN	Description
10.360	36	Woods, Fair, HSG A
10.360		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
6.8	205	0.0100	0.50		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
21.2	305	Total			

Summary for Reach DP1A:

Inflow Area = 0.550 ac, 0.00% Impervious, Inflow Depth > 0.00" for 10-yr event

Inflow = 0.00 cfs @ 20.00 hrs, Volume= 0.000 af

Outflow = 0.00 cfs @ 20.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 24

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP2A:

Inflow Area =	8.100 ac,	2.84% Impervious,	Inflow Depth > 0.00"	for 10-yr event
Inflow =	0.02 cfs @	20.00 hrs,	Volume=	0.003 af
Outflow =	0.02 cfs @	20.00 hrs,	Volume=	0.003 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP3A:

Inflow Area =	2.100 ac,	0.00% Impervious,	Inflow Depth > 0.00"	for 10-yr event
Inflow =	0.00 cfs @	20.00 hrs,	Volume=	0.001 af
Outflow =	0.00 cfs @	20.00 hrs,	Volume=	0.001 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP4A:

Inflow Area =	16.720 ac,	0.00% Impervious,	Inflow Depth = 0.00"	for 10-yr event
Inflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af
Outflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP5A:

Inflow Area =	1.790 ac,	0.00% Impervious,	Inflow Depth > 0.00"	for 10-yr event
Inflow =	0.00 cfs @	20.00 hrs,	Volume=	0.000 af
Outflow =	0.00 cfs @	20.00 hrs,	Volume=	0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP6A:

Inflow Area =	11.980 ac,	0.00% Impervious,	Inflow Depth = 0.00"	for 10-yr event
Inflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af
Outflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP7A:

Inflow Area =	5.270 ac,	0.00% Impervious,	Inflow Depth = 0.00"	for 10-yr event
Inflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af
Outflow =	0.00 cfs @	5.00 hrs,	Volume=	0.000 af, Atten= 0%, Lag= 0.0 min

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 25

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP8A:

Inflow Area = 10.360 ac, 0.00% Impervious, Inflow Depth = 0.00" for 10-yr event
Inflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Outflow = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Pond 1P: Infiltration Basin

Inflow Area = 13.320 ac, 23.50% Impervious, Inflow Depth > 0.26" for 10-yr event
Inflow = 1.59 cfs @ 12.46 hrs, Volume= 0.291 af
Outflow = 1.36 cfs @ 12.65 hrs, Volume= 0.289 af, Atten= 15%, Lag= 11.2 min
Discarded = 1.36 cfs @ 12.65 hrs, Volume= 0.289 af
Secondary = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Routed to Reach DP2A :

Routing by Stor-Ind method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
Peak Elev= 323.54' @ 12.65 hrs Surf.Area= 16,760 sf Storage= 620 cf

Plug-Flow detention time= 5.4 min calculated for 0.289 af (99% of inflow)
Center-of-Mass det. time= 3.7 min (895.4 - 891.7)

Volume	Invert	Avail.Storage	Storage Description
#1	323.50'	54,184 cf	Custom Stage Data (Prismatic) Listed below (Recalc)

Elevation (feet)	Surf.Area (sq-ft)	Inc.Store (cubic-feet)	Cum.Store (cubic-feet)
323.50	16,612	0	0
324.00	18,596	8,802	8,802
326.00	26,786	45,382	54,184

Device	Routing	Invert	Outlet Devices
#1	Discarded	323.50'	3.500 in/hr Exfiltration over Surface area
#2	Secondary	325.00'	10.0' long x 10.0' breadth Broad-Crested Rectangular Weir Head (feet) 0.20 0.40 0.60 0.80 1.00 1.20 1.40 1.60 Coef. (English) 2.49 2.56 2.70 2.69 2.68 2.69 2.67 2.64

Discarded OutFlow Max=1.36 cfs @ 12.65 hrs HW=323.54' (Free Discharge)
↑—1=Exfiltration (Exfiltration Controls 1.36 cfs)

Secondary OutFlow Max=0.00 cfs @ 5.00 hrs HW=323.50' (Free Discharge)
↑—2=Broad-Crested Rectangular Weir (Controls 0.00 cfs)

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 10-yr Rainfall=3.75"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 26

Summary for Pond 2P: Infiltration Trench

Inflow Area = 2.540 ac, 20.87% Impervious, Inflow Depth > 0.20" for 10-yr event
 Inflow = 0.21 cfs @ 12.56 hrs, Volume= 0.043 af
 Outflow = 0.21 cfs @ 12.58 hrs, Volume= 0.043 af, Atten= 0%, Lag= 0.8 min
 Discarded = 0.21 cfs @ 12.58 hrs, Volume= 0.043 af

Routing by Stor-Ind method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 Peak Elev= 322.01' @ 12.58 hrs Surf.Area= 2,413 sf Storage= 10 cf

Plug-Flow detention time= 0.8 min calculated for 0.043 af (100% of inflow)
 Center-of-Mass det. time= 0.5 min (906.5 - 906.0)

Volume	Invert	Avail.Storage	Storage Description
#1	322.00'	1,930 cf	Custom Stage Data (Prismatic) Listed below (Recalc) 4,826 cf Overall x 40.0% Voids
#2	324.00'	7,290 cf	Custom Stage Data (Prismatic) Listed below (Recalc)
		9,220 cf	Total Available Storage

Elevation (feet)	Surf.Area (sq-ft)	Inc.Store (cubic-feet)	Cum.Store (cubic-feet)
322.00	2,413	0	0
324.00	2,413	4,826	4,826

Elevation (feet)	Surf.Area (sq-ft)	Inc.Store (cubic-feet)	Cum.Store (cubic-feet)
324.00	2,413	0	0
326.00	4,877	7,290	7,290

Device	Routing	Invert	Outlet Devices
#1	Discarded	322.00'	15.000 in/hr Exfiltration over Surface area

Discarded OutFlow Max=0.84 cfs @ 12.58 hrs HW=322.01' (Free Discharge)
 ↑**1=Exfiltration** (Exfiltration Controls 0.84 cfs)

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 27

Time span=5.00-20.00 hrs, dt=0.05 hrs, 301 points
Runoff by SCS TR-20 method, UH=SCS, Weighted-CN
Reach routing by Stor-Ind+Trans method - Pond routing by Stor-Ind method

Subcatchment 1A: Runoff Area=0.550 ac 0.00% Impervious Runoff Depth>0.05"
Flow Length=150' Tc=15.2 min CN=37 Runoff=0.00 cfs 0.002 af

Subcatchment 1B: Runoff Area=2.540 ac 20.87% Impervious Runoff Depth>0.45"
Flow Length=150' Tc=15.2 min CN=50 Runoff=0.64 cfs 0.095 af

Subcatchment 2A: Runoff Area=8.100 ac 2.84% Impervious Runoff Depth>0.07"
Flow Length=533' Tc=38.2 min CN=38 Runoff=0.09 cfs 0.045 af

Subcatchment 2B: Runoff Area=13.320 ac 23.50% Impervious Runoff Depth>0.54"
Flow Length=1,509' Tc=14.0 min CN=52 Runoff=4.71 cfs 0.598 af

Subcatchment 3A: Runoff Area=2.100 ac 0.00% Impervious Runoff Depth>0.07"
Flow Length=302' Tc=19.2 min CN=38 Runoff=0.02 cfs 0.012 af

Subcatchment 4A: Runoff Area=16.720 ac 0.00% Impervious Runoff Depth>0.03"
Flow Length=298' Tc=17.9 min CN=36 Runoff=0.10 cfs 0.048 af

Subcatchment 5A: Runoff Area=1.790 ac 0.00% Impervious Runoff Depth>0.05"
Flow Length=269' Tc=14.5 min CN=37 Runoff=0.01 cfs 0.008 af

Subcatchment 6A: Runoff Area=11.980 ac 0.00% Impervious Runoff Depth>0.03"
Flow Length=550' Tc=26.6 min CN=36 Runoff=0.07 cfs 0.034 af

Subcatchment 7A: Runoff Area=5.270 ac 0.00% Impervious Runoff Depth>0.03"
Flow Length=350' Tc=17.5 min CN=36 Runoff=0.03 cfs 0.015 af

Subcatchment 8A: Runoff Area=10.360 ac 0.00% Impervious Runoff Depth>0.03"
Flow Length=305' Tc=21.2 min CN=36 Runoff=0.06 cfs 0.030 af

Reach DP1A: Inflow=0.00 cfs 0.002 af
Outflow=0.00 cfs 0.002 af

Reach DP2A: Inflow=0.09 cfs 0.045 af
Outflow=0.09 cfs 0.045 af

Reach DP3A: Inflow=0.02 cfs 0.012 af
Outflow=0.02 cfs 0.012 af

Reach DP4A: Inflow=0.10 cfs 0.048 af
Outflow=0.10 cfs 0.048 af

Reach DP5A: Inflow=0.01 cfs 0.008 af
Outflow=0.01 cfs 0.008 af

Reach DP6A: Inflow=0.07 cfs 0.034 af
Outflow=0.07 cfs 0.034 af

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 28

Reach DP7A:

Inflow=0.03 cfs 0.015 af
Outflow=0.03 cfs 0.015 af

Reach DP8A:

Inflow=0.06 cfs 0.030 af
Outflow=0.06 cfs 0.030 af

Pond 1P: Infiltration Basin

Peak Elev=323.85' Storage=6,049 cf Inflow=4.71 cfs 0.598 af
Discarded=1.46 cfs 0.595 af Secondary=0.00 cfs 0.000 af Outflow=1.46 cfs 0.595 af

Pond 2P: Infiltration Trench

Peak Elev=322.03' Storage=30 cf Inflow=0.64 cfs 0.095 af
Outflow=0.65 cfs 0.095 af

Total Runoff Area = 72.730 ac Runoff Volume = 0.887 af Average Runoff Depth = 0.15"
94.65% Pervious = 68.840 ac 5.35% Impervious = 3.890 ac

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 29

Summary for Subcatchment 1A:

Runoff = 0.00 cfs @ 16.35 hrs, Volume= 0.002 af, Depth> 0.05"

Routed to Reach DP1A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Area (ac)	CN	Description
0.170	39	>75% Grass cover, Good, HSG A
0.380	36	Woods, Fair, HSG A
0.550	37	Weighted Average
0.550		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
0.8	50	0.0400	1.00		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
15.2	150	Total			

Summary for Subcatchment 1B:

Runoff = 0.64 cfs @ 12.30 hrs, Volume= 0.095 af, Depth> 0.45"

Routed to Pond 2P : Infiltration Trench

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Area (ac)	CN	Description
* 0.270	98	Paved parking, HSG A (Existing)
* 0.260	98	Paved parking, HSG A (New)
1.210	39	>75% Grass cover, Good, HSG A
0.800	36	Woods, Fair, HSG A
2.540	50	Weighted Average
2.010		79.13% Pervious Area
0.530		20.87% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
0.8	50	0.0400	1.00		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
15.2	150	Total			

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 30

Summary for Subcatchment 2A:

Runoff = 0.09 cfs @ 15.15 hrs, Volume= 0.045 af, Depth> 0.07"

Routed to Reach DP2A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Area (ac)	CN	Description
0.230	98	Paved parking, HSG A
0.770	39	>75% Grass cover, Good, HSG A
7.100	36	Woods, Fair, HSG A
8.100	38	Weighted Average
7.870		97.16% Pervious Area
0.230		2.84% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
23.8	100	0.0200	0.07		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
14.4	433	0.0100	0.50		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
38.2	533	Total			

Summary for Subcatchment 2B:

Runoff = 4.71 cfs @ 12.23 hrs, Volume= 0.598 af, Depth> 0.54"

Routed to Pond 1P : Infiltration Basin

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Area (ac)	CN	Description
3.130	98	Paved parking, HSG A
8.430	39	>75% Grass cover, Good, HSG A
1.760	36	Woods, Fair, HSG A
13.320	52	Weighted Average
10.190		76.50% Pervious Area
3.130		23.50% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
8.9	78	0.0510	0.15		Sheet Flow, Grass: Dense n= 0.240 P2= 2.61"
5.1	1,431	0.0100	4.65	74.42	Channel Flow, Area= 16.0 sf Perim= 28.0' r= 0.57' n= 0.022 Earth, clean & straight
14.0	1,509	Total			

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 31

Summary for Subcatchment 3A:

Runoff = 0.02 cfs @ 14.81 hrs, Volume= 0.012 af, Depth> 0.07"
 Routed to Reach DP3A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Area (ac)	CN	Description
0.910	36	Woods, Fair, HSG A
1.190	39	>75% Grass cover, Good, HSG A
2.100	38	Weighted Average
2.100		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
15.3	100	0.0600	0.11		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
3.9	202	0.0300	0.87		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
19.2	302	Total			

Summary for Subcatchment 4A:

Runoff = 0.10 cfs @ 18.68 hrs, Volume= 0.048 af, Depth> 0.03"
 Routed to Reach DP4A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Area (ac)	CN	Description
15.420	36	Woods, Fair, HSG A
1.300	39	>75% Grass cover, Good, HSG A
16.720	36	Weighted Average
16.720		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
3.5	198	0.0350	0.94		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.9	298	Total			

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 32

Summary for Subcatchment 5A:

Runoff = 0.01 cfs @ 16.30 hrs, Volume= 0.008 af, Depth> 0.05"
Routed to Reach DP5A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Area (ac)	CN	Description
0.950	36	Woods, Fair, HSG A
0.840	39	>75% Grass cover, Good, HSG A
1.790	37	Weighted Average
1.790		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
12.5	100	0.1000	0.13		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
2.0	169	0.0400	1.40		Shallow Concentrated Flow, Short Grass Pasture Kv= 7.0 fps
14.5	269	Total			

Summary for Subcatchment 6A:

Runoff = 0.07 cfs @ 18.96 hrs, Volume= 0.034 af, Depth> 0.03"
Routed to Reach DP6A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Area (ac)	CN	Description
11.330	36	Woods, Fair, HSG A
0.650	39	>75% Grass cover, Good, HSG A
11.980	36	Weighted Average
11.980		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
12.2	450	0.0150	0.61		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
26.6	550	Total			

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 33

Summary for Subcatchment 7A:

Runoff = 0.03 cfs @ 18.73 hrs, Volume= 0.015 af, Depth> 0.03"

Routed to Reach DP7A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Area (ac)	CN	Description
0.830	39	>75% Grass cover, Good, HSG A
4.440	36	Woods, Fair, HSG A
5.270	36	Weighted Average
5.270		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
11.6	100	0.1200	0.14		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
5.9	250	0.0200	0.71		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.5	350	Total			

Summary for Subcatchment 8A:

Runoff = 0.06 cfs @ 18.83 hrs, Volume= 0.030 af, Depth> 0.03"

Routed to Reach DP8A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Area (ac)	CN	Description
10.360	36	Woods, Fair, HSG A
10.360		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
6.8	205	0.0100	0.50		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
21.2	305	Total			

Summary for Reach DP1A:

Inflow Area = 0.550 ac, 0.00% Impervious, Inflow Depth > 0.05" for 25-yr event
Inflow = 0.00 cfs @ 16.35 hrs, Volume= 0.002 af
Outflow = 0.00 cfs @ 16.35 hrs, Volume= 0.002 af, Atten= 0%, Lag= 0.0 min

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 34

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP2A:

Inflow Area =	8.100 ac,	2.84% Impervious,	Inflow Depth > 0.07"	for 25-yr event
Inflow =	0.09 cfs @	15.15 hrs,	Volume=	0.045 af
Outflow =	0.09 cfs @	15.15 hrs,	Volume=	0.045 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP3A:

Inflow Area =	2.100 ac,	0.00% Impervious,	Inflow Depth > 0.07"	for 25-yr event
Inflow =	0.02 cfs @	14.81 hrs,	Volume=	0.012 af
Outflow =	0.02 cfs @	14.81 hrs,	Volume=	0.012 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP4A:

Inflow Area =	16.720 ac,	0.00% Impervious,	Inflow Depth > 0.03"	for 25-yr event
Inflow =	0.10 cfs @	18.68 hrs,	Volume=	0.048 af
Outflow =	0.10 cfs @	18.68 hrs,	Volume=	0.048 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP5A:

Inflow Area =	1.790 ac,	0.00% Impervious,	Inflow Depth > 0.05"	for 25-yr event
Inflow =	0.01 cfs @	16.30 hrs,	Volume=	0.008 af
Outflow =	0.01 cfs @	16.30 hrs,	Volume=	0.008 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP6A:

Inflow Area =	11.980 ac,	0.00% Impervious,	Inflow Depth > 0.03"	for 25-yr event
Inflow =	0.07 cfs @	18.96 hrs,	Volume=	0.034 af
Outflow =	0.07 cfs @	18.96 hrs,	Volume=	0.034 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP7A:

Inflow Area =	5.270 ac,	0.00% Impervious,	Inflow Depth > 0.03"	for 25-yr event
Inflow =	0.03 cfs @	18.73 hrs,	Volume=	0.015 af
Outflow =	0.03 cfs @	18.73 hrs,	Volume=	0.015 af, Atten= 0%, Lag= 0.0 min

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 35

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP8A:

Inflow Area = 10.360 ac, 0.00% Impervious, Inflow Depth > 0.03" for 25-yr event
Inflow = 0.06 cfs @ 18.83 hrs, Volume= 0.030 af
Outflow = 0.06 cfs @ 18.83 hrs, Volume= 0.030 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Pond 1P: Infiltration Basin

Inflow Area = 13.320 ac, 23.50% Impervious, Inflow Depth > 0.54" for 25-yr event
Inflow = 4.71 cfs @ 12.23 hrs, Volume= 0.598 af
Outflow = 1.46 cfs @ 12.96 hrs, Volume= 0.595 af, Atten= 69%, Lag= 43.6 min
Discarded = 1.46 cfs @ 12.96 hrs, Volume= 0.595 af
Secondary = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Routed to Reach DP2A :

Routing by Stor-Ind method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
Peak Elev= 323.85' @ 12.96 hrs Surf.Area= 17,999 sf Storage= 6,049 cf

Plug-Flow detention time= 33.2 min calculated for 0.593 af (99% of inflow)
Center-of-Mass det. time= 31.6 min (896.5 - 864.9)

Volume	Invert	Avail.Storage	Storage Description
#1	323.50'	54,184 cf	Custom Stage Data (Prismatic) Listed below (Recalc)

Elevation (feet)	Surf.Area (sq-ft)	Inc.Store (cubic-feet)	Cum.Store (cubic-feet)
323.50	16,612	0	0
324.00	18,596	8,802	8,802
326.00	26,786	45,382	54,184

Device	Routing	Invert	Outlet Devices
#1	Discarded	323.50'	3.500 in/hr Exfiltration over Surface area
#2	Secondary	325.00'	10.0' long x 10.0' breadth Broad-Crested Rectangular Weir Head (feet) 0.20 0.40 0.60 0.80 1.00 1.20 1.40 1.60 Coef. (English) 2.49 2.56 2.70 2.69 2.68 2.69 2.67 2.64

Discarded OutFlow Max=1.46 cfs @ 12.96 hrs HW=323.85' (Free Discharge)
↑—1=Exfiltration (Exfiltration Controls 1.46 cfs)

Secondary OutFlow Max=0.00 cfs @ 5.00 hrs HW=323.50' (Free Discharge)
↑—2=Broad-Crested Rectangular Weir (Controls 0.00 cfs)

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 25-yr Rainfall=4.62"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 36

Summary for Pond 2P: Infiltration Trench

Inflow Area = 2.540 ac, 20.87% Impervious, Inflow Depth > 0.45" for 25-yr event
 Inflow = 0.64 cfs @ 12.30 hrs, Volume= 0.095 af
 Outflow = 0.65 cfs @ 12.32 hrs, Volume= 0.095 af, Atten= 0%, Lag= 0.7 min
 Discarded = 0.65 cfs @ 12.32 hrs, Volume= 0.095 af

Routing by Stor-Ind method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 Peak Elev= 322.03' @ 12.32 hrs Surf.Area= 2,413 sf Storage= 30 cf

Plug-Flow detention time= 0.8 min calculated for 0.095 af (100% of inflow)
 Center-of-Mass det. time= 0.5 min (874.7 - 874.2)

Volume	Invert	Avail.Storage	Storage Description
#1	322.00'	1,930 cf	Custom Stage Data (Prismatic) Listed below (Recalc) 4,826 cf Overall x 40.0% Voids
#2	324.00'	7,290 cf	Custom Stage Data (Prismatic) Listed below (Recalc)
		9,220 cf	Total Available Storage

Elevation (feet)	Surf.Area (sq-ft)	Inc.Store (cubic-feet)	Cum.Store (cubic-feet)
322.00	2,413	0	0
324.00	2,413	4,826	4,826

Elevation (feet)	Surf.Area (sq-ft)	Inc.Store (cubic-feet)	Cum.Store (cubic-feet)
324.00	2,413	0	0
326.00	4,877	7,290	7,290

Device	Routing	Invert	Outlet Devices
#1	Discarded	322.00'	15.000 in/hr Exfiltration over Surface area

Discarded OutFlow Max=0.84 cfs @ 12.32 hrs HW=322.03' (Free Discharge)
 ↑**1=Exfiltration** (Exfiltration Controls 0.84 cfs)

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 37

Time span=5.00-20.00 hrs, dt=0.05 hrs, 301 points
Runoff by SCS TR-20 method, UH=SCS, Weighted-CN
Reach routing by Stor-Ind+Trans method - Pond routing by Stor-Ind method

Subcatchment 1A: Runoff Area=0.550 ac 0.00% Impervious Runoff Depth>0.34"
Flow Length=150' Tc=15.2 min CN=37 Runoff=0.08 cfs 0.016 af

Subcatchment 1B: Runoff Area=2.540 ac 20.87% Impervious Runoff Depth>1.13"
Flow Length=150' Tc=15.2 min CN=50 Runoff=2.37 cfs 0.240 af

Subcatchment 2A: Runoff Area=8.100 ac 2.84% Impervious Runoff Depth>0.38"
Flow Length=533' Tc=38.2 min CN=38 Runoff=1.14 cfs 0.256 af

Subcatchment 2B: Runoff Area=13.320 ac 23.50% Impervious Runoff Depth>1.28"
Flow Length=1,509' Tc=14.0 min CN=52 Runoff=15.11 cfs 1.422 af

Subcatchment 3A: Runoff Area=2.100 ac 0.00% Impervious Runoff Depth>0.39"
Flow Length=302' Tc=19.2 min CN=38 Runoff=0.37 cfs 0.068 af

Subcatchment 4A: Runoff Area=16.720 ac 0.00% Impervious Runoff Depth>0.29"
Flow Length=298' Tc=17.9 min CN=36 Runoff=1.96 cfs 0.405 af

Subcatchment 5A: Runoff Area=1.790 ac 0.00% Impervious Runoff Depth>0.34"
Flow Length=269' Tc=14.5 min CN=37 Runoff=0.28 cfs 0.051 af

Subcatchment 6A: Runoff Area=11.980 ac 0.00% Impervious Runoff Depth>0.29"
Flow Length=550' Tc=26.6 min CN=36 Runoff=1.23 cfs 0.287 af

Subcatchment 7A: Runoff Area=5.270 ac 0.00% Impervious Runoff Depth>0.29"
Flow Length=350' Tc=17.5 min CN=36 Runoff=0.62 cfs 0.128 af

Subcatchment 8A: Runoff Area=10.360 ac 0.00% Impervious Runoff Depth>0.29"
Flow Length=305' Tc=21.2 min CN=36 Runoff=1.15 cfs 0.250 af

Reach DP1A: Inflow=0.08 cfs 0.016 af
Outflow=0.08 cfs 0.016 af

Reach DP2A: Inflow=1.14 cfs 0.256 af
Outflow=1.14 cfs 0.256 af

Reach DP3A: Inflow=0.37 cfs 0.068 af
Outflow=0.37 cfs 0.068 af

Reach DP4A: Inflow=1.96 cfs 0.405 af
Outflow=1.96 cfs 0.405 af

Reach DP5A: Inflow=0.28 cfs 0.051 af
Outflow=0.28 cfs 0.051 af

Reach DP6A: Inflow=1.23 cfs 0.287 af
Outflow=1.23 cfs 0.287 af

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 38

Reach DP7A:

Inflow=0.62 cfs 0.128 af
Outflow=0.62 cfs 0.128 af

Reach DP8A:

Inflow=1.15 cfs 0.250 af
Outflow=1.15 cfs 0.250 af

Pond 1P: Infiltration Basin

Peak Elev=324.90' Storage=27,088 cf Inflow=15.11 cfs 1.422 af
Discarded=1.80 cfs 1.150 af Secondary=0.00 cfs 0.000 af Outflow=1.80 cfs 1.150 af

Pond 2P: Infiltration Trench

Peak Elev=323.99' Storage=1,921 cf Inflow=2.37 cfs 0.240 af
Outflow=1.48 cfs 0.240 af

Total Runoff Area = 72.730 ac Runoff Volume = 3.122 af Average Runoff Depth = 0.52"
94.65% Pervious = 68.840 ac 5.35% Impervious = 3.890 ac

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 39

Summary for Subcatchment 1A:

Runoff = 0.08 cfs @ 12.58 hrs, Volume= 0.016 af, Depth> 0.34"

Routed to Reach DP1A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Area (ac)	CN	Description
0.170	39	>75% Grass cover, Good, HSG A
0.380	36	Woods, Fair, HSG A
0.550	37	Weighted Average
0.550		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
0.8	50	0.0400	1.00		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
15.2	150	Total			

Summary for Subcatchment 1B:

Runoff = 2.37 cfs @ 12.21 hrs, Volume= 0.240 af, Depth> 1.13"

Routed to Pond 2P : Infiltration Trench

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Area (ac)	CN	Description
* 0.270	98	Paved parking, HSG A (Existing)
* 0.260	98	Paved parking, HSG A (New)
1.210	39	>75% Grass cover, Good, HSG A
0.800	36	Woods, Fair, HSG A
2.540	50	Weighted Average
2.010		79.13% Pervious Area
0.530		20.87% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
0.8	50	0.0400	1.00		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
15.2	150	Total			

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 40

Summary for Subcatchment 2A:

Runoff = 1.14 cfs @ 12.83 hrs, Volume= 0.256 af, Depth> 0.38"

Routed to Reach DP2A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Area (ac)	CN	Description
0.230	98	Paved parking, HSG A
0.770	39	>75% Grass cover, Good, HSG A
7.100	36	Woods, Fair, HSG A
8.100	38	Weighted Average
7.870		97.16% Pervious Area
0.230		2.84% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
23.8	100	0.0200	0.07		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
14.4	433	0.0100	0.50		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
38.2	533	Total			

Summary for Subcatchment 2B:

Runoff = 15.11 cfs @ 12.18 hrs, Volume= 1.422 af, Depth> 1.28"

Routed to Pond 1P : Infiltration Basin

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Area (ac)	CN	Description
3.130	98	Paved parking, HSG A
8.430	39	>75% Grass cover, Good, HSG A
1.760	36	Woods, Fair, HSG A
13.320	52	Weighted Average
10.190		76.50% Pervious Area
3.130		23.50% Impervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
8.9	78	0.0510	0.15		Sheet Flow, Grass: Dense n= 0.240 P2= 2.61"
5.1	1,431	0.0100	4.65	74.42	Channel Flow, Area= 16.0 sf Perim= 28.0' r= 0.57' n= 0.022 Earth, clean & straight
14.0	1,509	Total			

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 41

Summary for Subcatchment 3A:

Runoff = 0.37 cfs @ 12.60 hrs, Volume= 0.068 af, Depth> 0.39"
Routed to Reach DP3A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Area (ac)	CN	Description
0.910	36	Woods, Fair, HSG A
1.190	39	>75% Grass cover, Good, HSG A
2.100	38	Weighted Average
2.100		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
15.3	100	0.0600	0.11		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
3.9	202	0.0300	0.87		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
19.2	302	Total			

Summary for Subcatchment 4A:

Runoff = 1.96 cfs @ 12.62 hrs, Volume= 0.405 af, Depth> 0.29"
Routed to Reach DP4A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Area (ac)	CN	Description
15.420	36	Woods, Fair, HSG A
1.300	39	>75% Grass cover, Good, HSG A
16.720	36	Weighted Average
16.720		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
3.5	198	0.0350	0.94		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.9	298	Total			

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 © 2021 HydroCAD Software Solutions LLC

Page 42

Summary for Subcatchment 5A:

Runoff = 0.28 cfs @ 12.57 hrs, Volume= 0.051 af, Depth> 0.34"
Routed to Reach DP5A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Area (ac)	CN	Description
0.950	36	Woods, Fair, HSG A
0.840	39	>75% Grass cover, Good, HSG A
1.790	37	Weighted Average
1.790		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
12.5	100	0.1000	0.13		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
2.0	169	0.0400	1.40		Shallow Concentrated Flow, Short Grass Pasture Kv= 7.0 fps
14.5	269	Total			

Summary for Subcatchment 6A:

Runoff = 1.23 cfs @ 12.73 hrs, Volume= 0.287 af, Depth> 0.29"
Routed to Reach DP6A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Area (ac)	CN	Description
11.330	36	Woods, Fair, HSG A
0.650	39	>75% Grass cover, Good, HSG A
11.980	36	Weighted Average
11.980		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
12.2	450	0.0150	0.61		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
26.6	550	Total			

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 43

Summary for Subcatchment 7A:

Runoff = 0.62 cfs @ 12.61 hrs, Volume= 0.128 af, Depth> 0.29"
Routed to Reach DP7A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Area (ac)	CN	Description
0.830	39	>75% Grass cover, Good, HSG A
4.440	36	Woods, Fair, HSG A
5.270	36	Weighted Average
5.270		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
11.6	100	0.1200	0.14		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
5.9	250	0.0200	0.71		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
17.5	350	Total			

Summary for Subcatchment 8A:

Runoff = 1.15 cfs @ 12.66 hrs, Volume= 0.250 af, Depth> 0.29"
Routed to Reach DP8A :

Runoff by SCS TR-20 method, UH=SCS, Weighted-CN, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Area (ac)	CN	Description
10.360	36	Woods, Fair, HSG A
10.360		100.00% Pervious Area

Tc (min)	Length (feet)	Slope (ft/ft)	Velocity (ft/sec)	Capacity (cfs)	Description
14.4	100	0.0700	0.12		Sheet Flow, Woods: Light underbrush n= 0.400 P2= 2.61"
6.8	205	0.0100	0.50		Shallow Concentrated Flow, Woodland Kv= 5.0 fps
21.2	305	Total			

Summary for Reach DP1A:

Inflow Area = 0.550 ac, 0.00% Impervious, Inflow Depth > 0.34" for 100-yr event
Inflow = 0.08 cfs @ 12.58 hrs, Volume= 0.016 af
Outflow = 0.08 cfs @ 12.58 hrs, Volume= 0.016 af, Atten= 0%, Lag= 0.0 min

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 44

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP2A:

Inflow Area =	8.100 ac,	2.84% Impervious,	Inflow Depth > 0.38"	for 100-yr event
Inflow =	1.14 cfs @	12.83 hrs,	Volume=	0.256 af
Outflow =	1.14 cfs @	12.83 hrs,	Volume=	0.256 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP3A:

Inflow Area =	2.100 ac,	0.00% Impervious,	Inflow Depth > 0.39"	for 100-yr event
Inflow =	0.37 cfs @	12.60 hrs,	Volume=	0.068 af
Outflow =	0.37 cfs @	12.60 hrs,	Volume=	0.068 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP4A:

Inflow Area =	16.720 ac,	0.00% Impervious,	Inflow Depth > 0.29"	for 100-yr event
Inflow =	1.96 cfs @	12.62 hrs,	Volume=	0.405 af
Outflow =	1.96 cfs @	12.62 hrs,	Volume=	0.405 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP5A:

Inflow Area =	1.790 ac,	0.00% Impervious,	Inflow Depth > 0.34"	for 100-yr event
Inflow =	0.28 cfs @	12.57 hrs,	Volume=	0.051 af
Outflow =	0.28 cfs @	12.57 hrs,	Volume=	0.051 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP6A:

Inflow Area =	11.980 ac,	0.00% Impervious,	Inflow Depth > 0.29"	for 100-yr event
Inflow =	1.23 cfs @	12.73 hrs,	Volume=	0.287 af
Outflow =	1.23 cfs @	12.73 hrs,	Volume=	0.287 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP7A:

Inflow Area =	5.270 ac,	0.00% Impervious,	Inflow Depth > 0.29"	for 100-yr event
Inflow =	0.62 cfs @	12.61 hrs,	Volume=	0.128 af
Outflow =	0.62 cfs @	12.61 hrs,	Volume=	0.128 af, Atten= 0%, Lag= 0.0 min

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 45

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Reach DP8A:

Inflow Area = 10.360 ac, 0.00% Impervious, Inflow Depth > 0.29" for 100-yr event
Inflow = 1.15 cfs @ 12.66 hrs, Volume= 0.250 af
Outflow = 1.15 cfs @ 12.66 hrs, Volume= 0.250 af, Atten= 0%, Lag= 0.0 min

Routing by Stor-Ind+Trans method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs

Summary for Pond 1P: Infiltration Basin

Inflow Area = 13.320 ac, 23.50% Impervious, Inflow Depth > 1.28" for 100-yr event
Inflow = 15.11 cfs @ 12.18 hrs, Volume= 1.422 af
Outflow = 1.80 cfs @ 13.86 hrs, Volume= 1.150 af, Atten= 88%, Lag= 100.8 min
Discarded = 1.80 cfs @ 13.86 hrs, Volume= 1.150 af
Secondary = 0.00 cfs @ 5.00 hrs, Volume= 0.000 af
Routed to Reach DP2A :

Routing by Stor-Ind method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
Peak Elev= 324.90' @ 13.86 hrs Surf.Area= 22,261 sf Storage= 27,088 cf

Plug-Flow detention time= 170.6 min calculated for 1.146 af (81% of inflow)
Center-of-Mass det. time= 115.0 min (953.7 - 838.7)

Volume	Invert	Avail.Storage	Storage Description
#1	323.50'	54,184 cf	Custom Stage Data (Prismatic) Listed below (Recalc)

Elevation (feet)	Surf.Area (sq-ft)	Inc.Store (cubic-feet)	Cum.Store (cubic-feet)
323.50	16,612	0	0
324.00	18,596	8,802	8,802
326.00	26,786	45,382	54,184

Device	Routing	Invert	Outlet Devices
#1	Discarded	323.50'	3.500 in/hr Exfiltration over Surface area
#2	Secondary	325.00'	10.0' long x 10.0' breadth Broad-Crested Rectangular Weir Head (feet) 0.20 0.40 0.60 0.80 1.00 1.20 1.40 1.60 Coef. (English) 2.49 2.56 2.70 2.69 2.68 2.69 2.67 2.64

Discarded OutFlow Max=1.80 cfs @ 13.86 hrs HW=324.90' (Free Discharge)
↑—1=Exfiltration (Exfiltration Controls 1.80 cfs)

Secondary OutFlow Max=0.00 cfs @ 5.00 hrs HW=323.50' (Free Discharge)
↑—2=Broad-Crested Rectangular Weir (Controls 0.00 cfs)

PROPOSED CONDITIONS

NY - Bullard Lane 24-hr S1 100-yr Rainfall=6.33"

Prepared by Lansing Eng

Printed 2/3/2026

HydroCAD® 10.10-7a s/n 10911 ©2021 HydroCAD Software Solutions LLC

Page 46

Summary for Pond 2P: Infiltration Trench

Inflow Area = 2.540 ac, 20.87% Impervious, Inflow Depth > 1.13" for 100-yr event
 Inflow = 2.37 cfs @ 12.21 hrs, Volume= 0.240 af
 Outflow = 1.48 cfs @ 12.58 hrs, Volume= 0.240 af, Atten= 38%, Lag= 22.0 min
 Discarded = 1.48 cfs @ 12.58 hrs, Volume= 0.240 af

Routing by Stor-Ind method, Time Span= 5.00-20.00 hrs, dt= 0.05 hrs
 Peak Elev= 323.99' @ 12.58 hrs Surf.Area= 2,413 sf Storage= 1,921 cf

Plug-Flow detention time= 13.8 min calculated for 0.239 af (100% of inflow)
 Center-of-Mass det. time= 13.6 min (858.2 - 844.6)

Volume	Invert	Avail.Storage	Storage Description
#1	322.00'	1,930 cf	Custom Stage Data (Prismatic) Listed below (Recalc) 4,826 cf Overall x 40.0% Voids
#2	324.00'	7,290 cf	Custom Stage Data (Prismatic) Listed below (Recalc)
		9,220 cf	Total Available Storage

Elevation (feet)	Surf.Area (sq-ft)	Inc.Store (cubic-feet)	Cum.Store (cubic-feet)
322.00	2,413	0	0
324.00	2,413	4,826	4,826

Elevation (feet)	Surf.Area (sq-ft)	Inc.Store (cubic-feet)	Cum.Store (cubic-feet)
324.00	2,413	0	0
326.00	4,877	7,290	7,290

Device	Routing	Invert	Outlet Devices
#1	Discarded	322.00'	15.000 in/hr Exfiltration over Surface area

Discarded OutFlow Max=0.84 cfs @ 12.58 hrs HW=323.99' (Free Discharge)
 ↑**1=Exfiltration** (Exfiltration Controls 0.84 cfs)



Appendix D:

Calculations- Storm Management, Green Infrastructure, Pipe Sizing



Steps 3 and 5 - Apply RR Techniques and Standard SMPs

Is this project subject to Section 4.3 of the NYS Design Manual for Enhanced Phosphorus Removal?						No		
What is the nature of this construction project?		Redevelopment with increase in impervious area						
Project Title	Bullard Lane		<i>Enter 90% Rainfall Event as P</i>					
P=	1.15	inches						
Calculate Required WQv								
Contributing Area (Acres)	Impervious Area (Acres)	Percent Impervious %	Rv	WQv (cf)	SMP Description			
Project Area Total	72.73	3.39	4.66	0.09	27,917			
SMP Practice								
1	41.22	0.00	0	0.05	0	Conservation of Natural Areas		
2	13.32	3.13	23	0.26	14,540	Infiltration Basin		
3	2.54	0.53	21	0.24	2,521	Dry Swale		
4								
5								
6								
7								
8								
9								
10								
11								
12								
13								
14								
15								
16								
17								
18								
19								
20								
21								
22								
23								
24								
25								
26								
27								
Sum of Practices	57.08	3.66	6	0.11	25,665			
Total	72.73	3.39	5	0.09	27917	Required WQv	0.641 af	

Steps 3 and 5 - Apply RR Techniques and Standard SMPs

Enter the Soils Data for the site						
Hydrologic Soil Group	Acres	S				
A	72.73	55%				
B		40%				
C		30%				
D		20%				
Total Area	72.73					
Calculate the Minimum RRv						
S =	0.55					
Impervious =	3.39	<i>acres</i>				
Precipitation	1.15	<i>inches</i>				
Rv	0.95					
Minimum RRv	0.170	<i>af</i>				
	7405	<i>cf</i>				

Steps 3 and 5 - Apply RR Techniques and Standard SMPs

Runoff Reduction Volume and Treated Volumes						
	Runoff Reduction Techniques/Standard SMPs		Total Contributing Area	Total Contributing Impervious Area	WQv Reduced (RRv)	WQv Treated
			(acres)	(acres)	(cf)	(cf)
RR Techniques	Conservation of Natural Areas	RR-1	41.22		15,822	
	Sheet Flow to Riparian Buffer/Filter Strip	RR-2	0.00	0.00	0	
	Tree Planting/Tree Pit/Tree Trench	RR-3	0.00	0.00	0	
	Disconnection of Rooftop Runoff	RR-4		0.00	0	
	Vegetated Swale	RR-5	0.00	0.00	0	
	Rain Garden	RR-6	0.00	0.00	0	
	Stormwater Planter	RR-7	0.00	0.00	0	
	Rainwater Harvesting Systems	RR-8	0.00	0.00	0	
	Porous Pavement	RR-9	0.00	0.00	0	
	Green Roof (Extensive & Intensive)	RR-10	0.00	0.00	0	
	Stream Daylighting	RR-11				
Standard SMPs w/ RRV Capacity	Infiltration Trench	I-1	2.54	0.53	2,521	0
	Infiltration Basin	I-2	13.32	3.13	14,540	0
	Dry Well	I-3	0.00	0.00	0	0
	Underground Infiltration System	I-4	0.00	0.00	0	0
	Infiltration Bioretention	F-4	0.00	0.00	0	0
	Filtration Bioretention	F-5	0.00	0.00	0	0
	Bioslope	F-6	0.00	0.00	0	0
	Dry swale	O-1	0.00	0.00	0	0
Standard SMPs	Micropool Extended Detention	P-1	5.00	3.13		14,540
	Wet Pond	P-2	0.00	0.00		0
	Wet Extended Detention	P-3	0.00	0.00		0
	Multiple Pond System	P-4	0.00	0.00		0
	Shallow Wetland	W-1	0.00	0.00		0
	Extended Detention Shallow Wetland	W-2	0.00	0.00		0
	Pond/Wetland System	W-3	0.00	0.00		0
	Pocket Wetland	W-4	0.00	0.00		0
	Gravel Wetland	W-5	0.00	0.00		0
	Surface Sand Filter	F-1	0.00	0.00		0
	Underground Sand Filter	F-2	0.00	0.00		0
	Perimeter Sand Filter	F-3	0.00	0.00		0
Wet Swale	O-2	0.00	0.00		0	
Alt. SMPs	Flow Based Alternative Practice	-	0.00	0.00		0
	Volume Based Alternative Practice	-				
Totals by RR Technique →			41.22	0.00	15,822	
Totals by Standard SMP w/RRV →			15.86	3.66	17,061	0
Totals by Standard SMP →			5.00	3.13		14,540
Totals by Alternative SMP →			0.00	0.00		0
Totals (RR Techniques + all SMPs) →			62.08	6.79	32,883	14,540

Steps 3 and 5 - Apply RR Techniques and Standard SMPs

#	NOI Question	Reported Value	
		cf	af
28	Total Water Quality Volume (WQv) Required	27917	0.641
30	Total RRV Provided	32883	0.755
31	Is RRV Provided \geq WQv Required?	Yes	
32	Minimum RRV	7405	0.170
32a	Is RRV Provided \geq Minimum RRV Required?	Yes	
33a	Total WQv Treated	14540	0.334
34	Sum of Volume Reduced & Treated	47423	1.089
35	Is Sum RRV Provided and WQv Provided \geq WQv Required?	Yes	

Steps 3 and 5 - Apply RR Techniques and Standard SMPs

Design Point:	Bullard Lane	Drainage Area Number	1				
Design Criteria							
Does the conservation area proposed have a minimum contiguous area of 10,000					Yes		
Is the conservation area permanently protected through establishment of a legal conservation easement?					Yes		
Does the conservation area receive runoff from existing or new impervious areas?					No		
Is Sheet Flow to Riparian Buffer or another area based practice already being used for this area?					No		
Sizing Criteria							
	Contributing Area (Acres)	Impervious Area (Acres)	Percent Impervious %	Rv	WQv (cf)	Precipitation (in)	
Required WQv	72.73	3.39	5	0.09	27,917	1.15	
Subtract Area Conserved	41.22						
Area Reduction WQv	31.51	3.39			0.09	12,095	1.15
Area Reduction Adjustments							
RRv Provided	15,822	cf					

Infiltration Basin (I-2)

Design Point:	Bullard Lane						
Enter Site Data For Drainage Area to be Treated by Practice							
Drainage Area Number	Contributing Area (Acres)	Impervious Area (Acres)	Percent Impervious %	Rv	WQv (cf)	Precipitation (in)	Description
2	13.32	3.13	23	0.26	14,540	1.15	Infiltration Basin
Design Criteria							
Enter underlying soil infiltration rate (based on geotechnical testing, refer to Appendix D)			7				
Is the contributing area to the practice an "Infiltration Restricted" stormwater hotspot?			No				
Is the contributing area to the practice an "Infiltration Prohibited" stormwater hotspot?			No				
Maximum contributing area (acres)			25				
Is the contributing area greater than the maximum allowed contributing area?			No				
Enter depth to seasonal high water table (ft)			3.33				
Enter depth to bedrock (ft)			10				
Enter pretreatment volume provided (cf)			3821				
Enter depth of freeboard (ft)			1				
Enter depth of basin (ft)			2.5				
Enter slope of maintenance access (%)			1				
Enter width of maintenance access (ft)			12				
Sizing Criteria							
			Value	Units	Notes		
Water Quality Volume		WQv	14540	cf			
Basin depth		db	2.5	ft			
Required Surface Area		Ab	5,816	sf			
Enter Surface Area Provided		Ab	16612	sf			
Determine Runoff Reduction							
RRv Provided		14,540	cf				

Infiltration Trench (I-1)

Design Point:	Bullard Lane						
Enter Site Data For Drainage Area to be Treated by Practice							
Drainage Area Number	Contributing Area (Acres)	Impervious Area (Acres)	Percent Impervious %	Rv	WQv (cf)	Precipitation (in)	Description
3	2.54	0.53	21	0.24	2,521	1.15	Dry Swale
Design Criteria							
Enter underlying soil infiltration rate (based on geotechnical testing, refer to Appendix D)			33				
Is the contributing area to the practice an "Infiltration Restricted" stormwater hotspot?			No				
Is the contributing area to the practice an "Infiltration Prohibited" stormwater hotspot?			No				
Is the contributing area greater than 5 acres?			No				
Enter depth to seasonal high water table (ft)			9				
Enter depth to bedrock (ft)			9				
Enter pretreatment volume provided (cf)			1261				
Enter depth of pea gravel (inches)			4				
Enter depth of stone reservoir (ft)			2				
Is an observation well provided?			Yes				
Sizing Criteria							
		Value	Units	Notes			
Water Quality Volume	WQv	2521	cf				
Porosity	n	0.40					
Stone Reservoir Depth	dt	2.0	ft				
Required Surface Area	At	3,152.00	sf				
Enter Surface Area Provided	At	3152	sf				
Determine Runoff Reduction							
RRv Provided	2,521	cf					



Appendix E:

Grading/Drainage/Sediment, Erosion Control Plan, and Landscaping Plan



LEGEND	
EXISTING FEATURES	PROPOSED FEATURES
↑	FIRE HYDRANT
—	WATER LINE
□	CATCH BASIN
●	STORM MANHOLE
—	STORM WATER LINE
—	SANITARY GRAVITY LINE
—	SANITARY FORCEMAIN
●	SANITARY STRUCTURE
●	GRINDER PUMP
●	SANITARY CLEANOUT
---	PROPERTY LINE

NOTE: PROPOSED 60' R.O.W. TO BE DEDICATED TO THE TOWN OF WILTON.

- REALLY SUBDIVISION LOT # (TYP.)
- STREET ADDRESS (TYP.)
- PROPOSED APPROXIMATE GARAGE FINISH FLOOR ELEVATION (TYP.)
- APPROXIMATE LOCATION AND DIRECTION OF SIGN

TRAFFIC CONTROL DEVICE SCHEDULE		
PLAN NO.	DESCRIPTION	QTY.
1	R1-1 "STOP" SIGN	2
2	ROAD I.D. SIGN "BULLARD LANE X ROAD A"	1
4	R2-1 "SPEED LIMIT 30 MPH" SIGN	3
5	STORM WATER WARNING SIGN	2
6	DEED RESTRICTED LANDS	18
7	W14-2 NO OUTLET SIGN	1

NOTE:
1. CONTACT HIGHWAY DEPARTMENT FOR SIGN TYPE & SIGN REQUIREMENTS.

- PROPOSED PROPERTY LINE (TYP.)
- BUILDING SETBACK LINE (TYP.)
- EXISTING TREELINE (TYP.)
- PROPOSED TREELINE (TYP.)
- 8"x8"x8" TAPPING SLEEVE & GY
- APPROXIMATE LOCATION OF EXISTING WATERMAIN. CONTRACTOR TO VERIFY LOCATION PRIOR TO CONSTRUCTION.
- 3' WIDE GRAVEL SHOULDER (TYP.)
- PROPOSED 1" HDPE WATER SERVICE (TYP.)
- PROPOSED ASPHALT DRIVEWAY (TYP.)
- STORMWATER INFILTRATION TRENCH #1
- WASTEWATER DISPOSAL SYSTEM (TYP.) SEE NOTES THIS SHEET




MATCH LINE
SEE SHEET LMG-2

- NOTES:
- ALL LOTS SHALL BE GRADED TO DIRECT SURFACE RUNOFF AWAY FROM THE BUILDINGS AND ALONG THE PROPERTY LINES TO MUNICIPALLY OWNED CONVEYANCE SYSTEMS UNLESS OTHERWISE INDICATED ON THE PLANS.
 - ALL LOTS SHALL DIRECT ROOF STORMWATER RUNOFF TOWARD THE TOWN ROAD AND THE STORMWATER CONVEYANCE SYSTEM. LOTS THAT CAN NOT PROVIDE POSITIVE DRAINAGE TO THE STREET SHALL HAVE GUTTERS INSTALLED TO CONVEY REAR DRAINING ROOF RUNOFF TOWARDS THE TOWN ROAD OR STORMWATER CONVEYANCE SYSTEM.
 - ROADWAY PAVING PERMITTED BETWEEN APRIL 1 AND NOVEMBER 1. REFER TO TOWN CODE SECTION 109-23 FOR ROAD CONSTRUCTION REQUIREMENTS. ANY STRUCTURES IN ROADWAY SHALL BE SET 1" BELOW BINDER AND A RISER RING INSTALLED FOR TOP COURSE PAVING.
 - WATERMAIN SHALL CONSIST OF 8" PVC C900 PIPE PER INSTALLED WATER & SEWER AUTHORITY SPECIFICATIONS. ALL PIPES TO BE WILTON PER AWWA C900 STANDARDS.
 - WATER SERVICES SHALL CONSIST OF 1" CTS HDPE, DR-9 WITH TRACER WIRE, H=15000 CORPORATION VALVE, H=15200 CURB VALVE & H=10314 VALVE BOX AND MATCHING STATIONARY ROD. CONTRACTOR SHALL COORDINATE WITH WILTON WATER & SEWER AUTHORITY PRIOR TO CONSTRUCTION AND ORDERING OF MATERIALS.
 - REFER TO DETAIL 7 AND TRAIL AMENITY NOTES ON SHEET DT-4 FOR SPECIFIC TRAIL AND AMENITY NOTES & DETAILS.
 - TEST PITS COMPLETED ON 12/23/2025 AND WITNESSED BY SCOH CONFIRM ADEQUATE SOIL PROFILES AND PERCOLATION RESULTS TO SUPPORT INDIVIDUAL WASTEWATER DISPOSAL SYSTEMS.
 - PER TOWN OF WILTON REGULATIONS, TEST PITS AND PERCOLATION TESTS SHALL BE COMPLETED ON EACH LOT PRIOR TO THE APPLICATION OF A BUILDING/SEPTIC SYSTEM PERMIT.
 - HOME BUILDER/CONTRACTOR SHALL CONFIRM SINGLE-FAMILY RESIDENCE SPECIFICATIONS REGARDING NUMBER OF BEDROOMS. INSTALLATION OF A GARBAGE GRINDER/WHIRLPOOL SPA TO CONFIRM WASTEWATER DISPOSAL SYSTEM SIZING IS ACCURATELY PROVIDED FOR EACH RESIDENCE.
 - INVERT ELEVATIONS OF DRIVEWAY CULVERT CROSSING SHALL BE VERIFIED AT TIME OF EACH INDIVIDUAL PROPERTY SURVEY OF THE GROUND WATER ELEVATION. DITCH LINE ELEVATION SHALL BE MAINTAINED DURING CONSTRUCTION.

Bullard Lane
(NOT MAINTAINED BY THE TOWN OF WILTON)

LAYOUT & MATERIALS PLAN (NORTH)



TOWN OF WILTON
WATER & SEWER AUTHORITY
PLEASE REFER TO FIRST SHEET FOR
APPROVAL DATE AND SIGNATURE

TOWN OF WILTON PLANNING BOARD
PLEASE REFER TO FIRST SHEET FOR
APPROVAL DATE AND
SIGNATURE

SARATOGA COUNTY DEPARTMENT OF HEALTH

LAYOUT,
MATERIALS &
GRADING PLAN
(NORTH)

PROJ. NO: 1061.01
SCALE: AS SHOWN
DATE: 2/03/2026
SHEET 5 OF 15

UNAUTHORIZED ADDITION TO THIS LOCATION OF THE BUSINESS ENGINEERING, P.C.

DATE: SEVEN (7) RECORDS/DESCRIPTION

PRELIMINARY / NOT FOR CONSTRUCTION

LANSING ENGINEERING
SARATOGA COUNTY, NEW YORK
REGISTERED PROFESSIONAL ENGINEER
NO. 1061.01


BULLARD LANE RESIDENTIAL SUBDIVISION
BULLARD LANE, TOWN OF WILTON, SARATOGA COUNTY, NEW YORK

CIVIL TRANSPORTATION/ENVIRONMENTAL LAND SURVEYING

LEGEND

EXISTING FEATURES	PROPOSED FEATURES

NOTE: PROPOSED 60' R.O.W. TO BE DEDICATED TO THE TOWN OF WILTON.




NOTE: APPROXIMATE LOCATION AND DIRECTION OF SIGN

TRAFFIC CONTROL DEVICE SCHEDULE


PLAN NO.	DESCRIPTION	QTY.
1	R1-1 "STOP" SIGN	2
2	ROAD I.D. SIGN "BULLARD LANE X ROAD A"	1
4	R2-1 "SPEED LIMIT 30 MPH" SIGN	3
5	STORM WATER WARNING SIGN	2
6	DEED RESTRICTED LANDS	18
7	W14-2 NO OUTLET SIGN	1

NOTE: 1. CONTACT HIGHWAY DEPARTMENT FOR SIGN TYPE & SIGN REQUIREMENTS.

- NOTES:
- ALL LOTS SHALL BE GRADED TO DIRECT SURFACE RUNOFF AWAY FROM THE BUILDINGS AND ALONG THE PROPERTY LINES TO MUNICIPALLY OWNED CONVEYANCE SYSTEMS UNLESS OTHERWISE INDICATED ON THE PLANS.
 - ALL LOTS SHALL DIRECT ROOF STORMWATER RUNOFF TOWARD THE TOWN ROAD AND THE STORMWATER CONVEYANCE SYSTEM. LOTS THAT CAN NOT PROVIDE POSITIVE DRAINAGE TO THE STREET SHALL HAVE GUTTERS INSTALLED TO CONVEY REAR DRAINING ROOF RUNOFF TOWARDS THE TOWN ROAD OR STORMWATER CONVEYANCE SYSTEM.
 - ROADWAY PAVING PERMITTED BETWEEN APRIL 1 AND NOVEMBER 1. REFER TO TOWN CODE SECTION 109-29 FOR ROAD CONSTRUCTION REQUIREMENTS. ANY STRUCTURES IN ROADWAY SHALL BE SET 1' BELOW BINDER AND A RISER RING INSTALLED FOR TOP COURSE PAVING.
 - WATERMAIN SHALL CONSIST OF 8" PVC C900 PIPE PER WILTON WATER & SEWER AUTHORITY SPECIFICATIONS. ALL PIPES TO BE INSTALLED PER AWWA C900 STANDARDS.
 - WATER SERVICES SHALL CONSIST OF 1" CTS HDPE, DR-9 WITH TRACER WIRE, H=15000 CORPORATION VALVE, H=15200 CURB VALVE & H=10314 VALVE BOX AND MATCHING SS STATIONARY ROD. CONTRACTOR SHALL COORDINATE WITH WILTON WATER & SEWER AUTHORITY PRIOR TO CONSTRUCTION AND ORDERING OF MATERIALS.
 - REFER TO DETAIL 7 AND TRAIL AMENITY NOTES ON SHEET DT-4 FOR SPECIFIC TRAIL AND AMENITY NOTES & DETAILS.
 - TEST PITS COMPLETED ON 12/23/2025 AND WITNESSED BY SCOH CONFIRM ADEQUATE SOIL PROFILES AND PERCOLATION RESULTS TO SUPPORT INDIVIDUAL WASTEWATER DISPOSAL SYSTEMS.
 - PER TOWN OF WILTON REGULATIONS, TEST PITS AND PERCOLATION TESTS SHALL BE COMPLETED ON EACH LOT PRIOR TO THE APPLICATION OF A BUILDING/SEPTIC SYSTEM PERMIT.
 - HOME BUILDER/CONTRACTOR SHALL CONFIRM SINGLE-FAMILY RESIDENCE SPECIFICATIONS REGARDING NUMBER OF BEDROOMS. INSTALLATION OF A GARAGE GRINDER/WHR/POOL SPA TO CONFIRM WASTEWATER DISPOSAL SYSTEM SIZING IS ACCURATELY PROVIDED FOR EACH RESIDENCE.
 - INVERT ELEVATIONS OF DRIVEWAY CULVERT CROSSING SHALL BE VERIFIED AT TIME OF EACH INDIVIDUAL PROPERTY SURVEY OF THE GROUND WATER ELEVATION. DITCH LINE ELEVATION SHALL BE MAINTAINED DURING CONSTRUCTION.

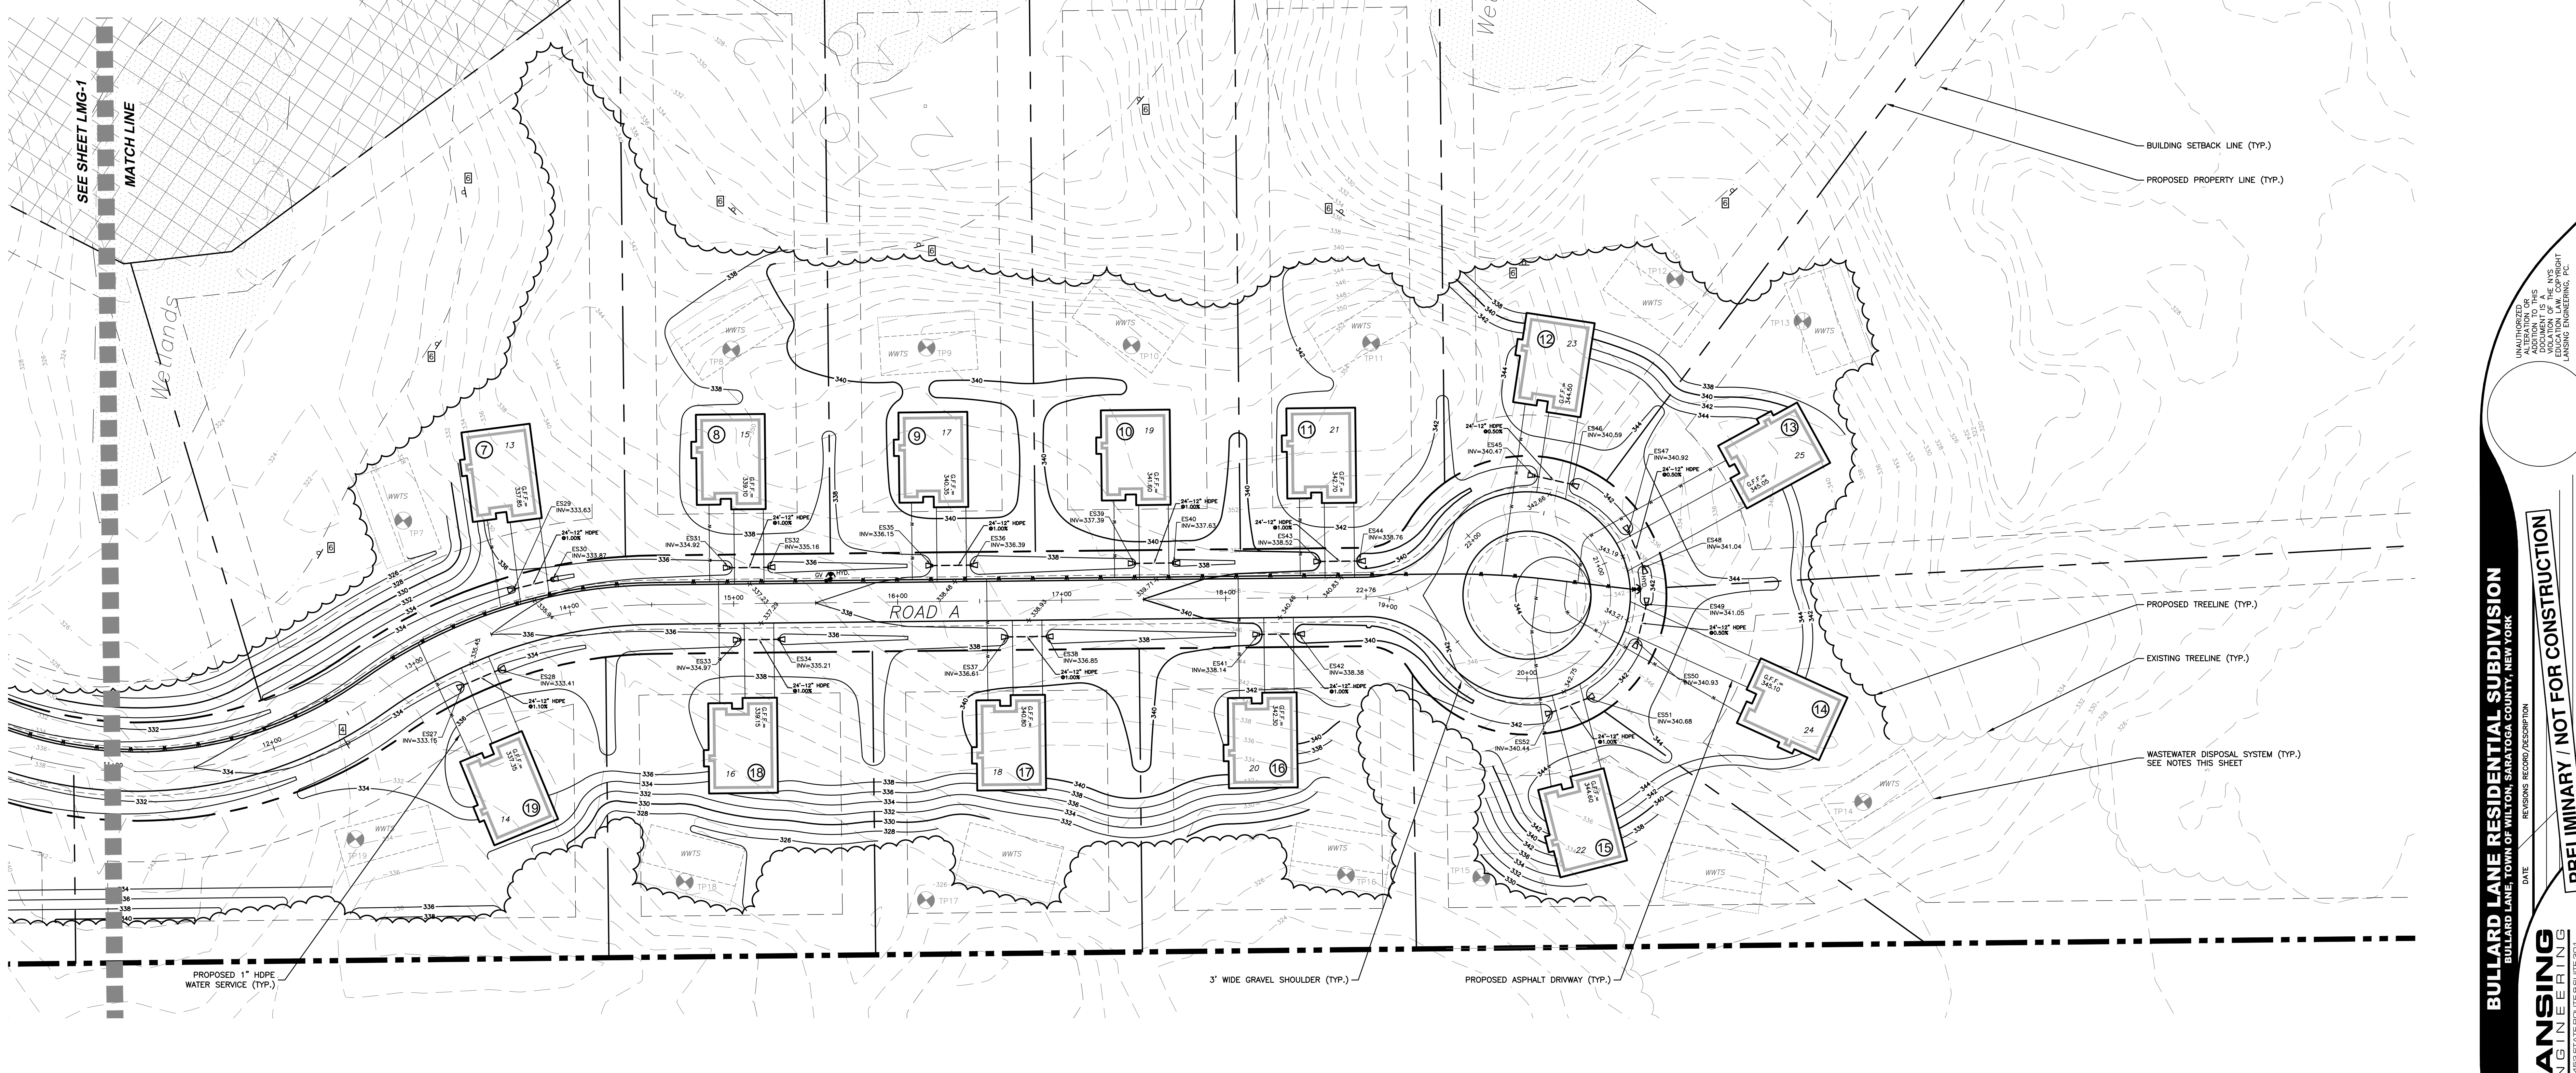

LAYOUT & MATERIALS PLAN (SOUTH)



TOWN OF WILTON
WATER & SEWER AUTHORITY
PLEASE REFER TO FIRST SHEET FOR
APPROVAL DATE AND SIGNATURE

TOWN OF WILTON PLANNING BOARD
PLEASE REFER TO FIRST SHEET FOR
APPROVAL DATE AND
SIGNATURE

SARATOGA COUNTY DEPARTMENT OF HEALTH

LAYOUT,
MATERIALS &
GRADING PLAN
(SOUTH)


PROJ. NO: 1061.01
SCALE: AS SHOWN
DATE: 2/03/2026
SHEET 6 OF 15

UNAUTHORIZED ADDITION TO THIS PLAN IS PROHIBITED. LOCATION OF THIS PLAN IS SUBJECT TO THE LANSING ENGINEERING, P.C. RECORDS. REVISED RECORD/DESCRIPTION. DATE: _____ CIVIL TRANSPORTATION/ENVIRONMENTAL/LAND DEVELOPMENT


BULLARD LANE RESIDENTIAL SUBDIVISION
 BULLARD LANE, TOWN OF WILTON, SARATOGA COUNTY, NEW YORK

PRELIMINARY / NOT FOR CONSTRUCTION

LANSING ENGINEERING
 800 WEST 10TH STREET
 SUITE 100
 WILTON, NY 12145
 (518) 838-8888

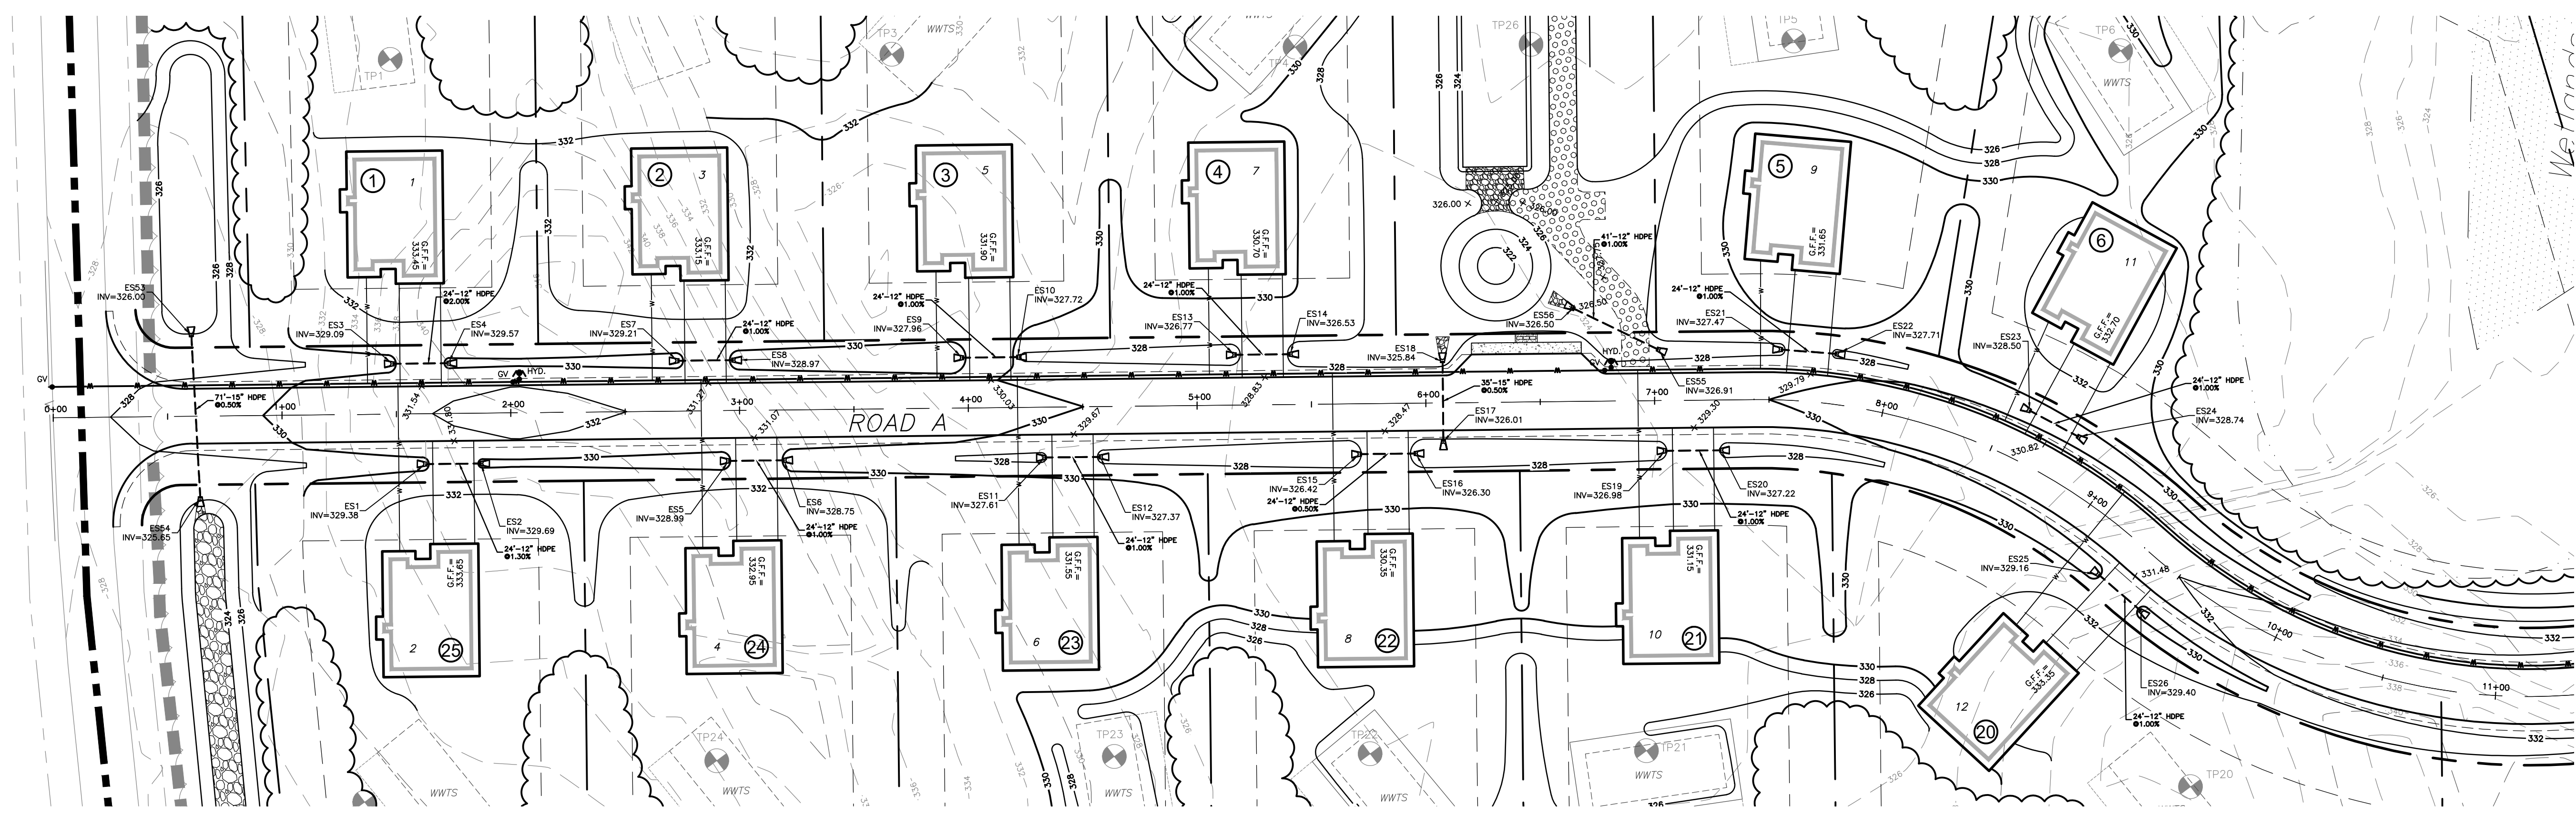


PLAN - ROAD A STA 0+00 TO 11+00




- NOTES:
- 1) FILLS GREATER THAN 5" PLACED WITHIN R.O.W. SHALL BE SELECT FILL: SAND, GRAVEL, STONE OR BLENDS OF THESE MATERIALS FREE FROM ORGANIC, FROZEN OR OTHER DELETERIOUS MATERIALS.
 - 2) ALL FILL SHALL BE COMPACTED TO 95 PERCENT OF THE MAXIMUM DENSITY OF THE MATERIAL USED.
 - 3) PLACE FILL MATERIALS IN LAYERS NOT MORE THAN 12" LOOSE DEPTH. LIFT HEIGHT SHALL BE GOVERNED BY THE ABILITY OF THE COMPACTION EQUIPMENT TO OBTAIN THE REQUIRED COMPACTION WITH 12" AS A MAXIMUM LIFT HEIGHT. BEFORE COMPACTION, MOISTEN OR AERATE EACH LAYER AS NECESSARY TO FACILITATE COMPACTION TO THE REQUIRE DENSITY.
 - 4) COMPACTION TESTING SHALL BE PERFORMED AT THE DISCRETION OF THE INSPECTING ENGINEER IN ACCORDANCE WITH AASHTO T238, NUCLEAR METHOD.
 - 5) DO NOT PLACE BACKFILL ON SURFACES THAT ARE MUDDY, FROZEN, OR CONTAIN FROST, ICE, PONDED WATER OR EXTRANEOUS DEBRIS.
 - 6) A MINIMUM OF 18" VERTICAL AND 10' HORIZONTAL SEPARATION IS REQUIRED BETWEEN SEWER (BOTH SANITARY AND STORM) AND WATER LINES.
 - 7) TYP. HYD. ASSEMBLY COMPRISED OF 8"x8"x6" TEE, 6" GATE VALVE AND HYDRANT ASSEMBLY.
 - 8) MINIMUM OF 5' OF COVER IS REQUIRED OVER WATERLINE.
 - 9) WATERMAIN SHALL CONSIST OF 8" PE4710 DR-11 "BLUESTRIPE" FOR DIRECTIONAL DRILLING PER WWSA SPECIFICATIONS. ALL PIPES TO BE INSTALLED PER AWWA C300 STANDARDS.

1

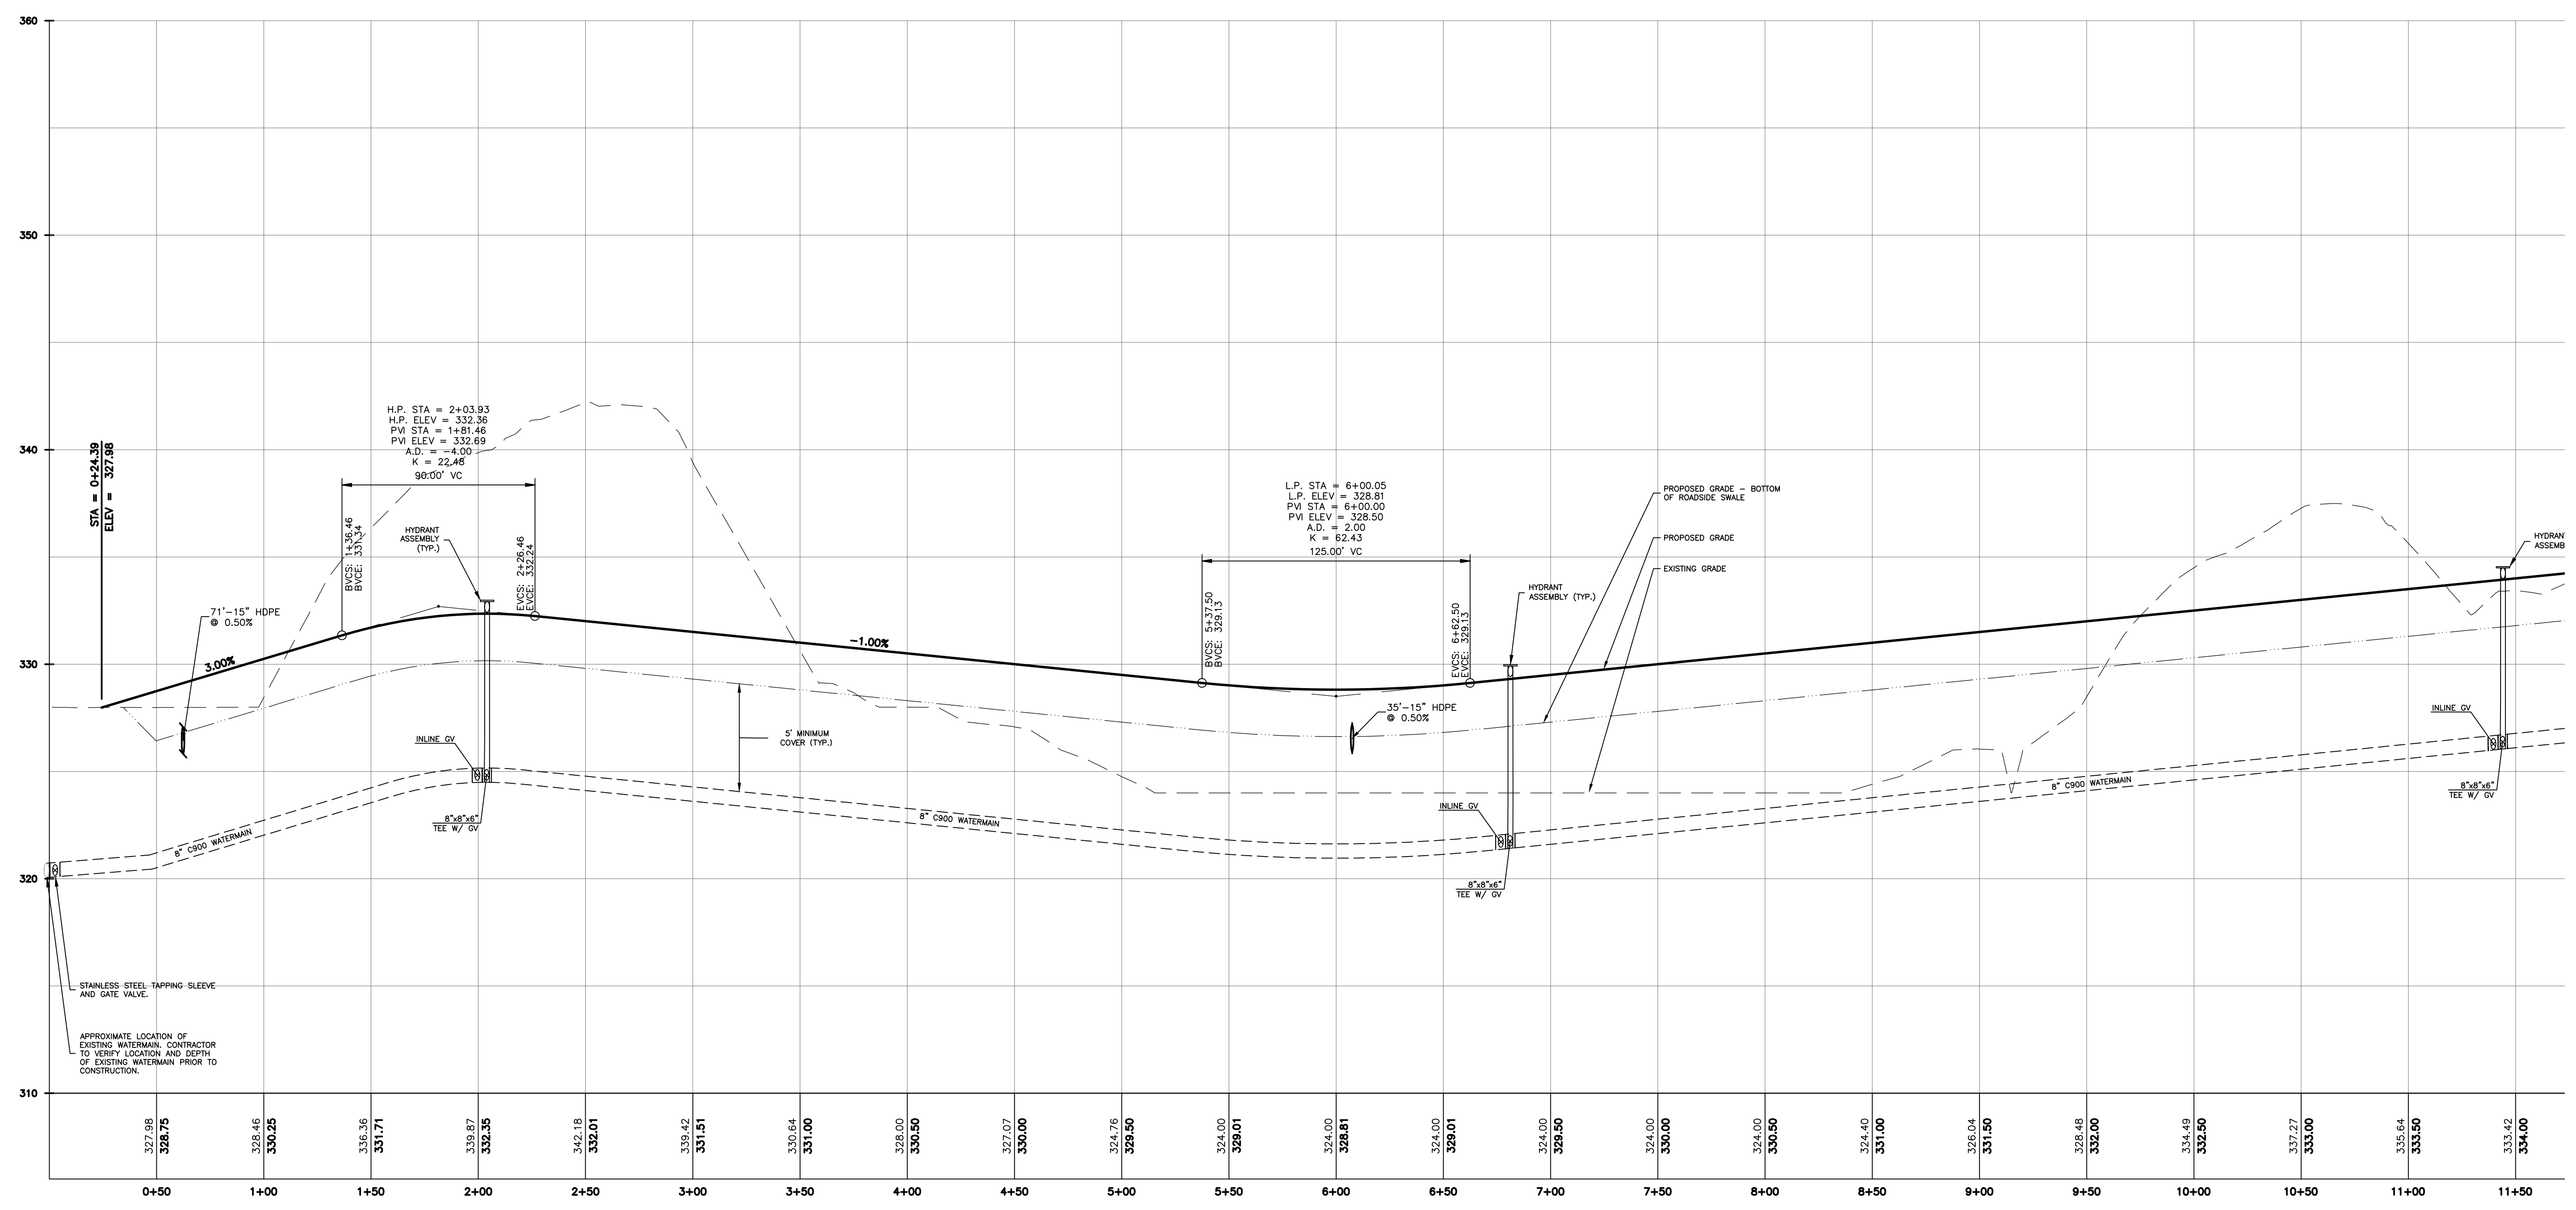

PROFILE - ROAD A STA 0+00 TO 11+00

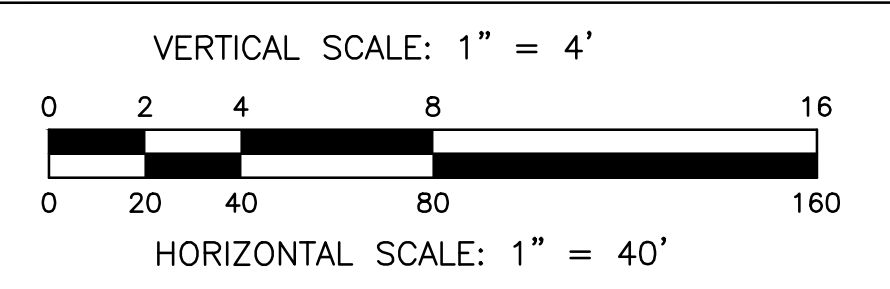

TOWN OF WILTON
WATER & SEWER AUTHORITY
PLEASE REFER TO FIRST SHEET FOR
APPROVAL DATE AND SIGNATURE

TOWN OF WILTON PLANNING BOARD
PLEASE REFER TO FIRST SHEET FOR
APPROVAL DATE AND
SIGNATURE

SARATOGA COUNTY DEPARTMENT OF HEALTH

2

UNAUTHORIZED OR
ADDITION TO THIS
DRAWING IS VOID
LOCATION OF THE INSIGHT
LANSING ENGINEERING, P.C.

REVISIONS RECORD/DESCRIPTION
DATE

PRELIMINARY / NOT FOR CONSTRUCTION

CIVIL TRANSPORTATION/ENVIRONMENTAL/LAND SURVEYING


LANSING ENGINEERING
SARATOGA COUNTY, NEW YORK
1000 W. STATE ST. SUITE 201
ALBANY, NY 12203
(518) 888-8888

BULLARD LANE RESIDENTIAL SUBDIVISION
BULLARD LANE, TOWN OF WILTON, SARATOGA COUNTY, NEW YORK

PLAN & PROFILE ROAD A (1 OF 2)



PROJ. NO: 1061.01
SCALE: AS SHOWN
DATE: 2/03/2026

PP-1
SHEET 7 OF 15

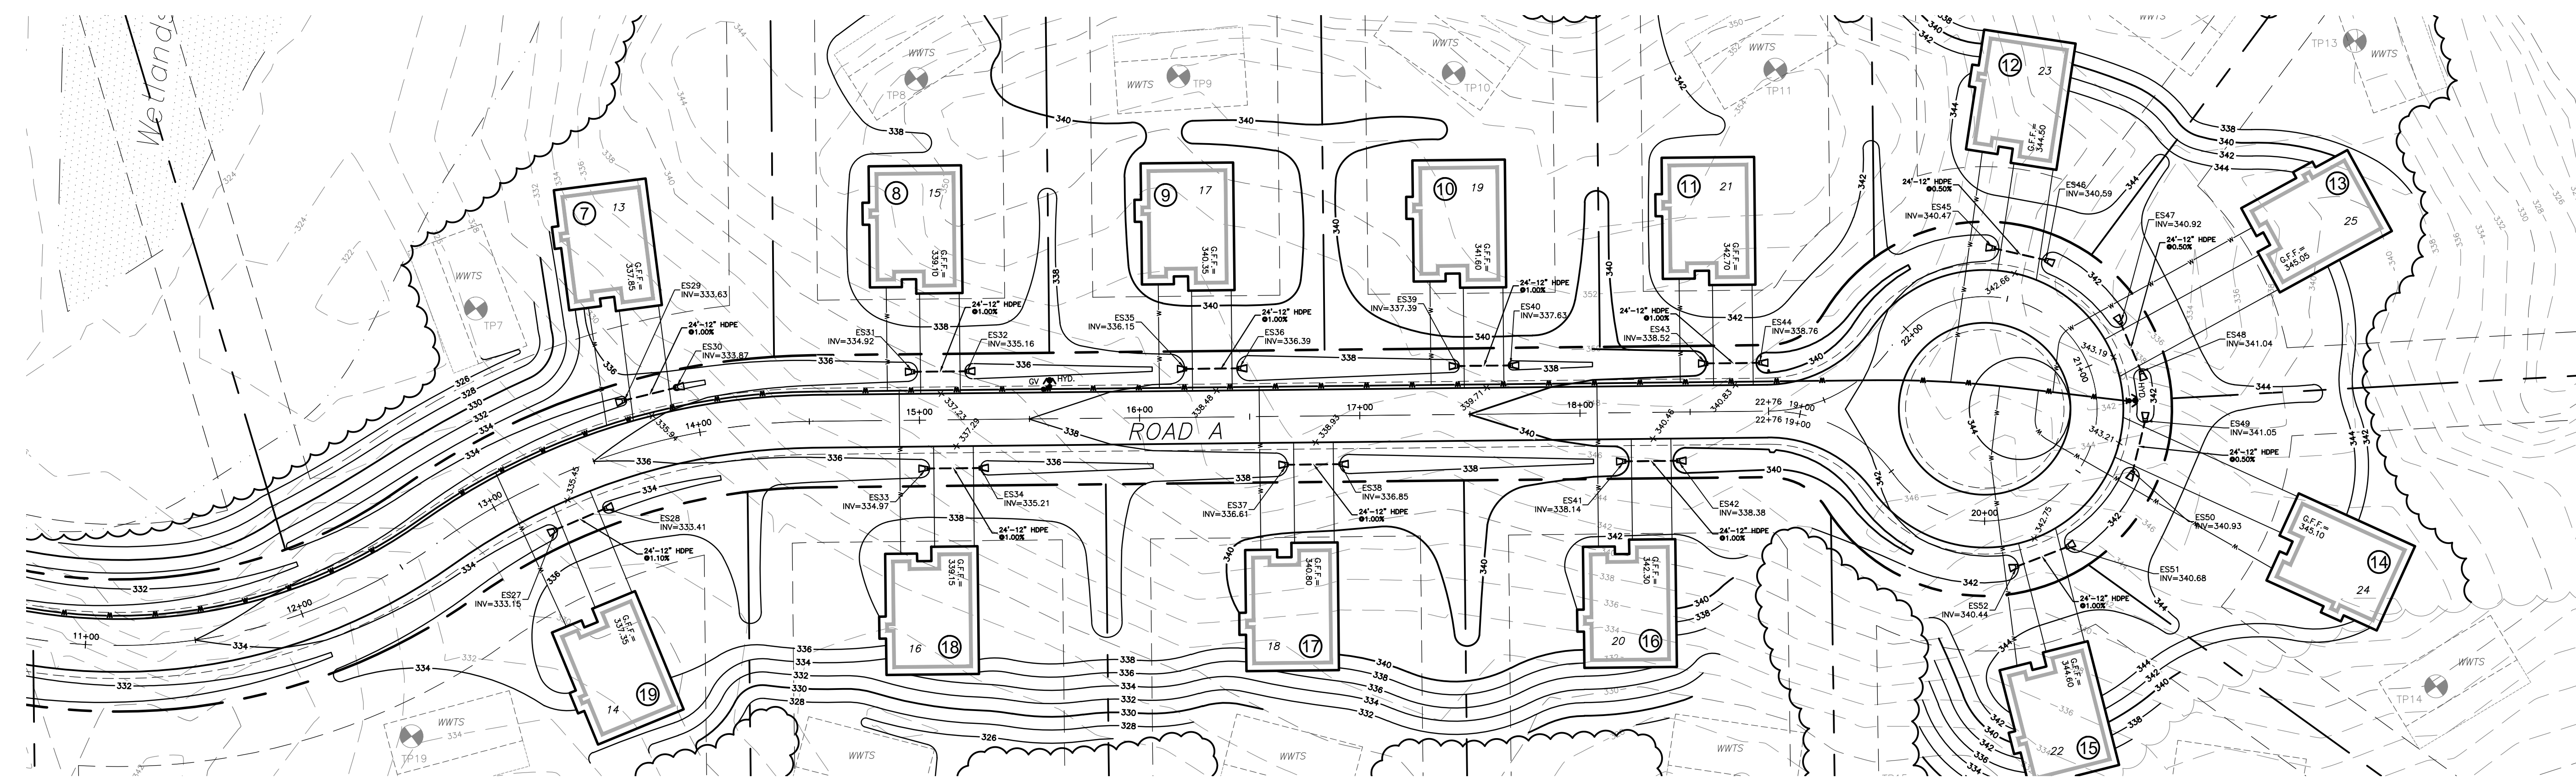


- NOTES:
- 1) FILLS GREATER THAN 6" PLACED WITHIN R.O.W. SHALL BE SELECT FILL: SAND, DURABLE, SAND, GRAVEL, STONE, OR BLENDS OF THESE MATERIALS FREE FROM ORGANIC, FROZEN OR OTHER DELETERIOUS MATERIALS.
 - 2) ALL FILL SHALL BE COMPACTED TO 95 PERCENT OF THE MAXIMUM DENSITY OF THE MATERIAL USED.
 - 3) PLACE FILL MATERIALS IN LAYERS NOT MORE THAN 12" LOOSE DEPTH. LIFT HEIGHT SHALL BE GOVERNED BY THE ABILITY OF THE COMPACTOR EQUIPMENT TO OBTAIN THE REQUIRED COMPACTION WITH 12" AS A MAXIMUM LIFT HEIGHT. BEFORE COMPACTION, MOISTEN OR AERATE EACH LAYER AS NECESSARY TO FACILITATE COMPACTION TO THE REQUIRED DENSITY.
 - 4) COMPACTION TESTING SHALL BE PERFORMED AT THE DISCRETION OF THE INSPECTING ENGINEER IN ACCORDANCE WITH AASHTO T238, NUCLEAR METHOD.
 - 5) DO NOT PLACE BACKFILL ON SURFACES THAT ARE MUDDY, FROZEN, OR CONTAIN FROST, ICE, PONDED WATER OR EXTRANEIOUS DEBRIS.
 - 6) A MINIMUM OF 18" VERTICAL AND 10' HORIZONTAL SEPARATION IS REQUIRED BETWEEN SINKER (BOTH SANITARY AND STORM) AND WATER LINES.
 - 7) TYP. HYD. ASSEMBLY COMPRISED OF 8"x6"x6" TEE, 6" GATE VALVE AND HYDRANT ASSEMBLY.
 - 8) MINIMUM OF 5' OF COVER IS REQUIRED OVER WATERLINE.
 - 9) WATERMAIN SHALL CONSIST OF 8" PE4710 OR-11 "BLUESTRIPE" FOR DIRECTIONAL DRILLING PER WWSA SPECIFICATIONS. ALL PIPES TO BE INSTALLED PER AWWA C900 STANDARDS.
- | SIETE | PERCENT PASSING |
|---------|-----------------|
| NO. 40 | 100 |
| NO. 60 | 97-70 |
| NO. 200 | 0-10 |

1 PLAN - ROAD A STA 11+00 TO 23+00

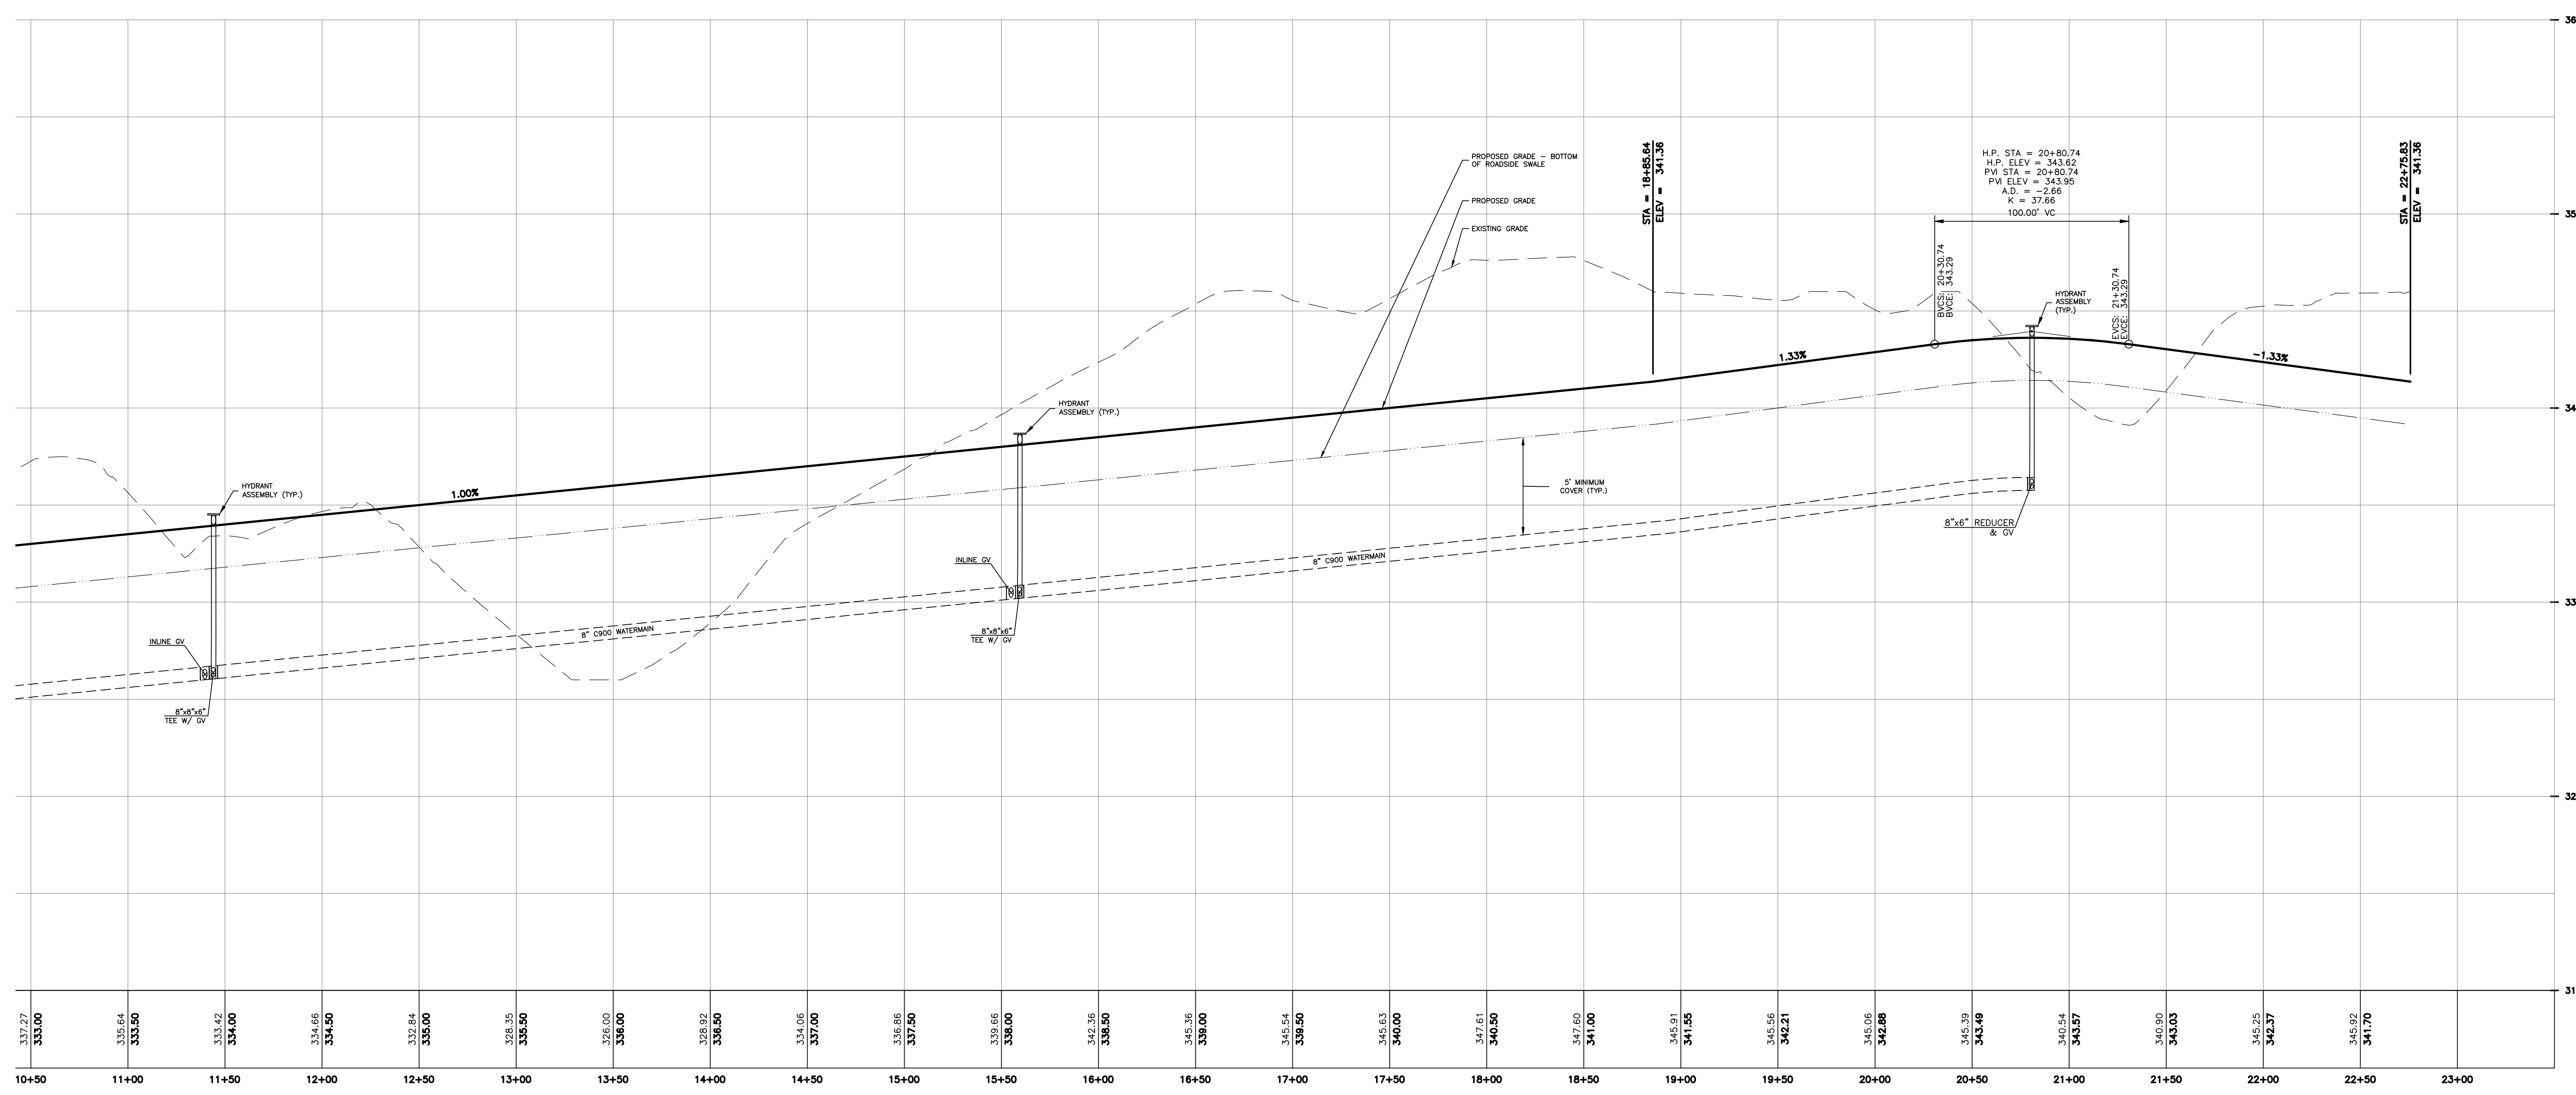

2 PROFILE - ROAD A STA 11+00 TO 23+00

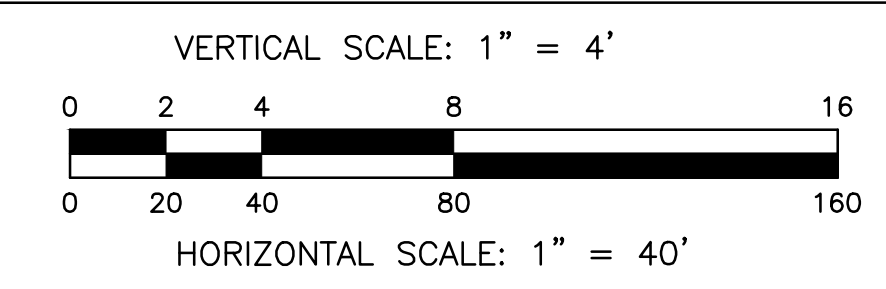

TOWN OF WILTON
WATER & SEWER AUTHORITY
PLEASE REFER TO FIRST SHEET FOR
APPROVAL DATE AND SIGNATURE

TOWN OF WILTON PLANNING BOARD
PLEASE REFER TO FIRST SHEET FOR
APPROVAL DATE AND
SIGNATURE

SARATOGA COUNTY DEPARTMENT OF HEALTH

UNAUTHORIZED
REPRODUCTION
OR ADDITION TO THIS
DRAWING WITHOUT THE
WRITTEN CONSENT OF
LANSING ENGINEERING, P.C.





REVISION RECORD/DESCRIPTION
PRELIMINARY / NOT FOR CONSTRUCTION
DATE





LANSING
ENGINEERING
P.C.
SARATOGA COUNTY, NEW YORK
12030 WILSON AVENUE
SARATOGA, NY 12158
(518) 888-8848


PLAN &
PROFILE ROAD
A (2 OF 2)

PROJ. NO: 1061.01
SCALE: AS SHOWN
DATE: 2/03/2026
PP-2
SHEET 8 OF 15

LEGEND

-  SILT FENCE
-  INLET PROTECTION
-  CHECK DAM
-  TEMPORARY SWALE

-  PHASE 1 = 4.50 AC. DISTURBANCE
-  PHASE 2 = 4.82 AC. DISTURBANCE
-  PHASE 3 = 4.51 AC. DISTURBANCE
-  PHASE 4 = 2.80 AC. DISTURBANCE

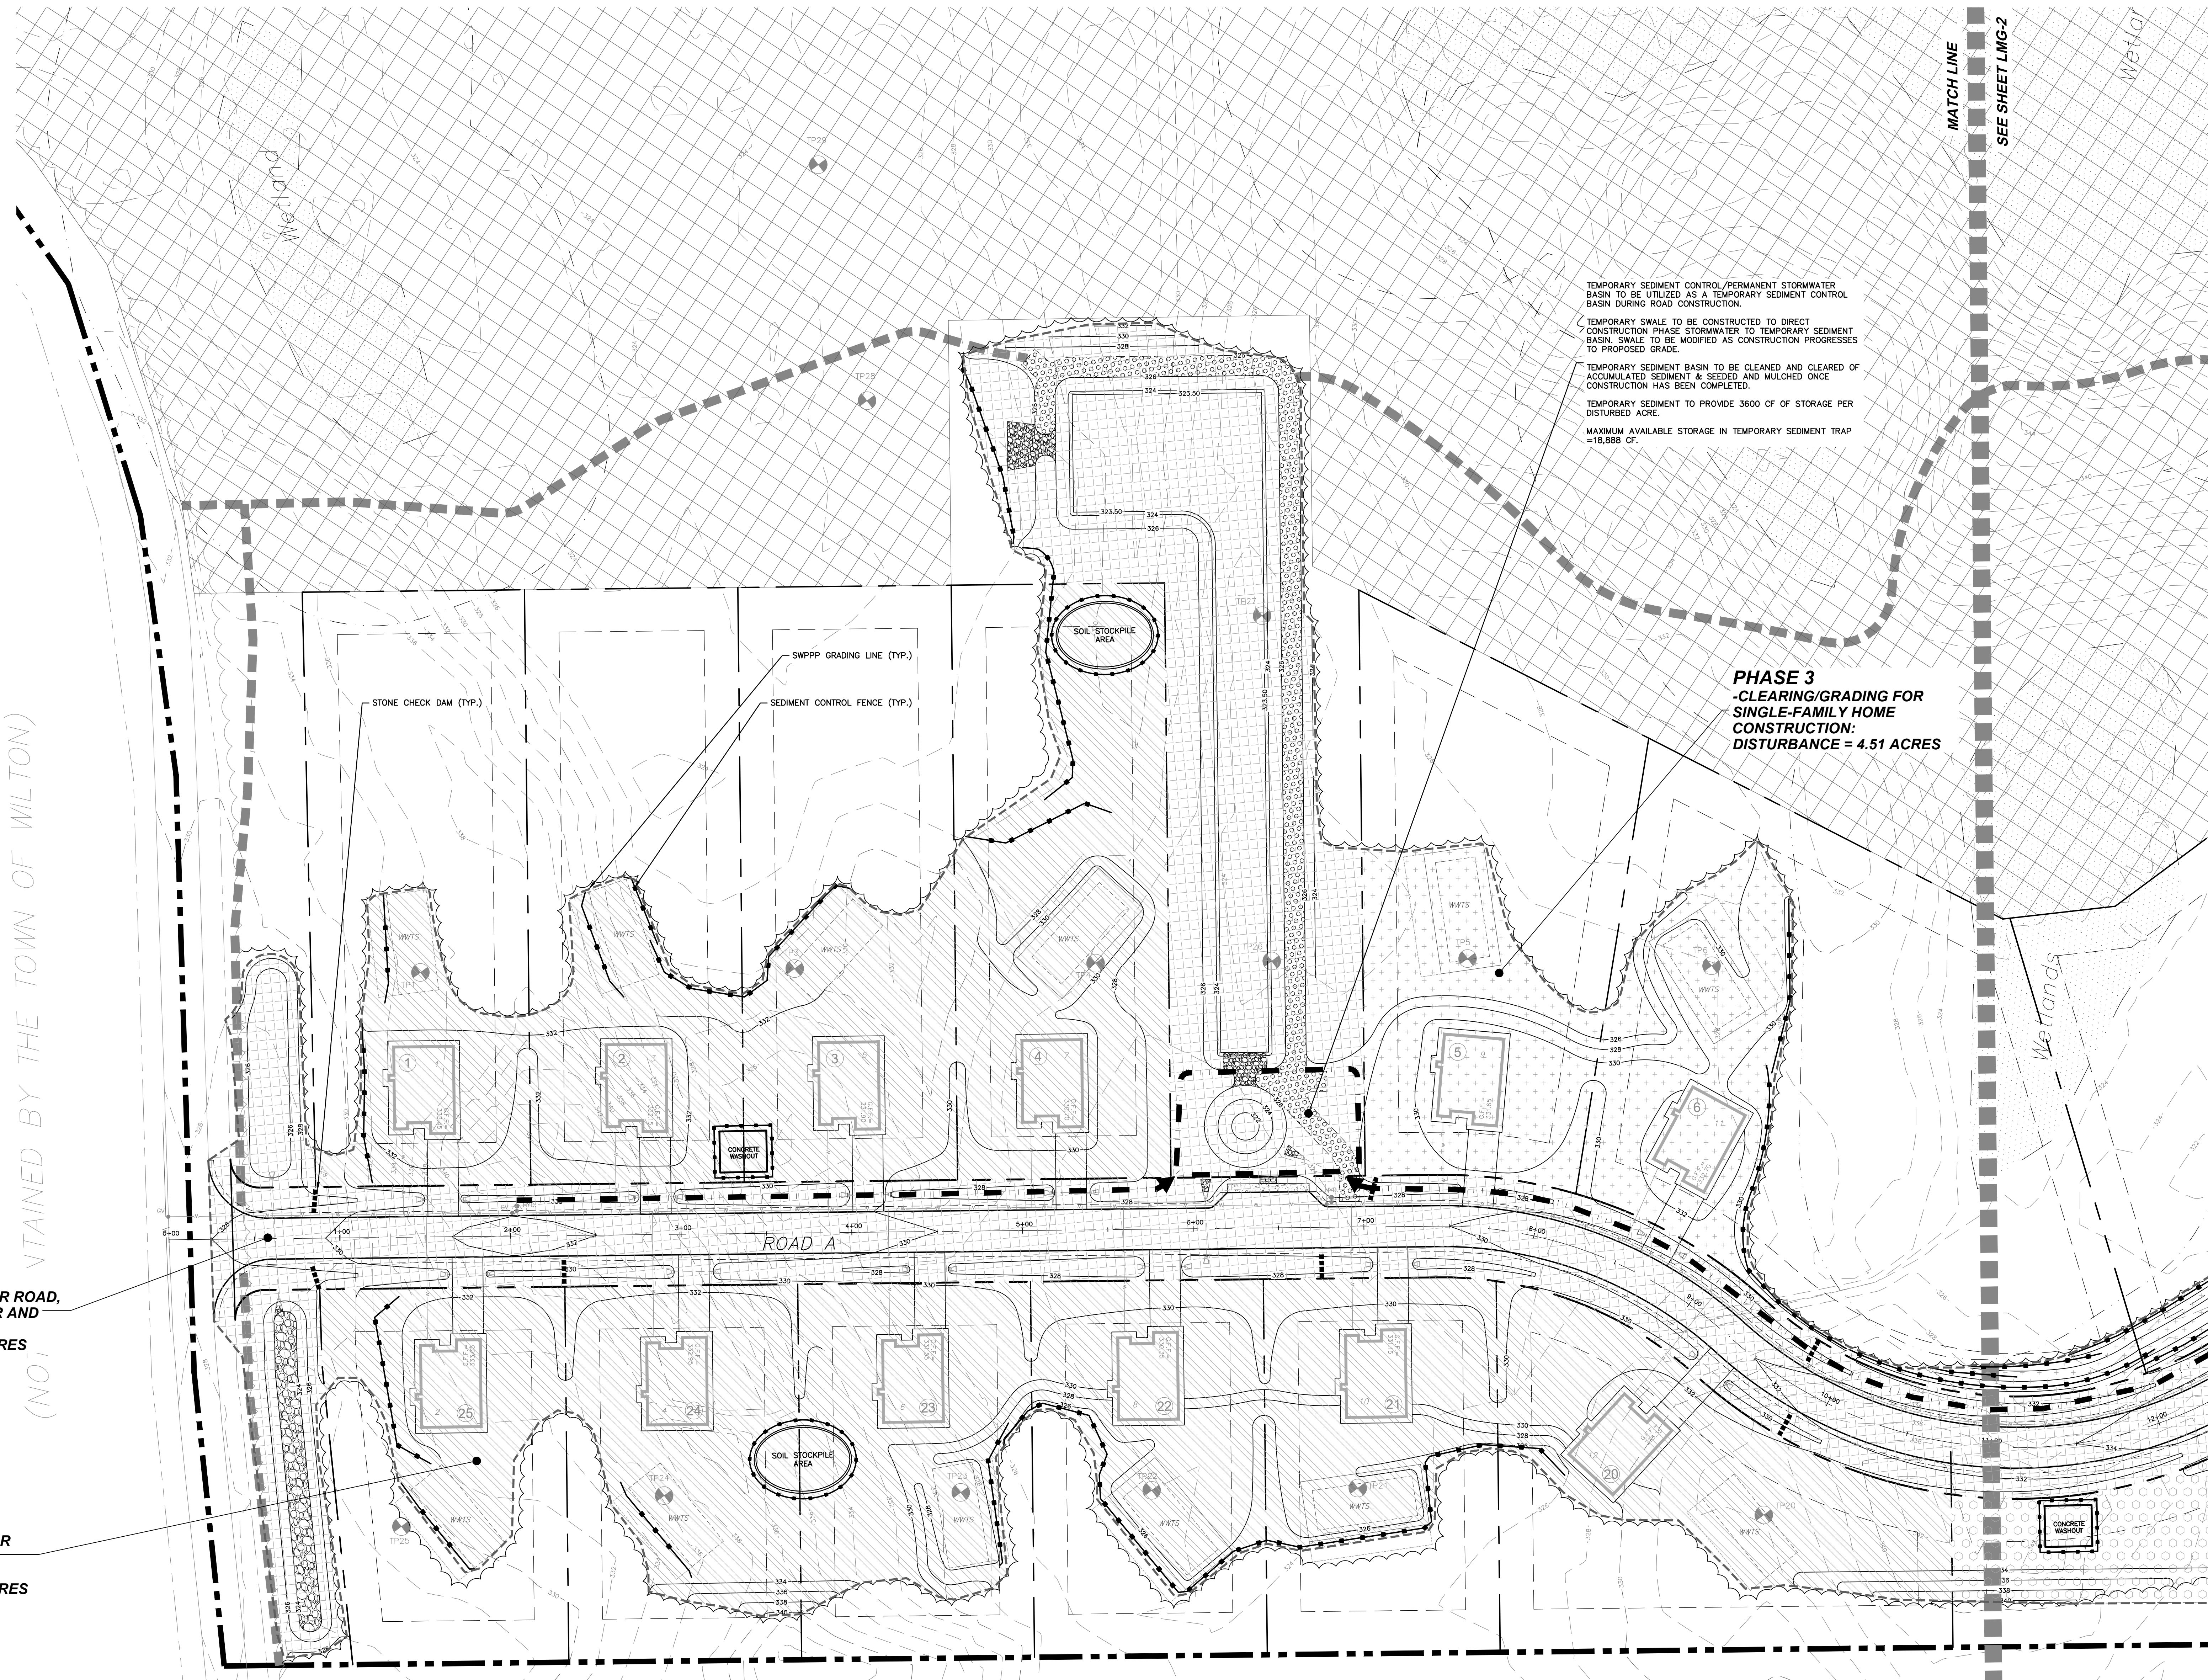

TEMPORARY SEDIMENT CONTROL/PERMANENT STORMWATER BASIN TO BE UTILIZED AS A TEMPORARY SEDIMENT CONTROL BASIN DURING ROAD CONSTRUCTION.

TEMPORARY SWALE TO BE CONSTRUCTED TO DIRECT CONSTRUCTION PHASE STORMWATER TO TEMPORARY SEDIMENT BASIN. SWALE TO BE MODIFIED AS CONSTRUCTION PROGRESSES TO PROPOSED GRADE.

TEMPORARY SEDIMENT BASIN TO BE CLEANED AND CLEARED OF ACCUMULATED SEDIMENT & SEEDED AND MULCHED ONCE CONSTRUCTION HAS BEEN COMPLETED.

TEMPORARY SEDIMENT TO PROVIDE 3600 CF OF STORAGE PER DISTURBED ACRE.

MAXIMUM AVAILABLE STORAGE IN TEMPORARY SEDIMENT TRAP = 18,888 CF.


PHASE 3
-CLEARING/GRADING FOR SINGLE-FAMILY HOME CONSTRUCTION:
DISTURBANCE = 4.51 ACRES

PHASE 1
-CLEARING/GRADING FOR ROAD, UTILITIES, STORMWATER AND MANAGEMENT AREA:
DISTURBANCE = 4.50 ACRES

PHASE 2
-CLEARING/GRADING FOR SINGLE-FAMILY HOME CONSTRUCTION:
DISTURBANCE = 4.82 ACRES

Bullard Lane
(NOT MAINTAINED BY THE TOWN OF WILTON)

EROSION & SEDIMENT CONTROL PLAN (NORTH)



TOWN OF WILTON
WATER & SEWER AUTHORITY
PLEASE REFER TO FIRST SHEET FOR APPROVAL DATE AND SIGNATURE

TOWN OF WILTON PLANNING BOARD
PLEASE REFER TO FIRST SHEET FOR APPROVAL DATE AND SIGNATURE

SARATOGA COUNTY DEPARTMENT OF HEALTH

EROSION & SEDIMENT CONTROL (NORTH)

PROJ. NO: 1061.01
SCALE: AS SHOWN
DATE: 2/03/2026

ESC-1
SHEET 9 OF 15

LANSING ENGINEERING
 585 WEST 10TH STREET
 MALDEN, NY 12548
 (518) 888-8848
 CIVIL, TRANSPORTATION, ENVIRONMENTAL, LAND DEVELOPMENT
 PRELIMINARY / NOT FOR CONSTRUCTION
 BULLARD LANE RESIDENTIAL SUBDIVISION
 BULLARD LANE, TOWN OF WILTON, SARATOGA COUNTY, NEW YORK
 REVISION RECORD/DESCRIPTION
 DATE
 UNAUTHORIZED ADDITION TO THIS DOCUMENT IS VOID. THE ASSOCIATION OF THE INSURANCE ENGINEERS, P.C.

LEGEND

- SILT FENCE
- INLET PROTECTION
- CHECK DAM
- TEMPORARY SWALE

- ▨ PHASE 1 = 4.50 AC. DISTURBANCE
- ▩ PHASE 2 = 4.82 AC. DISTURBANCE
- ▧ PHASE 3 = 4.51 AC. DISTURBANCE
- ▦ PHASE 4 = 2.80 AC. DISTURBANCE

TABLE 5.3 SOIL RESTORATION REQUIREMENTS*

TYPE OF SOIL DISTURBANCE	SOIL RESTORATION REQUIREMENT	COMMENTS/EXAMPLES
NO SOIL DISTURBANCE	RESTORATION NOT PERMITTED	PRESERVATION OF NATURAL FEATURES
MINIMAL SOIL DISTURBANCE	RESTORATION NOT PERMITTED	CLEARING AND GRUBBING
AREAS WHERE TOPSOIL IS STRIPPED ONLY - NO CHANGE IN GRADE	HSG A&B APPLY 6 INCHES OF TOPSOIL	PROTECT AREA FROM ANY ONGOING CONSTRUCTION ACTIVITIES
AREAS OF CUT OR FILL	HSG A&B AERATE AND APPLY 6 INCHES OF TOPSOIL	
HEAVY TRAFFIC AREAS ON SITE (ESPECIALLY IN A ZONE 5'-25' FEET AROUND BUILDINGS BUT NOT WITHIN A 5 FOOT PERIMETER AROUND FOUNDATION WALLS)	APPLY FULL SOIL RESTORATION (DE-COMPACT AND COMPOST ENHANCEMENT)	
AREAS WHERE RUNOFF REDUCTION AND/OR INFILTRATION PRACTICES ARE APPLIED	RESTORATION NOT REQUIRED, BUT MAY BE APPLIED TO ENHANCE THE REDUCTION SPECIFIED FOR APPROPRIATE PRACTICES	KEEP CONSTRUCTION EQUIPMENT FROM CROSSING THESE AREAS; TO PROTECT NEWLY INSTALLED PRACTICES FROM ANY ONGOING CONSTRUCTION ACTIVITIES, CONSTRUCT A SINGLE PHASE OPERATION FENCE AREA
REDEVELOPMENT PROJECTS	SOIL RESTORATION IS REQUIRED ON REDEVELOPMENT PROJECTS IN AREAS WHERE EXISTING IMPERVIOUS AREA WILL BE CONVERTED TO PERVIOUS AREA	


* TAKEN FROM PAGE 5-19 OF NEW YORK STATE STORMWATER DESIGN MANUAL (JANUARY, 2015)
 ** AERATION INCLUDES THE USE OF MACHINES SUCH AS TRACTOR-DRAWN IMPLEMENTS WITH COULTERS MAKING A NARROW SLIT IN THE SOIL, A ROLLER WITH MANY SPIKES MAKING INDENTATIONS IN THE SOIL, OR PRONGS WHICH FUNCTION LIKE A MINI-SUBSOILER.
 *** PER "DEEP RIPPING AND DE-COMPACTION, DEC 2008". A COPY IS INCLUDED WITHIN THE APPROVED SWPPP

RECOMMENDED SOIL EROSION AND SEDIMENT CONTROL MEASURES
 MEASURES SHOWN ARE TO DEFINE INTENT. ACTUAL MEASURES WILL BE IMPLEMENTED AS SITE CONDITIONS WARRANT BY THE CONTRACTOR. CONTRACTOR SHALL PROVIDE ALL NEEDED CONTROL MEASURES TO PREVENT SOIL EROSION.

- GENERAL MEASURES:**
- DAMAGE TO SURFACE WATERS RESULTING FROM EROSION AND SEDIMENTATION SHALL BE MINIMIZED BY STABILIZING DISTURBED AREAS AND BY REMOVING SEDIMENT FROM CONSTRUCTION SITE.
 - INsofar AS PRACTICABLE, EXISTING VEGETATION SHALL BE PRESERVED. FOLLOWING THE COMPLETION OF CONSTRUCTION ACTIVITIES IN ANY PORTION OF THE SITE, PERMANENT VEGETATION SHALL BE ESTABLISHED ON ALL EXPOSED SOILS.
 - SITE PREPARATION ACTIVITIES SHALL BE PLANNED TO MINIMIZE THE AREA AND DURATION OF SOIL DISRUPTION.
 - PERMANENT TRAFFIC CORRIDORS SHALL BE ESTABLISHED AND "ROUTES OF CONVENIENCE" SHALL BE AVOIDED.

- PARTICULAR MEASURES:**
- IMMEDIATELY FOLLOWING COMPLETION OF ANY AND ALL OF THE PROPOSED STORM DRAIN INLETS, STORM DRAIN INLET PROTECTION SHALL BE CONSTRUCTED.
 - DRAINAGE DITCH SEDIMENT FILTERS: UNTIL SUCH TIME AS FINAL SITE STABILIZATION IS COMPLETED, DITCHES SHALL RECEIVE TREATMENT WITH STONE CHECK DAMS SO AS TO EFFECTIVELY TRAP SEDIMENT AND MINIMIZE ITS RELEASE OFF-SITE. STONE CHECK DAMS SHALL BE CONSTRUCTED WITHIN EACH DITCH BEGINNING AT ITS DOWNSTREAM TERMINUS AND SHOULD NOT BE PLACED AT INTERVALS EXCEEDING 20 FEET.
 - TOPSOIL AND FILL THAT IS TO REMAIN STOCKPILED ON-SITE FOR PERIODS GREATER THAN 14-DAYS SHALL BE STABILIZED BY SEEDING AND MULCHING. PROVIDE SILT FENCE EROSION CONTROL DOWNGRADIENT OF SOIL STOCKPILE AREA.
 - IN NO CASE SHALL ERODIBLE MATERIALS BE STOCKPILED WITHIN 25 FEET OF ANY DITCH, STREAM, OR OTHER SURFACE WATER BODY.
 - PERMANENT VEGETATIVE COVER: IMMEDIATELY FOLLOWING THE COMPLETION OF CONSTRUCTION ACTIVITIES IN ANY PORTION OF THE SITE, PERMANENT VEGETATION SHALL BE ESTABLISHED ON ALL EXPOSED SOILS.
 - ALL HEALTHY TREES OF DESIRABLE SPECIES ARE TO BE PROTECTED FROM DAMAGE. ALL UNNECESSARY REMOVAL OF HEALTHY TREES SHALL BE AVOIDED.
 - THE CONTRACTOR IS TO ADHERE TO ALL REQUIREMENTS SET FORTH IN THE SWPPP.
 - WETLAND PROTECTION FENCE SHALL BE INSTALLED ALONG THE PERIMETER OF WETLANDS PRIOR TO THE START OF CONSTRUCTION.


MAINTENANCE OF EROSION CONTROL MEASURES
 THE DEVELOPER/CONTRACTOR OR THEIR BUILDER SHALL INSPECT AND MAINTAIN THE INTEGRITY AND FUNCTION OF ALL TEMPORARY EROSION CONTROL MEASURES THROUGHOUT THE DURATION OF THE DEVELOPMENT PROCESS. TO ASSURE PROPER FUNCTION, SILTATION BARRIERS SHALL BE MAINTAINED IN GOOD CONDITION AND REINFORCED, EXTENDED, REPAIRED OR REPLACED AS NECESSARY. WASHOUTS SHALL BE IMMEDIATELY REPAIRED, RE-SEEDED AND PROTECTED FROM FURTHER EROSION. ALL ACCUMULATED SEDIMENT SHALL BE REMOVED AND CONTAINED IN APPROPRIATE SPILL AREAS. WATER SHALL BE APPLIED TO NEWLY SEEDING AREAS AS NEEDED UNTIL GRASS COVER IS WELL ESTABLISHED. TO EFFECTIVELY CONTROL WIND EROSION, WATER SHALL BE APPLIED TO ALL EXPOSED SOILS AS NECESSARY UNTIL GROUND COVER IS PERMANENTLY ESTABLISHED.

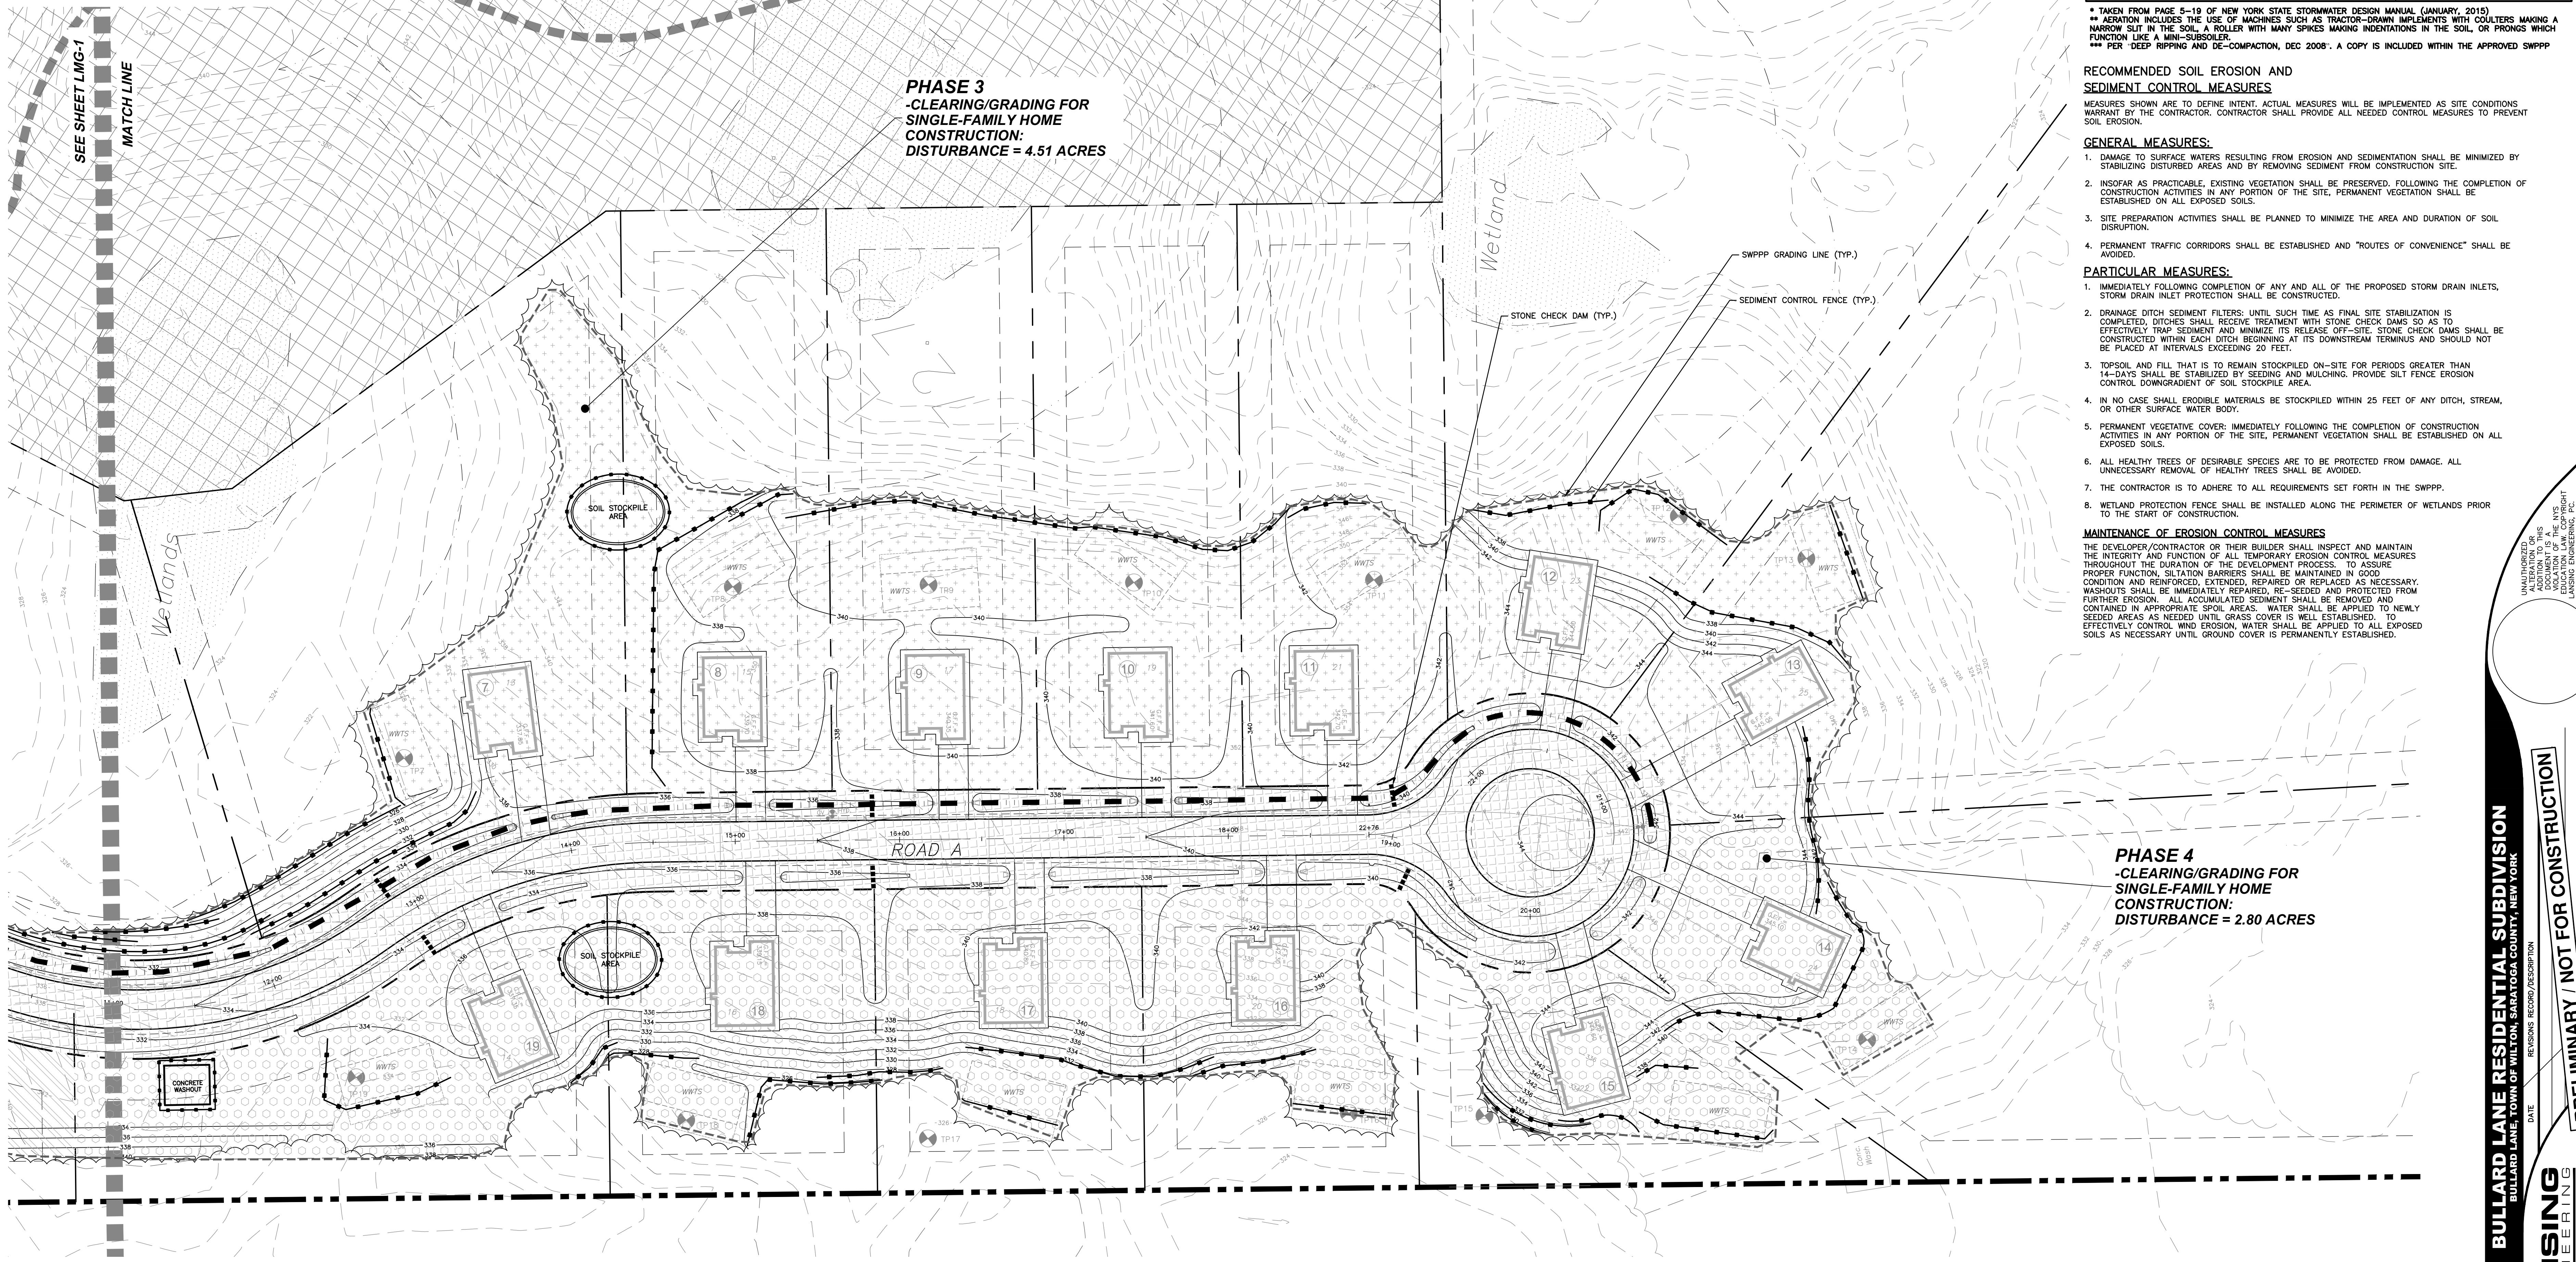

**PHASE 3
 -CLEARING/GRADING FOR
 SINGLE-FAMILY HOME
 CONSTRUCTION:
 DISTURBANCE = 4.51 ACRES**

**PHASE 4
 -CLEARING/GRADING FOR
 SINGLE-FAMILY HOME
 CONSTRUCTION:
 DISTURBANCE = 2.80 ACRES**

EROSION & SEDIMENT CONTROL PLAN (SOUTH)




TOWN OF WILTON
 WATER & SEWER AUTHORITY
 PLEASE REFER TO FIRST SHEET FOR
 APPROVAL DATE AND SIGNATURE

TOWN OF WILTON PLANNING BOARD
 PLEASE REFER TO FIRST SHEET FOR
 APPROVAL DATE AND
 SIGNATURE


SARATOGA COUNTY DEPARTMENT OF HEALTH

EROSION & SEDIMENT CONTROL (SOUTH)
 PROJ. NO: 1061.01
 SCALE: AS SHOWN
 DATE: 2/03/2026
ESC-2
 SHEET 10 OF 15

UNAUTHORIZED ADDITION TO THIS LOCATION OF THE INSIGHT LANSING ENGINEERING, P.C.
 BULLARD LANE RESIDENTIAL SUBDIVISION
 BULLARD LANE, TOWN OF WILTON, SARATOGA COUNTY, NEW YORK
 REVISION RECORD/DESCRIPTION
 DATE
 PRELIMINARY / NOT FOR CONSTRUCTION
 LANSING ENGINEERING
 SARATOGA COUNTY, NEW YORK
 (518) 888-8888

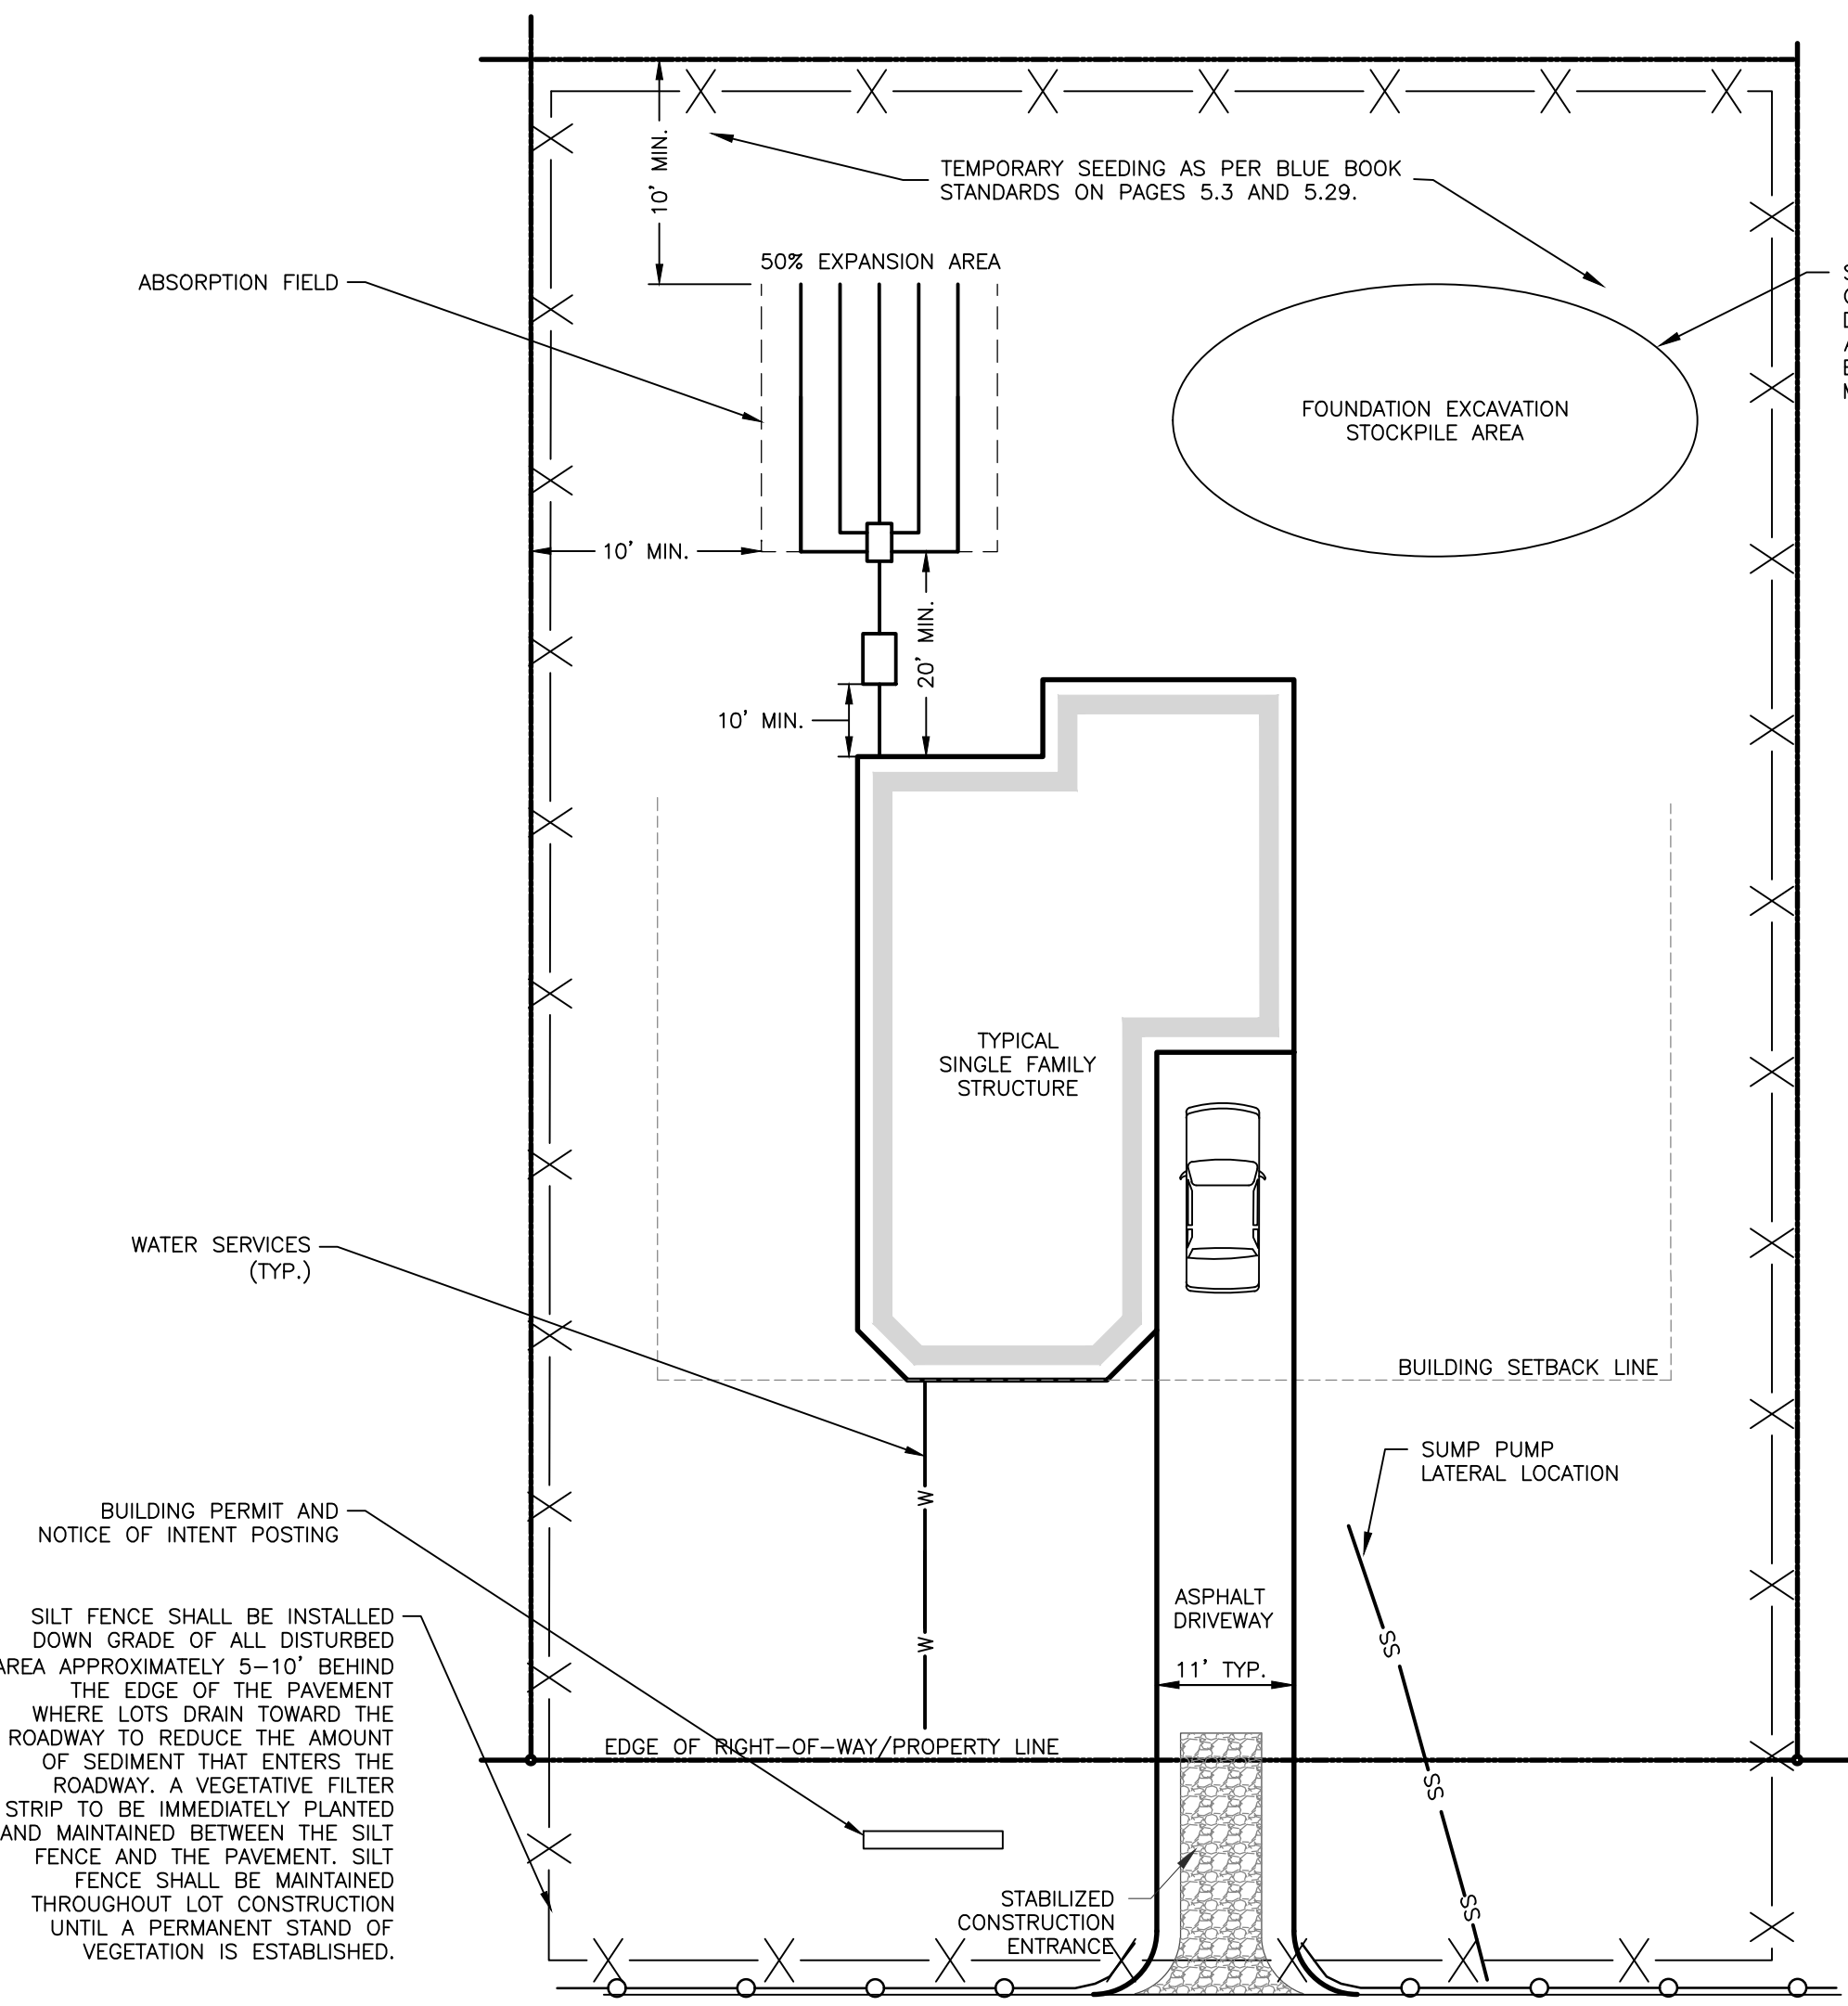


1 TYPICAL LOT LAYOUT & EROSION CONTROL
SCALE: NTS

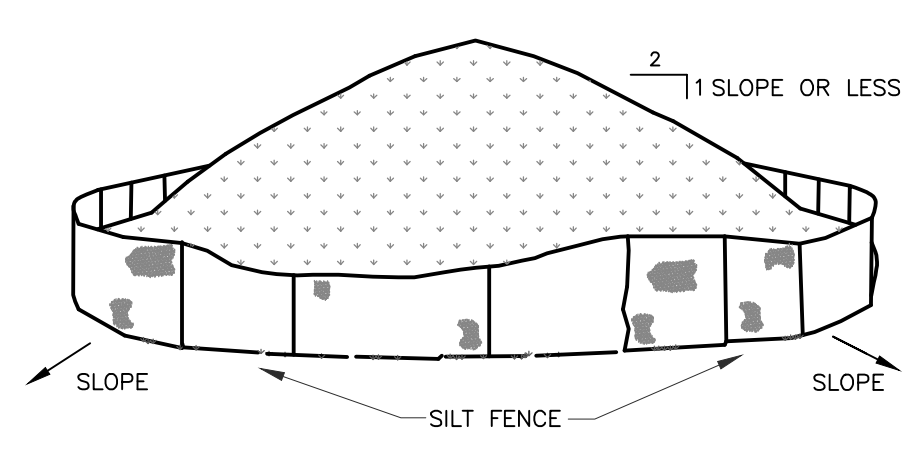


- AREA CHOSEN FOR STOCKPILING OPERATIONS SHALL BE DRY AND STABLE.
- MAXIMUM SLOPE OF STOCKPILE SHALL BE 1:2.
- SILT FENCING SHALL BE PLACED 5' DOWNSLOPE OF EACH PILE. UPON COMPLETION OF SOIL STOCKPILING, TOPSOIL SHALL BE STABILIZED WITH SEED AND MULCH IF NOT TO BE DISTURBED/UTILIZED WITHIN 14 DAYS.
- SEE ADDITIONAL DETAILS FOR INSTALLATION OF SILT FENCE.
- TEMPORARY PERIMETER DIKES MAY BE REQUIRED TO DIRECT CLEAN RUNOFF FROM STORAGE AREAS. REFER TO EROSION AND SEDIMENT CONTROL PLAN.

4 MATERIAL STORAGE & SOIL STOCKPILE STABILIZATION DETAIL
SCALE: NTS

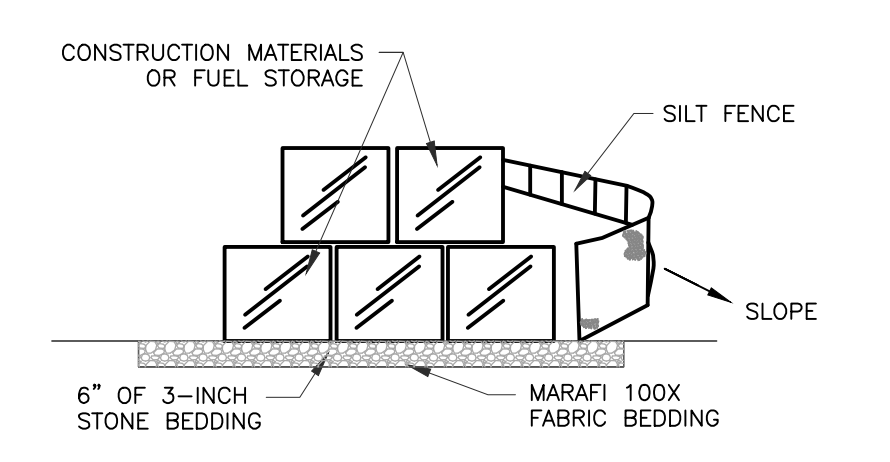


- AREA CHOSEN FOR STORAGE OPERATIONS SHALL BE DRY AND STABLE.
- MINIMUM DISTANCE TO A NATURAL WATER COURSE SHALL BE 50'.
- THE TOP SIX INCHES OF NATIVE MATERIAL SHALL BE REMOVED FROM MATERIAL/FUEL STORAGE AREA AND REPLACED WITH MARAFI 100X GEOTEXTILE FABRIC AND 6" INCHES OF CRUSHED STONE BEDDING. CRUSHED STONE SHALL MEET NYS DOT ITEM NO. 623.11 SPECIFICATIONS.
- SILT FENCING SHALL BE PLACED 5' DOWNSLOPE OF STORAGE AREA.
- TEMPORARY PERIMETER DIKES MAY BE REQUIRED TO DIRECT CLEAN RUNOFF FROM STORAGE AREAS. REFER TO EROSION AND SEDIMENT CONTROL PLAN.

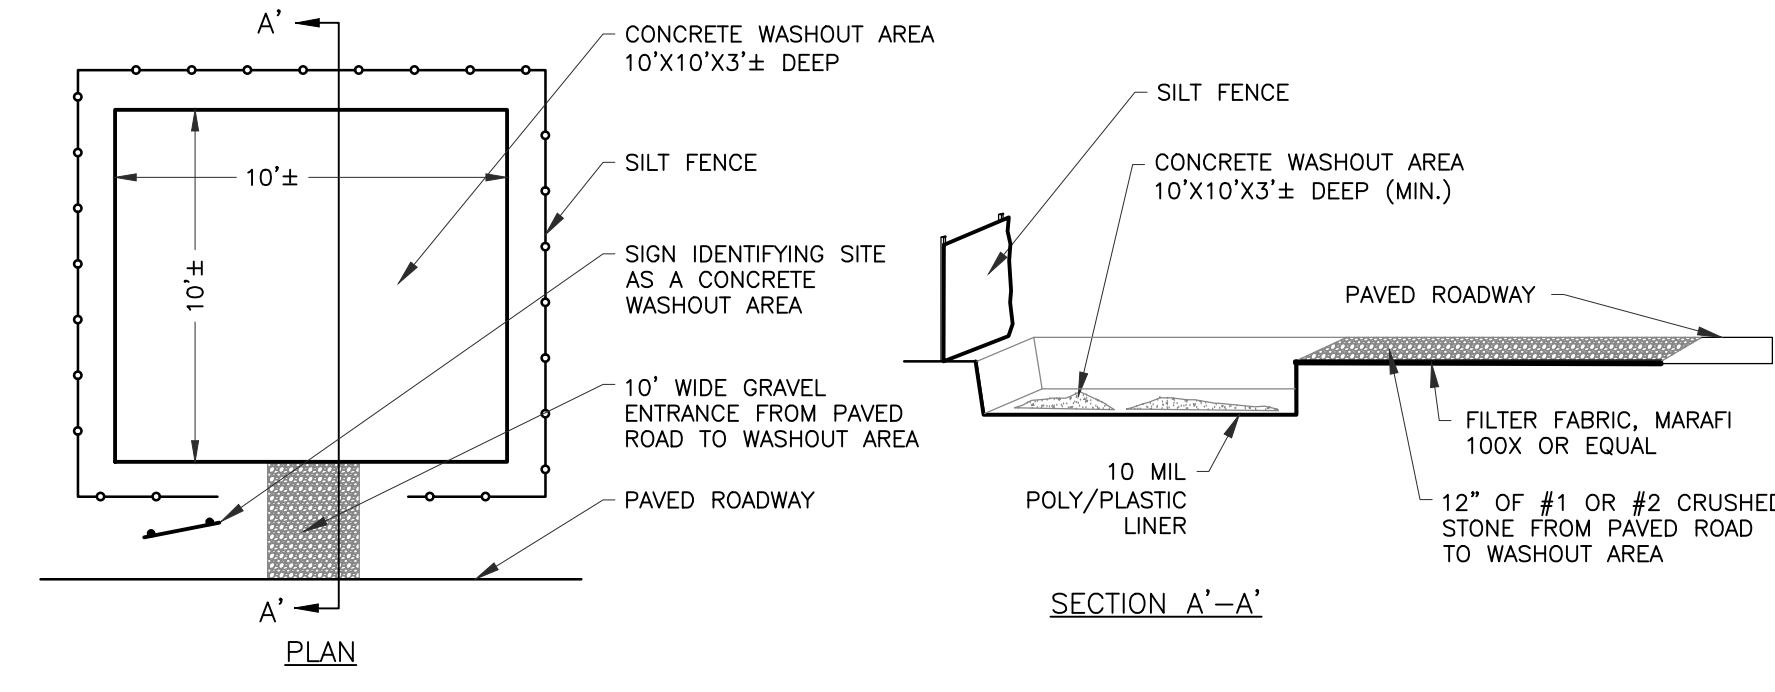


- CONSTRUCTION SPECIFICATIONS**
- CONCRETE WASHOUT LOCATION SHALL BE A MINIMUM OF 100' FROM SENSITIVE AREAS.
 - THE BASIN DIMENSIONS DEPICTED ABOVE ARE REQUIRED MINIMUMS. CONCRETE WASHOUT FACILITY SHALL BE CONSTRUCTED AND MAINTAINED IN SUFFICIENT QUANTITY AND SIZE TO CONTAIN ALL LIQUID AND CONCRETE WASTE GENERATED BY WASHOUT OPERATIONS. (APPROX. 60 GAL. OF WATER/WASTE PER TRUCK)
 - PLASTIC LINING MATERIAL SHALL BE 10 MIL(MINIMUM) POLY SHEETING AND BE FREE OF HOLES, TEARS, OR OTHER DEFECTS THAT COMPROMISE THE IMPERMEABILITY OF THE MATERIAL. LINER TO BE ANCHORED BEYOND THE TOP OF THE PIT WITH AN EARTHEN BERM, SAND BAGS, OR STONE.
 - WASHOUT FACILITY MUST BE CLEANED OR NEW FACILITIES MUST BE CONSTRUCTED AND READY FOR USE ONCE THE WASHOUT IS 75% FULL.
- MAINTENANCE AND CLEANING**
- DO NOT DISCHARGE LIQUID OR SLURRY TO WATERWAYS, STORM DRAINS OR DIRECTLY ONTO GROUND.
 - DO NOT USE SANITARY SEWER WITHOUT LOCAL APPROVAL.
 - PLACE A SECURE NON-COLLAPSING, NON-WATER COLLECTING COVER OVER THE FACILITY PRIOR TO PREDICTED WET WEATHER TO PREVENT ACCUMULATION AND OVERFLOW.
 - REMOVE AND DISPOSE OF HARDENED CONCRETE AND RETURN THE STRUCTURE TO A FUNCTIONAL STATE.
 - INSPECT THE WASHOUT FACILITY FOR SIGNS OF WEAKENING OR DAMAGE AND REPAIR AS NECESSARY (RE-LINE THE STRUCTURE WITH NEW POLY SHEETING AFTER EACH CLEANING).

5 CONCRETE WASHOUT AREA
SCALE: NTS

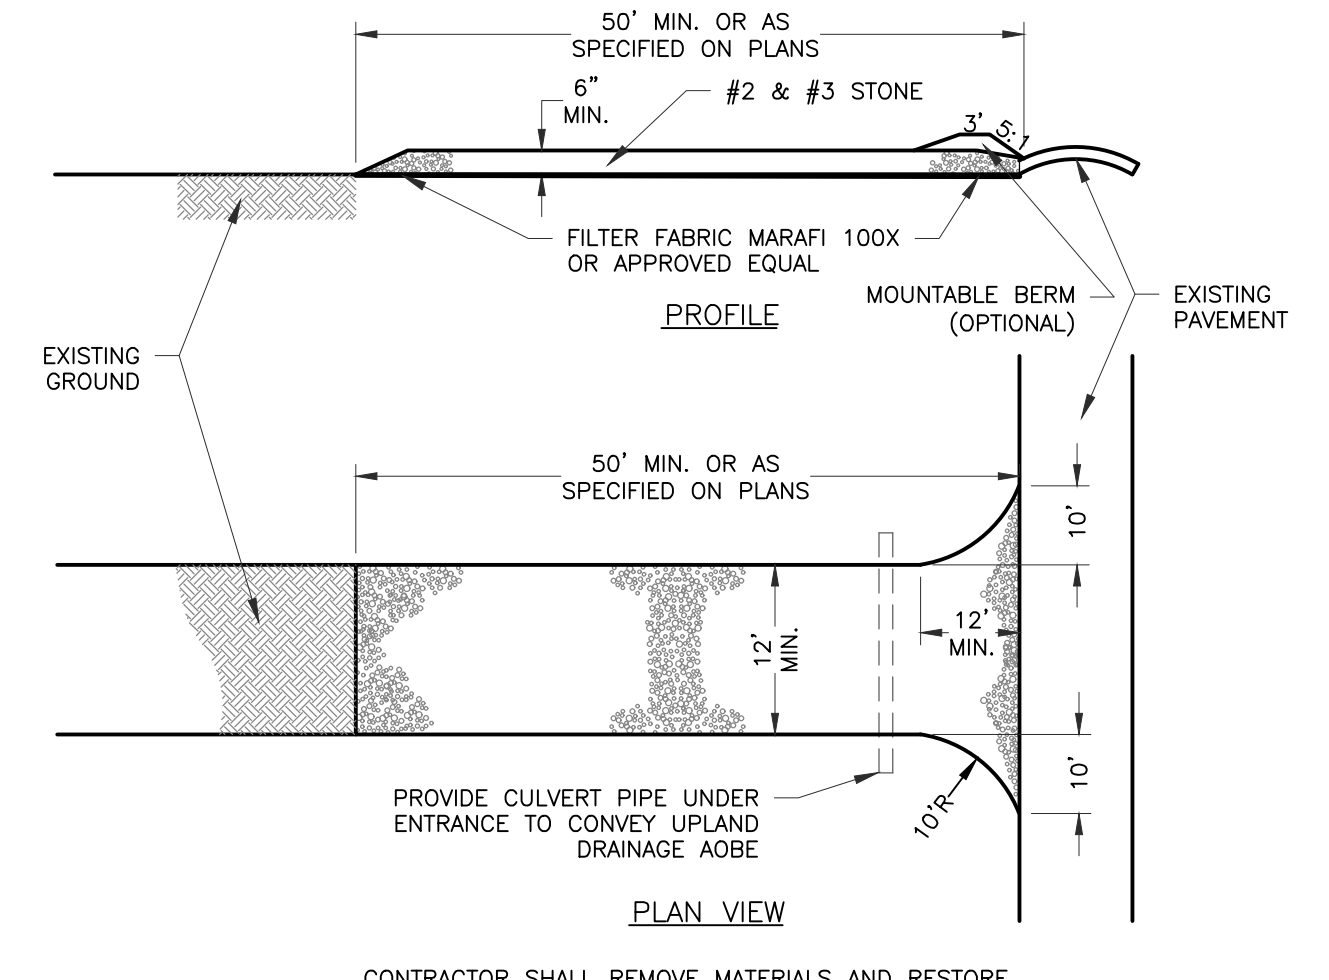

- CONTRACTOR SHALL REMOVE MATERIALS AND RESTORE ENTRANCE AREA, ESTABLISHING VEGETATIVE COVER.**
- NOTES:**
- STONE SIZE - USE MIXTURE OF #2 & #3 STONE (1-4 INCHES), OR RECLAIMED OR RECYCLED CONCRETE EQUIVALENT.
 - LENGTH - NOT LESS THAN FIFTY (50) FEET (EXCEPT ON A SINGLE RESIDENCE LOT WHERE A THIRTY (30) FOOT MINIMUM LENGTH WOULD APPLY).
 - THICKNESS - NOT LESS THAN SIX (6) INCHES.
 - WIDTH - TWELVE (12) FOOT MINIMUM, BUT NOT LESS THAN THE FULL WIDTH AT POINTS WHERE INGRESS OR EGRESS OCCURS. TWENTY-FOUR (24) FOOT IF SINGLE ENTRANCE TO SITE.
 - GEOTEXTILE - WILL BE PLACED OVER THE ENTIRE AREA PRIOR TO PLACING OF STONE.
 - SURFACE WATER - ALL SURFACE WATER FLOWING OR DIVERTED TOWARD CONSTRUCTION ENTRANCES SHALL BE PIPED ACROSS THE ENTRANCE. IF PIPING IS IMPRACTICAL, A MOUNTABLE BERM WITH 5:1 SLOPES WILL BE PERMITTED.
 - MAINTENANCE - THE ENTRANCE SHALL BE MAINTAINED IN A CONDITION WHICH WILL PREVENT TRACKING OR FLOWING OF SEDIMENT ONTO PUBLIC RIGHTS-OF-WAY. ALL SEDIMENT GRILLED, DROPPED, WASHED OR TRACKED ONTO PUBLIC RIGHTS-OF-WAY MUST BE REMOVED IMMEDIATELY.
 - WHEN WASHING IS REQUIRED, IT SHALL BE DONE ON A AREA STABILIZED WITH STONE AND WHICH DRAINS INTO AN APPROVED SEDIMENT TRAPPING DEVICE.
 - PERIODIC INSPECTION AND NEEDED MAINTENANCE SHALL BE PROVIDED AFTER EACH RAIN.

2 STABILIZED CONSTRUCTION ENTRANCE
SCALE: NTS

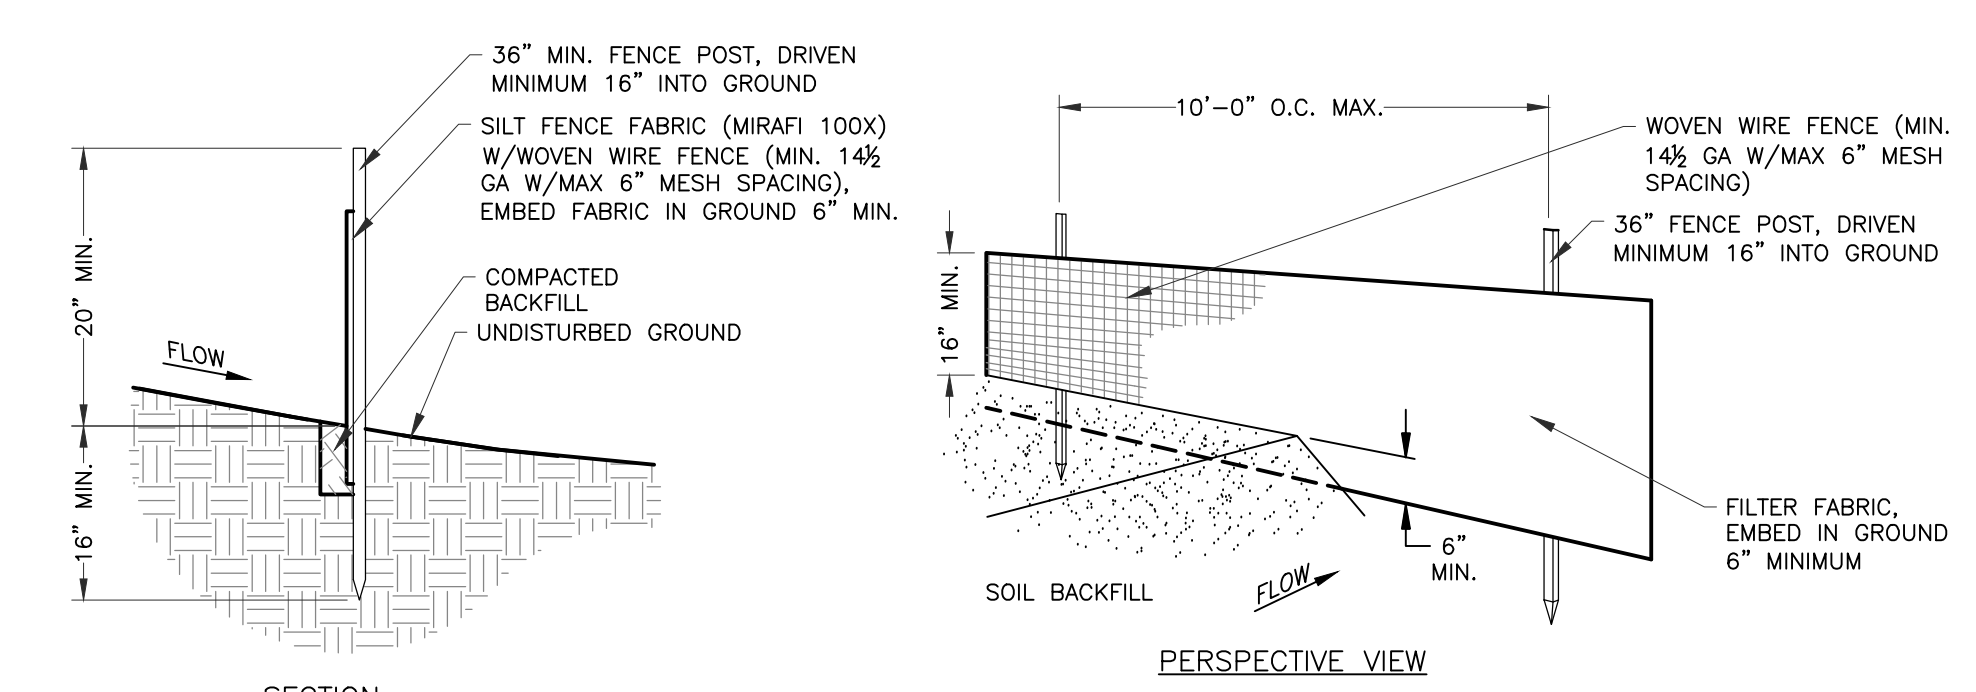


- CONSTRUCTION SPECIFICATIONS**
- WOVEN WIRE FENCE TO BE FASTENED SECURELY TO FENCE POSTS WITH WIRE TIES OR STAPLES. POSTS SHALL BE STEEL EITHER "T" OR "U" TYPE OR HARDWOOD.
 - FILTER CLOTH TO BE TO BE FASTENED SECURELY TO WOVEN WIRE FENCE WITH TIES SPACED EVERY 24" AT TOP AND MID SECTION. FENCE SHALL BE WOVEN WIRE, 1 1/2 GA, 6" MAXIMUM MESH OPENING.
 - WHEN TWO SECTIONS OF FILTER CLOTH ADJOIN EACH OTHER THEY SHALL BE OVER-LAPPED BY SIX INCHES AND FOLDED. FILTER CLOTH SHALL BE EITHER FILTER X, MIRAFI 100X, STABILINKA T140N, OR APPROVED EQUIVALENT.
 - PREFABRICATED UNITS SHALL BE GEOTAF, ENVROFENCE, OR APPROVED EQUIVALENT.
 - MAINTENANCE SHALL BE PERFORMED AS NEEDED AND MATERIAL REMOVED WHEN "BULGES" DEVELOP IN THE SILT FENCE.
- | SLOPE | STEEPNESS | SLOPE LENGTH/FENCE LENGTH (FT) | | |
|--------|--------------|--------------------------------|------------|----------|
| | | STANDARD | REINFORCED | SUPER |
| <2% | <50:1 | 300/1500 | N/A | N/A |
| 2-10% | 50:1 TO 10:1 | 125/1000 | 250/2000 | 300/2500 |
| 10-20% | 10:1 TO 5:1 | 100/750 | 150/1000 | 200/1000 |
| 20-33% | 5:1 TO 3:1 | 60/500 | 80/750 | 100/1000 |
| 33-50% | 3:1 TO 2:1 | 40/250 | 70/350 | 100/500 |
| >50% | >2:1 | 20/125 | 30/175 | 50/250 |
- STANDARD SILT FENCE (SF)** IS FABRIC ROLLS STAPLED TO WOODEN STAKES DRIVEN 16" IN THE GROUND.
REINFORCED SILT FENCE (RSF) IS FABRIC PLACED AGAINST WELDED WIRE FABRIC WITH ANCHORED STEEL POSTS DRIVEN 16" IN THE GROUND.
SUPER SILT FENCE (SSF) IS FABRIC PLACED AGAINST CHAIN LINK FENCE AS SUPPORT BACKING WITH POSTS DRIVEN 3' IN THE GROUND.

3 SEDIMENT CONTROL FENCE
SCALE: NTS


PIRE SIZE (IN)	PIRE SLOPE	STONE FILL APRON SIZES*		
		STONE DIMENSION (SQ. FT)	APRON THICKNESS (FT)	APRON LENGTH (LxL FT)
12	0-3%	4	LIGHT	18 10
	3-7%	6	MEDIUM	24 15
	7-10%	9	HEAVY	30 20
16,18	0-3%	6	LIGHT	18 14
	3-7%	9	MEDIUM	24 20
	7-10%	12	HEAVY	30 24
24	0-1%	6	MEDIUM	24 14
	1-2%	9	MEDIUM	24 20
	2-3%	12	MEDIUM	30 26
30	0-1%	12	MEDIUM	28 28
	0-1%	18	HEAVY	36 36
	0-1%	24	HEAVY	44 44
36	1-2%	15	HEAVY	36 32
	2-4%	18	HEAVY	36 40
	4-6%	21	HEAVY	36 45
42	0-1%	12	HEAVY	28 28
	1-2%	15	HEAVY	36 36
	2-3%	18	HEAVY	36 42
48	0-1%	12	MEDIUM	28 32
	1-2%	18	HEAVY	36 42
	2-3%	24	HEAVY	44 48
60	3-4%	24	HEAVY	44 52
	0-1%	18	HEAVY	32 44
	1-2%	24	HEAVY	44 58
60	2-3%	30	HEAVY	54 66
	3-4%	33	HEAVY	59 70

*THE ABOVE TEXT IS BASED ON: NYS DOT NEW YORK STATE STANDARDS & SPECIFICATIONS FOR EROSION & SEDIMENT CONTROL - FIGURE 3.16 OUTLET PROTECTION DESIGN - MINIMUM TAILWATER CONDITION (SECTION OF OUTLET PROTECTION FOR A ROUND PIPE FLOWING FULL, MINIMUM TAILWATER CONDITION: 1" x 4" (0.500) (0.500-NRCS)

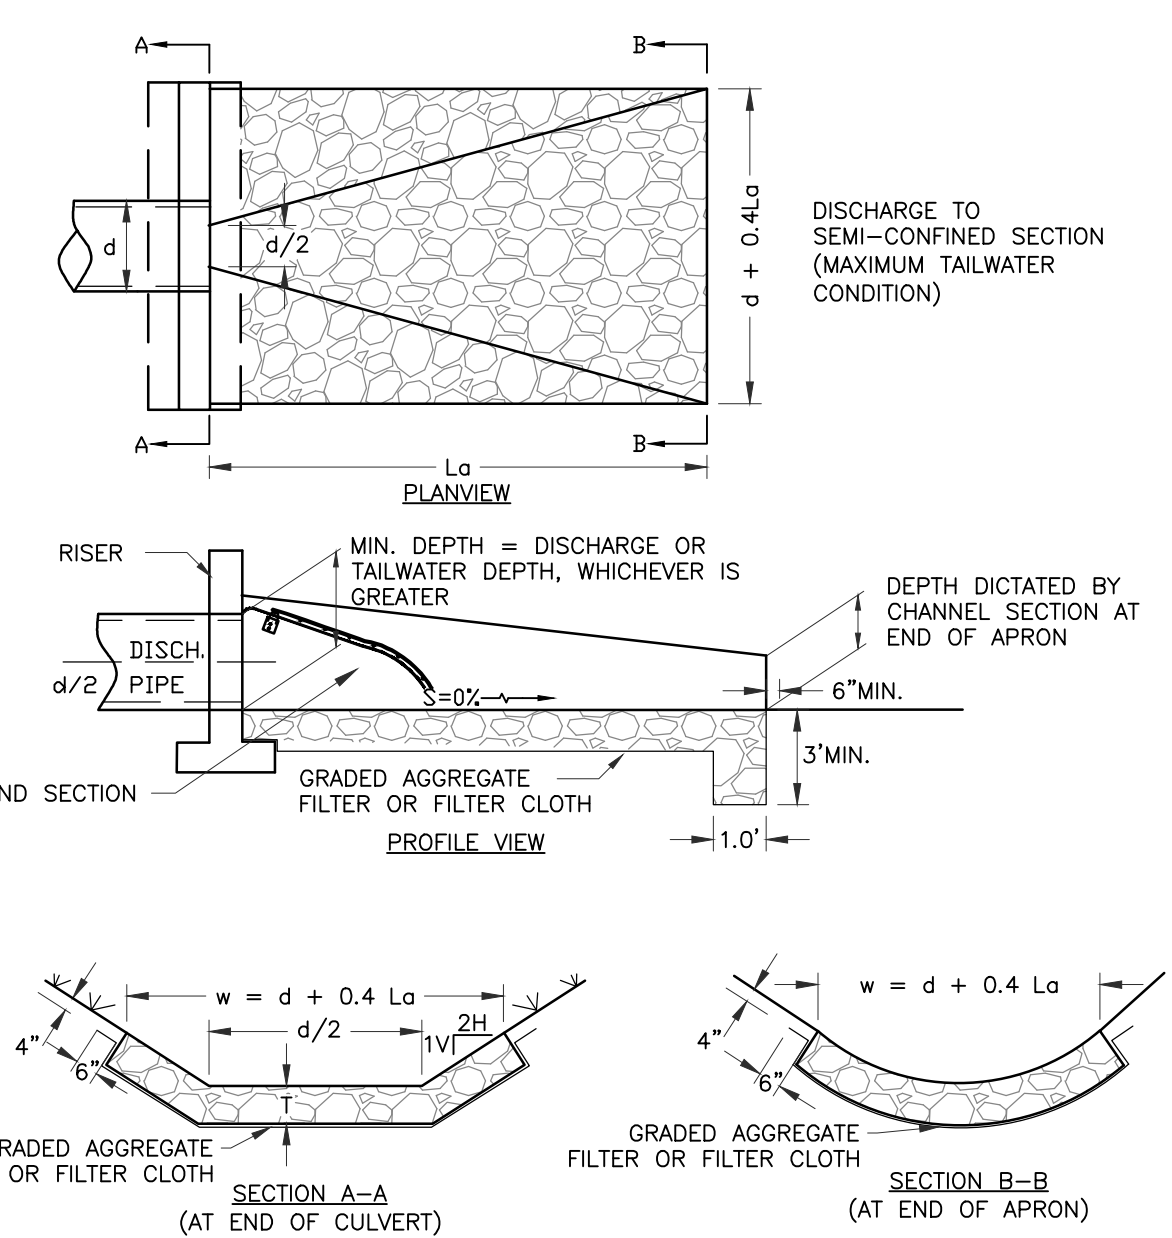


- NOTES:**
- SEE RIPRAP STANDARDS AND SPECIFICATION FOR MAXIMUM TAILWATER CONDITIONS, STONE FILL SIZES AND APRON SIZES.
 - APRON DIMENSIONS ARE BASED ON PIPES FLOWING FULL. USING ACTUAL FLOWS MAY RESULT IN DIFFERENT APRON DIMENSIONS.
 - MINIMUM THICKNESS OF THE STONE FILL LAYER SHALL BE 1.5 TIMES THE MAXIMUM STONE SIZE OR 450 GREATER THAN 15".

6 RIPRAP OUTLET PROTECTION
SCALE: NTS

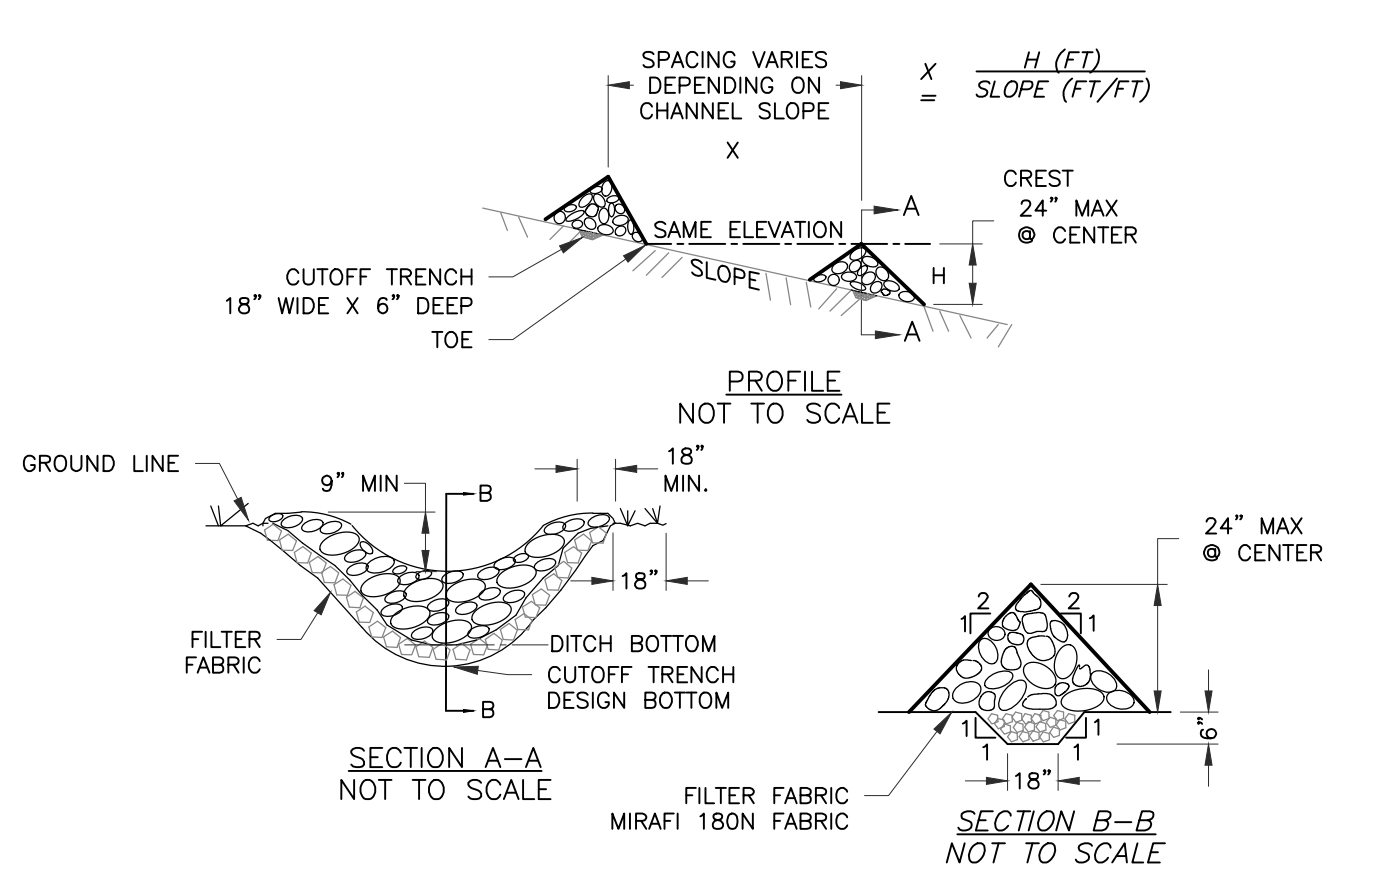


- CONSTRUCTION SPECIFICATIONS**
- STONE WILL BE PLACED ON A FILTER FABRIC FOUNDATION TO THE LINES, GRADES AND LOCATIONS SHOWN IN THE PLAN.
 - SET SPACING OF CHECK DAMS TO ASSUME THAT THE ELEVATIONS OF THE CREST OF THE DOWNSTREAM DAM IS AT THE SAME ELEVATION OF THE TOE OF THE UPSTREAM DAM.
 - EXTEND THE STONE A MINIMUM OF 1.5 FEET BEYOND THE DITCH BANKS TO PREVENT CUTTING AROUND THE DAM.
 - PROTECT THE CHANNEL DOWNSTREAM OF THE LOWEST CHECK DAM FROM SCOUR AND EROSION WITH STONE OR LINER AS APPROPRIATE.
 - ENSURE THAT CHANNEL APPURTENANCES SUCH AS CULVERT ENTRANCES BELOW CHECK DAMS ARE NOT SUBJECT TO DAMAGE OR BLOCKAGE FROM DISPLACED STONE. MAXIMUM DRAINAGE AREA TWO (2) ACRES.

7 STONE CHECK DAM DETAIL
SCALE: NTS

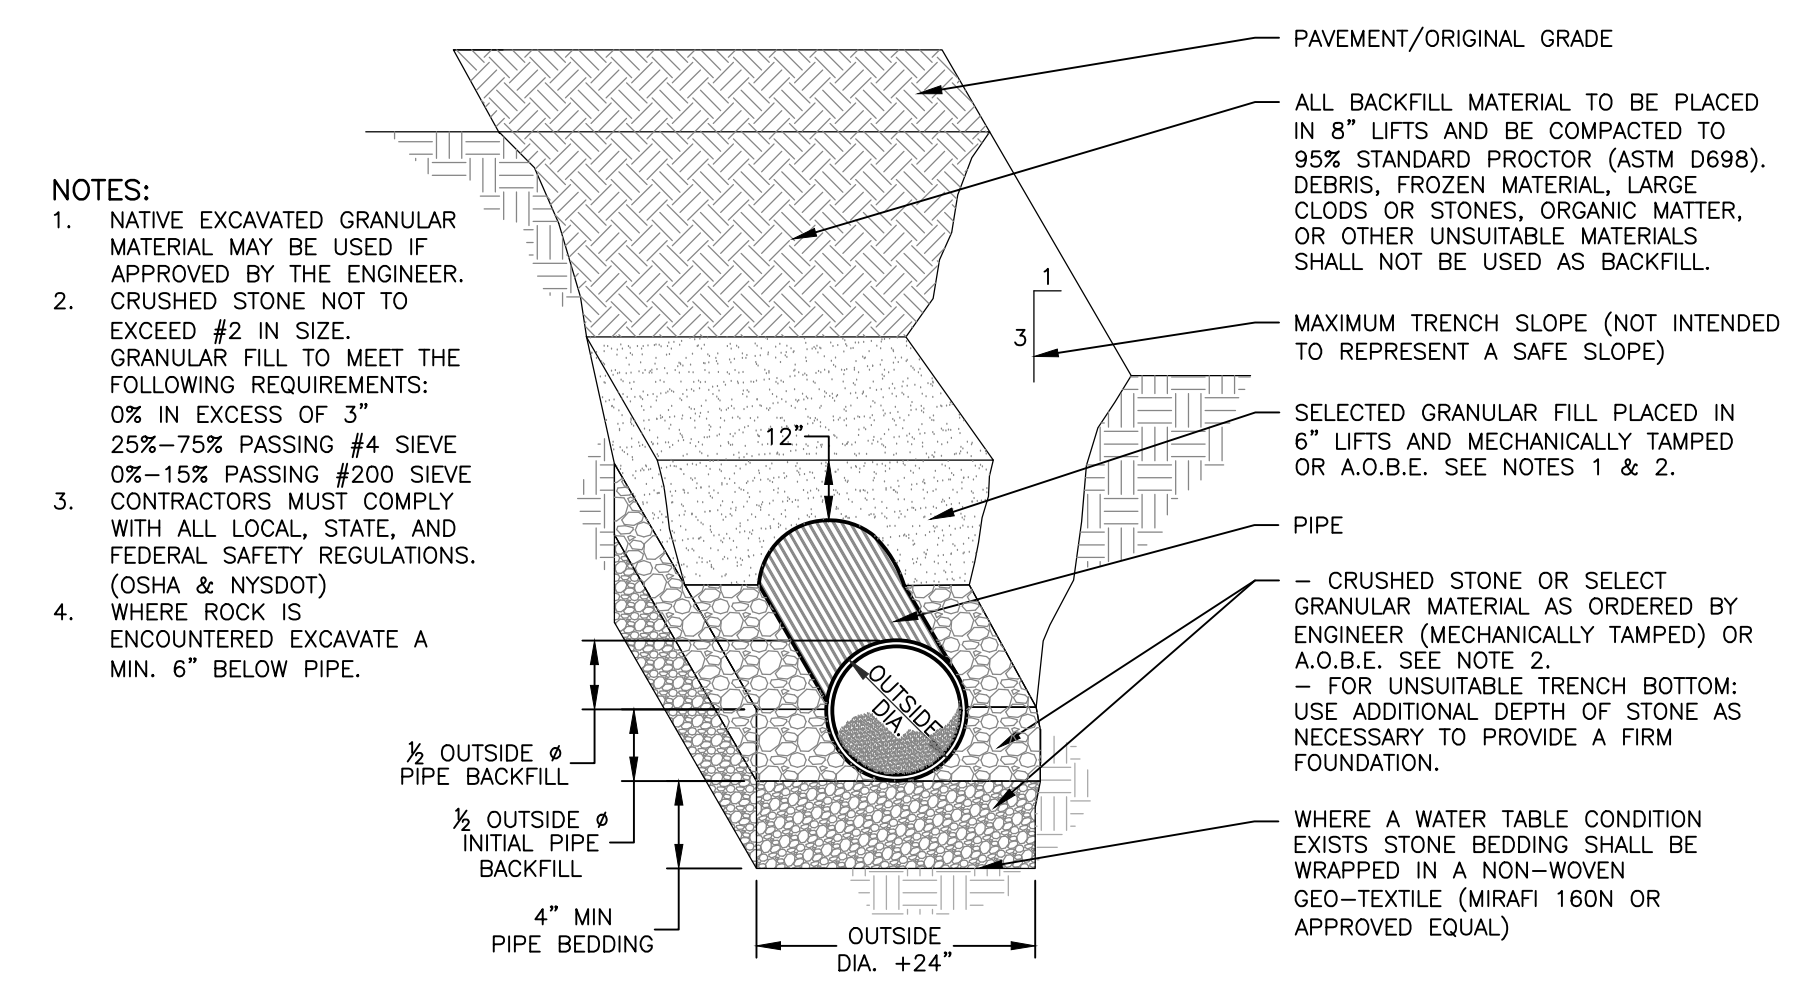

8 TYPICAL TRENCH DETAIL FOR CORRUGATED HDPE PIPE
SCALE: NTS

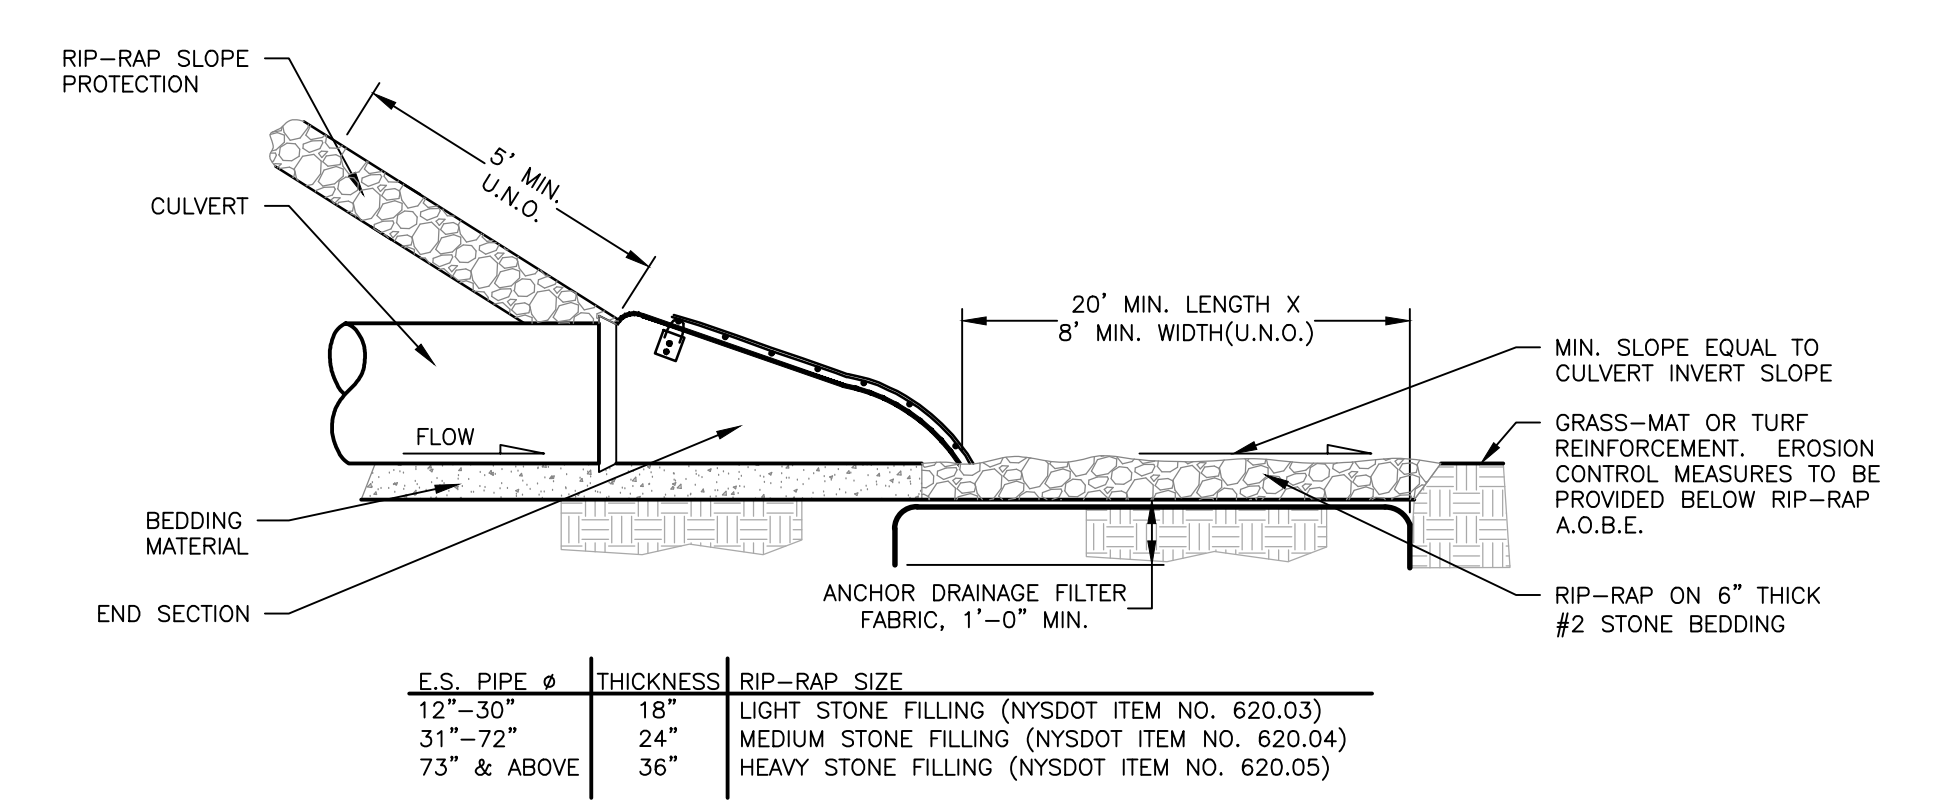

9 TYPICAL CULVERT DETAIL
SCALE: NTS


TOWN OF WILTON
WATER & SEWER AUTHORITY
PLEASE REFER TO FIRST SHEET FOR APPROVAL DATE AND SIGNATURE

TOWN OF WILTON PLANNING BOARD
PLEASE REFER TO FIRST SHEET FOR APPROVAL DATE AND SIGNATURE

SARATOGA COUNTY DEPARTMENT OF HEALTH


BULLARD LANE RESIDENTIAL SUBDIVISION
 BULLARD LANE, TOWN OF WILTON, SARATOGA COUNTY, NEW YORK
 PRELIMINARY / NOT FOR CONSTRUCTION
 EROSION RECORD/DESCRIPTION
 DATE: _____
 CIVIL TRANSPORTATION/ENVIRONMENTAL/LAND SURVEYING
 UNAUTHORIZED ADDITION TO THIS LOCATION OF THE INSULATION ENGINEERING



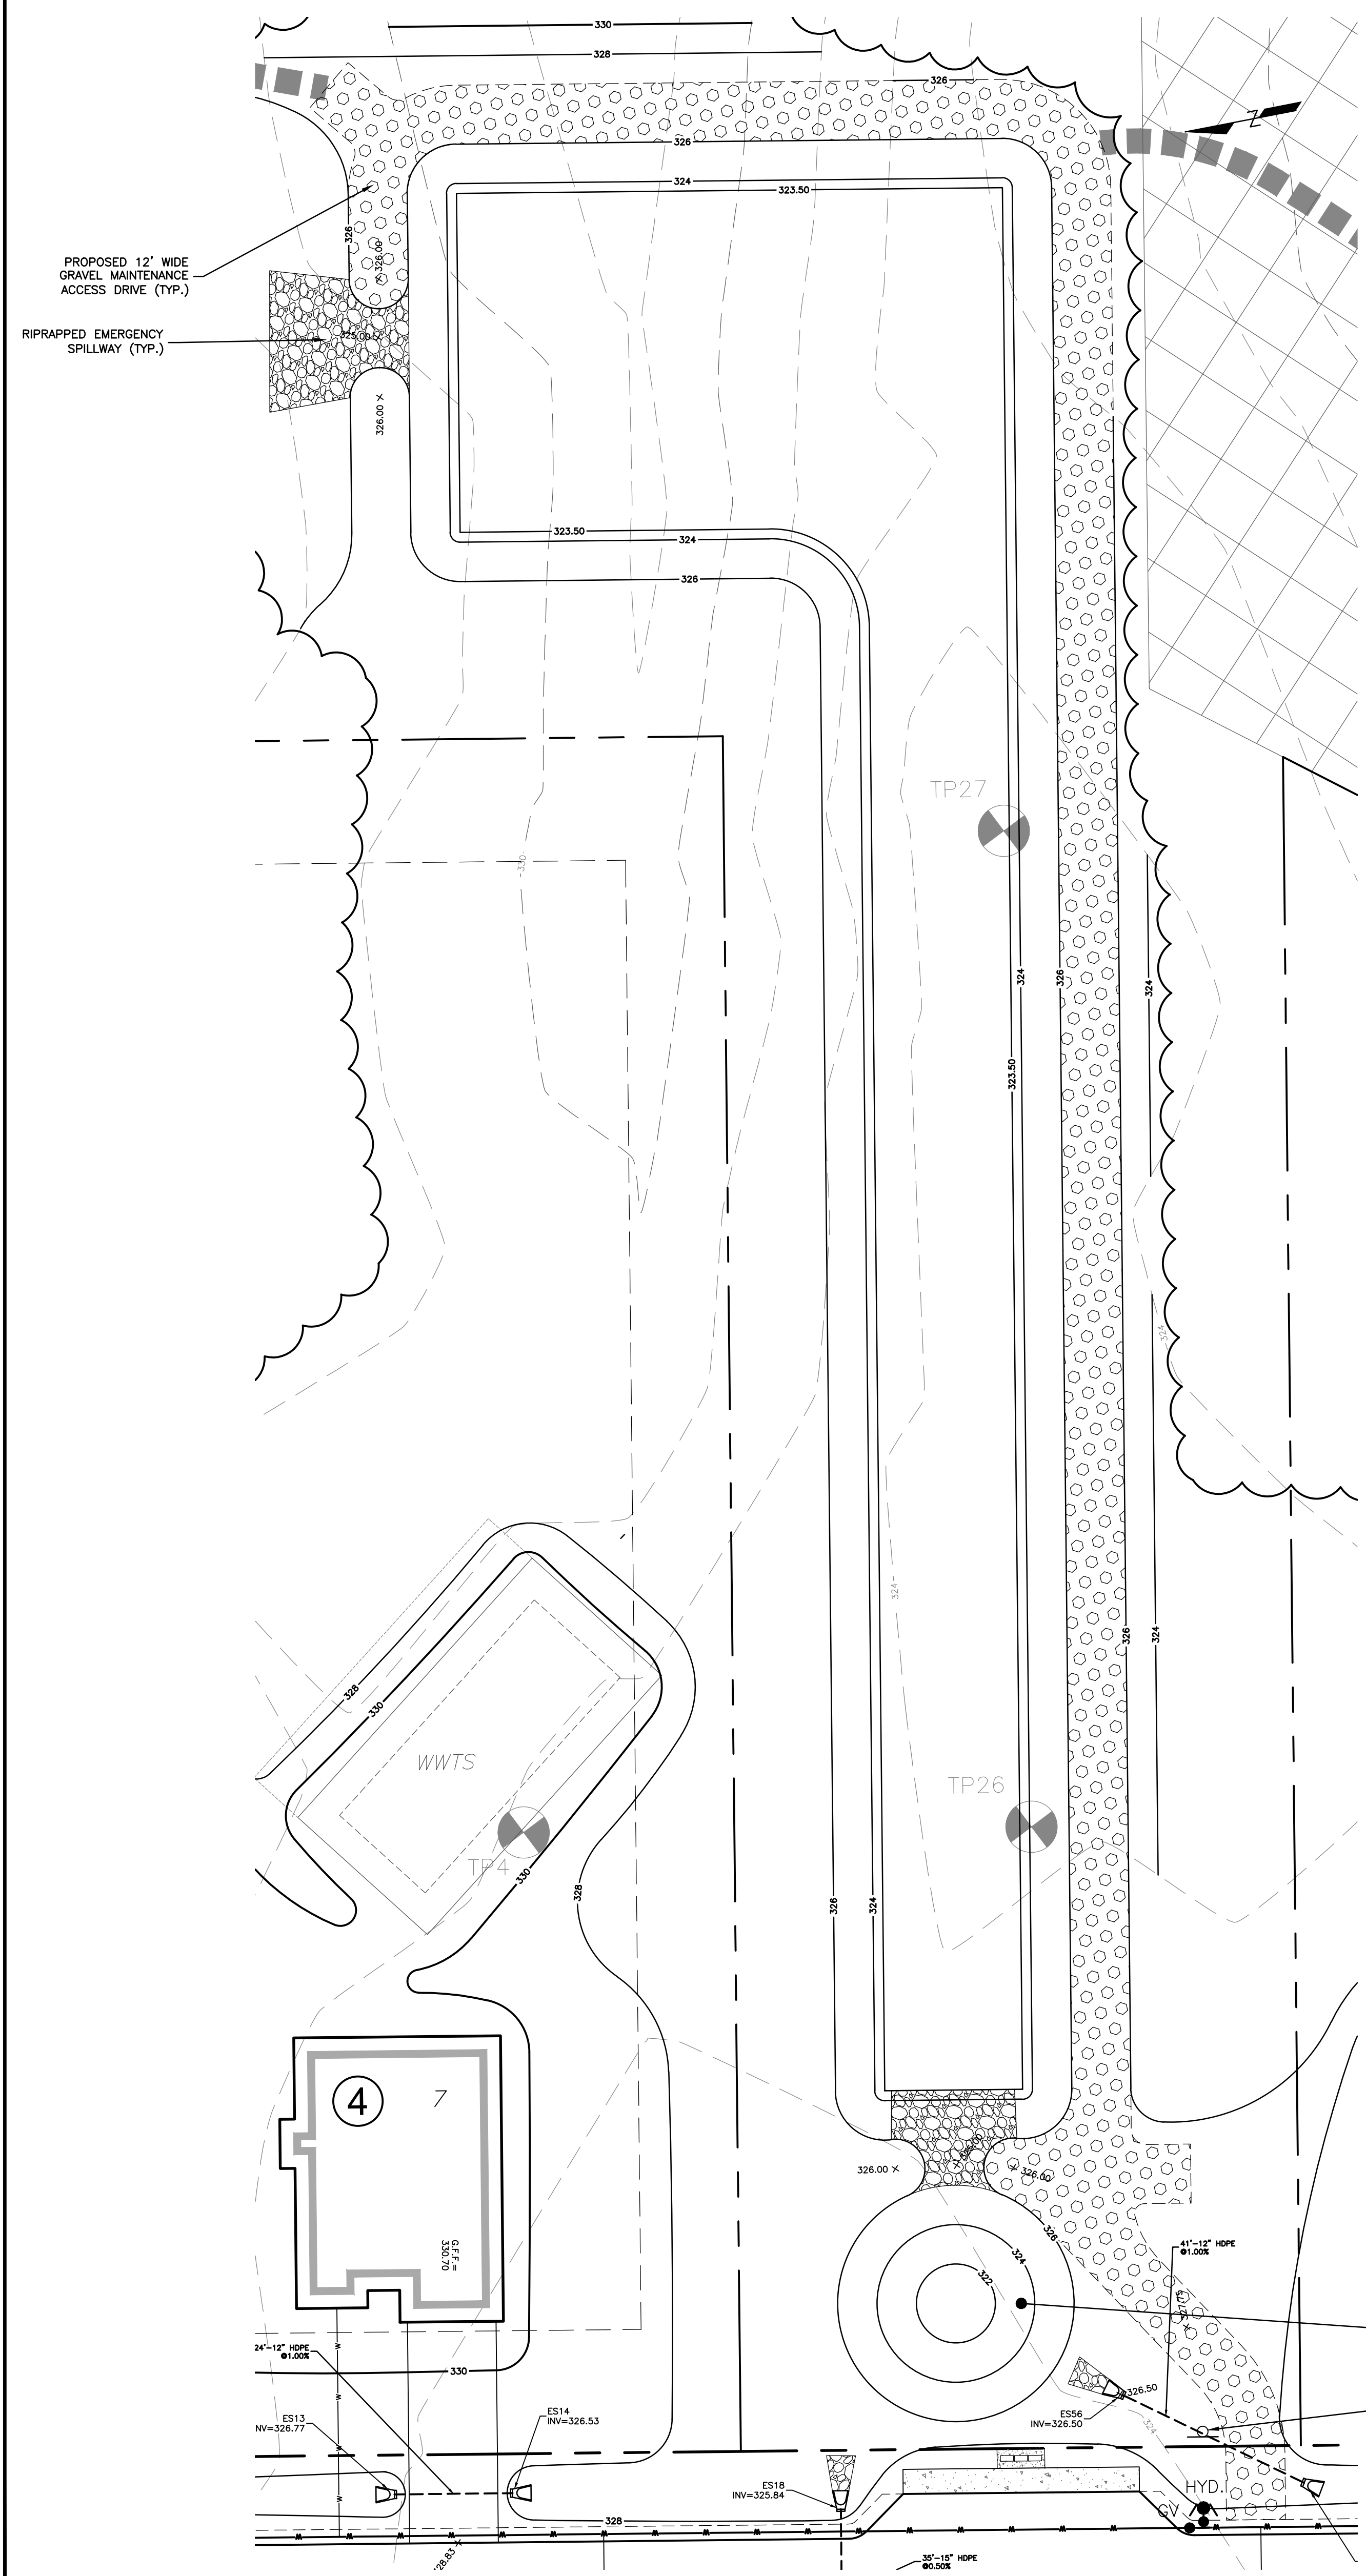


1 STORMWATER INFILTRATION BASIN 1
SCALE: 1"=20'


- EMBANKMENT FILL NOTES:**
- EMBANKMENT FILL FOR THE STORMWATER BASIN BERM SHALL CONSIST OF A CLEAN WELL GRADED MIXTURE OF SILT, CLAY, SAND AND GRAVEL WITH NO PARTICLES LARGER THAN (6) INCHES, EXCAVATED ON SITE SOILS SHALL BE SELECTIVELY STOCKPILED FOR USE AS EMBANKMENT FILL IN AREAS DESIGNATED BY THE ENGINEER. SOIL SUITABLE FOR USE AS EMBANKMENT FILL SHALL HAVE AT LEAST 40% BY WEIGHT FINER THAN THE NO. 200 SIEVE AND NO MORE THAN 15% BY WEIGHT COARSER THAN THE NO. 4 SIEVE. THE FILL SHALL BE FREE OF VEGETATION, ORGANIC MATERIAL AND FROZEN SOIL.
 - ALL FILL SHALL BE PLACED IN LIFTS NOT EXCEEDING (8) INCHES IN THICKNESS WHEN LOOSE AND BE COMPACTED TO A DENSITY OF AT LEAST 95% OF THE MAXIMUM DRY DENSITY AS DETERMINED IN ACCORDANCE WITH ASTM-1557.
 - ACCEPTABLE POND LINER WITHIN FOREBAY OPTIONS INCLUDE: A) 6"-12" OF CLAY SOIL (MINIMUM 50% PASSING THE #200 SIEVE AND A MAXIMUM PERMEABILITY OF 0.00001 CM/SEC), AND B) A 30 MIL POLYLINER.
 - THE STABILIZED ACCESS ROAD SHALL CONSIST OF (12) INCHES OF COMPACTED NYS DOT ITEM NO. 304.12.

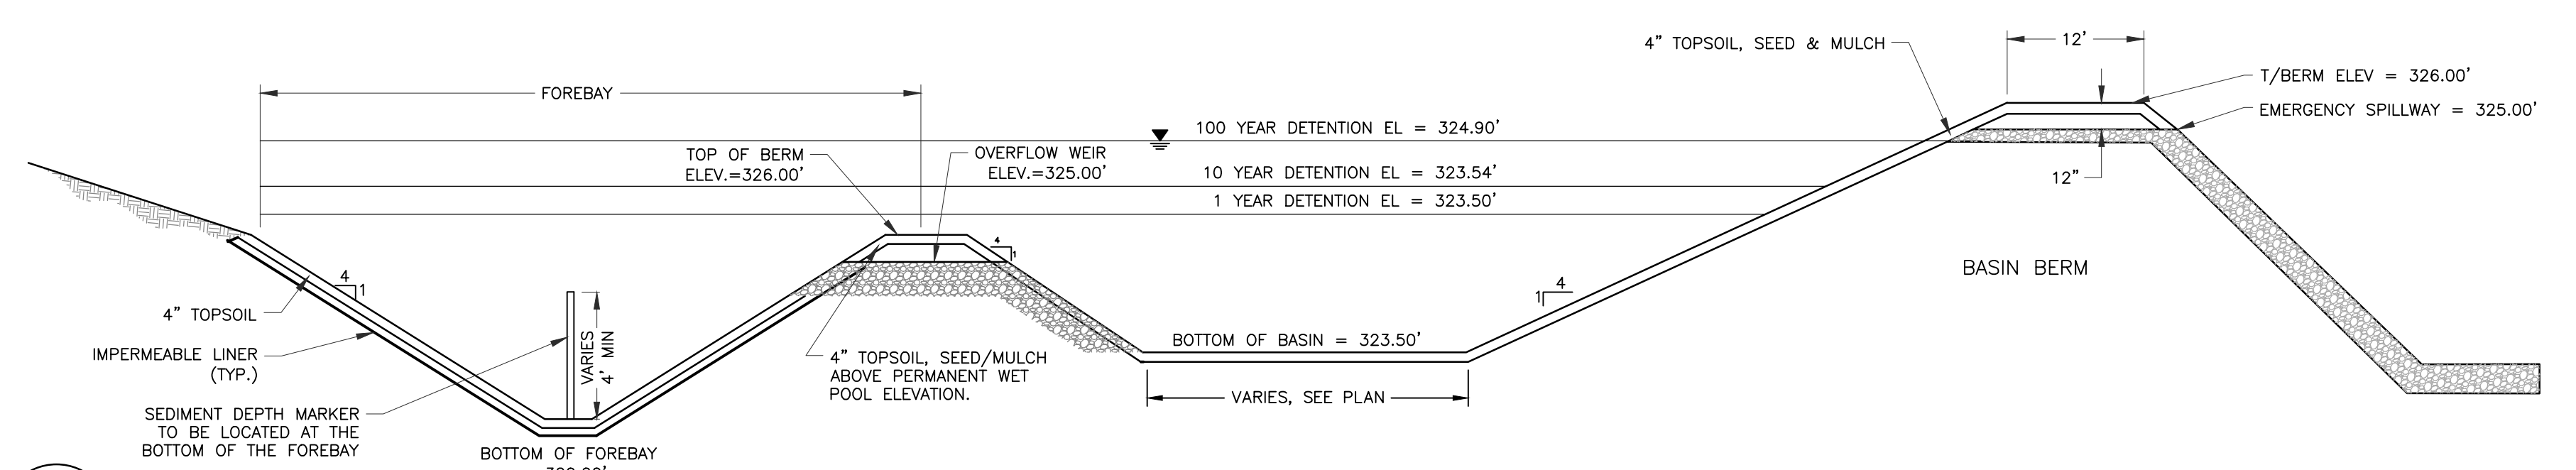


2 STORMWATER INFILTRATION BASIN 1
SCALE: NTS

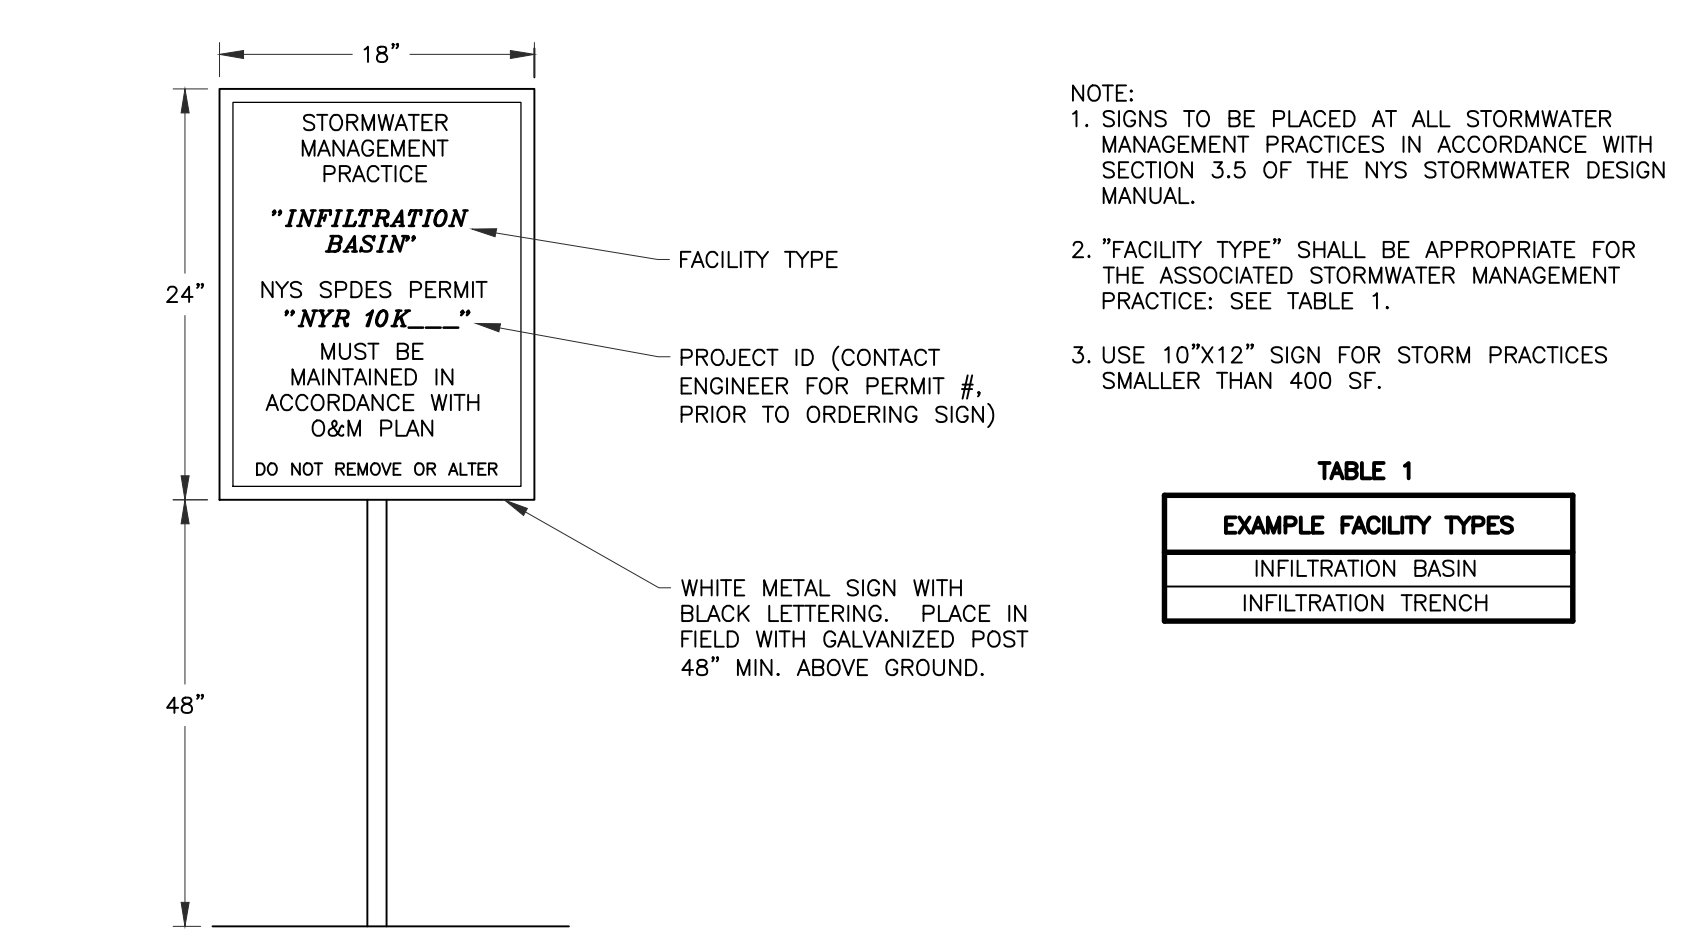


4 STORMWATER MANAGEMENT FACILITY NOTIFICATION SIGN
SCALE: NTS

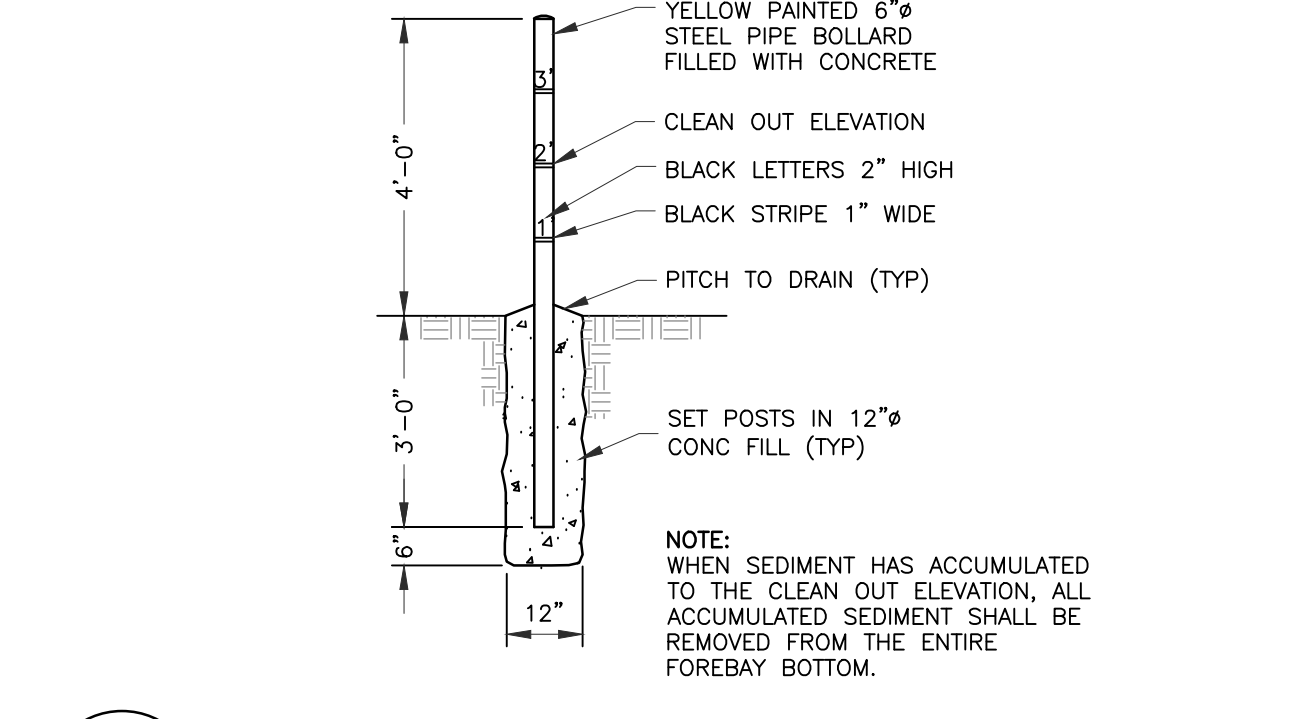


3 SEDIMENT DEPTH MARKER
SCALE: NTS

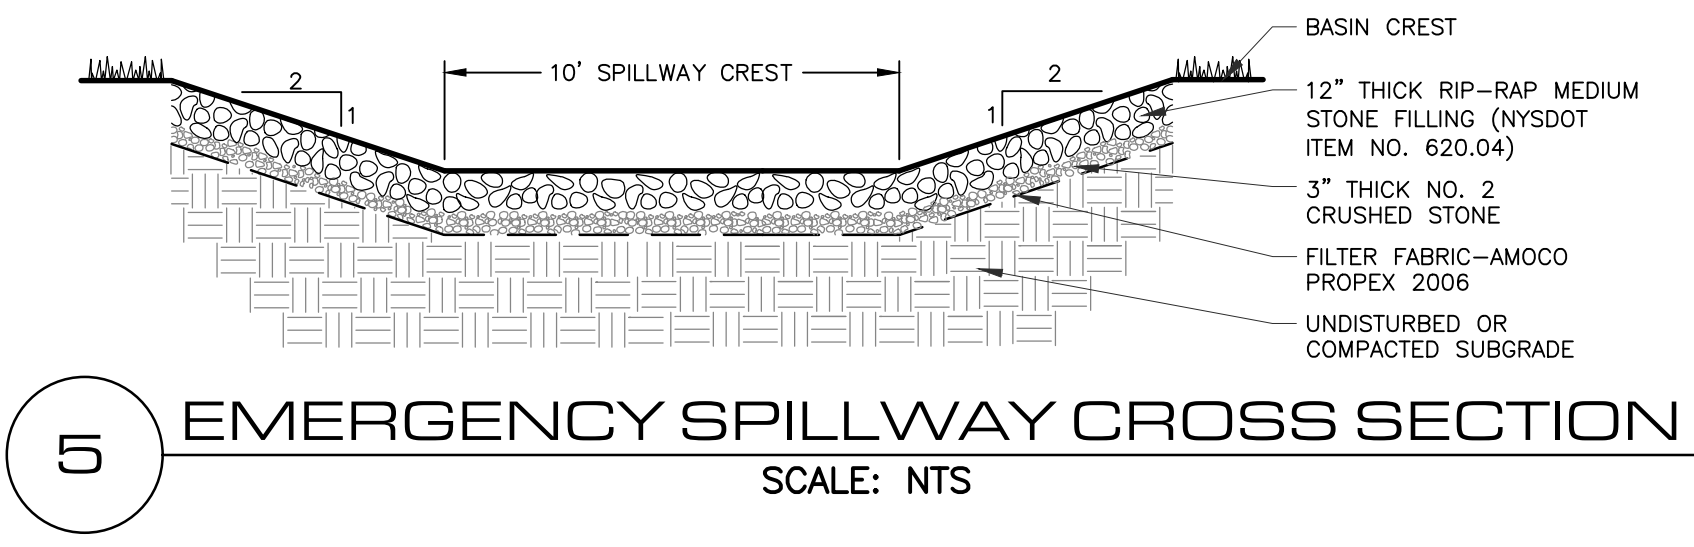


5 EMERGENCY SPILLWAY CROSS SECTION
SCALE: NTS

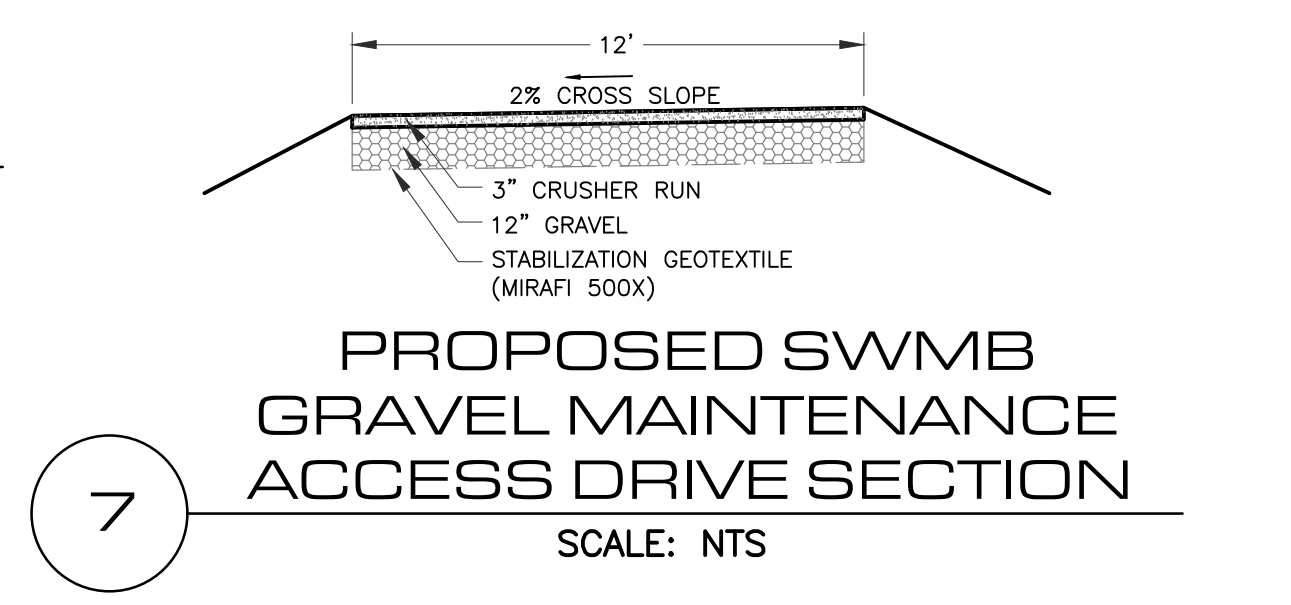


7 PROPOSED SWMB GRAVEL MAINTENANCE ACCESS DRIVE SECTION
SCALE: NTS

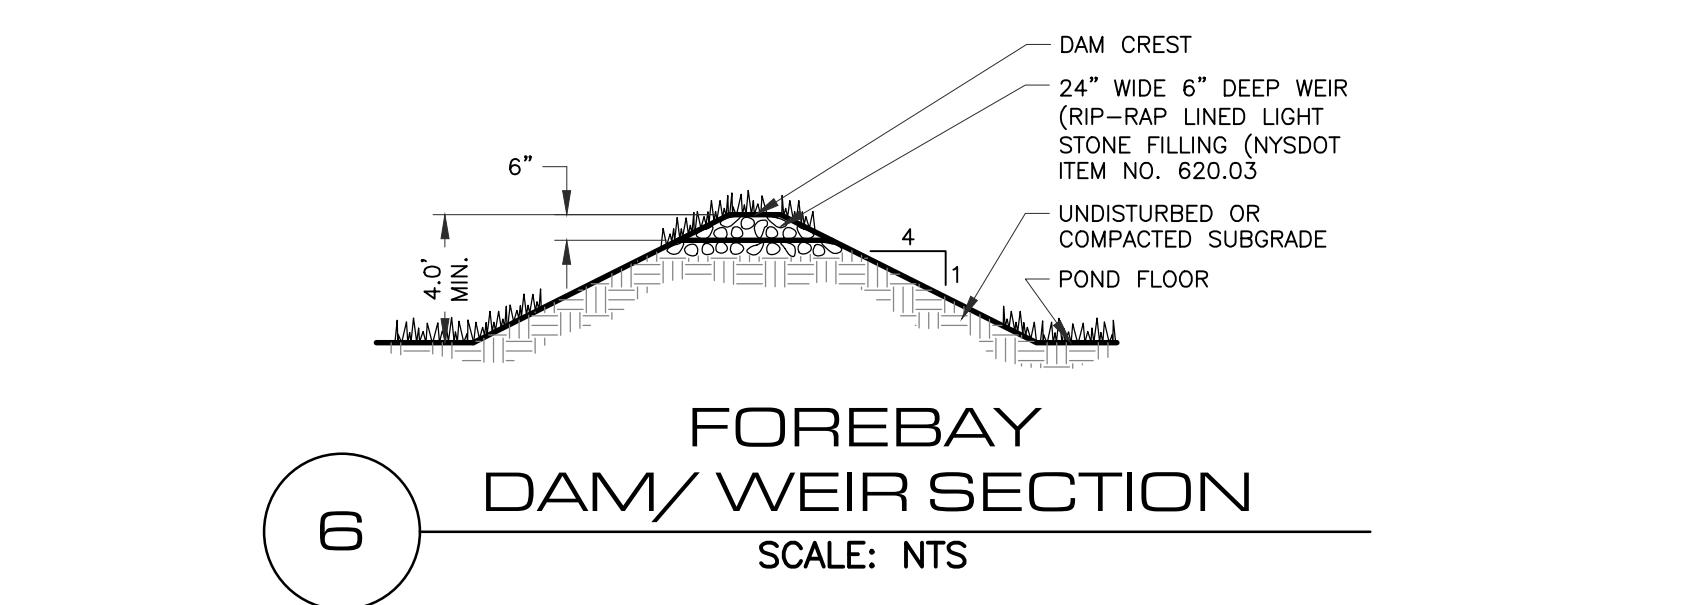

6 FOREBAY DAM/WEIR SECTION
SCALE: NTS

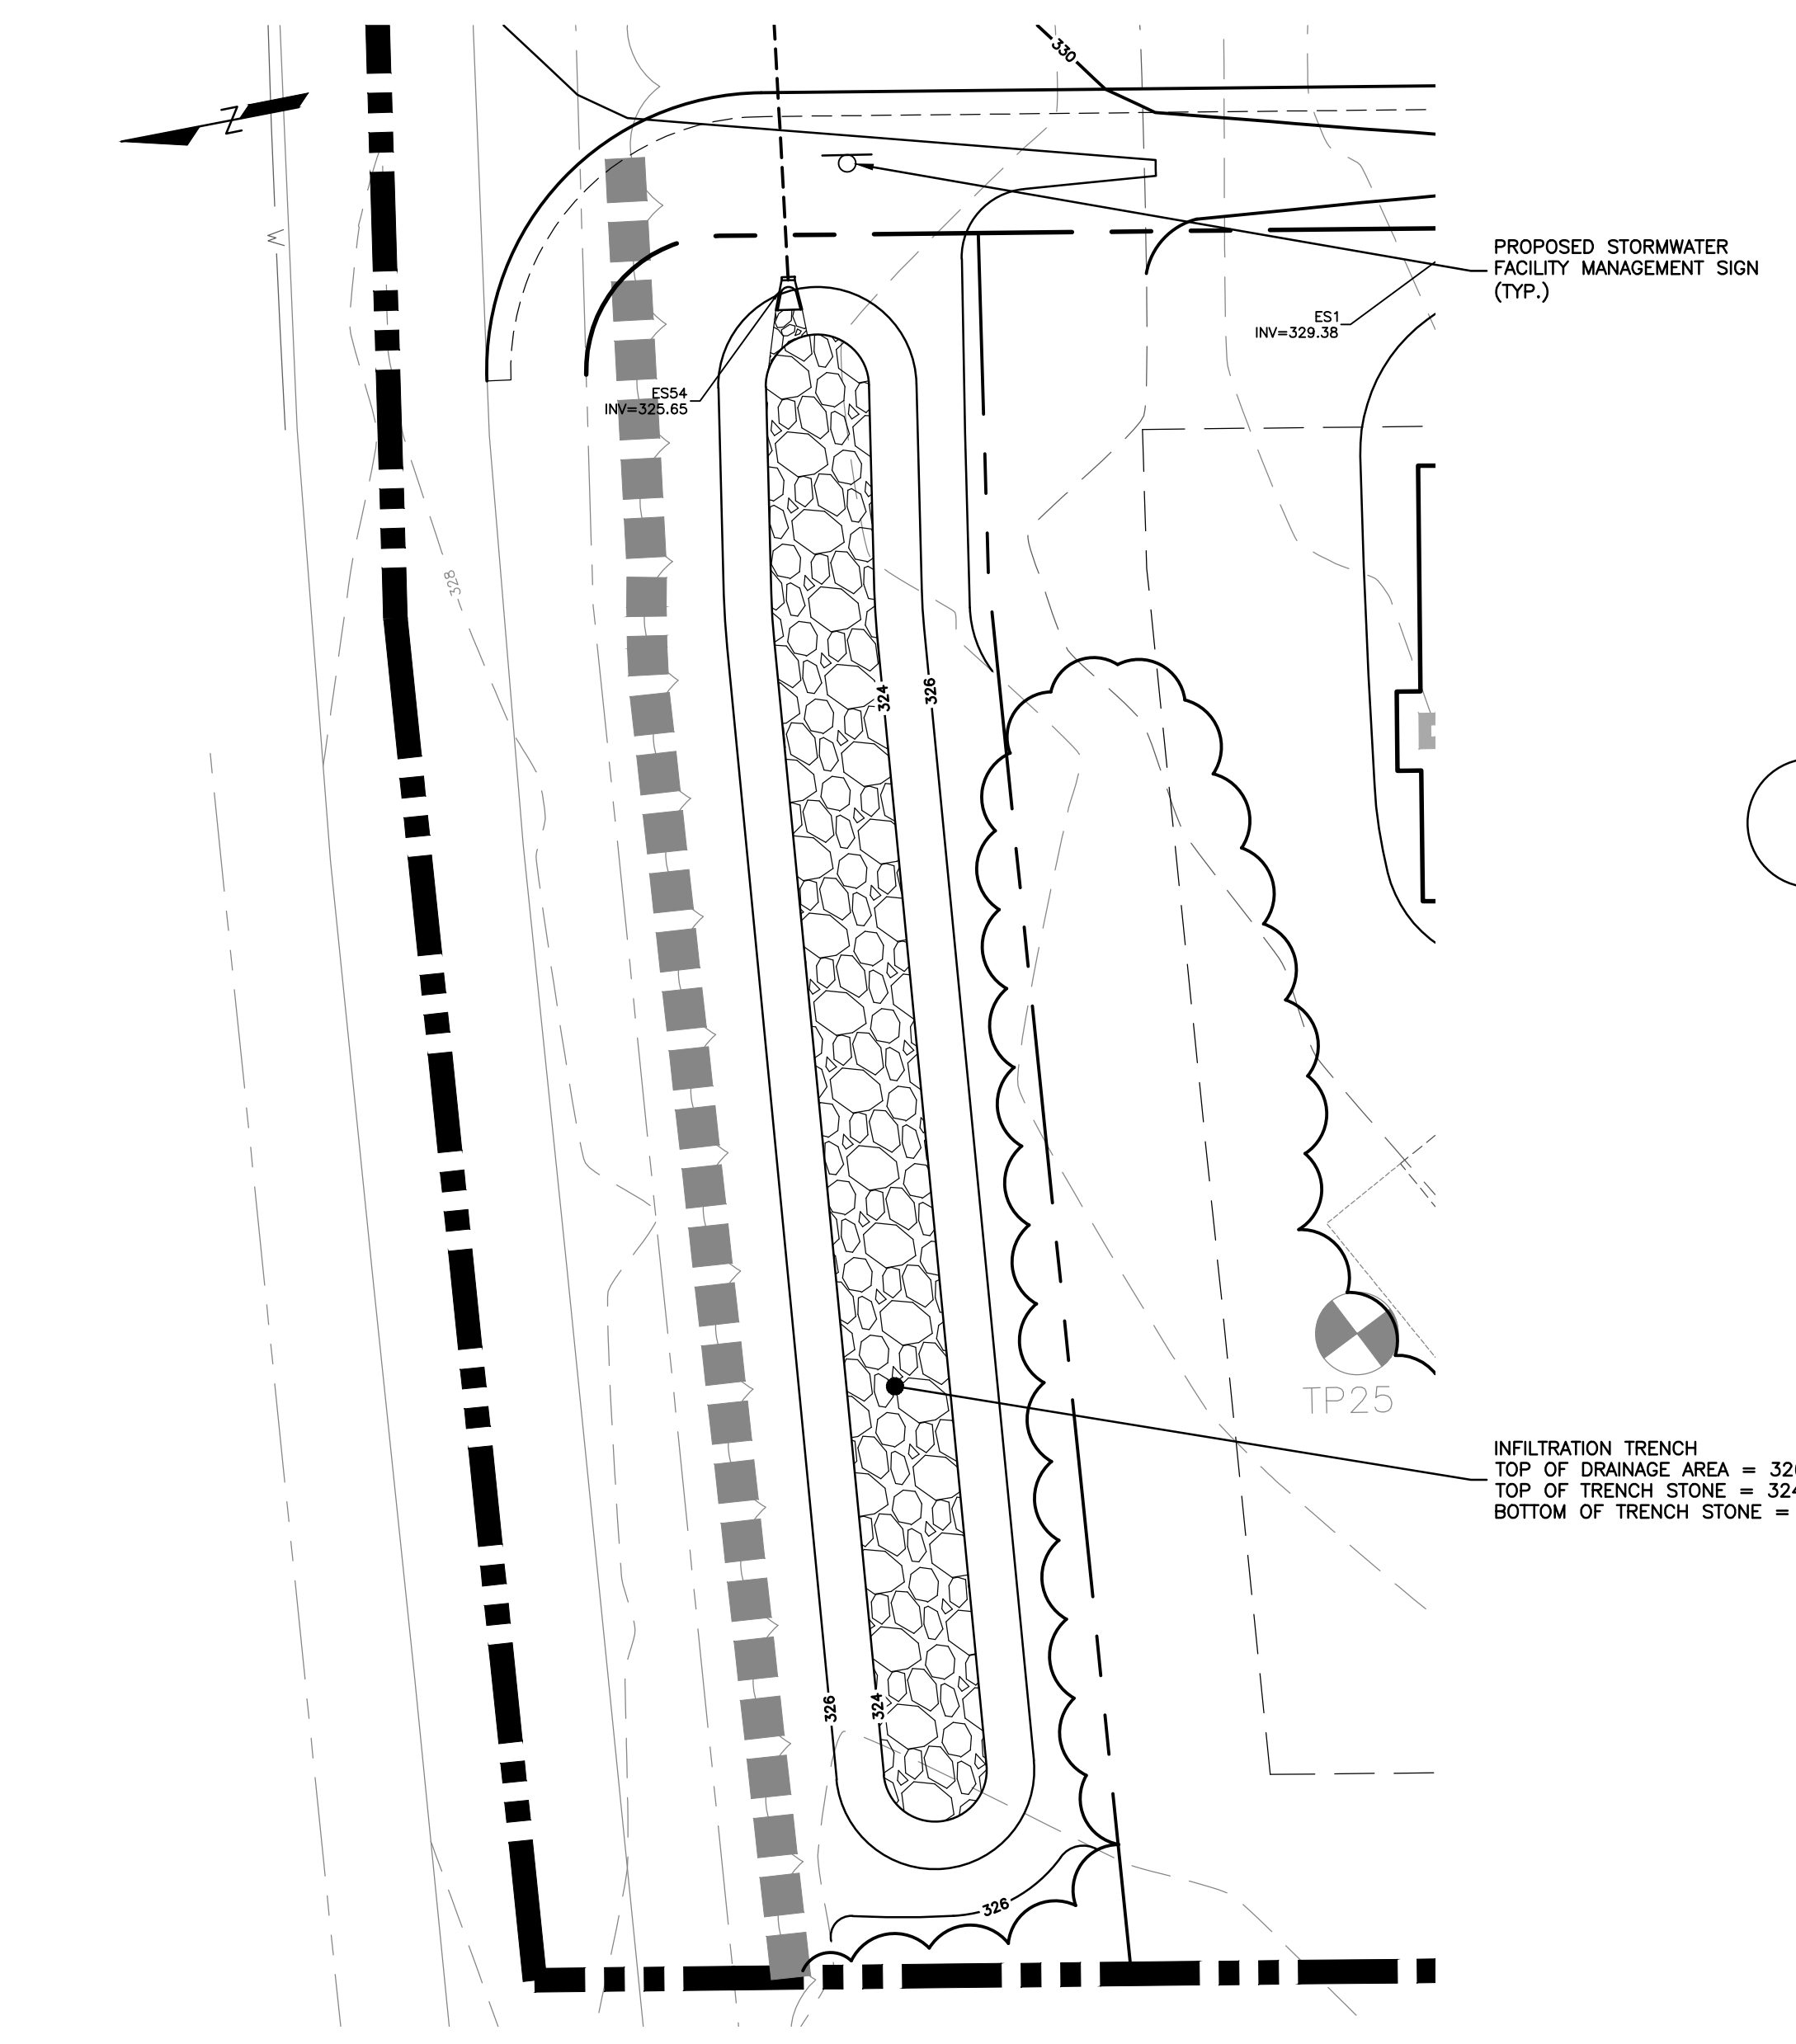

8 STORMWATER INFILTRATION TRENCH 1
SCALE: 1"=20'

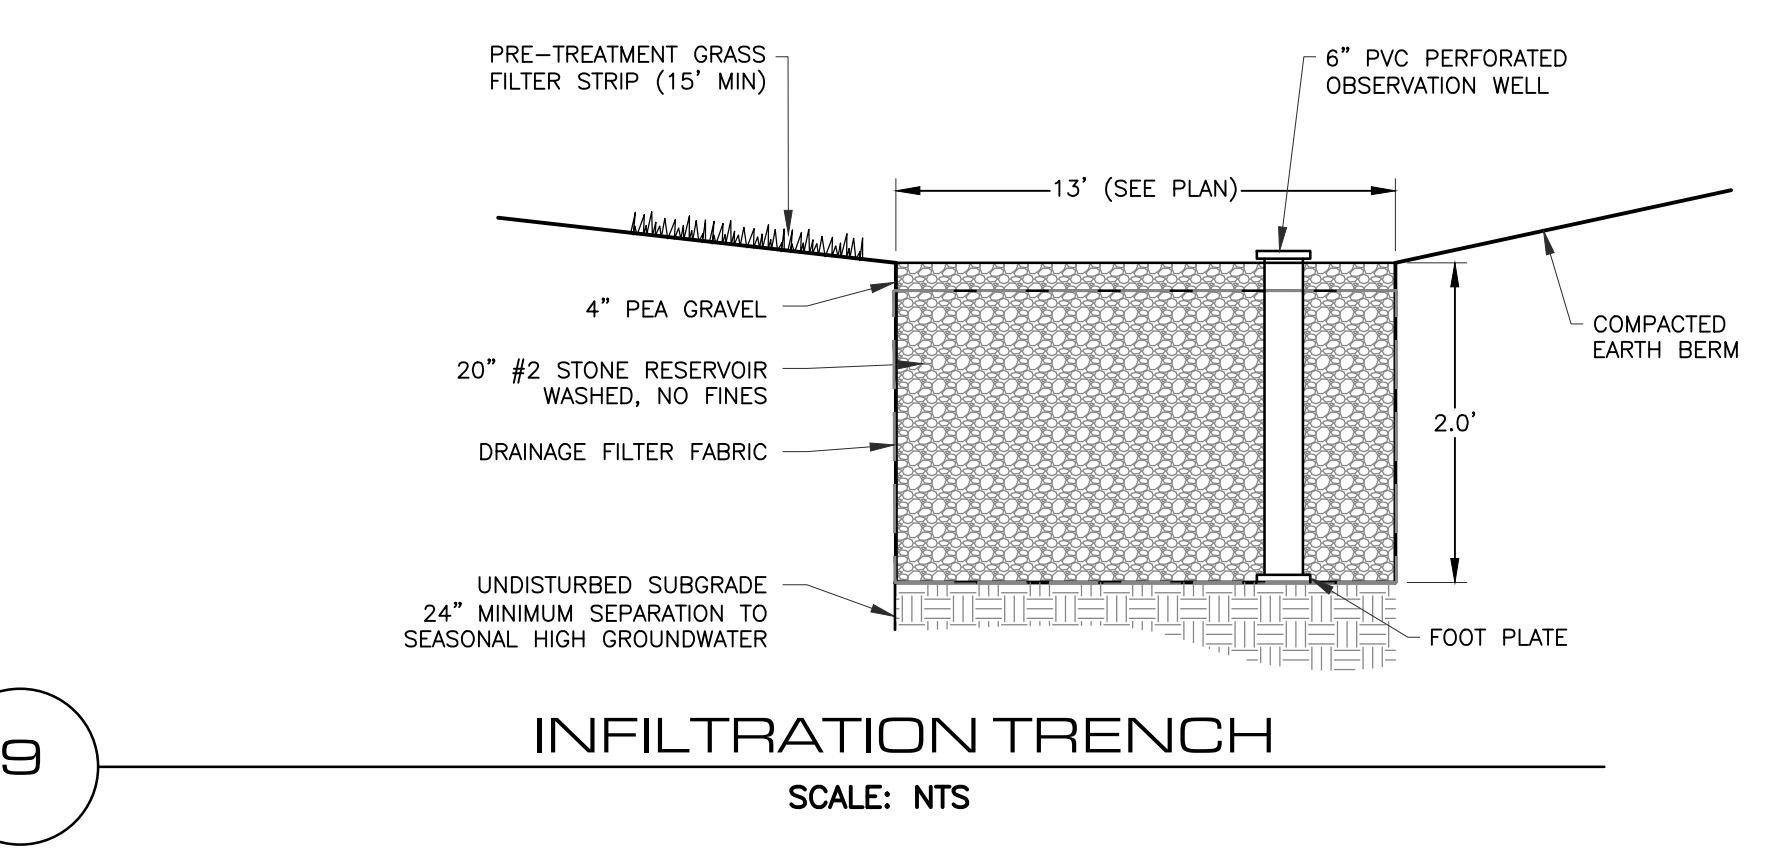

9 INFILTRATION TRENCH
SCALE: NTS

TOWN OF WILTON
WATER & SEWER AUTHORITY
PLEASE REFER TO FIRST SHEET FOR APPROVAL DATE AND SIGNATURE

TOWN OF WILTON PLANNING BOARD
PLEASE REFER TO FIRST SHEET FOR APPROVAL DATE AND SIGNATURE

SARATOGA COUNTY DEPARTMENT OF HEALTH

STORMWATER MANAGEMENT DETAILS

UNAUTHORIZED OR ADDITIONAL TO THIS LOCATION OF THE NYS PROFESSIONAL ENGINEERING SEALING ENGINEERING, P.C.

REVISIONS RECORD/DESCRIPTION

DATE

BULLARD LANE RESIDENTIAL SUBDIVISION
BULLARD LANE, TOWN OF WILTON, SARATOGA COUNTY, NEW YORK

PRELIMINARY / NOT FOR CONSTRUCTION

LANSING ENGINEERING
SARATOGA COUNTY, NEW YORK
REG. NO. 1061.01
E-1518 BBS/BSG

CIVIL TRANSPORTATION/ENVIRONMENTAL/LAND SURVEYING



Appendix F:

NYSDEC SPDES General Permit GP-0-25-001





Department of
Environmental
Conservation

NEW YORK STATE
DEPARTMENT OF ENVIRONMENTAL
CONSERVATION (NYSDEC)

SPDES GENERAL PERMIT
FOR STORMWATER DISCHARGES

From

CONSTRUCTION ACTIVITY

Permit No. GP-0-25-001

Construction General Permit (CGP)

Issued Pursuant to Article 17, Titles 7, 8 and Article 70
of the Environmental Conservation Law

Effective Date: January 29, 2025

Expiration Date: January 28, 2030

Scott E. Sheeley

Chief Permit Administrator



Authorized Signature

JAN. 29, 2025

Date

Address: NYSDEC
Division of Environmental Permits
625 Broadway, 4th Floor
Albany, N.Y. 12233-1750

PREFACE

Pursuant to Section 402 of the Clean Water Act (CWA), and 40 CFR 122.26(b)(14)(x), (15)(i), and (15)(ii), *stormwater discharges* from certain *construction activities* are unlawful unless they are authorized by a National Pollutant Discharge Elimination System (NPDES) permit or by a state permit program. New York State administers the approved State Pollutant Discharge Elimination System (SPDES) program with permits issued in accordance with the New York State Environmental Conservation Law (ECL) Article 17, Titles 7 and 8, and Article 70, as well as 6 NYCRR Parts 621 and 750.

Construction activities constitute construction of a *point source* and, therefore, pursuant to ECL sections 17-0505, 17-0701, and 17-0803, the *owner or operator* must have coverage under a SPDES permit prior to *commencement of construction activities*. The *owner or operator* cannot wait until there is an actual *discharge* from the *construction site* to obtain permit coverage.

***Note: The italicized words/phrases within this permit are defined in Appendix A.**

**NEW YORK STATE DEPARTMENT OF ENVIRONMENTAL CONSERVATION
SPDES CONSTRUCTION GENERAL PERMIT (CGP) GP-0-25-001
FOR STORMWATER DISCHARGES FROM CONSTRUCTION ACTIVITIES**

Table of Contents

Part I. How to Obtain Coverage and General Requirements	5
A. Eligibility Requirements	5
B. Types of <i>Discharges</i> Authorized	9
C. Prohibited <i>Discharges</i>	10
D. Electronic Notice of Intent (eNOI) Submittal.....	10
E. General Requirements for <i>Owners or Operators</i> with Permit Coverage	14
F. Permit Coverage for <i>Discharges</i> Authorized Under GP-0-20-001.....	18
G. Change of <i>Owner or Operator</i>	19
Part II. Water Quality-Based Effluent Limitations	20
A. Maintaining Water Quality	20
B. Effluent Limitations Applicable to <i>Discharges</i> from <i>Construction Activities</i>	20
C. Post-Construction Stormwater Management Practice (SMP) Requirements ...	23
Part III. Stormwater Pollution Prevention Plan (SWPPP)	28
A. General <i>SWPPP</i> Requirements	28
B. Required <i>SWPPP</i> Contents	32
C. Required <i>SWPPP</i> Components by Project Type.....	37
Part IV. Inspection and Maintenance Requirements	37
A. General Construction Site Inspection and Maintenance Requirements	37
B. Contractor Maintenance Inspection Requirements	37
C. <i>Qualified Inspector</i> Inspection Requirements.....	38
Part V. How to Terminate CGP Coverage.....	43
A. Electronic Notice of Termination (eNOT) Submittal.....	43
Part VI. Record Retention and Reporting.....	45
A. Record Retention	46
B. Reporting	46
Part VII. Standard Permit Requirements	46
A. Duty to Comply.....	46
B. Need to Halt or Reduce Activity Not a Defense.....	46
C. Penalties	46
D. False Statements	47
E. Re-Opener Clause	47
F. Duty to Mitigate	47
G. Requiring Another General Permit or Individual SPDES Permit.....	47
H. Duty to Provide Information.....	49
I. Extension	49
J. Signatories and Certification	50
K. Inspection and Entry	52
L. Confidentiality of Information.....	53
M. Other Permits May Be Required	53

N.	NYSDEC Orders or Civil Decrees/Judgments.....	53
O.	Property Rights	53
P.	Compliance with Interstate Standards.....	53
Q.	Oil and Hazardous Substance Liability.....	54
R.	Severability.....	54
S.	NYSDEC Approved Forms.....	54
APPENDIX A – Abbreviations and Definitions.....		55
	Abbreviations.....	55
	Definitions.....	56
APPENDIX B – Required SWPPP Components by Project Type.....		64
	Table 1.....	64
	Table 2.....	66
APPENDIX C – Watersheds Requiring Enhanced Phosphorus Removal.....		68
APPENDIX D – Impaired Waterbodies (by Construction Related Pollutants)		74
APPENDIX E – List of NYSDEC Regional Offices.....		80
APPENDIX F – SWPPP Preparer Certification Form		81
APPENDIX G – MS4 SWPPP Acceptance Form.....		83
APPENDIX H – NYCDEP SWPPP Acceptance/Approval Form		86
APPENDIX I – MS4 No Jurisdiction Form.....		89
APPENDIX J – Owner/Operator Certification Form		91

Part I. How to Obtain Coverage and General Requirements

To be covered under this permit, the *owner or operator* must meet all eligibility requirements in Part I.A. and follow the requirements for obtaining permit coverage in Part I.D., F., or G.

A. Eligibility Requirements

For a *common plan of development or sale*, the *phase(s)* that meet the eligibility requirements in Part I.A. may obtain coverage under this permit even if other *phase(s)* of the same *common plan of development or sale* do not meet the eligibility requirements and require an individual SPDES permit.

1. The *owner's or operator's construction activities* involve soil disturbances of:
 - a. one or more acres; or
 - b. less than one acre which are part of a *common plan of development or sale* that will ultimately disturb one or more acres; or
 - c. less than one acre where NYSDEC has determined that a SPDES permit is required for *stormwater discharges* based on the potential for contribution to a violation of a *water quality standard* or for significant contribution of pollutants to *surface waters of the State*.
 - i. 5,000 square feet or more, but less than one acre, and are in the New York City Watershed located east of the Hudson River, Appendix C Figure 1; or
 - ii. 20,000 square feet or more, but less than one acre, within the municipal boundaries of the City of New York (NYC); or
 - iii. less than 20,000 square feet which are part of a *common plan of development or sale* that will ultimately disturb 20,000 square feet or more, but less than one acre, within the municipal boundaries of NYC; or
 - iv. that creates 5,000 square feet or more of *impervious area* within the municipal boundaries of NYC.

2. *Discharges from the owner's or operator's construction activities* are/were not:
 - a. already covered by a different SPDES permit; or
 - b. covered under a different SPDES permit that was denied, terminated, or revoked; or
 - c. identified in an expired individual SPDES permit that was not renewed; or
 - d. required to obtain an individual SPDES permit or another general SPDES permit in accordance with Part VII.K.
3. If *construction activities* may adversely affect a species that is endangered or threatened, the *owner or operator* must obtain a:
 - a. permit issued pursuant to 6 NYCRR Part 182 for the project; or
 - b. letter issued by NYSDEC of non-jurisdiction pursuant to 6 NYCRR Part 182 for the project.
4. If *construction activities* have the potential to affect an *historic property*, the *owner or operator* must obtain one of the following:
 - a. documentation that the *construction activity* is not within an archeological buffer area indicated on the sensitivity map, and that the *construction activity* is not located on or immediately adjacent to a property listed or determined to be eligible for listing on the National or State Registers of Historic Places, and that there is no new permanent building on the *construction site* within the following distances from a building, structure, or object that is more than 50 years old, or if there is such a new permanent building on the *construction site* within those parameters that NYS Office of Parks, Recreation and Historic Preservation (OPRHP), a Historic Preservation Commission of a Certified Local Government, or a qualified preservation professional has determined that the building, structure, or object more than 50 years old is not historically/archeologically significant:
 - i. 1-5 acres of disturbance - 20 feet; or
 - ii. 5-20 acres of disturbance - 50 feet; or

- iii. 20+ acres of disturbance - 100 feet.
 - b. NYSDEC consultation form sent to OPRHP,¹ and copied to NYSDEC's Agency Historic Preservation Officer (APO), and
 - i. the State Environmental Quality Review Act (SEQR) Environmental Assessment Form (EAF) with a negative declaration or the Findings Statement, with documentation of OPRHP's agreement with the resolution; or
 - ii. documentation from OPRHP that the *construction activity* will result in No Impact; or
 - iii. documentation from OPRHP providing a determination of No Adverse Impact; or
 - iv. a Letter of Resolution signed by the *owner or operator*, OPRHP and the DEC APO which allows for this *construction activity* to be eligible for coverage under the general permit in terms of the State Historic Preservation Act (SHPA).
 - c. documentation of satisfactory compliance with Section 106 of the National Historic Preservation Act for a coterminous project area:
 - i. No Affect; or
 - ii. No Adverse Affect; or
 - iii. Executed Memorandum of Agreement.
 - d. documentation that SHPA Section 14.09 has been completed by NYSDEC or another state agency.
5. If *construction activities* are subject to SEQR, the *owner or operator* must obtain documentation that SEQR has been satisfied.
6. If *construction activities* are not subject to SEQR, but subject to the equivalent environmental review from another New York State or federal agency, the

¹ The consultation form can be submitted, along with other project information, through OPRHP's Cultural Resource Information System (CRIS) portal. If submitted through CRIS, paper copies of the consultation form need not be mailed.

owner or operator must obtain documentation that project review, pursuant to a process equivalent to SEQR from another New York State or federal agency, has been satisfied.

7. If *construction activities* require Uniform Procedures Act (UPA) Permits (see 6 NYCRR Part 621) from NYSDEC, or the equivalent from another New York State or federal agency, the *owner or operator* must:
 - a. obtain all such necessary permits; or
 - b. receive notification from NYSDEC pursuant to 6 NYCRR 621.3(a)(4) excepting Part I.A.7.a.
8. *Construction activities* are not eligible if they meet the following criteria in Part I.A.8.a. or b.:
 - a. For linear transportation and linear utility project types, the *construction activities*:
 - i. are within the watershed of *surface waters of the State* classified as AA or AA-S identified utilizing the Stormwater Interactive Map on NYSDEC's website; and
 - ii. are undertaken on land with no existing *impervious cover*; and
 - iii. disturb two or more acres of *steep slope*.
 - b. For all other project types, the *construction activities*:
 - i. are within the watershed of *surface waters of the State* classified as AA or AA-S identified utilizing the Stormwater Interactive Map on NYSDEC's website; and
 - ii. are undertaken on land with no existing *impervious cover*; and
 - iii. disturb one or more acres of *steep slope*.

B. Types of *Discharges* Authorized

1. The following *stormwater discharges* are authorized under this permit:
 - a. *Stormwater discharges*, including *stormwater* runoff, snowmelt runoff, and surface runoff and drainage, associated with *construction activity*, are authorized under this permit provided that appropriate *stormwater* controls are designed, installed, and maintained in accordance with Part II. and Part III.
 - b. *Stormwater discharges* from construction support activities at the *construction site* (including concrete or asphalt batch plants, equipment staging yards, material storage areas, excavated material disposal areas, and borrow areas) if the following requirements are met:
 - i. The support activity is directly related to the *construction site* required to have permit coverage for *stormwater discharges*; and
 - ii. The support activity is not a commercial operation, nor does it serve multiple unrelated *construction sites*; and
 - iii. The support activity does not continue to operate beyond the completion of the *construction activity* at the site it supports; and
 - iv. *Stormwater* controls are implemented in accordance with Part II. and Part III. for *discharges* from the support activity areas.
2. The following non-*stormwater discharges* associated with *construction activity* are authorized under this permit:
 - a. Non-*stormwater discharges* listed in 6 NYCRR 750-1.2(a)(29)(vi), with the following exception: “*Discharges* from firefighting activities are authorized only when the firefighting activities are emergencies/unplanned”; and
 - b. Non-*stormwater discharges* of waters to which other components have not been added that are used in accordance with the *SWPPP* to control dust or irrigate vegetation in stabilized areas; and
 - c. Uncontaminated *discharges* from *dewatering* operations

3. Authorized *discharges* of *stormwater* or authorized *discharges* of non-*stormwater*, commingled with a *discharge* authorized by a different SPDES permit and/or a *discharge* that does not require SPDES permit authorization, are also authorized under this permit.

C. Prohibited *Discharges*

1. Non-*stormwater discharges* prohibited under this permit include but are not limited to:
 - a. Wastewater from washout of concrete; and
 - b. Wastewater from washout and cleanout of stucco, paint, form release oils, curing compounds, and other construction materials; and
 - c. Fuels, oils, or other *pollutants* used in vehicle and equipment operation and maintenance; and
 - d. Soaps, solvents, or detergents used in vehicle and equipment washing or external building washdown; and
 - e. Toxic or hazardous substances from a spill or other release.

D. Electronic Notice of Intent (eNOI) Submittal

To receive authorization in accordance with Part I.D.3.b., the *owner or operator* must submit a complete eNOI in accordance with the requirements in Part I.D. The eNOI contains questions to: ensure eligibility requirements in Part I.A. have been met; obtain *owner or operator* contact information; obtain the total area to be disturbed and the existing/future *impervious areas* (rounded to the nearest tenth of an acre); confirm *Traditional Land Use Control MS4 Operator* jurisdiction over construction projects; satisfy the EPA eRule requirements; confirm that the Water Quality-Based Effluent Limitations in Part II. have been met; demonstrate consideration of the future risks due to climate change in accordance with Part III.A.2.; and confirm that the other *Stormwater Pollution Prevention Plan (SWPPP)* requirements in Part III. have been met.

1. An eNOI may be submitted for:
 - a. *construction activities* that are not part of a *common plan of development or sale*; or

- b. an entire *common plan of development or sale*; or
 - c. separate *phase(s)* of a *common plan of development or sale* if the following requirements are met:
 - i. the *common plan of development or sale* meets the eligibility requirements of Part I.A.5. or 6.; and
 - ii. the *phase(s)* meet(s) all other eligibility requirements of Part I.A.; and
 - iii. Part III.C. Required *SWPPP* Components by Project Type is based on the *common plan of development or sale*, not the *phase(s)*; or
 - d. *tree clearing* that is associated with, or will support, a *renewable energy* generation, transmission, or storage project that meets Part I.A.5. and 6., if the *tree clearing*:
 - i. meets all other eligibility requirements of Part I.A.; and
 - ii. will occur in NYSDEC's Regions 3-9; and
 - iii. is not within ¼ mile of a bat hibernaculum protected pursuant to 6 NYCRR Part 182; and
 - iv. will occur between November 1st and March 31st.
2. As prerequisites for submitting an eNOI, the *owner or operator* must:
- a. prepare a *SWPPP* for Part I.D.1.a., b., c., or d. in accordance with Part III.; and
 - b. based on the following criteria, upload the following signature forms signed in accordance with Part VII.J. to the eNOI prior to submission:
 - i. for all eNOIs:
 - 1. the *SWPPP* Preparer Certification Form, Appendix F, signed by the *SWPPP* preparer; and

2. the Owner/Operator Certification Form, Appendix J, signed by the *owner or operator*; and
- ii. if an eNOI includes *construction activities* within the municipal boundary(ies) of *Traditional Land Use Control MS4 Operator(s)* that will *discharge* to the *MS4(s)*:
 1. determine if the *Traditional Land Use Control MS4 Operator(s)* have review authority. A *Traditional Land Use Control MS4 Operator* does not have review authority where:
 - a. the *owner or operator* of the *construction activities* in Part I.D.2.b.ii. is the same entity as the *Traditional Land Use Control MS4 Operator* identified in Part I.D.2.b.ii.; or
 - b. there is a statute exempting the *owner or operator* from zoning review by the *Traditional Land Use Control MS4 Operator*; or
 - c. there is no such statute per Part I.D.2.b.ii.1.b., the *Traditional Land Use Control MS4 Operator* concludes, after public hearing, that it does not have zoning review authority in accordance with Legal Memorandum LU14 Updated January 2020 “Governmental Immunity from Zoning and Other Legislation”; and
 2. if the *Traditional Land Use Control MS4 Operator(s)* have review authority, submit the *SWPPP* to the *Traditional Land Use Control MS4 Operator(s)* for review and have:
 - a. if outside the municipal boundaries of NYC: the *MS4 SWPPP Acceptance Form*, Appendix G, signed by the principal executive officer or ranking elected official from the *Traditional Land Use Control MS4 Operator*, or by a duly authorized representative of that person in accordance with Part VII.J.2.; or

- b. if within the municipal boundaries of NYC: The City of New York Department of Environmental Protection (NYCDEP) SWPPP Acceptance/Approval Form, Appendix H, signed by the principal executive officer or ranking elected official from the Traditional Land Use Control MS4 Operator, or by a duly authorized representative of that person in accordance with Part VII.J.2.; and
 3. if the *Traditional Land Use Control MS4 Operator* does not have review authority, have the MS4 No Jurisdiction Form, Appendix I, signed by the principal executive officer or ranking elected official from the *Traditional Land Use Control MS4 Operator*, or by a duly authorized representative of that person in accordance with Part VII.J.2.
3. Submitting an eNOI:
- a. The *owner or operator* must submit a complete Notice of Intent electronically using a NYSDEC approved form.²
 - b. The *owner or operator* is authorized to *commence construction activity* as of the authorization date indicated in the Letter of Authorization (LOA), which is sent by NYSDEC after a complete eNOI is submitted.
 - i. If an eNOI is received for a *SWPPP* that deviates from one of the technical standards but demonstrates *equivalence* in accordance with Part III.B.1.a.ii. or Part III.B.2.b.ii., if the *SWPPP* includes *construction activities* that are not within the municipal boundary(ies) of *Traditional Land Use Control MS4 Operator(s)*, and/or if the *SWPPP* includes *construction activities* within the municipal boundary(ies) of *Traditional Land Use Control MS4 Operator(s)* that do not have review authority in accordance with Part I.D.2.b.ii.1., the authorization date indicated in the LOA will be 60 business days after the eNOI submission date.

² Unless NYSDEC grants a waiver in accordance with 40 CFR 127.15(c) or (d). All waiver requests must be submitted to Stormwater_info@dec.ny.gov or NYSDEC, Bureau of Water Permits, 625 Broadway, 4th Floor, Albany, New York 12233-3505.

- c. If *Traditional Land Use Control MS4 Operator(s)* have review authority in accordance with Part I.D.2.b.ii.2., the *owner or operator* must, within five business days of receipt of the LOA, send an electronic copy of the LOA to the *Traditional Land Use Control MS4 Operator(s)* with review authority.

E. General Requirements for Owners or Operators with Permit Coverage

1. As of the date the LOA is received, the *owner or operator* must make the eNOI, *SWPPP*, and LOA available for review and copying in accordance with the requirements in Part VII.H. When applicable, as of the date an updated LOA is received, the *owner or operator* must make the updated LOA available for review and copying in accordance with the requirements in Part VII.H.
2. The *owner or operator* must ensure compliance with all requirements of this permit and that the provisions of the *SWPPP*, including any changes made to the *SWPPP* in accordance with Part III.A.5., are properly implemented and maintained from the *commencement of construction activity* until:
 - a. all areas of disturbance have achieved *final stabilization*; and
 - b. the owner's or operator's coverage under this permit is terminated in accordance with Part V.A.5.a.
3. As of the date of the *commencement of construction activities* until Part I.E.2.a. and b. have been met, the *owner or operator* must maintain at the *construction site*, a copy of:
 - a. all documentation necessary to demonstrate eligibility with this permit; and
 - b. this permit; and
 - c. the *SWPPP*; and
 - d. the signed *SWPPP Preparer Certification Form*; and
 - e. the signed *MS4 SWPPP Acceptance Form* or signed *NYCDEP SWPPP Acceptance/Approval Form* or signed *MS4 No Jurisdiction Form* (when applicable); and
 - f. the signed *Owner/Operator Certification Form*; and

- g. the eNOI; and
 - h. the LOA; and
 - i. the LOA transmittal to the Traditional Land Use Control MS4 Operator in accordance with Part I.D.3.c. (when applicable).
4. The *owner or operator* must maintain at the *construction site*, until Part I.E.2.a. and b. have been met, as of the date the documents become final or are received, a copy of the:
- a. responsible contractor's or subcontractor's certification statement(s) in accordance with Part III.A.7.; and
 - b. inspection reports in accordance with Part IV.C.4. and 6.; and
 - c. Request to Disturb Greater Than Five Acres and the Authorization Letter to Disturb Greater Than Five Acres in accordance with Part I.E.6. (when applicable); and
 - d. Request to Continue Coverage and the Letter of Continued Coverage (LOCC) in accordance with Part I.F.2. and 4. (when applicable); and
 - e. The updated LOA(s) in accordance with Part I.E.9. (when applicable).
5. The *owner or operator* must maintain the documents in Part I.E.3. and 4. in a secure location, such as a job trailer, on-site construction office, or mailbox with lock. The secure location must be accessible during normal business hours to an individual performing a compliance inspection. The documents must be paper documents unless electronic documents are accessible to the inspector during an inspection to the same extent as a paper copy stored at the site would be. If electronic documents are kept on site, the *owner or operator* must maintain functional equipment on site available to an inspector during normal hours of operation such that an inspector may view the electronic documents in a format that can be read in a similar manner as a paper record and in a legally dependable format with no less evidentiary value than their paper equivalent.
6. The *owner or operator* must meet the following requirements prior to disturbing greater than five acres of soil at any one time:
- a. The *owner or operator* must submit a written Request to Disturb Greater Than Five Acres to:

- i. NYSDEC's Regional Office Division of Water staff based on the project location, Appendix E, if a *Traditional Land Use Control MS4 Operator* does not have review authority in accordance with Part I.D.2.b.ii.1.; or
 - ii. the *Traditional Land Use Control MS4 Operator*, if a *Traditional Land Use Control MS4 Operator* has review authority in accordance with Part I.D.2.b.ii.1.; or
 - iii. NYSDEC's Regional Office Division of Water staff based on the project location, Appendix E, and each involved *Traditional Land Use Control MS4 Operator*, if the project spans multiple municipalities with more than one *Traditional Land Use Control MS4 Operator* involved with review authority in accordance with Part I.D.2.b.ii.1.
- b. The written Request to Disturb Greater Than Five Acres must include:
- i. The SPDES permit identification number (Permit ID); and
 - ii. Full technical justification demonstrating why alternative methods of construction that would result in five acres of soil disturbance or less at any one time are not feasible; and
 - iii. The phasing plan for the project and sequencing plans for all *phases* from the *SWPPP* in accordance with Part III.B.1.d.; and
 - iv. Plans with locations and details of erosion and sediment control practices such that the heightened concern for erosion when disturbing greater than five acres at one time has been addressed; and
 - v. Acknowledgment that "the *owner or operator* will comply with the requirements in Part IV.C.2.b."; and
 - vi. Acknowledgment that "the *owner or operator* will comply with the requirements in Part II.B.1.b."
- c. The *owner or operator* must be in receipt of an Authorization Letter to Disturb Greater Than Five Acres, which will include when the

authorization begins and ends and indicate a maximum area (acres) of soil disturbance allowed at any one time, from:

- i. NYSDEC, if Part I.E.6.a.i. or iii. apply; or
 - ii. the *Traditional Land Use Control MS4 Operator*, if Part I.E.6.a.ii. applies.
7. Upon a finding of significant non-compliance with the practices described in the *SWPPP* or violation of this permit, NYSDEC may order an immediate stop to all *construction activity* at the site until the non-compliance is remedied. The stop work order must be in writing, describe the non-compliance in detail, and be sent to the *owner or operator*.
 8. If any human remains or archaeological remains are encountered during excavation, the *owner or operator* must immediately cease, or cause to cease, all *construction activity* in the area of the remains and notify the appropriate Regional Water Engineer (RWE).³ *Construction activity* shall not resume until written permission to do so has been received from the RWE.
 9. To be authorized to implement modifications to the information previously submitted in the eNOI, the *owner or operator* must:
 - a. notify NYSDEC via email at Stormwater_info@dec.ny.gov requesting access to update the eNOI; and
 - b. update the eNOI to reflect the modifications and resubmit the eNOI in accordance with Part I.D.; and
 - c. receive an updated LOA.
 10. The eNOI, *SWPPP*, LOA, updated LOAs (when applicable), and inspection reports required by this permit are public documents that the *owner or operator* must make available for review and copying by any person within five business days of the *owner or operator* receiving a written request by any such person to review these documents. Copying of documents will be done at the requester's expense.

³ The Regional Water Manager where a DEC Region does not have a RWE.

F. Permit Coverage for *Discharges* Authorized Under GP-0-20-001

When applicable:

1. Upon the effective date of this permit, an *owner or operator* of a *construction activity*, with coverage under GP-0-20-001, will have interim coverage under GP-0-25-001 for 45 calendar days starting on the effective date of GP-0-25-001 so long as the *owner or operator* maintains compliance with all applicable requirements of this permit.
2. Within 30 calendar days of the effective date of this permit, the *owner or operator*, with coverage under GP-0-20-001, must submit a complete Request to Continue Coverage electronically using a NYSDEC approved form,⁴ which contains the information identified in Part I.F.3. below, if:
 - a. the *owner or operator* continues to implement the SMP component in conformance with the technical standards in place at the time of initial project authorization; and
 - b. the *owner or operator* will comply with all non-design requirements of GP-0-25-001.
3. The Request to Continue Coverage form contains questions to: ensure eligibility requirements in Part I.A. have been met; verify *owner or operator* contact information; verify the permit identification number; verify the original eNOI submission ID, if applicable; verify Part I.F.2.a. and b.; verify the version of the Design Manual that the technical/design components conform to; and receive an updated Owner/Operator Certification Form, Appendix I.
4. The *owner or operator* has obtained continued coverage under GP-0-25-001 as of the date indicated in the LOCC, which is sent by NYSDEC after a complete Request to Continue Coverage form is submitted.
5. If the owner or operator does not submit the Request to Continue Coverage form in accordance with Part I.F.2. and 3., coverage under this permit is automatically terminated after interim coverage expires.

⁴ Unless NYSDEC grants a waiver in accordance with 40 CFR 127.15(c) or (d). All waiver requests must be submitted to Stormwater_info@dec.ny.gov or NYSDEC, Bureau of Water Permits, 625 Broadway, 4th Floor, Albany, New York 12233-3505.

G. Change of *Owner or Operator*

When applicable:

1. When property ownership changes, or when there is a change in operational control over the construction plans and specifications, the following process applies:
 - a. The new *owner or operator* must meet the applicable prerequisites for submitting an eNOI in accordance with Part I.D.2.; and
 - b. The new *owner or operator* must submit an eNOI in accordance with Part I.D.3.; and
 - c. Permit coverage for the new *owner or operator* will be effective upon receipt of the LOA in accordance with Part I.D.3.b.; and
 - d. The new *owner or operator*, upon receipt of their LOA, must provide their Permit ID to the original *owner or operator*; and
 - e. If the original *owner or operator* will no longer be the *owner or operator* of the *construction activity* identified in the original *owner's or operator's* eNOI, the original *owner or operator*, upon receipt of the new *owner's or operator's* Permit ID in accordance with Part I.G.1.d., must submit to NYSDEC a completed eNOT in accordance with Part V. that includes the name and Permit ID of the new *owner or operator*; or
 - f. If the original *owner or operator* maintains ownership of a portion of the *construction activity*, the original *owner or operator* must maintain their coverage under the permit by modifying their eNOI; modifications to the eNOI must include:
 - i. the revised area of disturbance and/or *impervious area(s)*; and
 - ii. the revised SMP information, if applicable; and
 - iii. a narrative description of what has changed; and
 - iv. the new *owner's or operator's* Permit ID for the portion of the project removed from the eNOI.

Owners or operators must follow Part I.E.9. to modify the eNOI.

Part II. Water Quality-Based Effluent Limitations

A. Maintaining Water Quality

NYSDEC expects that compliance with the requirements of this permit will control *discharges* necessary to meet applicable *water quality standards*. It shall be a violation of the *ECL* for any *discharge* to either cause or contribute to a violation of the following *water quality standards* as contained in Parts 700 through 705 of Title 6 of the Official Compilation of Codes, Rules and Regulations of the State of New York:

1. There must be no increase in turbidity that will cause a substantial visible contrast to natural conditions; and
2. There must be no increase in suspended, colloidal or settleable solids that will cause deposition or impair the waters for their best usages; and
3. There must be no residue from oil and floating substances, nor visible oil film, nor globules of grease.

If there is evidence indicating that the *stormwater discharges* authorized by this permit are causing, have the reasonable potential to cause, or are contributing to a violation of the *water quality standard*, the *owner or operator* must take appropriate corrective action in accordance with Part IV.C.5. of this permit and document in accordance with Part IV.C.4. of this permit. To address the *water quality standard* violation the *owner or operator* must include and implement appropriate controls in the *SWPPP* to correct the problem or obtain an individual SPDES permit.

If, despite compliance with the requirements of this permit, it is demonstrated that the *stormwater discharges* authorized by this permit are causing or contributing to a violation of *water quality standards*, or if NYSDEC determines that a modification of this permit is necessary to prevent a violation of *water quality standards*, the authorized *discharges* will no longer be eligible for coverage under this permit, and the *owner or operator* must obtain an individual SPDES permit prior to further *discharges* from the *construction site*.

B. Effluent Limitations Applicable to *Discharges* from *Construction Activities*

Discharges authorized by this permit must achieve, at a minimum, the effluent limitations in Part II.B.1.a., b., c., d., and e. These limitations represent the

degree of effluent reduction attainable by the application of best practicable technology currently available.

1. Erosion and Sediment Control Requirements - The *owner or operator* must select, design, install, implement, and maintain control measures to *minimize* the *discharge of pollutants* and prevent a violation of the *water quality standards*. The selection, design, installation, implementation, and maintenance of these control measures must meet the non-numeric effluent limitations in Part II.B.1.a., b., c., d., and e. and be in accordance with the New York State Standards and Specifications for Erosion and Sediment Control (BB), dated November 2016, using sound engineering judgment. Where control measures are not designed in conformance with the design criteria included in the technical standard, the *owner or operator* must include in *SWPPP* the reason(s) for the deviation, or alternative design, and provide information in the *SWPPP* demonstrating that the deviation or alternative design is *equivalent* to the technical standard.
 - a. **Erosion and Sediment Controls.** At a minimum, erosion and sediment controls must be selected, designed, installed, implemented, and maintained to:
 - i. *Minimize* soil erosion through application of runoff control and soil stabilization control measure to *minimize pollutant discharges*; and
 - ii. Control *stormwater discharges*, including both peak flow rates and total *stormwater* volume, to *minimize* channel and *streambank* erosion and scour in the immediate vicinity of the *discharge* points; and
 - iii. *Minimize* the amount of soil exposed during *construction activity*; and
 - iv. *Minimize* the disturbance of *steep slope*; and
 - v. *Minimize* sediment *discharges* from the site; and
 - vi. Provide and maintain *natural buffers* around surface waters, direct *stormwater* to vegetated areas and maximize *stormwater* infiltration to reduce *pollutant discharges*, unless *infeasible*; and
 - vii. *Minimize* soil compaction. *Minimizing* soil compaction is not required

where the intended function of a specific area of the site dictates that it be compacted; and

- viii. Unless *infeasible*, preserve a sufficient amount of topsoil to complete soil restoration and establish a uniform, dense vegetative cover; and
 - ix. *Minimize* dust. On areas of exposed soil, *minimize* dust through the appropriate application of water or other dust suppression techniques to control the generation of *pollutants* that could be discharged from the site.
- b. **Soil Stabilization.** In areas where soil disturbance activity has ceased, whether permanently or *temporarily ceased*, the application of soil stabilization measures must be initiated by the end of the next business day and completed within 14 calendar days from the date the current soil disturbance activity ceased. For *construction sites* that *directly discharge* to one of the 303(d) segments listed in Appendix D, or are located in one of the watersheds listed in Appendix C, or are authorized to disturb greater than five acres in accordance with Part I.E.5.a.viii., the application of soil stabilization measures must be initiated by the end of the next business day and completed within seven calendar days from the date the soil disturbance activity ceased.
- c. **Dewatering.** *Discharges* from *dewatering* activities, including *discharges* from *dewatering* of trenches and excavations, must be managed by appropriate control measures.
- d. **Pollution Prevention Measures.** Select, design, install, implement, and maintain effective pollution prevention measures to *minimize* the *discharge of pollutants* and prevent a violation of the *water quality standards*. At a minimum, such measures must be selected, designed, installed, implemented, and maintained to:
- i. *Minimize* the *discharge of pollutants* from equipment and vehicle washing, wheel wash water, and other wash waters. Soaps, detergents and solvents cannot be used; and
 - ii. *Minimize* the exposure of building materials, building products, construction wastes, trash, landscape materials, fertilizers, pesticides, herbicides, detergents, sanitary waste, hazardous and toxic waste, and other materials present on the site to precipitation

and to *stormwater*. *Minimization* of exposure is not required in cases where the exposure to precipitation and to *stormwater* will not result in a *discharge* of *pollutants*, or where exposure of a specific material or product poses little risk of *stormwater* contamination (such as final products and materials intended for outdoor use); and

- iii. Prevent the *discharge* of *pollutants* from spills and leaks and implement chemical spill and leak prevention and response procedures.

- e. **Surface Outlets.** When discharging from basins and impoundments, the surface outlets must be designed, constructed, and maintained in such a manner that sediment does not leave the basin or impoundment and that erosion at or below the outlet does not occur.

C. Post-Construction Stormwater Management Practice (SMP) Requirements

- 1. The *owner or operator* of a *construction activity* that requires post-construction SMPs, in accordance with Part III.C., must select, design, install, implement, and maintain the SMPs to meet the *performance criteria* in the New York State Stormwater Management Design Manual, dated July 31, 2024 (DM), using sound engineering judgment. Where SMPs are not designed in conformance with the *performance criteria* in the DM, the *owner or operator* must include in the *SWPPP* the reason(s) for the deviation or alternative design and provide information which demonstrates that the deviation or alternative design is *equivalent* to the technical standard.

- 2. The *owner or operator* of a *construction activity*, that requires SMPs in accordance with Part III.C., must design the practices to meet the applicable *sizing criteria* in Part II.C.2.a., b., c., or d.

a. Sizing Criteria for New Development

- i. Runoff Reduction Volume (RRv) and Water Quality Volume (WQv):
 - 1. Reduce the total WQv by application of RR techniques and standard SMPs with RRv capacity. The total WQv must be calculated in accordance with the criteria in Section 4.2 of the DM; or

2. Minimum RRv and Treatment of Remaining Total WQv: *Construction activities* that cannot meet the requirements in Part II.C.2.a.i.1. due to *site limitations* must direct runoff from all newly constructed *impervious areas* to a RR technique or standard SMP with RRv capacity unless *infeasible*. The specific *site limitations* that prevent the reduction of 100% of the WQv must be documented in the *SWPPP*. For each *impervious area* that is not directed to a RR technique or standard SMP with RRv capacity, the *SWPPP* must include documentation which demonstrates that all options were considered and for each option explains why it is considered *infeasible*.

In no case shall the runoff reduction achieved from the newly constructed *impervious areas* be less than the Minimum RRv as calculated using the criteria in Section 4.4 of the DM. The remaining portion of the total WQv that cannot be reduced must be treated by application of standard SMPs.

- ii. Channel Protection Volume (CPv): Provide 24 hour extended detention of the post-developed 1-year, 24-hour storm event, remaining after runoff reduction. Where a CPv control orifice is provided, the minimum orifice size must be 3 inches, with acceptable external trash rack or orifice protection. The CPv requirement does not apply when:
 1. Reduction of the entire CPv is achieved by application of runoff reduction techniques or infiltration systems; or
 2. The 1-year post-development peak *discharge* is less than or equal to 2.0 cfs without detention or velocity controls; or
 3. The site *directly discharges* into a fifth order or larger water body (stream, river, or lake), or tidal waters, where the increase in smaller flows will not impact the stream bank or channel integrity. However, the point of *discharge* must be adequately protected against scour and erosion by the increased peak *discharge*.

- iii. **Overbank Flood Control Criteria (Qp):** Requires storage to attenuate the post-development 10-year, 24-hour peak *discharge* rate (Qp) to predevelopment rates. The Qp requirement does not apply when:
 - 1. the site *directly discharges* to tidal waters or fifth order or larger streams, or
 - 2. A downstream analysis reveals that *overbank* control is not required.

- iv. **Extreme Flood Control Criteria (Qf):** Requires storage to attenuate the post-development 100-year, 24-hour peak *discharge* rate (Qf) to predevelopment rates. The Qf requirement does not apply when:
 - 1. the site *directly discharges* to tidal waters or fifth order or larger streams, or
 - 2. A downstream analysis reveals that *overbank* control is not required.

b. Sizing Criteria for New Development in Enhanced Phosphorus Removal Watersheds

- i. Runoff Reduction Volume (RRv) and Water Quality Volume (WQv):
 - 1. Reduce the WQv by application of RR techniques and standard SMPs with RRv capacity. The total WQv is the runoff volume from the 1-year, 24-hour design storm over the post-developed watershed and must be calculated in accordance with the criteria in Section 4.3 of the DM; or
 - 2. Minimum RRv and Treatment of Remaining Total WQv: *Construction activities* that cannot meet the criteria in Part II.C.2.b.i.1. due to *site limitations* must direct runoff from all newly constructed *impervious areas* to a RR technique or standard SMP with RRv capacity unless *infeasible*. The specific *site limitations* that prevent the reduction of 100% of the WQv must be documented in the *SWPPP*. For each *impervious area* that is not directed to a RR technique or standard SMP with RRv capacity, the *SWPPP* must include

documentation which demonstrates that all options were considered and for each option explains why it is considered *infeasible*.

In no case shall the runoff reduction achieved from the newly constructed *impervious areas* be less than the Minimum RRv as calculated using the criteria in Section 4.5 of the DM. The remaining portion of the total WQv that cannot be reduced must be treated by application of standard SMPs.

- ii. Channel Protection Volume (CPv): Provide 24 hour extended detention of the post-developed 1-year, 24-hour storm event, remaining after runoff reduction. Where a CPv control orifice is provided, the minimum orifice size must be 3 inches, with acceptable external trash rack or orifice protection. The CPv requirement does not apply when:
 1. Reduction of the entire CPv is achieved by application of runoff reduction techniques or infiltration systems; or
 2. The 1-year post-development peak *discharge* is less than or equal to 2.0 cfs; or
 3. The site *directly discharges* to tidal waters, or a fifth order or larger water body (stream, river, or lake) where the increase in smaller flows will not impact the stream bank or channel integrity. However, the point of *discharge* must be adequately protected against scour and erosion by the increased peak *discharge*.
- iii. *Overbank* Flood Control Criteria (Qp): Requires storage to attenuate the post-development 10-year, 24-hour peak *discharge* rate (Qp) to predevelopment rates. The Qp requirement does not apply when:
 1. the site *directly discharges* to tidal waters or fifth order or larger streams; or
 2. A downstream analysis reveals that *overbank* control is not required.

- iv. Extreme Flood Control Criteria (Qf): Requires storage to attenuate the post-development 100-year, 24-hour peak *discharge* rate (Qf) to predevelopment rates. The Qf requirement does not apply when:
 - 1. the site *directly discharges* to tidal waters or fifth order or larger streams; or
 - 2. A downstream analysis reveals that *overbank* control is not required.

c. Sizing Criteria for Redevelopment Activity

- i. Water Quality Volume (WQv): The WQv treatment objective for *redevelopment activity* must be addressed by one of the following options, as outlined in Section 9.2.1. *Redevelopment activities* located in an Enhanced Phosphorus Removal Watershed (see Part III.B.3. and Appendix C) must calculate the WQv in accordance with Section 4.3 of the DM. All other *redevelopment activities* must calculate the WQv in accordance with Section 4.2 of the DM.
 - 1. Reduce the existing *impervious cover* by a minimum of 25% of the total disturbed, *impervious area*. The Soil Restoration criteria in Section 5.1.6 of the DM must be applied to all newly created pervious areas; or
 - 2. Capture and treat 100% of the required WQv, for a minimum of 25% of the disturbed redevelopment *impervious area*, by implementation of standard SMPs or reduced by application of runoff reduction techniques; or
 - 3. Capture and treat 100% of the required WQv, for a minimum of 75% of the disturbed redevelopment *impervious area*, by implementation of a volume-based alternative SMP, as defined in Section 9.4 of the DM; or
 - 4. Capture and treat 100% of the required WQv, for a minimum of 75% of the disturbed redevelopment *impervious area*, by implementation of a flow-through alternative SMP sized to treat the peak rate of runoff from the WQv design storm; or

5. Application of a combination of 1 through 4 above that provide a weighted average of at least two of the above methods. Application of this method must be in accordance with the criteria in Section 9.2.1(A)(V) of the DM; or
6. If there is an existing SMP located on the site that captures and treats runoff from the *impervious area* that is being disturbed, the WQv treatment option selected must, at a minimum, provide treatment equal to the treatment that was being provided by the existing practice(s) if that treatment is greater than the treatment required by options 1 through 5 above.
 - ii. Channel Protection Volume (CPv) is not required if there is 0% change to hydrology that increases the *discharge* rate and volume from the project site.
 - iii. *Overbank* Flood Control (Qp) is not required if there is 0% change to hydrology that increases the *discharge* rate from the project site.
 - iv. Extreme Flood Control (Qf) is not required if there is 0% change to hydrology that increases the *discharge* rate from the project site.

d. *Sizing Criteria* for Combination of *Redevelopment Activity* and *New Development*

Construction projects, that include both *new development* and *redevelopment activity*, must use SMPs that meet the *sizing criteria* calculated as an aggregate of the *sizing criteria* in Part II.C.2.a. or b. for the *new development* portion of the project and Part II.C.2.c. for the *redevelopment activity* portion of the project.

Part III. Stormwater Pollution Prevention Plan (SWPPP)

A. General SWPPP Requirements

1. A SWPPP must be prepared and implemented by the *owner or operator* of all *construction activity* covered by this permit. All authorized *discharges* must be identified in the SWPPP. The SWPPP must document the selection, design, installation, implementation and maintenance of the control measures and

- practices that will be used to meet the effluent limitations in Part II.B. and, where applicable, the SMP requirements in Part II.C.
2. The *SWPPP* must demonstrate consideration in narrative format of the future physical risks due to climate change pursuant to the Community Risk and Resiliency Act (CRRA), 6 NYCRR Part 490, and associated guidance.
 - a. The owner or operator must consider:
 - i. the following physical risks due to climate change:
 - (i) increasing temperature; and
 - (ii) increasing precipitation; and
 - (iii) increasing variability in precipitation, including chance of drought; and
 - (iv) increasing frequency and severity of flooding; and
 - (v) rising sea level; and
 - (vi) increasing storm surge; and
 - (vii) shifting ecology.
 - ii. for each of the following:
 - (i) overall site planning; and
 - (ii) location, elevation, and sizing of:
 - a. control measures and practices; and
 - b. conveyance system(s); and
 - c. detention system(s).
 3. The *SWPPP* must describe the erosion and sediment control practices and where required, SMPs that will be used and/or constructed to reduce the *pollutants* in *stormwater discharges* and to assure compliance with the

requirements of this permit. In addition, the *SWPPP* must identify potential sources of pollution which may reasonably be expected to affect the quality of *stormwater discharges*.

4. All *SWPPPs*, that require the SMP component in accordance with Part III.B.2., must be prepared by a *qualified professional*.
5. The *owner or operator* must keep the *SWPPP* current so that, at all times, it accurately documents the erosion and sediment control practices that are being used or will be used during construction, and all SMPs that will be constructed on the site. At a minimum, the *owner or operator* must modify the *SWPPP*, including construction drawings:
 - a. whenever the current provisions prove to be ineffective in *minimizing pollutants* in *stormwater discharges* from the site; and
 - b. whenever there is a change in design, construction, or operation at the *construction site* that has or could have an effect on the *discharge of pollutants*; and
 - c. to address issues or deficiencies identified during an inspection by the *qualified inspector*, NYSDEC, or other regulatory authority; and
 - d. to document the final construction conditions in an as-built drawing.
6. NYSDEC may notify the *owner or operator* at any time that the *SWPPP* does not meet one or more of the minimum requirements of this permit. The notification must be in writing and identify the provisions of the *SWPPP* that require modification. Within fourteen (14) calendar days of such notification, or as otherwise indicated by NYSDEC, the *owner or operator* must make the required changes to the *SWPPP* and submit written notification to NYSDEC that the changes have been made. If the *owner or operator* does not respond to NYSDEC's comments in the specified time frame, NYSDEC may suspend the *owner's or operator's* coverage under this permit or require the *owner or operator* to obtain coverage under an individual SPDES permit in accordance with Part II.D.4.
7. Prior to the *commencement of construction activity*, the *owner or operator* must identify the contractor(s) and subcontractor(s) that will be responsible for installing, constructing, repairing, replacing, inspecting, and maintaining the erosion and sediment control practices included in the *SWPPP* and the

contractor(s) and subcontractor(s) that will be responsible for constructing the SMPs included in the *SWPPP*. The *owner or operator* must have each of the contractors and subcontractors identify at least one person from their company to be *trained contractor* that will be responsible for implementation of the *SWPPP*. The *owner or operator* must ensure that at least one *trained contractor* is on site daily when soil disturbance activities are being performed.

The *owner or operator* must have each of the contractors and subcontractors identified above sign a copy of the following certification statement below before the *commencement of construction activities*:

"I hereby certify under penalty of law that I understand and agree to comply with the requirements of the *SWPPP* and agree to implement any corrective actions identified by the *qualified inspector* during a site inspection. I also understand that the *owner or operator* must comply with the requirements of the most current version of the New York State Pollutant Discharge Elimination System (SPDES) Construction General Permit (CGP) for Stormwater Discharges from Construction Activities and that it is unlawful for any person to cause or contribute to a violation of *water quality standards*. Furthermore, I am aware that there are significant penalties for submitting false information, that I do not believe to be true, including the possibility of fine and imprisonment for knowing violations"

In addition to providing the certification statement above, the certification page must also identify the specific elements of the *SWPPP* that each contractor and subcontractor will be responsible for and include the name and title of the person providing the signature; the name and title of the *trained contractor* responsible for *SWPPP* implementation; the name, address and telephone number of the contracting firm; the address (or other identifying description) of the site; and the date the certification statement is signed. The *owner or operator* must attach the certification statement(s) to the copy of the *SWPPP* that is maintained at the *construction site*. If new or additional contractors are hired to implement measures identified in the *SWPPP* after the *commencement of construction activities*, they must also sign the certification statement and provide the information listed above prior to performing *construction activities*.

B. Required SWPPP Contents

1. Erosion and sediment control component - The *owner or operator* must prepare a *SWPPP* that includes erosion and sediment control practices.
 - a. Erosion and sediment control practices must be designed:
 - i. in conformance with the BB; or
 - ii. *equivalent* to the BB if deviating from Part III.B.1.a.i.
 - b. If the erosion and sediment control practices are designed in conformance with Part III.B.1.a.ii., the *SWPPP* must include a demonstration of *equivalence* to the BB.
 - c. At a minimum, the erosion and sediment control component of the *SWPPP* must include the following:
 - i. Background information about the scope of the project, including the location, type and size of project; and
 - ii. A site map/construction drawing(s) with north arrows for the project, including a general location map. At a minimum, the site map must show the total site area; all improvements; areas of disturbance; areas that will not be disturbed; existing vegetation; on-site and adjacent off-site surface water(s); floodplain/floodway boundaries; wetlands and drainage patterns that could be affected by the *construction activity*; existing and final contours; locations of different soil types with boundaries; material, waste, borrow or equipment storage areas located on adjacent properties; and location(s) of the *stormwater discharge(s)* and receiving surface water(s); and
 - iii. A description of the soil(s) present at the site, including an identification of the Hydrologic Soil Group (HSG); and
 - iv. A phasing plan for the project and sequencing plans for all *phases*, both of which must address clearing and grubbing, excavation and grading, utility and infrastructure installation, *final stabilization*,

and any other *construction activity* at the site that will result in soil disturbance.

1. The phasing plan must include:
 - a. a map delineating and labeling the limits of soil disturbance for all *phases* of a project; and
 - b. a table identifying the order and intended schedule of when each *phase* will begin and end its sequencing plan. The table must identify the total disturbed area for each *phase* at any one time and the total disturbed area for the overall project at any one time all on one timeline showing all overlapping quantities of disturbed area at any one time; and
2. A sequencing plan for a specific *phase* must include:
 - a. a table indicating the order and intended schedule of *construction activities* within a *phase*, and corresponding construction drawings with a description of the work to be performed; and
 - b. all permanent and *temporary stabilization* measures; and
- v. A description of the minimum erosion and sediment control practices to be installed or implemented for each *construction activity* that will result in soil disturbance. Include a schedule that identifies the timing of initial placement or implementation of each erosion and sediment control practice and the minimum time frames that each practice should remain in place or be implemented; and
- vi. A site map/construction drawing(s) showing the specific location(s), size(s), and length(s) of each erosion and sediment control practice; and
- vii. The dimensions, material specifications, installation details, and operation and maintenance requirements for all erosion and sediment control practices. Include the location and sizing of any

temporary sediment basins and structural practices that will be used to divert flows from exposed soils; and

- viii. A maintenance inspection schedule for the contractor(s) and subcontractor(s) identified in Part III.A.7. to ensure continuous and effective operation of the erosion and sediment control practices. The maintenance inspection schedule must be in accordance with the requirements in the BB technical standard; and
 - ix. A description of the pollution prevention measures that will be used to control litter, construction chemicals and construction debris from becoming a *pollutant* source in the *stormwater discharges*; and
 - x. A description and location of any *stormwater discharges* associated with industrial activity other than construction at the site, including, but not limited to, *stormwater discharges* from asphalt plants and concrete plants located on the *construction site*; and
 - xi. Identification of any elements of the design that are not in conformance with the design criteria in the BB technical standard. Include the reason for the deviation or alternative design and provide information which demonstrates that the deviation or alternative design is *equivalent* to the technical standard.
2. SMP component – The *owner or operator of construction activity* identified in Table 2 of Appendix B must prepare a *SWPPP* that includes SMPs.
- a. SMPs must be designed in conformance with the applicable *sizing criteria* in Part II.C.2.a., c., or d.; and
 - b. SMPs must be designed in conformance with the *performance criteria*:
 - i. in the DM; or
 - ii. *equivalent* to the DM if deviating from Part III.B.2.b.i.; or
 - iii. in the New York State Stormwater Management Design Manual, dated January 2015 (2015 Design Manual), or *equivalent* to it, if the following criteria are met:

1. The eNOI is submitted in accordance with Part I.D. before January 29, 2027 for *construction activities* that are either:
 - a. subject to governmental review and approval:
 - i. where the *owner or operator* made any application to that governmental entity prior to the effective date of this permit; and
 - ii. such application included a *SWPPP* developed using the 2015 Design Manual or *equivalent* to it; or
 - b. not subject to governmental review and approval:
 - i. where a fiscal allocation for the *construction activities* has been developed and approved by a governmental entity; and
 - ii. the *SWPPP* was developed using the 2015 Design Manual or *equivalent* to it; and
 - c. If SMPs are designed in conformance with Part III.B.2.b.ii., the *SWPPP* must include the reason(s) for the deviation or alternative design and a demonstration of *equivalence* to the DM; and
 - d. If SMPs are designed in conformance with Part III.B.2.b.iii., the *SWPPP* must include supporting information or documentation demonstrating that Part III.B.2.b.iii.1.a. or b. apply; and
 - e. The SMP component of the *SWPPP* must include the following:
 - i. Identification of all SMPs to be constructed as part of the project, including which option the SMP designs conform to, either Part III.B.2.b.i., ii., or iii. Include the dimensions, material specifications and installation details for each SMP; and
 - ii. A site map/construction drawing(s) showing the specific location and size of each SMP; and

- iii. A Stormwater Modeling and Analysis Report that includes:
 - (i) Map(s) showing pre-development conditions, including watershed/subcatchments boundaries, flow paths/routing, and design points; and
 - (ii) Map(s) showing post-development conditions, including watershed/subcatchments boundaries, flow paths/routing, design points and SMPs; and
 - (iii) Results of *stormwater* modeling (i.e. hydrology and hydraulic analysis) for the required storm events. Include supporting calculations (model runs), methodology, and a summary table that compares pre- and post-development runoff rates and volumes for the different storm events; and
 - (iv) Summary table, with supporting calculations, which demonstrates that each SMP has been designed in conformance with the *sizing criteria* included in the DM; and
 - (v) Identification of any *sizing criteria* that is not required based on the requirements included in Part II.C.; and
 - (vi) Identification of any elements of the design that are not in conformance with the *performance criteria* in the DM. Include the reason(s) for the deviation or alternative design and provide information which demonstrates that the deviation or alternative design is *equivalent* to the DM.
- iv. Soil testing results and locations (test pits, borings); and
- v. Infiltration test results, when required in accordance with Part III.B.2.a.; and
- vi. An operations and maintenance plan that includes inspection and maintenance schedules and actions to ensure continuous and effective operation of each SMP. The plan must identify the entity

that will be responsible for the long-term operation and maintenance of each practice; and

3. Enhanced Phosphorus Removal Standards - The *owner or operator* of *construction activity* identified in Table 2 of Appendix B that is located in a watershed identified in Appendix C must prepare a *SWPPP* that includes SMPs designed in conformance with the applicable *sizing criteria* in Part II.C.2.b., c., or d. and the *performance criteria* Enhanced Phosphorus Removal Standards included in the DM. At a minimum, the SMP component of the *SWPPP* must meet the requirements of Part III.B.2.

C. Required *SWPPP* Components by Project Type

Owners or operators of *construction activities*, identified in Table 1 of Appendix B, are required to prepare a *SWPPP* that only includes erosion and sediment control practices designed in accordance with Part III.B.1. *Owners or operators* of the *construction activities*, identified in Table 2 of Appendix B, must prepare a *SWPPP* that also includes SMPs designed in accordance with Part III.B.2 or 3.

For the entire area of disturbance, including the entire *common plan of development or sale* if applicable, the owner or operator must evaluate every bullet from Appendix B Table 1 and Table 2 separately. If bullets from both Table 1 and Table 2 apply, the *SWPPP* must include erosion and sediment control practices for all *construction activities* but SMPs for only those portions of the *construction activities* that fall under Table 2 bullet(s).

Part IV. Inspection and Maintenance Requirements

A. General Construction Site Inspection and Maintenance Requirements

1. The *owner or operator* must ensure that all erosion and sediment control practices (including pollution prevention measures), and all SMPs identified in the *SWPPP*, are inspected and maintained in accordance with Part IV.B. and C.

B. Contractor Maintenance Inspection Requirements

1. The *owner or operator* of each *construction activity*, identified in Tables 1 and 2 of Appendix B, must have a *trained contractor* inspect the erosion and sediment control practices and pollution prevention measures being

implemented within the active work area daily to ensure that they are being maintained in effective operating condition at all times. If deficiencies are identified, the contractor must:

- a. if the corrective action does not require engineering design:
 - i. begin implementing corrective actions within one business day; and
 - ii. complete the corrective actions within five business days; or
 - b. if the corrective action requires engineering design:
 - i. begin the engineering design process within five business days; and
 - ii. complete the corrective action in a reasonable time frame but no later than within 60 calendar days.
2. For *construction sites* where soil disturbance activities have been temporarily suspended (e.g. winter shutdown) and *temporary stabilization* measures have been applied to all disturbed areas, the *trained contractor* can stop conducting the maintenance inspections in accordance with Part IV.B.1. The *trained contractor* must begin conducting the maintenance inspections in accordance with Part IV.B.1. as soon as soil disturbance activities resume.
 3. For *construction sites* where soil disturbance activities have been shut down with partial project completion, the *trained contractor* can stop conducting the maintenance inspections in accordance with Part IV.B.1. if all areas disturbed as of the project shutdown date have achieved *final stabilization* and all SMPs required for the completed portion of the project have been constructed in conformance with the *SWPPP* and are operational.

C. Qualified Inspector Inspection Requirements

1. With the exception of the following *construction activities* identified in Tables 1 and 2 of Appendix B, a *qualified inspector* must conduct site inspections for all other *construction activities* identified in Tables 1 and 2 of Appendix B:
 - a. the construction of a single-family residential subdivision with 25% or less *impervious cover* at total site build-out that involves a soil disturbance of one (1) or more acres of land but less than or equal to five (5) acres and is

not located in one of the watersheds listed in Appendix C and not directly discharging to one of the 303(d) segments listed in Appendix D; and

- b. the construction of a single-family home that involves soil disturbances of one (1) or more acres but less than or equal to five (5) acres and is not located in one of the watersheds listed in Appendix C and not directly discharging to one of the 303(d) segments listed in Appendix D; and
 - c. construction on *agricultural property* that involves soil disturbances of one (1) or more acres but less than five (5) acres; and
 - d. *construction activities* located in the New York City Watershed located east of the Hudson River, see Appendix C Figure 1, that involve soil disturbances of 5,000 square feet or more, but less than one acre.
2. The *qualified inspector* must conduct site inspections in accordance with the following timetable:
- a. For *construction sites* where soil disturbance activities are on-going, the *qualified inspector* must conduct a site inspection at least once every seven (7) calendar days; or
 - b. For *construction sites* where soil disturbance activities are on-going and the *owner or operator* has received authorization in accordance with Part I.E.6. to disturb greater than five (5) acres of soil at any one time, the *qualified inspector* must conduct at least two (2) site inspections every seven (7) calendar days. The two (2) inspections must be separated by a minimum of two (2) full calendar days; or
 - c. For *construction sites* where soil disturbance activities have been temporarily suspended (e.g. winter shutdown) and *temporary stabilization* measures have been applied to all disturbed areas, the *qualified inspector* must conduct a site inspection at least once every thirty (30) calendar days. The *owner or operator* must notify the DOW Water (SPDES) Program contact at the Regional Office (see contact information in Appendix E) or, in areas under the jurisdiction of a *Traditional Land Use Control MS4 Operator*, the *Traditional Land Use Control MS4 Operator* (provided the *Traditional Land Use Control MS4 Operator* is not the *owner or operator* of the *construction activity*) by hard copy or email prior to reducing the inspections to this frequency and again by hard copy or email prior to re-commencing construction; or

- d. For *construction sites* where soil disturbance activities have been shut down with partial project completion, the requirement to have the *qualified inspector* conduct inspections ceases if all areas disturbed as of the project shutdown date have achieved *final stabilization* and all SMPs required for the completed portion of the project have been constructed in conformance with the *SWPPP* and are operational. The *owner or operator* must notify the DOW Water (SPDES) Program contact at the Regional Office (see contact information in Appendix E) or, in areas subject to the review authority of *Traditional Land Use Control MS4 Operator(s)* in accordance with Part I.D.2.b.ii.1., the *Traditional Land Use Control MS4 Operator(s)* (provided the *Traditional Land Use Control MS4 Operator(s)* are not the *owners or operators* of the *construction activity*) in writing prior to the shutdown and again in writing prior to resuming *construction activity*. If soil disturbance activities are not resumed within 2 years from the date of shutdown, the *owner or operator* must terminate coverage by meeting the requirements of Part V; or
 - e. For *construction sites* involving soil disturbance of one (1) or more acres that *directly discharge* to one of the 303(d) segments listed in Appendix D or is located in one of the watersheds listed in Appendix C, the *qualified inspector* must conduct at least two (2) site inspections every seven (7) calendar days. The two (2) inspections must be separated by a minimum of two (2) full calendar days.
3. At a minimum, the *qualified inspector* must inspect:
- a. all erosion and sediment control practices and pollution prevention measures to ensure integrity and effectiveness; and
 - b. all SMPs under construction to ensure that they are constructed in conformance with the *SWPPP*; and
 - c. all areas of disturbance that have not achieved *final stabilization*; and
 - d. all points of *discharge* to *surface waters of the State* located within, or immediately adjacent to, the property boundaries of the *construction site*; and
 - e. all points of *discharge* from the *construction site*.

4. The *qualified inspector* must prepare an inspection report subsequent to each and every inspection. At a minimum, the inspection report must include and/or address all of the following, for all *construction activities* except those listed in Part IV.C.1.:
 - a. Permit identification number; and
 - b. Date and time of inspection; and
 - c. Name and title of person(s) performing inspection; and
 - d. A description of the weather and soil conditions (e.g. dry, wet, saturated) at the time of the inspection, including the temperature at the time of the inspection; and
 - e. A description of the condition of the runoff at all points of *discharge* from the *construction site*. This must include identification of any *discharges* of sediment from the *construction site*. Include *discharges* from conveyance systems (i.e. pipes, culverts, ditches, etc.) and overland flow; and
 - f. A description of the condition of all *surface waters of the State* located within, or immediately adjacent to, the property boundaries of the *construction site* which receive runoff from disturbed areas. This must include identification of any *discharges* of sediment to the *surface waters of the State*; and
 - g. Identification of all erosion and sediment control practices and pollution prevention measures that need repair or maintenance; and
 - h. Identification of all erosion and sediment control practices and pollution prevention measures that were not installed properly or are not functioning as designed and need to be reinstalled or replaced; and
 - i. Description and sketch (map) of areas with active soil disturbance activity, areas that have been disturbed but are inactive at the time of the inspection, and areas that have been stabilized (temporary and/or final) since the last inspection; and
 - j. Estimates, in square feet or acres, of the following areas:

- i. Total area with active soil disturbance (not requiring either *temporary stabilization* or *final stabilization*); and
 - ii. Total area with inactive soil disturbance (requiring either *temporary stabilization* or *final stabilization*); and
 - iii. Total area that has achieved *temporary stabilization*; and
 - iv. Total area that has achieved *final stabilization*; and
 - k. Current stage of construction of all SMPs and identification of all *construction activity* on site that is not in conformance with the *SWPPP* and technical standards; and
 - l. Corrective action(s) that must be taken to install, repair, replace or maintain erosion and sediment control practices and pollution prevention measures; and to correct deficiencies identified with the construction of the SMP(s); and
 - m. Identification and status of all corrective actions that were required by previous inspection; and
 - n. Digital photographs, with date stamp, that clearly show the condition of all practices that have been identified as needing corrective actions. The *qualified inspector* must attach color copies of the digital photographs to the inspection report being maintained onsite within seven (7) calendar days of the date of the inspection. The *qualified inspector* must also take digital photographs, with date stamp, that clearly show the condition of the practice(s) after the corrective action has been completed. The *qualified inspector* must attach paper color copies of the digital photographs to the inspection report that documents the completion of the corrective action work within seven (7) calendar days of that inspection.
5. Within one business day of the completion of an inspection, the *qualified inspector* must notify the *owner or operator*, and appropriate contractor or subcontractor identified in Part III.A.7., of any corrective actions that need to be taken. The contractor or subcontractor must:
- a. if the corrective action does not require engineering design:

- i. begin implementing corrective actions within one business day; and
 - ii. complete the corrective actions within five business days; or
- b. if the corrective action requires engineering design:
- i. begin the engineering design process within five business days; and
 - ii. complete the corrective action in a reasonable time frame but no later than within 60 calendar days.
6. All inspection reports must be signed by the *qualified inspector*. In accordance with Part I.E.3., the inspection reports must be maintained on site with the *SWPPP*.

Part V. How to Terminate CGP Coverage

A. Electronic Notice of Termination (eNOT) Submittal

The eNOT contains questions to ensure requirements in Part V.A. have been met.

1. An *owner or operator* must terminate coverage when one or more of the following requirements have been met:
 - a. Total project completion:
 - i. all *construction activity* identified in the *SWPPP* has been completed; and
 - ii. all areas of disturbance have achieved *final stabilization*; and
 - iii. all temporary, structural erosion and sediment control measures have been removed; and
 - iv. all SMPs have been constructed in conformance with the *SWPPP* and are operational; and
 - v. an as-built drawing has been prepared; or

- b. Planned shutdown with partial project completion:
 - i. all soil disturbance activities have ceased; and
 - ii. all areas disturbed as of the project shutdown date have achieved *final stabilization*; and
 - iii. all temporary, structural erosion and sediment control measures have been removed; and
 - iv. all SMPs required for the completed portion of the project have been constructed in conformance with the *SWPPP* and are operational; and
 - v. an as-built drawing has been prepared; or
 - c. In accordance with Part I.G. Change of Owner or Operator; or
 - d. The *owner or operator* has obtained coverage under an alternative general SPDES permit or an individual SPDES permit.
2. For *construction activities* that require *qualified inspector* inspections in accordance with Part IV.C.1. and have met Part V.A.1.a. or b., the *owner or operator* must have the *qualified inspector* perform a final site inspection prior to submitting the eNOT. The *qualified inspector* must, by signing the “Final Stabilization” and “Post-Construction Stormwater Management Practice(s)” certification statements on the eNOT, certify that all the requirements in Part V.A.1.a. or b. have been achieved.
3. For *construction activities* that are subject to the review authority of *Traditional Land Use Control MS4 Operator(s)* in accordance with Part I.D.2.b.ii.1. and meet Part V.A.1.a. or b., the *owner or operator* must have the *Traditional Land Use Control MS4 Operator(s)* sign the “MS4 Acceptance” statement on the eNOT in accordance with the requirements in Part VII.J. A *Traditional Land Use Control MS4 Operator* official, by signing this statement, determined that it is acceptable for the *owner or operator* to submit the eNOT in accordance with the requirements of this Part. A *Traditional Land Use Control MS4 Operator* can make this determination by performing a final site inspection themselves or by accepting the *qualified inspector’s* final site inspection certification(s) when required in Part V.A.2.

4. For *construction activities* that require SMPs and meet Part V.A.1.a. or b., the *owner or operator* must, prior to submitting the eNOT, ensure one of the following:
 - a. for SMP(s) that were constructed by a private entity, but will be owned, operated, and maintained by a public entity, the SMP(s) and any right-of-way(s) needed to operate and maintain such practice(s) have been deeded to the municipality in which the practice(s) is located; or
 - b. for SMP(s) that are privately owned, but will be operated and maintained by a public entity, an executed operation and maintenance agreement is in place with the municipality that will operate and maintain the SMP(s); or
 - c. for SMP(s) that are privately owned, the *owner or operator* has a mechanism in place that requires operation and maintenance of the practice(s) in accordance with the operation and maintenance plan, such as a deed covenant in the *owner or operator's* deed of record; or
 - d. for SMP(s) that are owned by a public or private institution (e.g. school, university, hospital), government agency or authority, or public utility, the *owner or operator* has policies and procedures in place that ensure operation and maintenance of the practices in accordance with the operation and maintenance plan.
5. An *owner or operator* that has met the requirements of Part V.A.1., 2., 3., and 4. must request termination of coverage under this permit by submitting a complete Notice of Termination form electronically using a NYSDEC approved form.⁵
 - a. The owner's or operator's coverage is terminated as of the termination date indicated in the Letter of Termination (LOT), which is sent by NYSDEC after a complete eNOT is submitted.

⁵ Unless NYSDEC grants a waiver in accordance with 40 CFR 127.15(c) or (d). All waiver requests must be submitted to Stormwater_info@dec.ny.gov or NYSDEC, Bureau of Water Permits, 625 Broadway, 4th Floor, Albany, New York 12233-3505.

Part VI. Record Retention and Reporting

A. Record Retention

The *owner or operator* must retain a copy of the documents listed in Part I.E.3. and a copy of the LOT for a period of at least five years from the date that NYSDEC accepts a complete NOT submitted in accordance with Part V.

B. Reporting

Except for the eNOI, the signature forms associated with the eNOI, and the eNOT, all other written correspondence requested by NYSDEC, including individual permit applications, must be sent to the address of the appropriate DOW (SPDES) Program contact at the Regional Office listed in Appendix E.

Part VII. Standard Permit Requirements

For the purposes of this permit, examples of contractors and subcontractors include: third-party maintenance and construction contractors.

A. Duty to Comply

The *owner or operator*, and all contractors or subcontractors, must comply with all requirements of this permit. Any non-compliance with the requirements of this permit constitutes a violation of the New York State Environmental Conservation Law (ECL), and its implementing regulations, and is grounds for enforcement action. Filing of a request for termination of coverage under this permit, or a notification of planned changes or anticipated non-compliance, does not limit, diminish or stay compliance with any requirements of this permit.

B. Need to Halt or Reduce Activity Not a Defense

The necessity to halt or reduce the *construction activity* regulated by this permit, in order to maintain compliance with the requirements of this permit, must not be a defense in an enforcement action.

C. Penalties

There are substantial criminal, civil, and administrative penalties associated with violating the requirements of this permit. Fines of up to \$37,500 per day for each

violation and imprisonment for up to 15 years may be assessed depending upon the nature and degree of the offense.

D. False Statements

Any person who knowingly makes any false material statement, representation, or certification in any application, record, report, or other document filed or required to be maintained under this permit, including monitoring reports or reports of compliance or noncompliance must, upon conviction, be punished in accordance with ECL §71-1933 and or New York State Penal Law Articles 175 and 210.

E. Re-Opener Clause

Upon issuance of this permit, a determination has been made on the basis of a submitted Notice of Intent, plans, or other available information, that compliance with the specified permit requirements will reasonably protect classified water use and assure compliance with applicable *water quality standards*. Satisfaction of the requirements of this permit notwithstanding, if operation pursuant to this permit causes or contributes to a condition in contravention of State *water quality standards* or guidance values, or if NYSDEC determines that a modification is necessary to prevent impairment of the best use of the waters or to assure maintenance of *water quality standards* or compliance with other provisions of ECL Article 17 or the Clean Water Act (CWA), or any regulations adopted pursuant thereto, NYSDEC may require such modification and the Commissioner may require abatement action to be taken by the *owner or operator* and may also prohibit such operation until the modification has been implemented.

F. Duty to Mitigate

The *owner or operator*, and its contractors and subcontractors, must take all reasonable steps to *minimize* or prevent any *discharge* in violation of this permit which has a reasonable likelihood of adversely affecting human health or the environment.

G. Requiring Another General Permit or Individual SPDES Permit

NYSDEC may require any *owner or operator* authorized to *discharge* in accordance with this permit to apply for and obtain an individual SPDES permit or apply for authorization to *discharge* in accordance with another general SPDES permit.

1. Cases where an individual SPDES permit or authorization to discharge in accordance with another general SPDES permit may be required include, but is not limited to the following:

Part VII.G.1.a.

- a. the *owner or operator* is not in compliance with the conditions of this permit or does not meet the requirements for coverage under this permit; and
 - b. a change has occurred in the availability of demonstrated technology or practices for the control or abatement of *pollutants* applicable to the *point source*; and
 - c. new effluent limitation guidelines or new source performance standards are promulgated that are applicable to *point sources* authorized to *discharge* in accordance with this permit; and
 - d. existing effluent limitation guidelines or new source performance standards that are applicable to *point sources* authorized to *discharge* in accordance with this permit are modified; and
 - e. a water quality management plan containing requirements applicable to such *point sources* is approved by NYSDEC; and
 - f. circumstances have changed since the time of the request to be covered so that the *owner or operator* is no longer appropriately controlled under this permit, or either a temporary or permanent reduction or elimination of the authorized *discharge* is necessary; and
 - g. the *discharge* is in violation of section 17-0501 of the ECL; and
 - h. the *discharge(s)* is a significant contributor of *pollutants*. In making this determination, NYSDEC may consider the following factors:
 - i. the location of the *discharge(s)* with respect to *surface waters of the State*; and
 - ii. the size of the *discharge(s)*; and
 - iii. the quantity and nature of the *pollutants discharged* to *surface waters of the State*; and
 - iv. other relevant factors including compliance with other provisions of ECL Article 17, or the CWA.
2. When NYSDEC requires any *owner or operator* authorized by this permit to apply for an individual SPDES permit as provided for in this subdivision, it must notify the *owner or operator* in writing that a permit application is required. This notice must include a brief statement of the reasons for this decision, an application

form, a statement setting a time for the *owner or operator* to file the application for an individual SPDES permit, and a deadline, not sooner than 180 days from the *owner's or operator's* receipt of the notification letter, whereby the authorization to *discharge* under this permit must be terminated. NYSDEC may grant additional time upon demonstration, to the satisfaction of the RWE,⁶ that additional time to apply for an alternative authorization is necessary or where NYSDEC has not provided a permit determination in accordance with 6 NYCRR Part 621.

3. When an individual SPDES permit is issued to an *owner or operator* authorized to *discharge* under this permit for the same *discharge(s)*, this permit authorization for *construction activities* authorized under the individual SPDES permit is automatically terminated on the effective date of the individual SPDES permit unless termination is earlier in accordance with 6 NYCRR Part 750.

H. Duty to Provide Information

The *owner or operator* must furnish to NYSDEC, within five business days, unless otherwise set forth by NYSDEC, any information that NYSDEC may request to determine whether cause exists to determine compliance with this permit or to determine whether cause exists for requiring an individual SPDES permit in accordance with 6 NYCRR 750-1.21(e) (see Part VII.G. Requiring Another General Permit or Individual Permit).

The *owner or operator* must make available to NYSDEC, for inspection and copying, or furnish to NYSDEC within 25 business days of receipt of a NYSDEC request for such information, any information retained in accordance with this permit.

Except for Part I.D.4. and 5. and Part I.G., the following applies: where the *owner or operator* becomes aware that it failed to submit any relevant facts on the Notice of Intent, or submitted incorrect information in a Notice of Intent or in any report to NYSDEC, the *owner or operator* must submit such facts or corrected information to NYSDEC within five business days.

I. Extension

In the event a new permit is not issued and effective prior to the expiration of this permit, and this permit is extended pursuant to the State Administrative Procedure Act and 6 NYCRR Part 621, then the *owner or operator* with coverage under this permit may continue to operate and *discharge* in accordance with the requirements of this permit until a new permit is issued and effective.

⁶ The Regional Water Manager where a DEC Region does not have a RWE.

J. Signatories and Certification

The Notice of Intent, Notice of Termination, and reports required by this permit must be signed as provided in 40 CFR §122.22.

1. All Notices of Intent and Notices of Termination must be signed as follows:

a. For a corporation. By a responsible corporate officer. For the purpose of this section, a responsible corporate officer means:

(i) a president, secretary, treasurer, or vice-president of the corporation in charge of a principal business function, or any other person who performs similar policy- or decision-making functions for the corporation; or

(ii) the manager of one or more manufacturing, production or operating facilities, provided, the manager is authorized to make management decisions which govern the operation of the regulated facility including having the explicit or implicit duty of making major capital investment recommendations, and initiating and directing other comprehensive measures to assure long term environmental compliance with environmental laws and regulations; the manager can ensure that the necessary systems are established or actions taken to gather complete and accurate information for Notice of Intent or Notice of Termination requirements; and where authority to sign documents has been assigned or delegated to the manager in accordance with corporate procedures.

Note: NYSDEC does not require specific assignments or delegations of authority to responsible corporate officers identified in 40 CFR §122.22(a)(1)(i). NYSDEC will presume that these responsible corporate officers have the requisite authority to sign the Notice of Intent or Notice of Termination unless the corporation has notified NYSDEC to the contrary. Corporate procedures governing authority to sign a Notice of Intent or Notice of Termination may provide for assignment or delegation to applicable corporate positions under 40 CFR §122.22(a)(1)(ii) rather than to specific individuals.

b. For a partnership or sole proprietorship. By a general partner or the proprietor, respectively.

- c. For a municipality, State, Federal, or other public agency. By either a principal executive officer or ranking elected official. For purposes of this section, a principal executive officer of a Federal agency includes:
 1. the chief executive officer of the agency; or
 2. a senior executive officer having responsibility for the overall operations of a principal geographic unit of the agency (e.g., Regional Administrators of EPA).
2. All reports required by this permit, and other information requested by NYSDEC, must be signed by a person described in Part VII.J.1., or by a duly authorized representative of that person. A person is a duly authorized representative only if:
 - a. The authorization is made in writing by a person described in Part VII.J.1. or using the Duly Authorized Form, found on the DEC website; and
 - b. The authorization specifies either an individual or a position having responsibility for the overall operation of the regulated facility or activity, position of equivalent responsibility, or an individual or position having overall responsibility for environmental matters for the company. (A duly authorized representative may thus be either a named individual or any individual occupying a named position); and
 - c. The written authorization is submitted to NYSDEC.
3. Changes to authorization. If an authorization under Part VII.J.2. is no longer accurate because a different individual or position has responsibility for the overall operation of the *construction activity*, a new authorization satisfying the requirements of Part VII.J.2. must be submitted to NYSDEC prior to or together with any reports, information, or applications to be signed by an authorized representative.
4. Certification. Any person signing a document under Part VII.J.1. or 2. must make the following certification:

I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who

manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

5. Electronic reporting. If documents described in Part VII.J.1. or 2. are submitted electronically by or on behalf of the *construction activity* with coverage under this permit, any person providing the electronic signature for such documents must meet all relevant requirements of this section, and must ensure that all of the relevant requirements of 40 CFR Part 3 (including, in all cases, subpart D to Part 3) (Cross-Media Electronic Reporting) and 40 CFR Part 127 (NPDES Electronic Reporting Requirements) are met for that submission.

K. Inspection and Entry

The *owner or operator* must allow NYSDEC, the USEPA Regional Administrator, the applicable county health department, or any authorized representatives of those entities, or, in the case of a *construction site* which *discharges* through an *MS4*, an authorized representative of the *MS4* receiving the *discharge*, upon the presentation of credentials and other documents as may be required by law, to:

1. enter upon the *owner's or operator's* premises where a regulated facility or activity is located or conducted or where records must be kept under the requirements of this permit; and
2. have access to and copy at reasonable times, any records that must be kept under the requirements of this permit, including records required to be maintained for purposes of operation and maintenance; and
3. inspect at reasonable times any facilities, equipment (including monitoring and control equipment), practices or operations regulated or required under this permit; and
4. sample or monitor at reasonable times, for the purposes of assuring general SPDES permit compliance or as otherwise authorized by the CWA or ECL, any substances or parameters at any location; and
5. enter upon the property of any contributor to the regulated facility or activity under authority of the *owner or operator*.

L. Confidentiality of Information

The following must not be held confidential: this permit, the fact sheet for this permit, the name and address of any *owner or operator*, effluent data, the Notice of Intent, and information regarding the need to obtain an individual permit or an alternative general SPDES permit. This includes information submitted on forms themselves and any attachments used to supply information required by the forms (except information submitted on usage of substances). Upon the request of the *owner or operator*, NYSDEC must make determinations of confidentiality in accordance with 6 NYCRR Part 616, except as set forth in the previous sentence. Any information accorded confidential status must be disclosed to the Regional Administrator upon his or her written request. Prior to disclosing such information to the Regional Administrator, NYSDEC will notify the Regional Administrator of the confidential status of such information.

M. Other Permits May Be Required

Nothing in this permit relieves the *owner or operator* from a requirement to obtain any other permits required by law.

N. NYSDEC Orders or Civil Decrees/Judgments

The issuance of this permit by the NYSDEC, and the coverage under this permit by the *owner or operator*, does not supersede, revoke, or rescind any existing order on consent or civil Decree/Judgment, or modification to any such documents or to any order issued by the Commissioner, or any of the terms, conditions, or requirements contained in such order or modification therefore, unless expressly noted.

O. Property Rights

Coverage under this permit does not convey any property rights in either real or personal property, or any exclusive privileges, nor does it authorize any injury to private property or any invasion of personal rights, nor any infringement of Federal, State, or local laws or regulations, nor does it obviate the necessity of obtaining the assent of any other jurisdiction as required by law for the *discharge* authorized.

P. Compliance with Interstate Standards

If the *construction activity* covered by this permit originates within the jurisdiction of an interstate water pollution control agency, then the *construction activity* must also comply with any applicable effluent standards or *water quality standards* promulgated by that interstate agency and as set forth in this permit for such *construction activities*.

Q. Oil and Hazardous Substance Liability

Coverage under this permit does not affect the imposition of responsibilities upon, or the institution of any legal action against, the *owner or operator* under section 311 of the CWA, which must be in conformance with regulations promulgated pursuant to section 311 governing the applicability of section 311 of the CWA to *discharges* from facilities with *NPDES* permits, nor must such issuance preclude the institution of any legal action or relieve the *owner or operator* from any responsibilities, liabilities, or penalties to which the *owner or operator* is or may be subject pursuant to the Comprehensive Environmental Response, Compensation and Liability Act of 1980, 42 U.S.C. section 9601 et seq. (CERCLA).

R. Severability

The provisions of this permit are severable, and if any provision of this permit, or the application of any provision of this permit to any circumstance, is held invalid, the application of such provision to other circumstances, and the remainder of this permit, must not be affected thereby.

S. NYSDEC Approved Forms

The *owner or operator* must provide all relevant information that is requested by NYSDEC, and required by this permit, on all NYSDEC approved forms.

APPENDIX A – Abbreviations and Definitions

Abbreviations

APO – Agency Preservation Officer
BB – New York State Standards and Specifications for Erosion and Sediment Control (Blue Book), dated November 2016
BMP – Best Management Practice
CPESC – Certified Professional in Erosion and Sediment Control
CPv – Channel Protection Volume
CWA – Clean Water Act (or the Federal Water Pollution Control Act, 33 U.S.C. §1251 et seq)
DM – New York State Stormwater Management Design Manual (Design Manual), dated July 31, 2024
DOW – Division of Water
EAF – Environmental Assessment Form
ECL – chapter 43-B of the Consolidated Laws of the State of New York, entitled the Environmental Conservation Law
EPA – U.S. Environmental Protection Agency
HSG – Hydrologic Soil Group
MS4 – Municipal Separate Storm Sewer System
NOI – Notice of Intent
NOT – Notice of Termination
NPDES – National Pollutant Discharge Elimination System
NYC – The City of New York
NYCDEP – The City of New York Department of Environmental Protection
NYSDEC – The New York State Department of Environmental Conservation
OPRHP – Office of Parks, Recreation and Historic Places
Qf – Extreme Flood
Qp – Overbank Flood
RR – Runoff Reduction
RRv – Runoff Reduction Volume
RWE – Regional Water Engineer
SEQR – State Environmental Quality Review Act
SHPA – State Historic Preservation Act
SMP – Post-Construction Stormwater Management Practice
SPDES – State Pollutant Discharge Elimination System
SWPPP – Stormwater Pollution Prevention Plan
TMDL – Total Maximum Daily Load
UPA – Uniform Procedures Act
USDA – United States Department of Agriculture
WQv – Water Quality Volume

Definitions

All definitions in this section are solely for the purposes of this permit. If a word is not italicized in the permit, use its common definition.

Agricultural Building – a structure designed and constructed to house farm implements, hay, grain, poultry, livestock or other horticultural products; excluding any structure designed, constructed or used, in whole or in part, for human habitation, as a place of employment where agricultural products are processed, treated or packaged, or as a place used by the public.

Agricultural Property – the land for construction of a barn, *agricultural building*, silo, stockyard, pen or other structural practices identified in Table II in the “Agricultural Best Management Practice Systems Catalogue” (dated June 2023).

Alter Hydrology from Pre- to Post-Development Conditions – the post-development peak flow rate(s) has increased by more than 5% of the pre-developed condition for the design storm of interest (e.g. 10 yr and 100 yr).

Combined Sewer System – a sewer system which conveys sewage and *stormwater* through a single pipe system to a publicly owned treatment works.

Commence (Commencement of) Construction Activities – the initial disturbance of soils associated with clearing, grading or excavation activities; or other construction related activities that disturb or expose soils such as demolition, stockpiling of fill material, and the initial installation of erosion and sediment control practices required in the *SWPPP*. See definition for “*Construction Activity(ies)*” also.

Common Plan of Development or Sale – a contiguous area where multiple separate and distinct *construction activities* are occurring, or may occur, under one plan. The “common plan” of development or sale is broadly defined as any announcement or piece of documentation (including a sign, public notice or hearing, marketing plan, advertisement, drawing, permit application, State Environmental Quality Review Act (SEQR) environmental assessment form or other documents, zoning request, computer design, etc.) or physical demarcation (including boundary signs, lot stakes, surveyor markings, etc.) indicating *construction activities* may occur on a specific plot. A *common plan of development or sale* is comprised of two or more *phases*.

Common plan of development or sale does not include separate and distinct *construction activities* that are occurring, or may occur, under one plan that are at least 1/4 mile apart provided any interconnecting road, pipeline or utility project that is part of the same “common plan” is not concurrently being disturbed.

Construction Activity(ies) – identified within 40 CFR 122.26(b)(14)(x), 122.26(b)(15)(i), and 122.26(b)(15)(ii), any clearing, grading, excavation, filling, demolition or stockpiling activities that result in soil disturbance. Clearing activities can include, but are not limited to, mechanized logging equipment operation, the cutting and skidding of trees, stump removal and/or brush root removal.

Construction activity does not include routine maintenance that is performed to maintain the original line and grade, hydraulic capacity, or original purpose of a facility, which is excluded from the calculation of the soil disturbance for a project. Routine maintenance includes, but is not limited to:

- Re-grading of gravel roads or parking lots; and
- Cleaning and shaping of existing roadside ditches and culverts that maintains the approximate original line and grade, and maintains or improves the hydraulic capacity of the ditch; and
- Replacement of existing culverts that maintains the approximate original line and grade, and maintains or improves the hydraulic capacity of a ditch; and
- Replacement of existing bridges that maintains the approximate original line and grade, and maintains or improves the hydraulic capacity beneath the bridges; and
- Cleaning and shaping of existing roadside ditches that does not maintain the approximate original grade, hydraulic capacity and purpose of the ditch if the changes to the line and grade, hydraulic capacity or purpose of the ditch are installed to improve water quality and quantity controls (e.g. installing grass lined ditch); and
- Placement of aggregate shoulder backing that stabilizes the transition between the road shoulder and the ditch or *embankment*; and
- Full depth milling and filling of existing asphalt pavements, replacement of concrete pavement slabs, and similar work that does not expose soil or disturb the bottom six (6) inches of subbase material; and
- Long-term use of equipment storage areas at or near highway maintenance facilities; and
- Removal of sediment from the edge of the highway to restore a previously existing sheet-flow drainage connection from the highway surface to the highway ditch or *embankment*; and
- Existing use of Canal Corp owned upland disposal sites for the canal, and
- Replacement of curbs, gutters, sidewalks and guide rail posts; and
- Maintenance of ski trails including brush hog use and mowing; and
- Above ground snowmaking pipe replacement; and
- Replacement of existing utility poles; etc.

Construction Site – the land area where *construction activity(ies)* will occur. See also the definitions for “*Commence (Commencement of) Construction Activities*” and “*Common Plan of Development or Sale.*”

Dewatering – the act of draining rainwater and/or groundwater from building foundations, vaults or excavations/trenches.

Directly Discharge(s)(ing) (to a specific surface waterbody) – runoff flows from a *construction site* by overland flow and the first point of *discharge* is the specific surface waterbody, or runoff flows from a *construction site* to a separate storm sewer system and the first point of *discharge* from the separate storm sewer system is the specific surface waterbody.

Discharge(s)(d) – any addition of any *pollutant* to waters of the State through an outlet or *point source*.

Embankment – an earthen or rock slope that supports a road/highway.

Equivalent (Equivalence) – the practice or measure meets all the performance, longevity, maintenance, and safety objectives of the technical standard and will provide an equal or greater degree of water quality protection.

Final Stabilization – all soil disturbance activities have ceased and a uniform, perennial vegetative cover with a density of eighty (80) percent over the entire pervious surface has been established; or other *equivalent* stabilization measures, such as permanent landscape mulches, rock rip-rap or washed/crushed stone have been applied on all disturbed areas that are not covered by permanent structures, concrete or pavement.

Historic Property – any building, structure, site, object or district that is listed on the State or National Registers of Historic Places or is determined to be eligible for listing on the State or National Registers of Historic Places.

Impervious Area (Cover) – all impermeable surfaces that cannot effectively infiltrate rainfall. This includes paved, concrete and compacted gravel surfaces (i.e. parking lots, driveways, roads, runways and sidewalks); building rooftops and miscellaneous impermeable structures such as patios, pools, and sheds.

Infeasible – not technologically possible, or not economically practicable and achievable considering best industry practices.

Minimize(ing)(ation) – reduce and/or eliminate to the extent achievable using control measures (including best management practices) that are technologically available and economically practicable and achievable in light of best industry practices.

Municipal Separate Storm Sewer System (MS4) - a conveyance or system of conveyances (including roads with drainage systems, municipal streets, catch basins, curbs, gutters, ditches, man-made channels, or storm drains):

1. owned or operated by a State, city, town, village, borough, county, parish, district, association, or other public body (created by or pursuant to State law) having jurisdiction over disposal of sewage, industrial wastes, *stormwater*, or other wastes, including special districts under State law such as a sewer district, flood control district or drainage district, or similar entity, or an Indian tribe or an authorized Indian tribal organization, or a designated and approved management agency under section 208 of the CWA, that *discharges to surface waters of the State*; and
2. designed or used for collecting or conveying *stormwater*; and
3. which is not a *combined sewer system*; and
4. which is not part of a Publicly Owned Treatment Works (POTW) as defined at 40 CFR 122.2.

Natural Buffer(s) – an undisturbed area with natural cover running along a surface water (e.g. wetland, stream, river, lake, etc.).

New Development – any land disturbance that does not meet the definition of *Redevelopment Activity* included in this appendix.

New York State Erosion and Sediment Control Certificate Program – a certificate program that establishes and maintains a process to identify and recognize individuals who are capable of developing, designing, inspecting and maintaining erosion and sediment control plans on projects that disturb soils in New York State. The certificate program is administered by the New York State Conservation District Employees Association.

Nonpoint Source(s) – any source of water pollution or *pollutants* which is not a discrete conveyance or *point source* permitted pursuant to Title 7 or 8 of Article 17 of the Environmental Conservation Law (see ECL Section 17-1403).

Overbank – flow events that exceed the capacity of the stream channel and spill out into the adjacent floodplain.

Owner or Operator – the person, persons, or legal entity which owns or leases the property on which the *construction activity* is occurring; an entity that has operational control over the construction plans and specifications, including the ability to make modifications to the plans and specifications; and/or an entity that has day-to-day operational control of those activities at a project that are necessary to ensure compliance with the permit requirements.

Performance Criteria – the six performance criteria for each group of SMPs in Chapters 5 and 6 of the technical standard, New York State Stormwater Management Design Manual (DM), dated July 31, 2024. These include feasibility, conveyance, pretreatment, treatment, landscaping, and maintenance. It does not include the *Sizing Criteria* (i.e. WQv, RRV, CPv, Qp and Qf) in Part I.C.2. of the permit.

Phase – a defined area in which *construction activities* are occurring or will occur separate from other defined area(s).

Point Source – any discernible, confined, and discrete conveyance, including but not limited to any pipe, ditch, channel, tunnel, conduit, well, discrete fissure, container, rolling stock, concentrated animal feeding operation, vessel or other floating craft, or landfill leachate collection system from which *pollutants* are or may be *discharged*.

Pollutant(s) – dredged spoil, filter backwash, solid waste, incinerator residue, sewage, garbage, sewage sludge, munitions, chemical wastes, biological materials, radioactive materials, heat, wrecked or discarded equipment, rock, sand and industrial, municipal, agricultural waste and ballast *discharged* into water; which may cause or might reasonably be expected to cause pollution of the waters of the state in contravention of the standards or guidance values adopted as provided in 6 NYCRR Parts 700 et seq.

Qualified Inspector – a person that is knowledgeable in the principles and practices of erosion and sediment control, such as a licensed Professional Engineer, Certified Professional in Erosion and Sediment Control (CPESC), Registered Landscape Architect, *New York State Erosion and Sediment Control Certificate Program* holder or other NYSDEC endorsed individual(s).

It can also mean someone working under the direct supervision of, and at the same company as, the licensed Professional Engineer or Registered Landscape Architect, provided that person has training in the principles and practices of erosion and sediment control. Training in the principles and practices of erosion and sediment control means that the individual working under the direct supervision of the licensed Professional Engineer or Registered Landscape Architect has received four (4) hours of NYSDEC endorsed training in proper erosion and sediment control principles from a Soil and Water Conservation District, or other NYSDEC endorsed entity. After receiving the initial training, the individual working under the direct supervision of the licensed Professional Engineer or Registered Landscape Architect shall receive four (4) hours of training every three (3) years.

It can also mean a person that meets the *Qualified Professional* qualifications in addition to the *Qualified Inspector* qualifications.

Note: Inspections of any SMPs that include structural components, such as a dam for an impoundment, shall be performed by a licensed Professional Engineer.

Qualified Professional – a person that is knowledgeable in the principles and practices of *stormwater* management and treatment, such as a licensed Professional Engineer, Registered Landscape Architect or other NYSDEC endorsed individual(s). Individuals preparing *SWPPPs* that require the SMP component must have an understanding of the principles of hydrology, water quality management practice design, water quantity control design, and, in many cases, the principles of hydraulics. All components of the *SWPPP* that involve the practice of engineering, as defined by the NYS Education Law (see Article 145), shall be prepared by, or under the direct supervision of, a professional engineer licensed to practice in the State of New York.

Redevelopment Activity(ies) – the disturbance and reconstruction of existing *impervious area*, including *impervious areas* that were removed from a project site within five (5) years of preliminary project plan submission to the local government (i.e. site plan, subdivision, etc.).

Renewable Energy – electricity or thermal energy generated by renewable energy systems through use of the following technologies: solar thermal, photovoltaics, on land and offshore wind, hydroelectric, geothermal electric, geothermal ground source heat, tidal energy, wave energy, ocean thermal, and fuel cells which do not utilize a fossil fuel resource in the process of generating electricity.

Site Limitations – site conditions that prevent the use of an infiltration technique and or infiltration of the total WQv. Typical *site limitations* include: seasonal high groundwater, shallow depth to bedrock, and soils with an infiltration rate less than 0.5 inches/hour. The existence of *site limitations* shall be confirmed and documented using actual field testing (i.e. test pits, soil borings, and infiltration test) or using information from the most current United States Department of Agriculture (USDA) Soil Survey for the County where the project is located.

Sizing Criteria – the criteria included in Part I.C.2 of the permit that are used to size SMPs. The criteria include; Water Quality Volume (WQv), Runoff Reduction Volume (RRv), Channel Protection Volume (Cpv), *Overbank Flood* (Qp), and Extreme Flood (Qf).

Steep Slope – land area designated on the current United States Department of Agriculture (USDA) Soil Survey as Soil Slope Phase D, (provided the map unit name or description is inclusive of slopes greater than 25%), or Soil Slope Phase E or F, (regardless of the map unit name), or a combination of the three designations.

Stormwater – that portion of precipitation that, once having fallen to the ground, is in excess of the evaporative or infiltrative capacity of soils, or the retentive capacity of surface features, which flows or will flow off the land by surface runoff to waters of the State.

Streambank – the terrain alongside the bed of a creek or stream. The bank consists of the sides of the channel, between which the flow is confined.

Stormwater Pollution Prevention Plan (SWPPP) – a project specific report, including construction drawings, that among other things: describes the *construction activity(ies)*, identifies the potential sources of pollution at the *construction site*; describes and shows the *stormwater* controls that will be used to control the *pollutants* (i.e. erosion and sediment controls; for many projects, includes SMPs); and identifies procedures the *owner or operator* will implement to comply with the requirements of the permit. See Part III of the permit for a complete description of the information that must be included in the *SWPPP*.

Surface Waters of the State – shall be construed to include lakes, bays, sounds, ponds, impounding reservoirs, springs, rivers, streams, creeks, estuaries, marshes, inlets, canals, the Atlantic ocean within the territorial seas of the state of New York and all other bodies of surface water, natural or artificial, inland or coastal, fresh or salt, public or private (except those private waters that do not combine or effect a junction with natural surface waters), which are wholly or partially within or bordering the state or within its jurisdiction. Waters of the state are further defined in 6 NYCRR Parts 800 to 941.

Temporarily Ceased – an existing disturbed area will not be disturbed again within 14 calendar days of the previous soil disturbance.

Temporary Stabilization – exposed soil has been covered with material(s) as set forth in the technical standard, New York Standards and Specifications for Erosion and Sediment Control, to prevent the exposed soil from eroding. The materials can include, but are not limited to, mulch, seed and mulch, and erosion control mats (e.g. jute twisted yarn, excelsior wood fiber mats).

Total Maximum Daily Load (TMDL) – the sum of the allowable loads of a single *pollutant* from all contributing point and *nonpoint sources*. It is a calculation of the maximum amount of a *pollutant* that a *waterbody* can receive and still meet *water quality standards*, and an allocation of that amount to the *pollutant's* sources. A TMDL stipulates Waste Load Allocations (WLA) for *point source discharges*, Load Allocations (LA) for *nonpoint sources*, and a margin of safety (MOS).

Traditional Land Use Control MS4 Operator – a city, town, or village with land use control authority that is authorized to *discharge* under New York State DEC's SPDES General Permit For Stormwater Discharges from Municipal Separate Stormwater Sewer Systems (MS4s) or the City of New York's Individual SPDES Permit for their Municipal Separate Storm Sewer Systems (NY-0287890).

Trained Contractor – an employee from the contracting (construction) company, identified in Part III.A.7., that has received four (4) hours of NYSDEC endorsed training

in proper erosion and sediment control principles from a Soil and Water Conservation District, or other NYSDEC endorsed entity. After receiving the initial training, the *trained contractor* shall receive four (4) hours of training every three (3) years.

It can also mean an employee from the contracting (construction) company, identified in Part III.A.7., that meets the *qualified inspector* qualifications (e.g. licensed Professional Engineer, Certified Professional in Erosion and Sediment Control (CPESC), Registered Landscape Architect, *New York State Erosion and Sediment Control Certificate Program* holder, or someone working under the direct supervision of, and at the same company as, the licensed Professional Engineer or Registered Landscape Architect, provided they have received four (4) hours of NYSDEC endorsed training in proper erosion and sediment control principles from a Soil and Water Conservation District, or other NYSDEC endorsed entity).

The *trained contractor* is responsible for the day-to-day implementation of the *SWPPP*.

Tree Clearing – *construction activities* limited to felling and removal of trees.

Tree clearing does not include hand felling and leaving the trees in place with no support from mechanized equipment, which is not considered *construction activity* requiring coverage under this permit.

Water Quality Standard – such measures of purity or quality for any waters in relation to their reasonable and necessary use as promulgated in 6 NYCRR Part 700 et seq.

APPENDIX B – Required SWPPP Components by Project Type

Table 1

CONSTRUCTION ACTIVITIES THAT REQUIRE THE PREPARATION OF A SWPPP THAT ONLY INCLUDES EROSION AND SEDIMENT CONTROLS

The following *construction activities* that involve soil disturbances of one (1) or more acres of land, but less than five (5) acres:

- Single-family home not located in one of the watersheds listed in Appendix C and not directly discharging to one of the 303(d) segments listed in Appendix D
- Single-family residential subdivisions with 25% or less *impervious cover* at total site build-out and not located in one of the watersheds listed in Appendix C and not directly discharging to one of the 303(d) segments listed in Appendix D
- Construction of a barn or other *agricultural building*, silo, stock yard or pen.
- Structural agricultural conservation practices as identified in Table II in the “Agricultural Best Management Practice Systems Catalogue” (dated June 2023) that include construction or reconstruction of *impervious area* or *alter hydrology from pre- to post-development* conditions.

The following *construction activities* that involve soil disturbances between five thousand (5000) square feet and one (1) acre of land:

- All construction activities located in the New York City Watershed located east of the Hudson River, see Appendix C Figure 1, that involve soil disturbances between five thousand (5,000) square feet and one (1) acre of land.

Within the municipal boundaries of NYC:

- Stand-alone road reconstruction, where the total soil disturbance from only that road construction, is less than one (1) acre of land.

The following *construction activities*:

- Installation of underground linear utilities; such as gas lines, fiber-optic cable, cable TV, electric, telephone, sewer mains, and water mains
- Environmental enhancement projects, such as wetland mitigation, *stormwater* retrofits, stream restoration, and resiliency projects that reconstruct shoreline areas to address sea level rise
- Pond construction
- Linear bike paths running through areas with vegetative cover, including bike paths surfaced with an *impervious cover*
- Cross-country ski trails, walking/hiking trails, and mountain biking trails, including a de minimis parking lot (maximum 10 spaces total, sized for passenger cars) with 35 feet minimum preservation of undisturbed area downgradient from the parking lot
- Dam rehabilitation (the structure of the dam itself)
- Sidewalks, bike paths, or walking paths, surfaced with an *impervious cover*, that are not part of residential, commercial, or institutional development;
- Sidewalks, bike paths, or walking paths, surfaced with an *impervious cover*, that include incidental shoulder or curb work along an existing highway to support construction of the sidewalk, bike path, or walking path.

Table 1 (Continued)
CONSTRUCTION ACTIVITIES THAT REQUIRE THE PREPARATION OF A SWPPP
THAT ONLY INCLUDES EROSION AND SEDIMENT CONTROLS

The following *construction activities*:

- Slope stabilization
- Slope flattening that changes the grade of the site, but does not significantly change the runoff characteristics
- Spoil areas that will be covered with vegetation
- Vegetated open space (i.e. recreational parks, lawns, meadows, fields, downhill ski trails) that do not *alter hydrology from pre- to post-development* conditions
- Athletic fields (natural grass) that do not include the construction or reconstruction of *impervious area* and do not *alter hydrology from pre- to post-development* conditions
- Demolition where vegetation will be established, and no *redevelopment activity* is planned¹
- Installation or replacement of either an overhead electric transmission line or a ski lift tower that does not include the construction of permanent access roads or parking areas surfaced with *impervious cover*.
- Solar array field areas that have tables elevated off the ground, spaced one table width apart, do not *alter hydrology from pre- to post-development conditions*, and address water quality volume and runoff reduction volume by maintaining sheet flow on slopes less than 8%.
- Structural agricultural conservation practices as identified in Table II in the “Agricultural Best Management Practice Systems Catalogue” (dated June 2023) that do not include construction or reconstruction of *impervious area* and do not *alter hydrology from pre- to post-development* conditions.
- Temporary access roads, median crossovers, detour roads, lanes, or other temporary *impervious areas* that will be restored to pre-construction conditions once the *construction activity* is complete (in this context, “temporary” means the *impervious area* will be in place for two years or less)
- Other *construction activities* that do not include the construction or reconstruction of *impervious area*, and do not *alter hydrology from pre- to post-development* conditions, and are not listed in Table 2.

1. If the site is redeveloped in the future, a new eNOI must be submitted.

Table 2**CONSTRUCTION ACTIVITIES THAT REQUIRE THE PREPARATION OF A SWPPP THAT INCLUDES POST-CONSTRUCTION STORMWATER MANAGEMENT PRACTICES (SMPs)****The following *construction activities*:**

- Single-family home located in one of the watersheds listed in Appendix C or *directly discharging* to one of the 303(d) segments listed in Appendix D
- Single-family home that disturbs five (5) or more acres of land
- Single-family residential subdivisions located in one of the watersheds listed in Appendix C or *directly discharging* to one of the 303(d) segments listed in Appendix D
- Single-family residential subdivisions that involve soil disturbances of between one (1) and five (5) acres of land with greater than 25% *impervious cover* at total site build-out
- Single-family residential subdivisions that involve soil disturbances of between 20,000 square feet and one (1) acre of land within the municipal boundaries of NYC with greater than 25% *impervious cover* at total site build-out
- Single-family residential subdivisions that involve soil disturbances of five (5) or more acres of land, and single-family residential subdivisions that involve soil disturbances of less than five (5) acres that are part of a *common plan of development or sale* that will ultimately disturb five (5) or more acres of land
- Multi-family residential developments; includes duplexes, townhomes, condominiums, senior housing complexes, apartment complexes, and mobile home parks
- Creation of 5,000 square feet or more of *impervious area* in the municipal boundaries of NYC
- Airports
- Amusement parks
- Breweries, cideries, and wineries, including establishments constructed on agricultural land
- Campgrounds
- Cemeteries that include the construction or reconstruction of *impervious area* (>5% of disturbed area) or *alter the hydrology from pre- to post-development* conditions
- Commercial developments
- Churches and other places of worship
- Construction of a barn or other *agricultural building* (e.g. silo) that involves soil disturbance greater than five acres.
- Structural agricultural conservation practices as identified in Table II in the “Agricultural Best Management Practice Systems Catalogue” (dated June 2023) that involves soil disturbance greater than five acres and include the construction or reconstruction of *impervious area* or *alter hydrology from pre- to post-development* conditions.
- Facility buildings, including ski lodges, restroom buildings, pumphouses, ski lift terminals, and maintenance and groomer garages
- Institutional development; includes hospitals, prisons, schools and colleges
- Industrial facilities; includes industrial parks
- Landfills; including creation of landfills or capping landfills.
- Municipal facilities; includes highway garages, transfer stations, office buildings, POTWs, water treatment plants, and water storage tanks
- Golf courses
- Office complexes

Table 2 (Continued)

CONSTRUCTION ACTIVITIES THAT REQUIRE THE PREPARATION OF A SWPPP THAT INCLUDES POST-CONSTRUCTION STORMWATER MANAGEMENT PRACTICES (SMPs)

The following *construction activities*:

- Permanent laydown yards and equipment storage lots
- Playgrounds that include the construction or reconstruction of *impervious area*
- Sports complexes
- Racetracks; includes racetracks with earthen (dirt) surfaces
- Road construction or reconstruction, outside the municipal boundaries of NYC
- Road construction within the municipal boundaries of NYC
- Stand-alone road reconstruction, within the municipal boundaries of NYC where the total soil disturbance from that road reconstruction involves soil disturbance of one (1) acre or more of land
- Parking lot construction or reconstruction (as with all Table 2 bullets, this includes parking lots constructed as part of the *construction activities* listed in Table 1, unless a Table 1 bullet specifies otherwise)
- Athletic fields (natural grass) that include the construction or reconstruction of *impervious area* (>5% of disturbed area) or *alter the hydrology from pre- to post-development* conditions
- Athletic fields with artificial turf
- Permanent access roads, parking areas, substations, compressor stations, and well drilling pads, surfaced with *impervious cover*, and constructed as part of an overhead electric transmission line, wind-power, cell tower, oil or gas well drilling, sewer or water main, ski lift, or other linear utility project
- Sidewalks, bike paths, or walking paths, surfaced with an *impervious cover*, that are part of a residential, commercial or institutional development
- Sidewalks, bike paths, or walking paths, surfaced with an *impervious cover*, that are part of highway construction or reconstruction
- Solar array field areas on slopes greater than 8% that cannot maintain sheet flow using management practices identified in the BB or the DM
- Solar array field areas on slopes less than 8% that will *alter the hydrology from pre- to post-development* conditions
- Solar array field areas with tables that are not elevated high enough to achieve *final stabilization* beneath the tables
- Traditional *impervious areas* associated with solar development (e.g. roads, buildings, transformers)
- Utility pads surfaced with *impervious cover*, including electric vehicle charging stations
- All other *construction activities* that include the construction or reconstruction of *impervious area* or *alter the hydrology from pre- to post-development* conditions, and are not listed in Table 1

APPENDIX C – Watersheds Requiring Enhanced Phosphorus Removal

Watersheds where *owners or operators of construction activities* identified in Table 2 of Appendix B must prepare a *SWPPP* that includes *SMPs* designed in conformance with the Enhanced Phosphorus Removal Standards included in the DM technical standard.

- Entire New York City Watershed located east of the Hudson River – Figure 1
- Onondaga Lake Watershed – Figure 2
- Greenwood Lake Watershed – Figure 3
- Oscawana Lake Watershed – Figure 4
- Kinderhook Lake Watershed – Figure 5

Figure 1 - New York City Watershed East of the Hudson

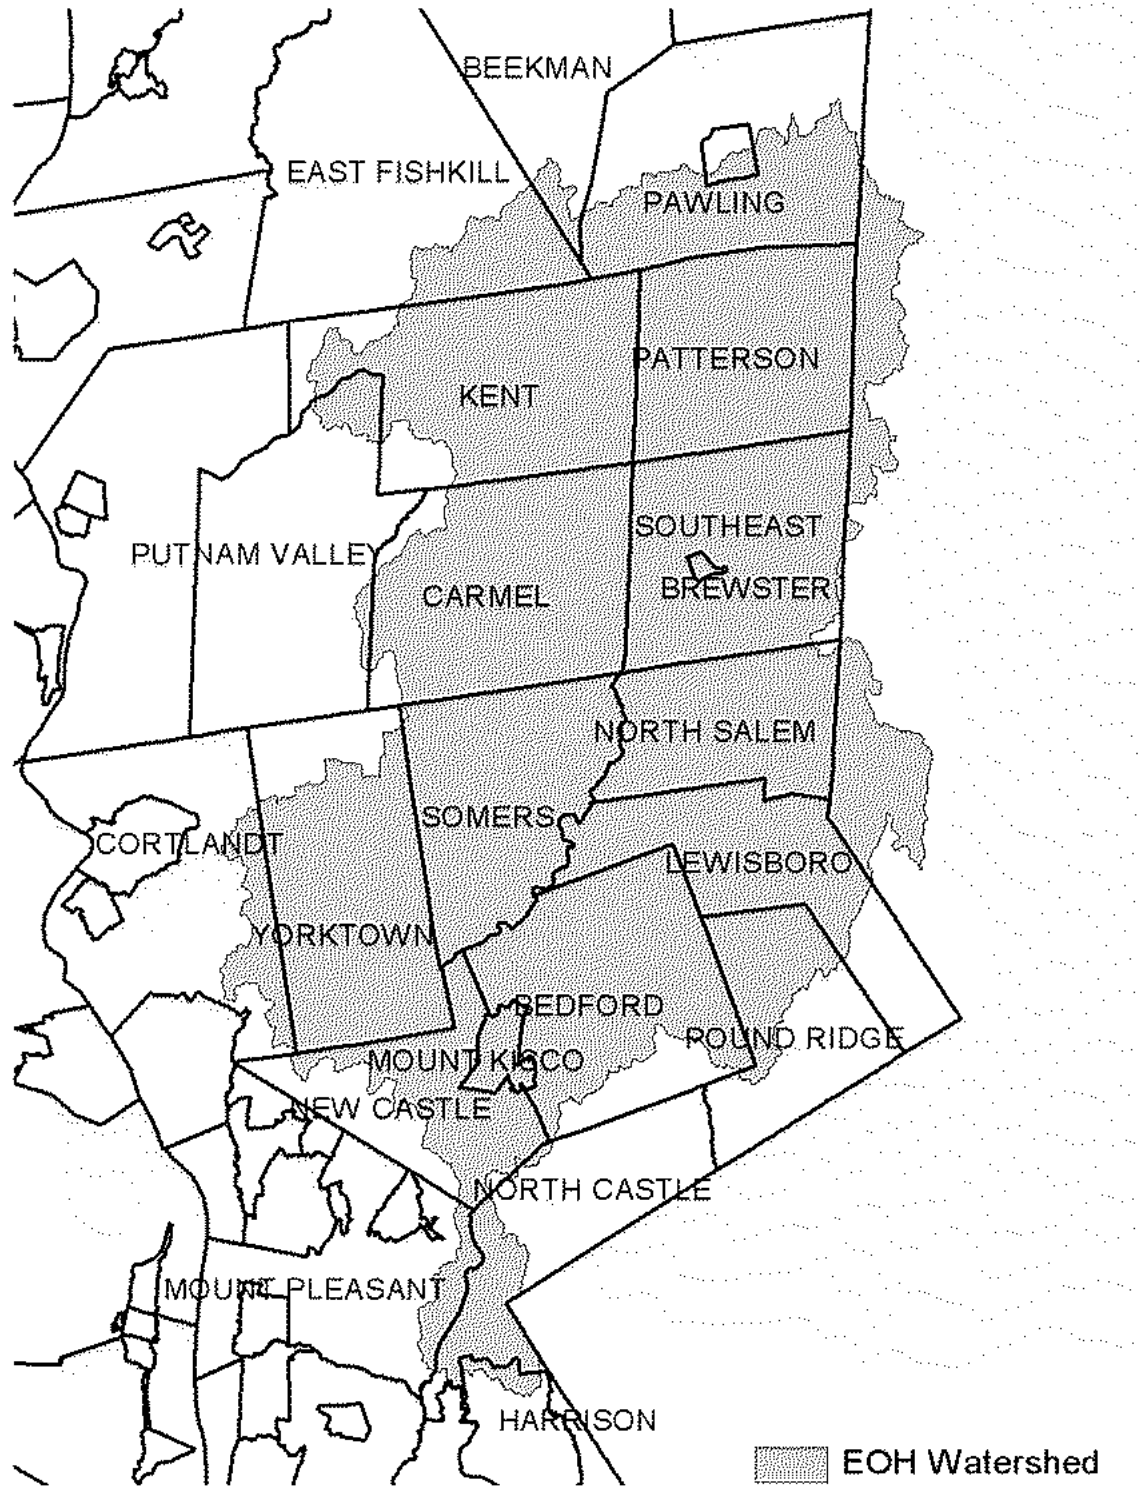


Figure 2 - Onondaga Lake Watershed

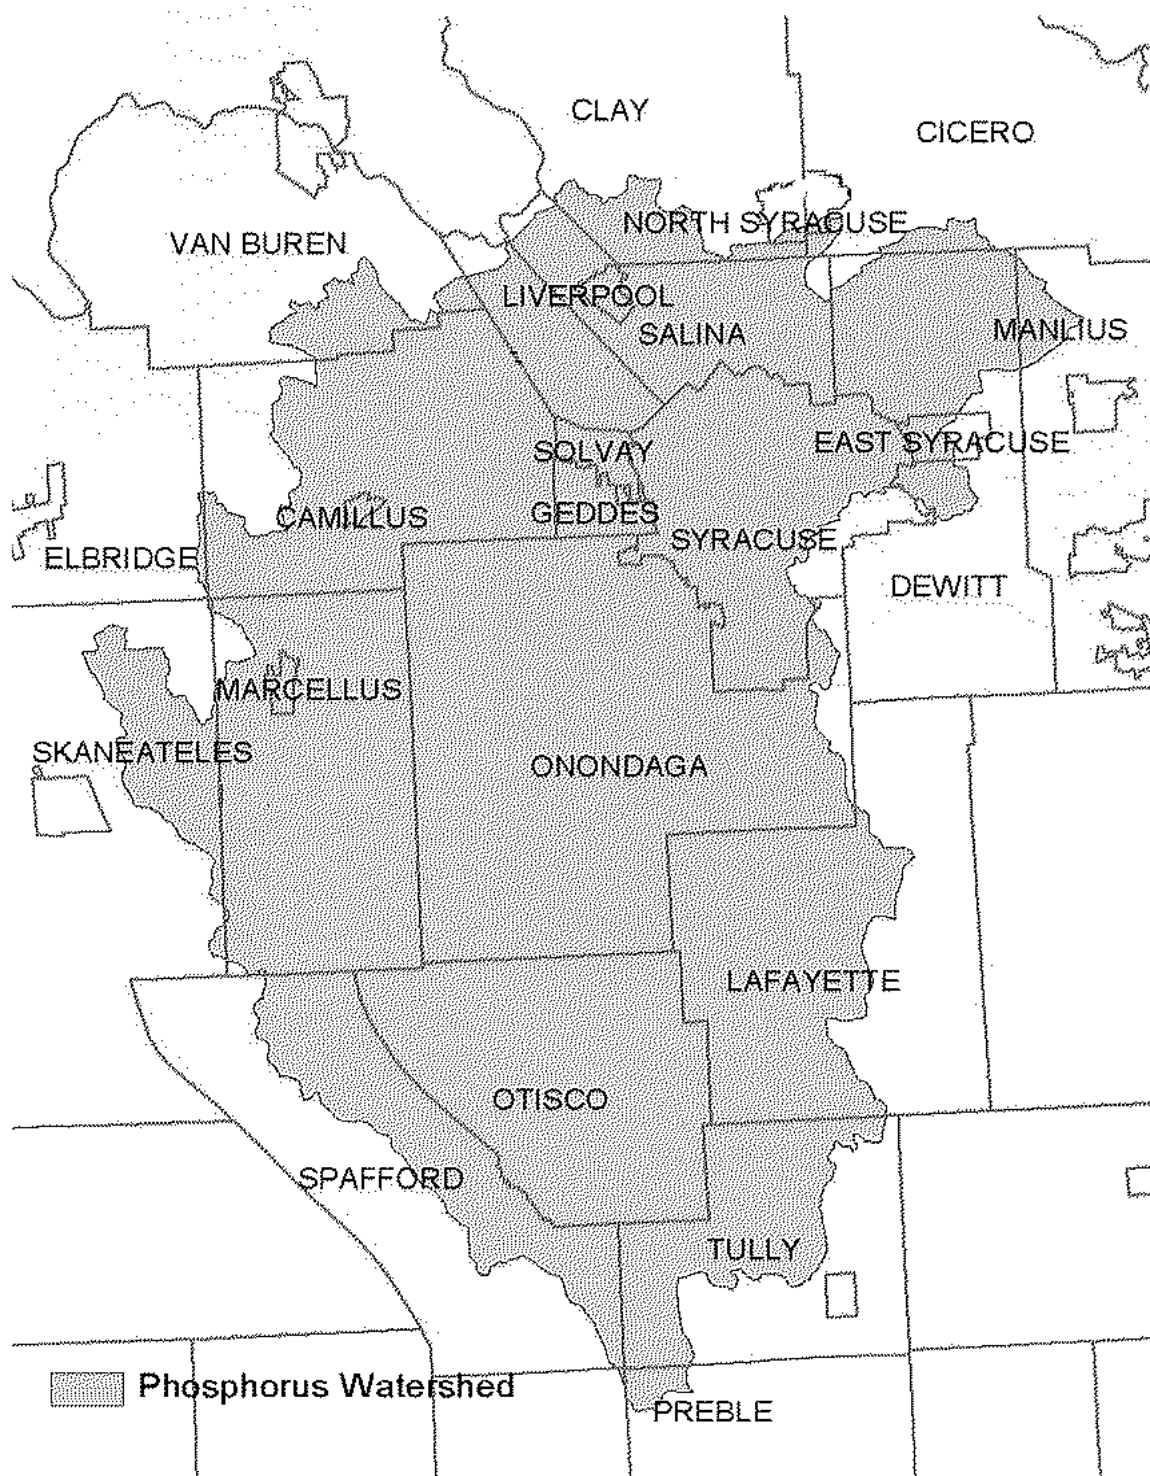


Figure 3 - Greenwood Lake Watershed



Figure 4 - Oscawana Lake Watershed


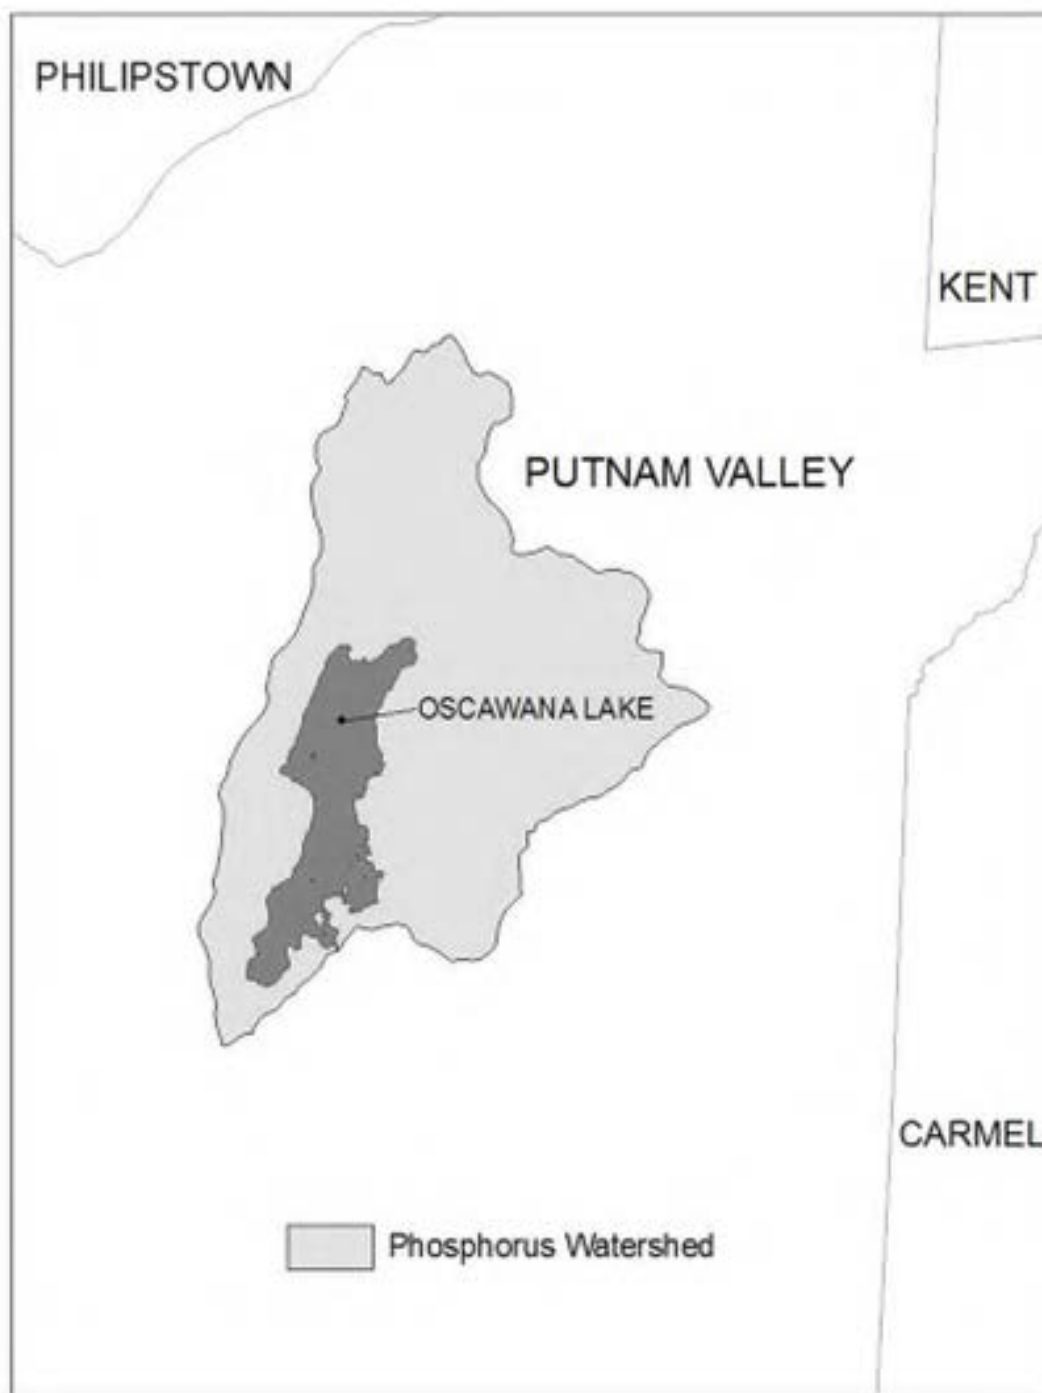


Figure 5 - Kinderhook Lake Watershed

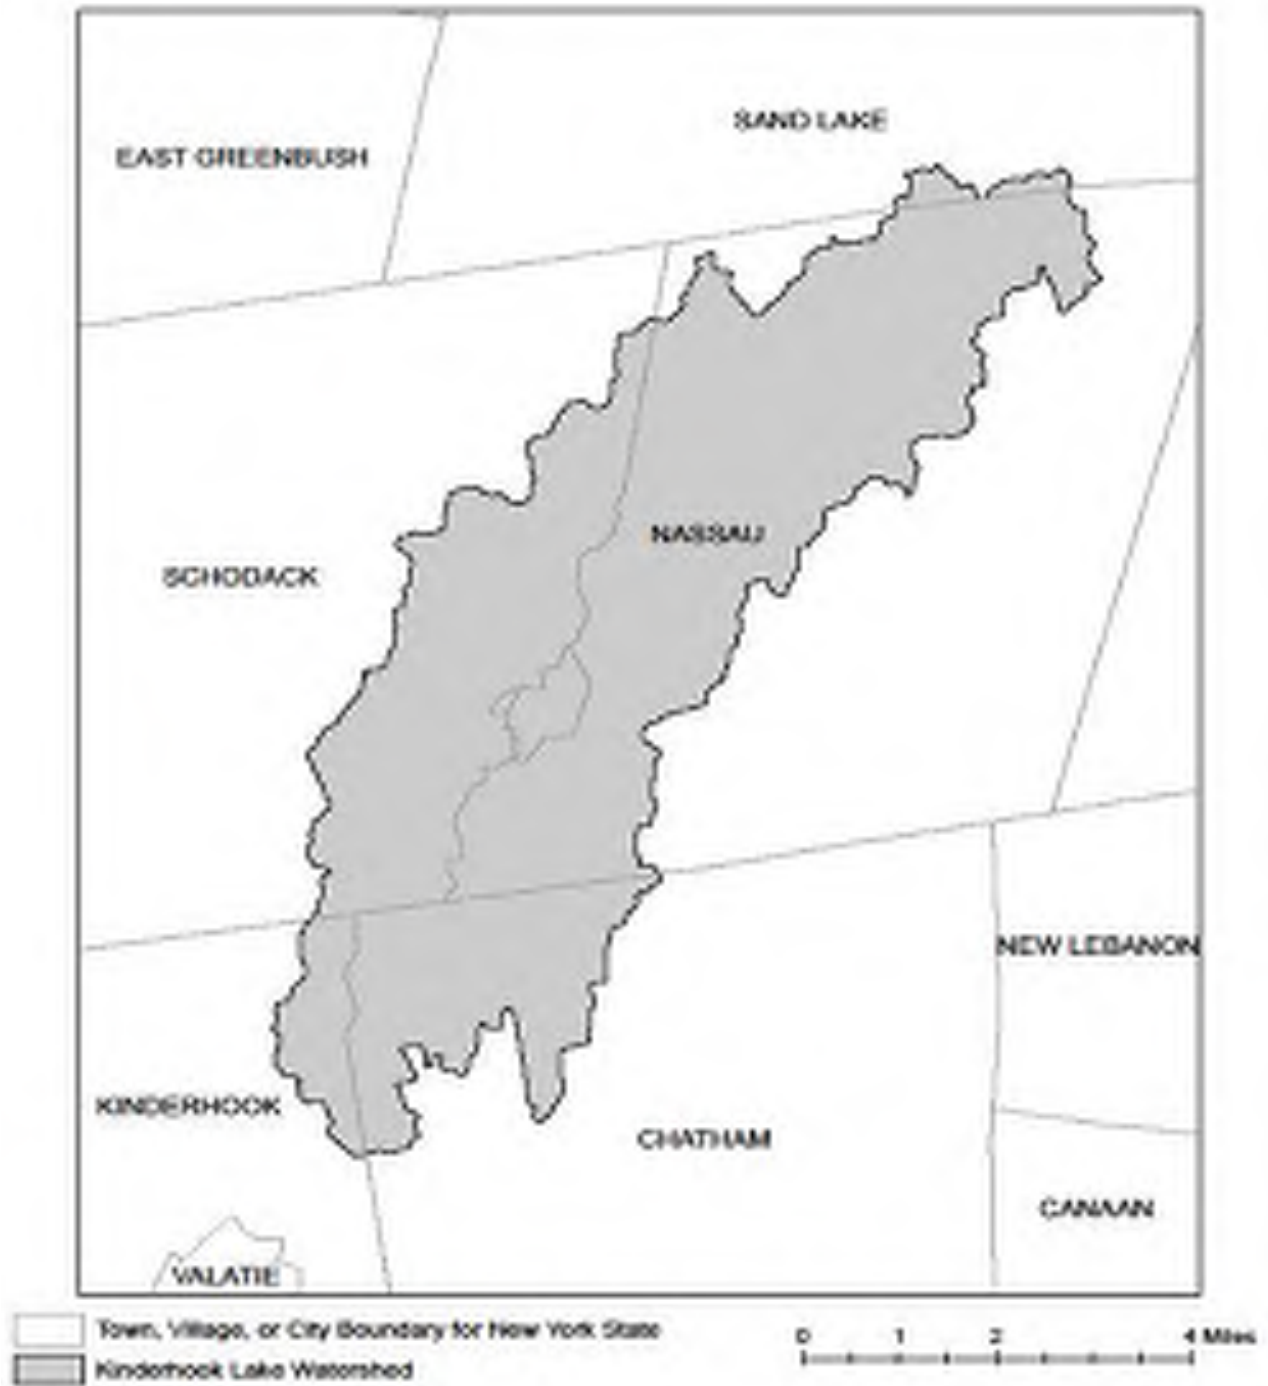

APPENDIX D – Impaired Waterbodies (by Construction Related Pollutants)

List of waterbodies impaired by *pollutants* related to *construction activity*, including turbidity, silt/sediment, and nutrients (e.g. nitrogen, phosphorus). This list is a subset of “The Final New York State 2018 Section 303(d) List of Impaired Waters Requiring a TMDL” dated June 2020.

County	Waterbody	Pollutant
Albany	Ann Lee (Shakers) Pond, Stump Pond (1201-0096)	Phosphorus
Albany	Lawsons Lake (1301-0235)	Phosphorus
Allegany	Amity Lake, Saunders Pond (0403-0054)	Phosphorus
Allegany	Andover Pond (0403-0056)	Phosphorus
Bronx	Reservoir No.1/Lake Isle (1702-0075)	Phosphorus
Bronx	Van Cortlandt Lake (1702-0008)	Phosphorus
Broome	Blueberry, Laurel Lakes (1404-0033)	Phosphorus
Broome	Fly Pond, Deer Lake (1404-0038)	Phosphorus
Broome	Minor Tribs to Lower Susquehanna (0603-0044)	Phosphorus
Broome	Whitney Point Lake/Reservoir (0602-0004)	Phosphorus
Cattaraugus	Allegheny River/Reservoir (0201-0023)	Phosphorus
Cattaraugus	Beaver Lake/Alma Pond (0201-0073)	Phosphorus
Cattaraugus	Case Lake (0201-0020)	Phosphorus
Cattaraugus	Linlyco/Club Pond (0201-0035)	Phosphorus
Cayuga	Duck Lake (0704-0025)	Phosphorus
Cayuga	Owasco Inlet, Upper, and tribs (0706-0014)	Nutrients
Chautauqua	Chadakoin River and tribs (0202-0018)	Phosphorus
Chautauqua	Hulburt/Clymer Pond (0202-0079)	Phosphorus
Chautauqua	Middle Cassadaga Lake (0202-0002)	Phosphorus
Clinton	Great Chazy River, Lower, Main Stem (1002-0001)	Silt/Sediment
Columbia	Robinson Pond (1308-0003)	Phosphorus
Cortland	Dean Pond (0602-0077)	Phosphorus
Dutchess	Fallkill Creek (1301-0087)	Phosphorus
Dutchess	Hillside Lake (1304-0001)	Phosphorus
Dutchess	Wappingers Lake (1305-0001)	Phosphorus
Dutchess	Wappingers Lake (1305-0001)	Silt/Sediment
Erie	Beeman Creek and tribs (0102-0030)	Phosphorus
Erie	Delaware Park Pond (0101-0026)	Phosphorus
Erie	Ellicott Creek, Lower, and tribs (0102-0018)	Phosphorus
Erie	Ellicott Creek, Lower, and tribs (0102-0018)	Silt/Sediment
Erie	Green Lake (0101-0038)	Phosphorus
Erie	Little Sister Creek, Lower, and tribs (0104-0045)	Phosphorus
Erie	Murder Creek, Lower, and tribs (0102-0031)	Phosphorus

Erie	Rush Creek and tribs (0104-0018)	Phosphorus
Erie	Scajaquada Creek, Lower, and tribs (0101-0023)	Phosphorus
Erie	Scajaquada Creek, Middle, and tribs (0101-0033)	Phosphorus
Erie	Scajaquada Creek, Upper, and tribs (0101-0034)	Phosphorus
Erie	South Branch Smoke Cr, Lower, and tribs (0101-0036)	Phosphorus
Erie	South Branch Smoke Cr, Lower, and tribs (0101-0036)	Silt/Sediment
Genesee	Bigelow Creek and tribs (0402-0016)	Phosphorus
Genesee	Black Creek, Middle, and minor tribs (0402-0028)	Phosphorus
Genesee	Black Creek, Upper, and minor tribs (0402-0048)	Phosphorus
Genesee	Bowen Brook and tribs (0102-0036)	Phosphorus
Genesee	LeRoy Reservoir (0402-0003)	Phosphorus
Genesee	Mill Pond (0402-0050)	Phosphorus
Genesee	Oak Orchard Cr, Upper, and tribs (0301-0014)	Phosphorus
Genesee	Oatka Creek, Middle, and minor tribs (0402-0031)	Phosphorus
Genesee	Tonawanda Cr, Middle, Main Stem (0102-0002)	Phosphorus
Greene	Schoharie Reservoir (1202-0012)	Silt/Sediment
Greene	Sleepy Hollow Lake (1301-0059)	Silt/Sediment
Herkimer	Steele Creek tribs (1201-0197)	Phosphorus
Herkimer	Steele Creek tribs (1201-0197)	Silt/Sediment
Kings	Hendrix Creek (1701-0006) 18	Nitrogen
Kings	Prospect Park Lake (1701-0196)	Phosphorus
Lewis	Mill Creek/South Branch, and tribs (0801-0200)	Nutrients
Livingston	Christie Creek and tribs (0402-0060)	Phosphorus
Livingston	Conesus Lake (0402-0004)	Phosphorus
Livingston	Mill Creek and minor tribs (0404-0011)	Silt/Sediment
Monroe	Black Creek, Lower, and minor tribs (0402-0033)	Phosphorus
Monroe	Buck Pond (0301-0017)	Phosphorus
Monroe	Cranberry Pond (0301-0016)	Phosphorus
Monroe	Durand, Eastman Lakes (0302-0037)	Phosphorus
Monroe	Lake Ontario Shoreline, Western (0301-0069) 9	Phosphorus
Monroe	Long Pond (0301-0015)	Phosphorus
Monroe	Mill Creek and tribs (0302-0025)	Phosphorus 2
Monroe	Mill Creek/Blue Pond Outlet and tribs (0402-0049)	Phosphorus
Monroe	Minor Tribs to Irondequoit Bay (0302-0038)	Phosphorus
Monroe	Rochester Embayment - East (0302-0002) [9]	Phosphorus
Monroe	Rochester Embayment - West (0301-0068) 9	Phosphorus
Monroe	Shipbuilders Creek and tribs (0302-0026)	Phosphorus 2
Monroe	Thomas Creek/White Brook and tribs (0302-0023)	Phosphorus

Nassau	Bannister Creek/Bay (1701-0380)	Nitrogen
Nassau	Beaver Lake (1702-0152)	Phosphorus
Nassau	Browswere Bay (1701-0383)	Nitrogen
Nassau	Camaans Pond (1701-0052)	Phosphorus
Nassau	East Meadow Brook, Upper, and tribs (1701-0211)	Silt/Sediment
Nassau	East Rockaway Channel (1701-0381)	Nitrogen
Nassau	Glen Cove Creek, Lower, and tribs (1702-0146)	Silt/Sediment
Nassau	Grant Park Pond (1701-0054)	Phosphorus
Nassau	Hempstead Bay, Broad Channel (1701-0032)	Nitrogen
Nassau	Hempstead Lake (1701-0015)	Phosphorus
Nassau	Hewlett Bay (1701-0382)	Nitrogen
Nassau	Hog Island Channel (1701-0220)	Nitrogen
Nassau	Massapequa Creek, Upper, and tribs (1701-0174)	Phosphorus
Nassau	Milburn/Parsonage Creeks, Upp, and tribs (1701-0212)	Phosphorus
Nassau	Reynolds Channel, East (1701-0215) [12]	Nitrogen
Nassau	Reynolds Channel, West (1701-0216) 12	Nitrogen
Nassau	Tidal Tribs to Hempstead Bay (1701-0218)	Nitrogen
Nassau	Tribs (fresh) to East Bay (1701-0204)	Silt/Sediment
Nassau	Tribs (fresh) to East Bay (1701-0204)	Phosphorus
Nassau	Tribs to Smith Pond/Halls Pond (1701-0221)	Phosphorus
Nassau	Woodmere Channel (1701-0219)	Nitrogen
New York	Harlem Meer (1702-0103)	Phosphorus
New York	The Lake in Central Park (1702-0105)	Phosphorus
Niagara	Bergholtz Creek and tribs (0101-0004)	Phosphorus
Niagara	Hyde Park Lake (0101-0030)	Phosphorus
Niagara	Lake Ontario Shoreline, Western (0301-0053) 9	Phosphorus
Niagara	Lake Ontario Shoreline, Western (0301-0072) 9	Phosphorus
Oneida	Ballou, Nail Creeks (1201-0203)	Phosphorus
Onondaga	Ley Creek and tribs (0702-0001) 10	Nutrients (phosphorus)
Onondaga	Minor Tribs to Onondaga Lake (0702-0022) 10	Nutrients (phosphorus)
Onondaga	Minor Tribs to Onondaga Lake (0702-0022) 10	Nitrogen (NH ₃ , NO ₂)
Onondaga	Onondaga Creek, Lower (0702-0023) 10	Nutrients (phosphorus)
Onondaga	Onondaga Creek, Lower, and tribs (0702-0023)	Turbidity
Onondaga	Onondaga Creek, Middle, and tribs (0702-0004)	Turbidity
Onondaga	Onondaga Creek, Upper, and tribs (0702-0024)	Turbidity
Ontario	Great Brook and minor tribs (0704-0034)	Phosphorus 2
Ontario	Great Brook and minor tribs (0704-0034)	Silt/Sediment

Ontario	Hemlock Lake Outlet and minor tribs (0402-0013)	Phosphorus
Ontario	Honeoye Lake (0402-0032)	Phosphorus
Orange	Brown Pond Reservoir (1303-0013)	Phosphorus
Orange	Lake Washington (1303-0012)	Phosphorus
Orange	Minor Tribs to Middle Wallkill (1306-0061)	Phosphorus
Orange	Monhagen Brook and tribs (1306-0074)	Phosphorus
Orange	Orange Lake (1301-0008) [16]	Phosphorus
Orange	Quaker Creek and tribs (1306-0025)	Phosphorus
Orange	Wallkill River, Middle, Main Stem (1306-0038)	Phosphorus
Orange	Wallkill River, Upper, and Minor tribs (1306-0017)	Phosphorus
Orleans	Glenwood Lake (0301-0041)	Phosphorus
Orleans	Lake Ontario Shoreline, Western (0301-0070) 9	Phosphorus
Orleans	Lake Ontario Shoreline, Western (0301-0071) 9	Phosphorus
Oswego	Lake Neatahwanta (0701-0018)	Nutrients (phosphorus)
Oswego	Pleasant Lake (0703-0047)	Phosphorus
Putnam	Lost Lake, Putnam Lake (1302-0053)	Phosphorus
Putnam	Minor Tribs to Croton Falls Reservoir (1302-0001)	Phosphorus
Queens	Bergen Basin (1701-0009) 18	Nitrogen
Queens	Jamaica Bay, Eastern, and tribs, Queens (1701-0005) 18	Nitrogen
Queens	Kissena Lake (1702-0258)	Phosphorus
Queens	Meadow Lake (1702-0030)	Phosphorus
Queens	Shellbank Basin (1701-0001) 18	Nitrogen
Queens	Willow Lake (1702-0031)	Phosphorus
Rensselaer	Nassau Lake (1310-0001)	Phosphorus
Rensselaer	Snyders Lake (1301-0043)	Phosphorus
Richmond	Grassmere Lake/Bradys Pond (1701-0357)	Phosphorus
Rockland	Congers Lake, Swartout Lake (1501-0019)	Phosphorus
Rockland	Rockland Lake (1501-0021)	Phosphorus
Saratoga	Ballston Lake (1101-0036)	Phosphorus
Saratoga	Dwaas Kill and tribs (1101-0007)	Phosphorus
Saratoga	Dwaas Kill and tribs (1101-0007)	Silt/Sediment
Saratoga	Lake Lonely (1101-0034)	Phosphorus
Saratoga	Round Lake (1101-0060)	Phosphorus
Saratoga	Tribs to Lake Lonely (1101-0001)	Phosphorus
Schenectady	Collins Lake (1201-0077)	Phosphorus
Schenectady	Duane Lake (1311-0006)	Phosphorus
Schenectady Lake	Mariaville Lake (1201-0113)	Phosphorus
Schuyler	Cayuta Lake (0603-0005)	Phosphorus

Seneca	Reeder Creek and tribs (0705-0074)	Phosphorus
St.Lawrence	Black Lake Outlet, Black Lake (0906-0001)	Phosphorus
St.Lawrence	Fish Creek and minor tribs (0906-0026)	Phosphorus
Steuben	Smith Pond (0502-0012)	Phosphorus
Suffolk	Agawam Lake (1701-0117)	Phosphorus
Suffolk	Big/Little Fresh Ponds (1701-0125)	Phosphorus
Suffolk	Canaan Lake (1701-0018)	Phosphorus
Suffolk	Canaan Lake (1701-0018)	Silt/Sediment
Suffolk	Fresh Pond (1701-0241)	Phosphorus
Suffolk	Great South Bay, East (1701-0039)	Nitrogen
Suffolk	Great South Bay, Middle (1701-0040)	Nitrogen
Suffolk	Great South Bay, West (1701-0173)	Nitrogen
Suffolk	Lake Ronkonkoma (1701-0020)	Phosphorus
Suffolk	Mattituck/Marratooka Pond (1701-0129)	Phosphorus
Suffolk	Mill and Seven Ponds (1701-0113)	Phosphorus
Suffolk	Millers Pond (1702-0013)	Phosphorus
Suffolk	Moriches Bay, East (1701-0305)	Nitrogen
Suffolk	Moriches Bay, West (1701-0038)	Nitrogen
Suffolk	Quantuck Bay (1701-0042)	Nitrogen
Suffolk	Shinnecock Bay and Inlet (1701-0033)	Nitrogen
Suffolk	Tidal Tribs to West Moriches Bay (1701-0312)	Nitrogen
Sullivan	Bodine, Montgomery Lakes (1401-0091)	Phosphorus
Sullivan	Davies Lake (1402-0047)	Phosphorus
Sullivan	Evens Lake (1402-0004)	Phosphorus
Sullivan	Pleasure Lake (1402-0055)	Phosphorus
Sullivan	Swan Lake (1401-0063)	Phosphorus
Tompkins	Cayuga Lake, Southern End (0705-0040)	Phosphorus
Tompkins	Cayuga Lake, Southern End (0705-0040)	Silt/Sediment
Ulster	Ashokan Reservoir (1307-0004)	Silt/Sediment
Ulster	Esopus Creek, Lower, Main Stem (1307-0010) [17]	Turbidity
Ulster	Esopus Creek, Middle, Main Stem (1307-0003) 17	Turbidity
Ulster	Esopus Creek, Upper, and minor tribs (1307-0007)[3]	Silt/Sediment
Ulster	Wallkill River, Lower, Main Stem (1306-0027)	Phosphorus
Warren	Hague Brook and tribs (1006-0006)	Silt/Sediment
Warren	Huddle/Finkle Brooks and tribs (1006-0003)	Silt/Sediment
Warren	Indian Brook and tribs (1006-0002)	Silt/Sediment
Warren	Lake George (1006-0016) and tribs	Silt/Sediment
Warren	Tribs to Lake George, East Shore (1006-0020)	Silt/Sediment
Warren	Tribs to Lake George, Lk.George Village (1006-0008)	Silt/Sediment

Washington	Wood Cr/Champlain Canal and tribs (1005-0036)	Phosphorus
Westchester	Lake Katonah (1302-0136)	Phosphorus
Westchester	Lake Lincolndale (1302-0089)	Phosphorus
Westchester	Lake Meahagh (1301-0053)	Phosphorus
Westchester	Lake Mohegan (1301-0149)	Phosphorus
Westchester	Lake Shenorock (1302-0083)	Phosphorus
Westchester	Mamaroneck River, Lower (1702-0071)	Silt/Sediment
Westchester	Mamaroneck River, Upp, & minor tribs (1702-0123)	Silt/Sediment
Westchester	Saw Mill River (1301-0007)	Phosphorus
Westchester	Saw Mill River, Middle, and tribs (1301-0100)	Phosphorus
Westchester	Sheldrake River (1702-0069)	Phosphorus
Westchester	Sheldrake River (1702-0069)	Silt/Sedimnt
Westchester	Silver Lake (1702-0040)	Phosphorus
Westchester	Teatown Lake (1302-0150)	Phosphorus
Westchester	Truesdale Lake (1302-0054)	Phosphorus
Westchester	Wallace Pond (1301-0140)	Phosphorus

APPENDIX E – List of NYSDEC Regional Offices

<u>Region</u>	<u>COVERING THE FOLLOWING COUNTIES:</u>	<u>DIVISION OF ENVIRONMENTAL PERMITS (DEP) PERMIT ADMINISTRATORS</u>	<u>DIVISION OF WATER (DOW) WATER (SPDES) PROGRAM</u>
1	NASSAU AND SUFFOLK	50 CIRCLE ROAD STONY BROOK, NY 11790 TEL. (631) 444-0365	50 CIRCLE ROAD STONY BROOK, NY 11790-3409 TEL. (631) 444-0405
2	BRONX, KINGS, NEW YORK, QUEENS AND RICHMOND	1 HUNTERS POINT PLAZA, 47-40 21ST ST. LONG ISLAND CITY, NY 11101-5407 TEL. (718) 482-4997	1 HUNTERS POINT PLAZA, 47-40 21ST ST. LONG ISLAND CITY, NY 11101-5407 TEL. (718) 482-4933
3	DUTCHESS, ORANGE, PUTNAM, ROCKLAND, SULLIVAN, ULSTER AND WESTCHESTER	21 SOUTH PUTT CORNERS ROAD NEW PALTZ, NY 12561-1696 TEL. (845) 256-3059	220 WHITE PLAINS ROAD, SUITE 110 TEL. (914) 428 - 2505
4	ALBANY, COLUMBIA, DELAWARE, GREENE, MONTGOMERY, OTSEGO, RENSSELAER, SCHENECTADY AND SCHOHARIE	1130 NORTH WESTCOTT ROAD SCHENECTADY, NY 12306-2014 TEL. (518) 357-2069	1130 NORTH WESTCOTT ROAD SCHENECTADY, NY 12306-2014 TEL. (518) 357-2045
5	CLINTON, ESSEX, FRANKLIN, FULTON, HAMILTON, SARATOGA, WARREN AND WASHINGTON	1115 STATE ROUTE 86, Po Box 296 RAY BROOK, NY 12977-0296 TEL. (518) 897-1234	232 GOLF COURSE ROAD WARRENSBURG, NY 12885-1172 TEL. (518) 623-1200
6	HERKIMER, JEFFERSON, LEWIS, ONEIDA AND ST. LAWRENCE	STATE OFFICE BUILDING 317 WASHINGTON STREET WATERTOWN, NY 13601-3787 TEL. (315) 785-2245	STATE OFFICE BUILDING 207 GENESEE STREET UTICA, NY 13501-2885 TEL. (315) 793-2554
7	BROOME, CAYUGA, CHENANGO, CORTLAND, MADISON, ONONDAGA, OSWEGO, TIOGA AND TOMPKINS	5786 WIDEWATERS PARKWAY SYRACUSE, NY 13214-1867 TEL. (315) 426-7438	5786 WIDEWATERS PARKWAY SYRACUSE, NY 13214-1867 TEL. (315) 426-7500
8	CHEMUNG, GENESEE, LIVINGSTON, MONROE, ONTARIO, ORLEANS, SCHUYLER, SENECA, STEUBEN, WAYNE AND YATES	6274 EAST AVON-LIMA ROADAVON, NY 14414-9519 TEL. (585) 226-2466	6274 EAST AVON-LIMA RD. AVON, NY 14414-9519 TEL. (585) 226-2466
9	ALLEGANY, CATTARAUGUS, CHAUTAUQUA, ERIE, NIAGARA AND WYOMING	700 DELAWARE AVENUE BUFFALO, NY 14209-2999 TEL. (716) 851-7165	700 DELAWARE AVENUE BUFFALO, NY 14209-2999 TEL. (716) 851-7070



Appendix G:

Construction Phase Inspection Report (Sample Form)



WEEKLY SWPPP SITE INSPECTION REPORT

Project:
LE Project Number:
Contractor:
Inspector's Name/Title:
NYR#:

Date and Time:
Temperature:
Ambient Conditions:
Soil Conditions:
LE SIMPL:

INSPECTION CHECKLIST

Record Keeping

- | | | | |
|--------------------------|--------------------------|--------------------------|---|
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 1) Is the Notice of Intent and NOI Acknowledgement Letter retained at the construction site? |
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 2) Is the MS4 Acceptance Form retained at the construction site? |
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 3) Is a copy of the General Permit (GP-0-25-001) and SWPPP retained at the construction site? |
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 4) Are all necessary contractor certifications signed and retained at the construction site? |
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 5) Are SWPPP inspection reports signed and retained at the construction site? |

Visual Observations

- | | | | |
|--------------------------|--------------------------|--------------------------|--|
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 6) Are there currently less than 5 acres of disturbed soils at the site? |
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 7) Are natural resource areas (i.e. streams, surface waterbodies, wetlands, trees, etc.) protected with barriers or similar erosion and sediment controls? |
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 8) Have permanent stormwater controls such as sediment basins and conveyance systems been constructed? (Not applicable during beginning phases of construction) |
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 9) Were all stormwater discharges clear or the same as receiving waters on the day of inspection? This includes receiving waters, all conveyance systems (i.e. pipes, culverts, ditches, etc.) and overland flow. Please describe the quality and quantity at all points of discharge from the site and the condition of receiving waters. |
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 10) Are catch basins/storm drain inlets properly protected? |
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 11) Have vegetative or structural stabilization measures been implemented on all inactive areas where there are exposed soils? |

Visual Observations (cont'd)

- | | | | |
|--------------------------|--------------------------|--------------------------|---|
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 12) Have vegetative or structural stabilization methods been implemented on any inactive critical slopes (high probability of erosion) where there are exposed soils? |
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 13) Have on-site vehicle tracking sediments and other eroded sediments been cleared? |
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 14) Is the construction entrance preventing sediment from being tracked onto the street? |
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 15) Are roads and properties adjacent to the construction site free of sediment and/or debris? |
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 16) Is dust adequately controlled at the construction site? |
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 17) Have all erosion and sediment control practices and pollution prevention measures been installed properly and are they functioning as designed? |
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 18) Are all erosion and sediment control practices and pollution prevention measures being maintained to ensure integrity and effectiveness? |
| Yes | No | N/A | |
| <input type="checkbox"/> | <input type="checkbox"/> | <input type="checkbox"/> | 19) Have all post-construction erosion and sediment controls been constructed as designed? (Not applicable during beginning phases of construction) |





GENERAL REMINDERS

SPECIFIC COMMENTS

DISCHARGE LOCATIONS & DRAINAGE PATHWAYS (areas subject to change)

Location (see map)	Description	Discharge	Receiving Waters	Construction Status	Comments & Recommendations

SITE MAP

	ACTIVE SOILS	~ 0.00 acres +/-
	INACTIVE SOILS NOT STABILIZED	~ 0.00 acres +/-
	TEMPORARILY STABILIZED SOILS	~ 0.00 acres +/-
	PERMANENTLY STABILIZED SOILS	~ 0.00 acres +/-

CERTIFICATION

Lansing Engineering Qualified Inspector Signature: _____

Date: _____





Appendix H:
MS4 Acceptance Form





Department of Environmental Conservation

MS4 SWPPP Acceptance Form

for construction activities seeking authorization under the

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(In accordance with CGP Part I.D.2.b., the completed form must be attached to the eNOI and submitted to NYSDEC electronically.)

I. Project Owner/Operator Information

1. Owner/Operator Name:

2. Contact Person:

3. Street Address:

4. City/State/Zip:

II. Project Site Information

5. Project/Site Name:

6. Street Address:

7. City/State/Zip:

III. Stormwater Pollution Prevention Plan (SWPPP) Review and Acceptance Information

8. SWPPP Reviewed by:

9. Title/Position:

10. Date Final SWPPP Reviewed and Accepted:

IV. Regulated MS4 Information

11. Name of MS4 Operator:

12. MS4 SPDES Permit Identification Number: NYR20A

13. Street Address:

14. City/State/Zip:

15. Telephone Number:

MS4 SWPPP Acceptance Form - continued

V. Certification Statement - MS4 Official (principal executive officer or ranking elected official) or Duly Authorized Representative

I hereby certify that the final Stormwater Pollution Prevention Plan (SWPPP) for the construction project identified in section II. of this form has been reviewed and meets the substantive requirements in the SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP). Note: The MS4 Operator, through the acceptance of the SWPPP, assumes no responsibility for the accuracy and adequacy of the design included in the SWPPP. In addition, review and acceptance of the SWPPP by the MS4 Operator does not relieve the owner/operator or their SWPPP preparer of responsibility or liability for errors or omissions in the plan.

Printed Name¹:

Title/Position:

Signature:

Date:

VI. Additional Information

¹ Printed name of the principal executive officer or ranking elected official for the MS4 Operator or their duly authorized representative in accordance with CGP Part VII.J.2.



Appendix I:
Notice of Intent (NOI)





SWPPP Preparer Certification Form

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(In accordance with CGP Part I.D.2.b., the completed form must be attached to the eNOI and submitted to NYSDEC electronically.)

Project/Site Name:

eNOI Submission ID:

Owner/Operator Name:

Certification Statement – SWPPP Preparer

I hereby certify that the Stormwater Pollution Prevention Plan (SWPPP) has been prepared in accordance with the requirements of GP-0-25-001. I certify under penalty of law that the SWPPP and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

SWPPP Preparer First Name

MI

SWPPP Preparer Last Name

Signature

Date



Appendix J:

Notice of Termination (NOT) Documentation





Department of
Environmental
Conservation

eNOT Owner or Operator Certification

for construction activities seeking termination from the

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(The completed form must be attached to the eNOT, which must be submitted to NYSDEC electronically in accordance with CGP Part V.A.5.)

I. Project Owner/Operator Information

- a. Owner/Operator Name:
- b. Contact Person:
- c. Street Address:
- d. City/State/Zip:

II. Project Site Information

- a. Project/Site Name:
- b. Street Address:
- c. City/State/Zip:
- d. CGP SPDES Permit ID:

III. Certification Statement

I certify that I have met the requirements of CGP Part V.A.1., 2., 3., and 4. I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

- a. Printed name of the Owner or Operator:
- b. Title/Position:
- c. Signature:
- d. Date:



eNOT Qualified Inspector Certification – SMPs

for construction activities seeking termination from the

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(The completed form must be attached to the eNOT, which must be submitted to NYSDEC electronically in accordance with CGP Part V.A.5.)

I. Project Owner/Operator Information

- a. Owner/Operator Name:
- b. Contact Person:
- c. Street Address:
- d. City/State/Zip:

II. Project Site Information

- a. Project/Site Name:
- b. Street Address:
- c. City/State/Zip:
- d. CGP SPDES Permit ID:

III. Certification Statement

I hereby certify that all the requirements in CGP Part V.A.1.a.iv. or CGP Part V.A.1.b.iv. have been achieved. I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

- a. Printed name of the Qualified Inspector:
- b. Title/Position:
- c. Signature:
- d. Date:



eNOT Qualified Inspector Certification – Final Stabilization

for construction activities seeking termination from the

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(The completed form must be attached to the eNOT, which must be submitted to NYSDEC electronically in accordance with CGP Part V.A.5.)

I. Project Owner/Operator Information

- a. Owner/Operator Name:
- b. Contact Person:
- c. Street Address:
- d. City/State/Zip:

II. Project Site Information

- a. Project/Site Name:
- b. Street Address:
- c. City/State/Zip:
- d. CGP SPDES Permit ID:

III. Certification Statement

I hereby certify that all the requirements in CGP Part V.A.1.a.i., ii., and iii. or CGP Part V.A.1.b.i., ii., and iii. have been achieved. I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

- a. Printed name of the Qualified Inspector:
- b. Title/Position:
- c. Signature:
- d. Date:



Department of
Environmental
Conservation

eNOT MS4 Acceptance

for construction activities seeking termination from the

SPDES General Permit for Stormwater Discharges from Construction Activity, GP-0-25-001 (CGP)

(The completed form must be attached to the eNOT, which must be submitted to NYSDEC electronically in accordance with CGP Part V.A.5.)

I. Project Owner/Operator Information

- a. Owner/Operator Name:
- b. Contact Person:
- c. Street Address:
- d. City/State/Zip:

II. Project Site Information

- a. Project/Site Name:
- b. Street Address:
- c. City/State/Zip:
- d. CGP SPDES Permit ID:

III. Traditional Land Use Control MS4 Operator Information

- a. Name of MS4 Operator:
- b. MS4 SPDES Permit ID Number: NYR20A
- c. Street Address:
- d. City/State/Zip:
- e. Telephone Number:

IV. Certification Statement

I have determined that it is acceptable for the owner or operator of the construction project identified above to submit the electronic Notice of Termination in accordance with CGP Part V. I certify under penalty of law that this document and all attachments were prepared under my direction or supervision in accordance with a system designed to assure that qualified personnel properly gather and evaluate the information submitted. Based on my inquiry of the person or persons who manage the system, or those persons directly responsible for gathering the information, the information submitted is, to the best of my knowledge and belief, true, accurate, and complete. I am aware that there are significant penalties for submitting false information, including the possibility of fine and imprisonment for knowing violations.

- a. Printed name of the principal executive officer or ranking elected official for the MS4 Operator or their duly authorized representative in accordance with CGP Part VII.J.2.:
- b. Title/Position:
- c. Signature:
- d. Date:



Appendix K:
Deep Ripping and Decompaction





New York State
DEPARTMENT OF ENVIRONMENTAL CONSERVATION

Division of Water

Deep-Ripping and Decompaction

April 2008

New York State
Department of Environmental Conservation

Document Prepared by:

John E. Lacey,
Land Resource Consultant and Environmental Compliance Monitor
(Formerly with the Division of Agricultural Protection and Development Services,
NYS Dept. of Agriculture & Markets)

Alternative Stormwater Management Deep-Ripping and Decompaction

Description

The two-phase practice of 1) “Deep Ripping;” and 2) “Decompaction” (deep subsoiling), of the soil material as a step in the cleanup and restoration/landscaping of a construction site, helps mitigate the physically induced impacts of soil compression; i.e.: soil compaction or the substantial increase in the bulk density of the soil material.

Deep Ripping and Decompaction are key factors which help in restoring soil pore space and permeability for water infiltration. Conversely, the physical actions of cut-and-fill work, land grading, the ongoing movement of construction equipment and the transport of building materials throughout a site alter the architecture and structure of the soil, resulting in: the mixing of layers (horizons) of soil materials, compression of those materials and diminished soil porosity which, if left unchecked, severely impairs the soil’s water holding capacity and vertical drainage (rainfall infiltration), from the surface downward.

In a humid climate region, compaction damage on a site is virtually guaranteed over the duration of a project. Soil in very moist to wet condition when compacted, will have severely reduced permeability. Figure 1 displays the early stage of the deep-ripping phase (Note that all topsoil was stripped prior to construction access, and it remains stockpiled until the next phase – decompaction – is complete). A heavy-duty tractor is pulling a three-shank ripper on the first of several series of incrementally deepening passes through the construction access corridor’s densely compressed subsoil material. Figure 2 illustrates the approximate volumetric composition of a loam surface soil when conditions are good for plant growth, with adequate natural pore space for fluctuating moisture conditions.



Fig. 1. A typical deep ripping phase of this practice, during the first in a series of progressively deeper “rips” through severely compressed subsoil.

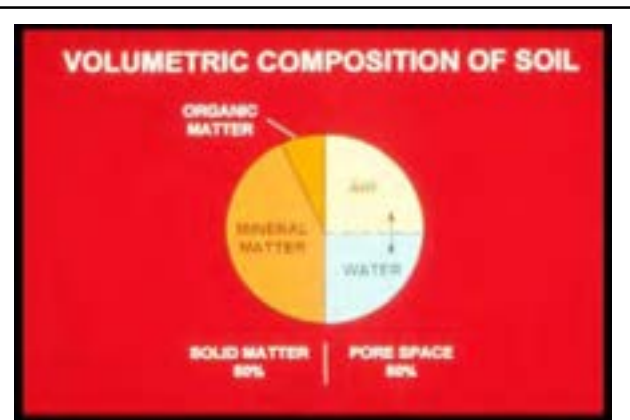


Fig. 2. About 50% of the volume of undisturbed loam surface soil is pore space, when soil is in good condition for plant growth. Brady, 2002.

Recommended Application of Practice

The objective of Deep Ripping and Decompaction is to effectively fracture (vertically and laterally) through the thickness of the physically compressed subsoil material (see Figure 3), restoring soil porosity and permeability and aiding infiltration to help reduce runoff. Together with topsoil stripping, the “two-phase” practice of Deep Ripping and Decompaction first became established as a “best management practice” through ongoing success on commercial farmlands affected by heavy utility construction right-of-way projects (transmission pipelines and large power lines).



Fig. 3. Construction site with significant compaction of the deep basal till subsoil extends 24 inches below this exposed cut-and-fill work surface.

Soil permeability, soil drainage and cropland productivity were restored. For broader construction application, the two-phase practice of Deep Ripping and Decompaction is best adapted to areas impacted with significant soil compaction, on contiguous open portions of large construction sites and inside long, open construction corridors used as temporary access over the duration of construction. Each mitigation area should have minimal above-and-below-ground obstructions for the easy avoidance and maneuvering of a large tractor and ripping/decompacting implements. Conversely, the complete two-phase practice is not recommended in congested or obstructed areas due to the limitations on tractor and implement movement.

Benefits

Aggressive “deep ripping” through the compressed thickness of exposed subsoil before the replacement/respreading of the topsoil layer, followed by “decompaction,” i.e.: “sub-soiling,” through the restored topsoil layer down into the subsoil, offers the following benefits:

- Increases the project (larger size) area’s direct surface infiltration of rainfall by providing the open site’s mitigated soil condition and lowers the demand on concentrated runoff control structures
- Enhances direct groundwater recharge through greater dispersion across and through a broader surface than afforded by some runoff-control structural measures
- Decreases runoff volume generated and provides hydrologic source control
- May be planned for application in feasible open locations either alone or in

conjunction with plans for structural practices (e.g., subsurface drain line or infiltration basin) serving the same or contiguous areas

- Promotes successful long-term revegetation by restoring soil permeability, drainage and water holding capacity for healthy (rather than restricted) root-system development of trees, shrubs and deep rooted ground cover, minimizing plant drowning during wet periods and burnout during dry periods.

Feasibility/Limitations

The effectiveness of Deep Ripping and Decompaction is governed mostly by site factors such as: the original (undisturbed) soil's hydrologic characteristics; the general slope; local weather/timing (soil moisture) for implementation; the space-related freedom of equipment/implement maneuverability (noted above in **Recommended Application of Practice**), and by the proper selection and operation of tractor and implements (explained below in **Design Guidance**). The more notable site-related factors include:

Soil

In the undisturbed condition, each identified soil type comprising a site is grouped into one of four categories of soil hydrology, Hydrologic Soil Group A, B, C or D, determined primarily by a range of characteristics including soil texture, drainage capability when thoroughly wet, and depth to water table. The natural rates of infiltration and transmission of soil-water through the undisturbed soil layers for Group A is "high" with a low runoff potential while soils in Group B are moderate in infiltration and the transmission of soil-water with a moderate runoff potential, depending somewhat on slope. Soils in Group C have slow rates of infiltration and transmission of soil-water and a moderately high runoff potential influenced by soil texture and slope; while soils in Group D have exceptionally slow rates of infiltration and transmission of soil-water, and high runoff potential.

In Figure 4, the profile displays the undisturbed horizons of a soil in Hydrologic Soil Group C and the naturally slow rate of infiltration through the subsoil. The slow rate of infiltration begins immediately below the topsoil horizon (30 cm), due to the limited amount of macro pores, e.g.: natural subsoil fractures, worm holes and root channels. Infiltration after the construction-induced mixing and compression of such subsoil material is virtually absent; but can be restored back to this natural level with the two-phase practice of deep ripping and decompaction, followed by the permanent establishment of an appropriate, deep taproot

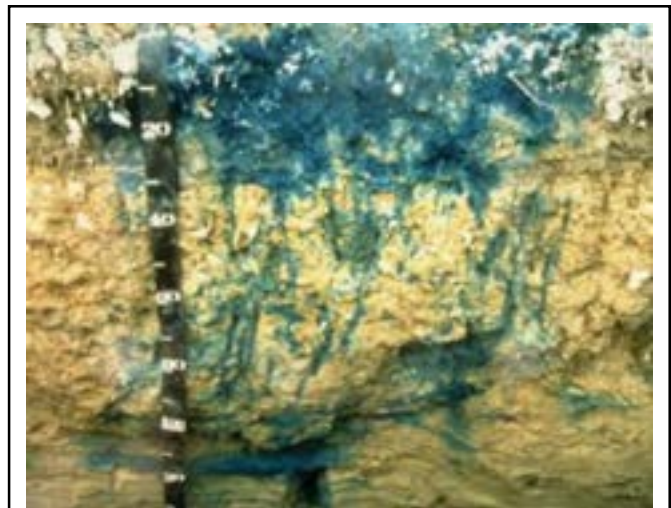


Fig. 4. Profile (in centimeters) displaying the infiltration test result of the natural undisturbed horizons of a soil in Hydrologic Soil Group C.

lawn/ground cover to help maintain the restored subsoil structure. Infiltration after construction-induced mixing and compression of such subsoil material can be notably rehabilitated with the Deep Ripping and Decomposition practice, which prepares the site for the appropriate long-term lawn/ground cover mix including deep taproot plants such as clover, fescue or trefoil, etc. needed for all rehabilitated soils.

Generally, soils in Hydrologic Soil Groups A and B, which respectively may include deep, well-drained, sandy-gravelly materials or deep, moderately well-drained basal till materials, are among the easier ones to restore permeability and infiltration, by deep ripping and decomposition. Among the many different soils in Hydrologic Soil Group C are those unique glacial tills having a natural fragipan zone, beginning about 12 to 18 inches (30 – 45cm), below surface. Although soils in Hydrologic Soil Group C do require a somewhat more carefully applied level of the Deep Ripping and Decomposition practice, it can greatly benefit such affected areas by reducing the runoff and fostering infiltration to a level equal to that of pre-disturbance.

Soils in Hydrologic Soil Group D typically have a permanent high water table close to the surface, influenced by a clay or other highly impervious layer of material. In many locations with clay subsoil material, the bulk density is so naturally high that heavy trafficking has little or no added impact on infiltration; and structural runoff control practices rather than Deep Ripping and Decomposition should be considered.

The information about Hydrologic Soil Groups is merely a general guideline. Site-specific data such as limited depths of cut-and-fill grading with minimal removal or translocation of the inherent subsoil materials (as analyzed in the county soil survey) or, conversely, the excavation and translocation of deeper, unconsolidated substratum or consolidated bedrock materials (unlike the analyzed subsoil horizons' materials referred to in the county soil survey) should always be taken into account.

Sites made up with significant quantities of large rocks, or having a very shallow depth to bedrock, are not conducive to deep ripping and decomposition (subsoiling); and other measures may be more practical.

Slope

The two-phase application of 1) deep ripping and 2) decomposition (deep subsoiling), is most practical on flat, gentle and moderate slopes. In some situations, such as but not limited to temporary construction access corridors, inclusion areas that are moderately steep along a project's otherwise gentle or moderate slope may also be deep ripped and decomposed. For limited instances of moderate steepness on other projects, however, the post-construction land use and the relative alignment of the potential ripping and decomposition work in relation to the lay of the slope should be reviewed for safety and practicality. In broad construction areas predominated by moderately steep or steep slopes, the practice is generally not used.

Local Weather/Timing/Soil Moisture

Effective fracturing of compressed subsoil material from the exposed work surface, laterally and vertically down through the affected zone is achieved only when the soil material is moderately dry to moderately moist. Neither one of the two-phases, deep ripping nor decomposition (deep

subsoiling), can be effectively conducted when the soil material (subsoil or replaced topsoil) is in either a “plastic” or “liquid” state of soil consistency. Pulling the respective implements legs through the soil when it is overly moist only results in the “slicing and smearing” of the material or added “squeezing and compression” instead of the necessary fracturing. Ample drying time is needed for a “rippable” soil condition not merely in the material close to the surface, but throughout the material located down to the bottom of the physically compressed zone of the subsoil.

The “poor man’s Atterberg field test” for soil plasticity is a simple “hand-roll” method used for quick, on-site determination of whether or not the moisture level of the affected soil material is low enough for: effective deep ripping of subsoil; respreading of topsoil in a friable state; and final decompaction (deep subsoiling). Using a sample of soil material obtained from the planned bottom depth of ripping, e.g.: 20 - 24 inches below exposed subsoil surface, the sample is hand rolled between the palms down to a 1/8-inch diameter thread. (Use the same test for stored topsoil material before respreading on the site.) If the respective soil sample crumbles apart in segments no greater than 3/8 of an inch long, by the time it is rolled down to 1/8 inch diameter, it is low enough in moisture for deep ripping (or topsoil replacement), and decompaction. Conversely, as shown in Figure 5, if the rolled sample stretches out in increments greater than 3/8 of an inch long before crumbling, it is in a “plastic” state of soil consistency and is too wet for subsoil ripping (as well as topsoil replacement) and final decompaction.



Fig. 5. Augered from a depth of 19 inches below the surface of the replaced topsoil, this subsoil sample was hand rolled to a 1/8-inch diameter. The test shows the soil at this site stretches out too far without crumbling; it indicates the material is in a plastic state of consistence, too wet for final decompaction (deep subsoiling) at this time.

Design Guidance

Beyond the above-noted site factors, a vital requirement for the effective Deep Ripping and Decompaction (deep subsoiling), is implementing the practice in its distinct, two-phase process:

- 1) Deep rip the affected thickness of exposed subsoil material (see Figure 10 and 11), aggressively fracturing it before the protected topsoil is reapplied on the site (see Figure 12); and
- 2) Decompact (deep subsoil), simultaneously through the restored topsoil layer and the upper half of the affected subsoil (Figure 13). The second phase, “decompaction,” mitigates the partial recompaction which occurs during the heavy process of topsoil spreading/grading. Prior to deep ripping and decompacting the site, all construction activity, including construction equipment and material storage, site cleanup and trafficking (Figure 14), should be finished; and the site closed off to further disturbance. Likewise, once the practice is underway and the area’s soil permeability and

rainfall infiltration are being restored, a policy limiting all further traffic to permanent travel lanes is maintained.

The other critical elements, outlined below, are: using the proper implements (deep, heavy-duty rippers and subsoilers), and ample pulling-power equipment (tractors); and conducting the practice at the appropriate speed, depth and pattern(s) of movement.

Note that an appropriate plan for the separate practice of establishing a healthy perennial ground cover, with deep rooting to help maintain the restored soil structure, should be developed in advance. This may require the assistance of an agronomist or landscape horticulturist.

Implements

Avoid the use of all undersize implements. The small-to-medium, light-duty tool will, at best, only “scarify” the uppermost surface portion of the mass of compacted subsoil material. The term “chisel plow” is commonly but incorrectly applied to a broad range of implements. While a few may be adapted for the moderate subsoiling of non-impacted soils, the majority are less durable and used for only lighter land-fitting (see Figure 6).



Fig. 6. A light duty chisel implement, not adequate for either the deep ripping or decompaction (deep subsoiling) phase.



Fig. 7. One of several variations of an agricultural ripper. This unit has long, rugged shanks mounted on a steel V-frame for deep, aggressive fracturing through Phase 1.

Use a “heavy duty” agricultural-grade, deep ripper (see Figures 7,9,10 and 11) for the first phase: the lateral and vertical fracturing of the mass of exposed and compressed subsoil, down and through, to the bottom of impact, prior to the replacement of the topsoil layer. (Any oversize rocks which are uplifted to the subsoil surface during the deep ripping phase are picked and removed.) Like the heavy-duty class of implement for the first phase, the decompaction (deep subsoiling) of Phase 2 is conducted with the heavy-duty version of the deep subsoiler. More preferable is the angled-leg variety of deep subsoiler (shown in Figures 8 and 13). It minimizes the inversion of the subsoil and topsoil layers while laterally and vertically fracturing the upper half of the previously ripped subsoil layer and all of the topsoil layer by delivering a momentary, wave-like “lifting and shattering” action up through the soil layers as it is pulled.

Pulling-Power of Equipment

Use the following rule of thumb for tractor horsepower (hp) whenever deep ripping and decompacting a significantly impacted site: For both types of implement, have at least 40 hp of tractor pull available for each mounted shank/ leg.

Using the examples of a 3-shank and a 5-shank implement, the respective tractors should have 120 and 200 hp available for fracturing down to the final depth of 20-to-24 inches per phase. Final depth for the deep ripping in Phase 1 is achieved incrementally by a progressive series of passes (see Depth and Patterns of Movement, below); while for Phase 2, the full operating depth of the deep subsoiler is applied from the beginning.

The operating speed for pulling both types of implement should not exceed 2 to 3 mph. At this slow and managed rate of operating speed, maximum functional performance is sustained by the tractor and the implement performing the soil fracturing. Referring to Figure 8, the implement is the 6-leg version of the deep angled-leg subsoiler. Its two outside legs are “chained up” so that only four legs will be engaged (at the maximum depth), requiring no less than 160 hp, (rather than 240 hp) of pull. The 4-wheel drive, articulated-frame tractor in Figure 8 is 174 hp. It will be decompacting this unobstructed, former construction access area simultaneously through 11 inches of replaced topsoil and the upper 12 inches of the previously deep-ripped subsoil. In constricted areas of Phase 1) Deep Ripping, a medium-size tractor with adequate hp, such as the one in Figure 9 pulling a 3-shank deep ripper, may be more maneuverable.

Some industrial-grade variations of ripping implements are attached to power graders and bulldozers. Although highly durable, they are generally not recommended. Typically, the shanks or “teeth” of these rippers are too short and stout; and they are mounted too far apart to achieve the well-distributed type of lateral and vertical fracturing of the soil materials necessary to restore soil permeability and infiltration. In addition, the power graders and bulldozers, as pullers, are far less maneuverable for turns and patterns than the tractor.



Fig. 8. A deep, angled-leg subsoiler, ideal for Phase 2 decompaction of after the topsoil layer is graded on top of the ripped subsoil.



Fig. 9. This medium tractor is pulling a 3-shank deep ripper. The severely compacted construction access corridor is narrow, and the 120 hp tractor is more maneuverable for Phase 1 deep ripping (subsoil fracturing), here.

Depth and Patterns of Movement

As previously noted both Phase 1 Deep Ripping through significantly compressed, exposed subsoil and Phase 2 Decompaction (deep subsoiling) through the replaced topsoil and upper subsoil need to be performed at maximum capable depth of each implement. With an implement's guide wheels attached, some have a "normal" maximum operating depth of 18 inches, while others may go deeper. In many situations, however, the tractor/implement operator must first remove the guide wheels and other non essential elements from the implement. This adapts the ripper or the deep subsoiler for skillful pulling with its frame only a few inches above surface, while the shanks or legs, fracture the soil material 20-to-24 inches deep.

There may be construction sites where the depth of the exposed subsoil's compression is moderate, e.g.: 12 inches, rather than deep. This can be verified by using a $\frac{3}{4}$ inch cone penetrometer and a shovel to test the subsoil for its level of compaction, incrementally, every three inches of increasing depth. Once the full thickness of the subsoil's compacted zone is finally "pieced" and there is a significant drop in the psi measurements of the soil penetrometer, the depth/thickness of compaction is determined. This is repeated at several representative locations of the construction site. If the thickness of the site's subsoil compaction is verified as, for example, ten inches, then the Phase 1 Deep Ripping can be correspondingly reduced to the implement's minimum operable depth of 12 inches. However, the Phase 2 simultaneous Decompaction (subsoiling) of an 11 inch thick layer of replaced topsoil and the upper subsoil should run at the subsoiling implements full operating depth.



Fig. 10. An early pass with a 3-shank deep ripper penetrating only 8 inches into this worksite's severely compressed subsoil.



Fig. 11. A repeat run of the 3-shank ripper along the same patterned pass area as Fig. 9; here, incrementally reaching 18 of the needed 22 inches of subsoil fracture.

Typically, three separate series (patterns) are used for both the Phase 1 Deep Ripping and the Phase 2 Decompaction on significantly compacted sites. For Phase 1, each series begins with a moderate depth of rip and, by repeat-pass, continues until full depth is reached. Phase 2 applies the full depth of Decompaction (subsoiling), from the beginning.

Every separate series (pattern) consists of parallel, forward-and-return runs, with each progressive

pass of the implement's legs or shanks evenly staggered between those from the previous pass. This compensates for the shank or leg-spacing on the implement, e.g., with 24-to-30 inches between each shank or leg. The staggered return pass ensures lateral and vertical fracturing actuated every 12 to 15 inches across the densely compressed soil mass.

Large, Unobstructed Areas

For larger easy areas, use the standard patterns of movement:

- The first series (pattern) of passes is applied lengthwise, parallel with the longest spread of the site; gradually progressing across the site's width, with each successive pass.
- The second series runs obliquely, crossing the first series at an angle of about 45 degrees.
- The third series runs at right angle (or 90 degrees), to the first series to complete the fracturing and shattering on severely compacted sites, and avoid leaving large unbroken blocks of compressed soil material. (In certain instances, the third series may be optional, depending on how thoroughly the first two series loosen the material and eliminate large chunks/blocks of material as verified by tests with a 3/4-inch cone penetrometer.)



Fig. 12. Moderately dry topsoil is being replaced on the affected site now that Phase 1 deep ripping of the compressed subsoil is complete.



Fig. 13. The same deep, angled-leg subsoiler shown in Fig. 7 is engaged at maximum depth for Phase 2, decompaction (deep soiling), of the replaced topsoil and the upper subsoil materials.

Corridors

In long corridors of limited width and less maneuverability than larger sites, e.g.: along compacted areas used as temporary construction access, a modified series of pattern passes are used.

- First, apply the same initial lengthwise, parallel series of passes described above.

- A second series of passes makes a broad “S” shaped pattern of rips, continually and gradually alternating the “S” curves between opposite edges inside the compacted corridor.
- The third and final series again uses the broad, alternating S pattern, but it is “flip-flopped” to continually cross the previous S pattern along the corridor’s centerline. This final series of the S pattern curves back along the edge areas skipped by the second series.

Maintenance and Cost

Once the two-phase practice of Deep Ripping and Decomposition is completed, two items are essential for maintaining a site’s soil porosity and permeability for infiltration. They are: planting and maintaining the appropriate ground cover with deep roots to maintain the soil structure (see Figure 15); and keeping the site free of traffic or other weight loads.

Note that site-specific choice of an appropriate vegetative ground-cover seed mix, including the proper seeding ratio of one or more perennial species with a deep taproot system and the proper amount of lime and soil nutrients (fertilizer mix) adapted to the soil-needs, are basic to the final practice of landscaping, i.e: surface tillage, seeding/planting/fertilizing and culti-packing or mulching is applied. The "maintenance" of an effectively deep-ripped and decompacted area is generally limited to the successful perennial (long-term) landscape ground cover; as long as no weight-bearing force of soil compaction is applied.



Fig. 14. The severely compacted soil of a temporary construction yard used daily by heavy equipment for four months; shown before deep ripping, topsoil replacement, and decompaction.



Fig. 15. The same site as Fig. 14 after deep ripping of the exposed subsoil, topsoil replacement, decompaction through the topsoil and upper subsoil and final surface tillage and revegetation to maintain soil permeability and infiltration.

The Deep Ripping and Decompaction practice is, by necessity, more extensive than periodic subsoiling of farmland. The cost of deep ripping and decompacting (deep subsoiling), will vary according to the depth and severity of soil-material compression and the relative amount of tractor and implement time that is required. In some instances, depending on open maneuverability, two-to-three acres of compacted project area may be deep-ripped in one day. In other situations of more severe compaction and - or less maneuverability, as little as one acre may be fully ripped in a day. Generally, if the Phase 1) Deep Ripping is fully effective, the Phase 2) Decompaction should be completed in $2/3$ to $3/4$ of the time required for Phase 1.

Using the example of two acres of Phase 1) Deep Ripping in one day, at \$1800 per day, the net cost is \$900 per acre. If the Phase 2) Decompacting or deep subsoiling takes $3/4$ the time as Phase 1, it costs \$675 per acre for a combined total of \$1575 per acre to complete the practice (these figures do not include the cost of the separate practice of topsoil stripping and replacement). Due to the many variables, it must be recognized that cost will be determined by the specific conditions or constraints of the site and the availability of proper equipment.

Resources

Publications:

- American Society of Agricultural Engineers. 1971. *Compaction of Agricultural Soils*. ASAE.
- Brady, N.C., and R.R. Weil. 2002. *The Nature and Properties of Soils*. 13th ed. Pearson Education, Inc.
- Baver, L.D. 1948. *Soil Physics*. John Wiley & Sons.
- Carpachi, N. 1987 (1995 fifth printing). *Excavation and Grading Handbook, Revised*. 2nd ed. Craftsman Book Company
- Ellis, B. (Editor). 1997. *Safe & Easy Lawn Care: The Complete Guide to Organic Low Maintenance Lawn*. Houghton Mifflin.
- Harpstead, M.I., T.J. Sauer, and W.F. Bennett. 2001. *Soil Science Simplified*. 4th ed. Iowa State University Press.
- Magdoff, F., and H. van Es. 2000. *Building Soils for Better Crops*. 2nd ed. Sustainable Agricultural Networks
- McCarthy, D.F. 1993. *Essentials of Soil Mechanics and Foundations, Basic Geotechnics* 4th ed. Regents/Prentice Hall.
- Plaster, E.J. 1992. *Soil Science & Management*. 3rd ed. Delmar Publishers.
- Union Gas Limited, Ontario, Canada. 1984. *Rehabilitation of Agricultural Lands, Dawn-Kerwood Loop Pipeline; Technical Report*. Ecological Services for Planning, Ltd.; Robinson, Merritt & Devries, Ltd. and Smith, Hoffman Associates, Ltd.
- US Department of Agriculture in cooperation with Cornell University Agricultural Experiment Station. Various years. *Soil Survey of (various names) County, New York*. USDA.

Internet Access:

- Examples of implements:
V-Rippers. Access by internet search of *John Deere Ag -New Equipment for 915* (larger-frame model) *V-Rippe*; and, *for 913* (smaller-frame model) *V-Ripper*. Deep, angled-leg subsoiler. Access by internet search of: *Bigham Brothers Shear Bolt Paratill-Subsoiler*.
http://salesmanual.deere.com/sales/salesmanual/en_NA/primary_tillage/2008/feature/rippers/915v_pattern_frame.html?sbu=ag&link=prodcats Last visited March 08.
- Soils data of USDA Natural Resources Conservation Service. *NRCS Web Soil Survey*.
<http://websoilsurvey.nrcs.usda.gov/app/> and *USDA-NRCS Official Soil Series Descriptions; View by Name*. <http://ortho.ftw.nrcs.usda.gov/cgi-bin/osd/osdname.cgi> . Last visited Jan. 08.
- Soil penetrometer information. Access by internet searches of: *Diagnosing Soil Compaction using a Penetrometer (soil compaction tester)*, *PSU Extension*; as well as *Dickey-john Soil Compaction Tester*.
<http://www.dickey-johnproducts.com/pdf/SoilCompactionTest.pdf> and <http://cropsoil.psu.edu/Extension/Facts/uc178pdf> Last visited Sept. 07



Appendix L:
Permit Eligibility



**Full Environmental Assessment Form
Part 1 - Project and Setting**

Instructions for Completing Part 1

Part 1 is to be completed by the applicant or project sponsor. Responses become part of the application for approval or funding, are subject to public review, and may be subject to further verification.

Complete Part 1 based on information currently available. If additional research or investigation would be needed to fully respond to any item, please answer as thoroughly as possible based on current information; indicate whether missing information does not exist, or is not reasonably available to the sponsor; and, when possible, generally describe work or studies which would be necessary to update or fully develop that information.

Applicants/sponsors must complete all items in Sections A & B. In Sections C, D & E, most items contain an initial question that must be answered either “Yes” or “No”. If the answer to the initial question is “Yes”, complete the sub-questions that follow. If the answer to the initial question is “No”, proceed to the next question. Section F allows the project sponsor to identify and attach any additional information. Section G requires the name and signature of the applicant or project sponsor to verify that the information contained in Part 1 is accurate and complete.

A. Project and Applicant/Sponsor Information.

Name of Action or Project:		
Project Location (describe, and attach a general location map):		
Brief Description of Proposed Action (include purpose or need):		
Name of Applicant/Sponsor:		Telephone:
		E-Mail:
Address:		
City/PO:	State:	Zip Code:
Project Contact (if not same as sponsor; give name and title/role):		Telephone:
		E-Mail:
Address:		
City/PO:	State:	Zip Code:
Property Owner (if not same as sponsor):		Telephone:
		E-Mail:
Address:		
City/PO:	State:	Zip Code:

B. Government Approvals

B. Government Approvals, Funding, or Sponsorship. (“Funding” includes grants, loans, tax relief, and any other forms of financial assistance.)

Government Entity	If Yes: Identify Agency and Approval(s) Required	Application Date (Actual or projected)
a. City Counsel, Town Board, or Village Board of Trustees <input type="checkbox"/> Yes <input type="checkbox"/> No		
b. City, Town or Village Planning Board or Commission <input type="checkbox"/> Yes <input type="checkbox"/> No		
c. City, Town or Village Zoning Board of Appeals <input type="checkbox"/> Yes <input type="checkbox"/> No		
d. Other local agencies <input type="checkbox"/> Yes <input type="checkbox"/> No		
e. County agencies <input type="checkbox"/> Yes <input type="checkbox"/> No		
f. Regional agencies <input type="checkbox"/> Yes <input type="checkbox"/> No		
g. State agencies <input type="checkbox"/> Yes <input type="checkbox"/> No		
h. Federal agencies <input type="checkbox"/> Yes <input type="checkbox"/> No		
<p>i. Coastal Resources.</p> <p><i>i.</i> Is the project site within a Coastal Area, or the waterfront area of a Designated Inland Waterway? <input type="checkbox"/> Yes <input type="checkbox"/> No</p> <p><i>ii.</i> Is the project site located in a community with an approved Local Waterfront Revitalization Program? <input type="checkbox"/> Yes <input type="checkbox"/> No</p> <p><i>iii.</i> Is the project site within a Coastal Erosion Hazard Area? <input type="checkbox"/> Yes <input type="checkbox"/> No</p>		

C. Planning and Zoning

C.1. Planning and zoning actions.

Will administrative or legislative adoption, or amendment of a plan, local law, ordinance, rule or regulation be the only approval(s) which must be granted to enable the proposed action to proceed? Yes No

- **If Yes**, complete sections C, F and G.
- **If No**, proceed to question C.2 and complete all remaining sections and questions in Part 1

C.2. Adopted land use plans.

a. Do any municipally- adopted (city, town, village or county) comprehensive land use plan(s) include the site where the proposed action would be located? Yes No

If Yes, does the comprehensive plan include specific recommendations for the site where the proposed action would be located? Yes No

b. Is the site of the proposed action within any local or regional special planning district (for example: Greenway; Brownfield Opportunity Area (BOA); designated State or Federal heritage area; watershed management plan; or other?) Yes No

If Yes, identify the plan(s):

c. Is the proposed action located wholly or partially within an area listed in an adopted municipal open space plan, or an adopted municipal farmland protection plan? Yes No

If Yes, identify the plan(s):

C.3. Zoning

a. Is the site of the proposed action located in a municipality with an adopted zoning law or ordinance. Yes No
If Yes, what is the zoning classification(s) including any applicable overlay district?

b. Is the use permitted or allowed by a special or conditional use permit? Yes No

c. Is a zoning change requested as part of the proposed action? Yes No

If Yes,

i. What is the proposed new zoning for the site? _____

C.4. Existing community services.

a. In what school district is the project site located? _____

b. What police or other public protection forces serve the project site?

c. Which fire protection and emergency medical services serve the project site?

d. What parks serve the project site?

D. Project Details

D.1. Proposed and Potential Development

a. What is the general nature of the proposed action (e.g., residential, industrial, commercial, recreational; if mixed, include all components)?

b. a. Total acreage of the site of the proposed action? _____ acres
b. Total acreage to be physically disturbed? _____ acres
c. Total acreage (project site and any contiguous properties) owned or controlled by the applicant or project sponsor? _____ acres

c. Is the proposed action an expansion of an existing project or use? Yes No
i. If Yes, what is the approximate percentage of the proposed expansion and identify the units (e.g., acres, miles, housing units, square feet)? % _____ Units: _____

d. Is the proposed action a subdivision, or does it include a subdivision? Yes No
If Yes,

i. Purpose or type of subdivision? (e.g., residential, industrial, commercial; if mixed, specify types)

ii. Is a cluster/conservation layout proposed? Yes No

iii. Number of lots proposed? _____

iv. Minimum and maximum proposed lot sizes? Minimum _____ Maximum _____

e. Will the proposed action be constructed in multiple phases? Yes No

i. If No, anticipated period of construction: _____ months

ii. If Yes:

- Total number of phases anticipated _____
- Anticipated commencement date of phase 1 (including demolition) _____ month _____ year
- Anticipated completion date of final phase _____ month _____ year

• Generally describe connections or relationships among phases, including any contingencies where progress of one phase may determine timing or duration of future phases: _____

f. Does the project include new residential uses? Yes No
 If Yes, show numbers of units proposed.

	<u>One Family</u>	<u>Two Family</u>	<u>Three Family</u>	<u>Multiple Family (four or more)</u>
Initial Phase	_____	_____	_____	_____
At completion	_____	_____	_____	_____
of all phases	_____	_____	_____	_____

g. Does the proposed action include new non-residential construction (including expansions)? Yes No
 If Yes,

i. Total number of structures _____

ii. Dimensions (in feet) of largest proposed structure: _____ height; _____ width; and _____ length

iii. Approximate extent of building space to be heated or cooled: _____ square feet

h. Does the proposed action include construction or other activities that will result in the impoundment of any liquids, such as creation of a water supply, reservoir, pond, lake, waste lagoon or other storage? Yes No
 If Yes,

i. Purpose of the impoundment: _____

ii. If a water impoundment, the principal source of the water: Ground water Surface water streams Other specify: _____

iii. If other than water, identify the type of impounded/contained liquids and their source.

iv. Approximate size of the proposed impoundment. Volume: _____ million gallons; surface area: _____ acres

v. Dimensions of the proposed dam or impounding structure: _____ height; _____ length

vi. Construction method/materials for the proposed dam or impounding structure (e.g., earth fill, rock, wood, concrete):

D.2. Project Operations

a. Does the proposed action include any excavation, mining, or dredging, during construction, operations, or both? Yes No
 (Not including general site preparation, grading or installation of utilities or foundations where all excavated materials will remain onsite)
 If Yes:

i. What is the purpose of the excavation or dredging? _____

ii. How much material (including rock, earth, sediments, etc.) is proposed to be removed from the site?

- Volume (specify tons or cubic yards): _____
- Over what duration of time? _____

iii. Describe nature and characteristics of materials to be excavated or dredged, and plans to use, manage or dispose of them.

iv. Will there be onsite dewatering or processing of excavated materials? Yes No
 If yes, describe. _____

v. What is the total area to be dredged or excavated? _____ acres

vi. What is the maximum area to be worked at any one time? _____ acres

vii. What would be the maximum depth of excavation or dredging? _____ feet

viii. Will the excavation require blasting? Yes No

ix. Summarize site reclamation goals and plan: _____

b. Would the proposed action cause or result in alteration of, increase or decrease in size of, or encroachment into any existing wetland, waterbody, shoreline, beach or adjacent area? Yes No
 If Yes:

i. Identify the wetland or waterbody which would be affected (by name, water index number, wetland map number or geographic description): _____

ii. Describe how the proposed action would affect that waterbody or wetland, e.g. excavation, fill, placement of structures, or alteration of channels, banks and shorelines. Indicate extent of activities, alterations and additions in square feet or acres:

iii. Will the proposed action cause or result in disturbance to bottom sediments? Yes No

If Yes, describe: _____

iv. Will the proposed action cause or result in the destruction or removal of aquatic vegetation? Yes No

If Yes:

- acres of aquatic vegetation proposed to be removed: _____
- expected acreage of aquatic vegetation remaining after project completion: _____
- purpose of proposed removal (e.g. beach clearing, invasive species control, boat access): _____
- proposed method of plant removal: _____
- if chemical/herbicide treatment will be used, specify product(s): _____

v. Describe any proposed reclamation/mitigation following disturbance: _____

c. Will the proposed action use, or create a new demand for water? Yes No

If Yes:

i. Total anticipated water usage/demand per day: _____ gallons/day

ii. Will the proposed action obtain water from an existing public water supply? Yes No

If Yes:

- Name of district or service area: _____
- Does the existing public water supply have capacity to serve the proposal? Yes No
- Is the project site in the existing district? Yes No
- Is expansion of the district needed? Yes No
- Do existing lines serve the project site? Yes No

iii. Will line extension within an existing district be necessary to supply the project? Yes No

If Yes:

- Describe extensions or capacity expansions proposed to serve this project: _____
- Source(s) of supply for the district: _____

iv. Is a new water supply district or service area proposed to be formed to serve the project site? Yes No

If Yes:

- Applicant/sponsor for new district: _____
- Date application submitted or anticipated: _____
- Proposed source(s) of supply for new district: _____

v. If a public water supply will not be used, describe plans to provide water supply for the project: _____

vi. If water supply will be from wells (public or private), what is the maximum pumping capacity: _____ gallons/minute.

d. Will the proposed action generate liquid wastes? Yes No

If Yes:

i. Total anticipated liquid waste generation per day: _____ gallons/day

ii. Nature of liquid wastes to be generated (e.g., sanitary wastewater, industrial; if combination, describe all components and approximate volumes or proportions of each): _____

iii. Will the proposed action use any existing public wastewater treatment facilities? Yes No

If Yes:

- Name of wastewater treatment plant to be used: _____
- Name of district: _____
- Does the existing wastewater treatment plant have capacity to serve the project? Yes No
- Is the project site in the existing district? Yes No
- Is expansion of the district needed? Yes No

• Do existing sewer lines serve the project site? Yes No
 • Will a line extension within an existing district be necessary to serve the project? Yes No
 If Yes:
 • Describe extensions or capacity expansions proposed to serve this project: _____

iv. Will a new wastewater (sewage) treatment district be formed to serve the project site? Yes No
 If Yes:
 • Applicant/sponsor for new district: _____
 • Date application submitted or anticipated: _____
 • What is the receiving water for the wastewater discharge? _____

v. If public facilities will not be used, describe plans to provide wastewater treatment for the project, including specifying proposed receiving water (name and classification if surface discharge or describe subsurface disposal plans):

vi. Describe any plans or designs to capture, recycle or reuse liquid waste: _____

e. Will the proposed action disturb more than one acre and create stormwater runoff, either from new point sources (i.e. ditches, pipes, swales, curbs, gutters or other concentrated flows of stormwater) or non-point source (i.e. sheet flow) during construction or post construction? Yes No
 If Yes:
 i. How much impervious surface will the project create in relation to total size of project parcel?
 _____ Square feet or _____ acres (impervious surface)
 _____ Square feet or _____ acres (parcel size)
 ii. Describe types of new point sources. _____

iii. Where will the stormwater runoff be directed (i.e. on-site stormwater management facility/structures, adjacent properties, groundwater, on-site surface water or off-site surface waters)?

 • If to surface waters, identify receiving water bodies or wetlands: _____

• Will stormwater runoff flow to adjacent properties? Yes No

iv. Does the proposed plan minimize impervious surfaces, use pervious materials or collect and re-use stormwater? Yes No

f. Does the proposed action include, or will it use on-site, one or more sources of air emissions, including fuel combustion, waste incineration, or other processes or operations? Yes No
 If Yes, identify:
 i. Mobile sources during project operations (e.g., heavy equipment, fleet or delivery vehicles)

 ii. Stationary sources during construction (e.g., power generation, structural heating, batch plant, crushers)

 iii. Stationary sources during operations (e.g., process emissions, large boilers, electric generation)

g. Will any air emission sources named in D.2.f (above), require a NY State Air Registration, Air Facility Permit, or Federal Clean Air Act Title IV or Title V Permit? Yes No
 If Yes:
 i. Is the project site located in an Air quality non-attainment area? (Area routinely or periodically fails to meet ambient air quality standards for all or some parts of the year) Yes No
 ii. In addition to emissions as calculated in the application, the project will generate:
 • _____ Tons/year (short tons) of Carbon Dioxide (CO₂)
 • _____ Tons/year (short tons) of Nitrous Oxide (N₂O)
 • _____ Tons/year (short tons) of Perfluorocarbons (PFCs)
 • _____ Tons/year (short tons) of Sulfur Hexafluoride (SF₆)
 • _____ Tons/year (short tons) of Carbon Dioxide equivalent of Hydroflouorocarbons (HFCs)
 • _____ Tons/year (short tons) of Hazardous Air Pollutants (HAPs)

h. Will the proposed action generate or emit methane (including, but not limited to, sewage treatment plants, landfills, composting facilities)? Yes No
 If Yes:
 i. Estimate methane generation in tons/year (metric): _____
 ii. Describe any methane capture, control or elimination measures included in project design (e.g., combustion to generate heat or electricity, flaring): _____

i. Will the proposed action result in the release of air pollutants from open-air operations or processes, such as quarry or landfill operations? Yes No
 If Yes: Describe operations and nature of emissions (e.g., diesel exhaust, rock particulates/dust): _____

j. Will the proposed action result in a substantial increase in traffic above present levels or generate substantial new demand for transportation facilities or services? Yes No
 If Yes:
 i. When is the peak traffic expected (Check all that apply): Morning Evening Weekend
 Randomly between hours of _____ to _____.
 ii. For commercial activities only, projected number of truck trips/day and type (e.g., semi trailers and dump trucks): _____
 iii. Parking spaces: Existing _____ Proposed _____ Net increase/decrease _____
 iv. Does the proposed action include any shared use parking? Yes No
 v. If the proposed action includes any modification of existing roads, creation of new roads or change in existing access, describe: _____
 vi. Are public/private transportation service(s) or facilities available within 1/2 mile of the proposed site? Yes No
 vii. Will the proposed action include access to public transportation or accommodations for use of hybrid, electric or other alternative fueled vehicles? Yes No
 viii. Will the proposed action include plans for pedestrian or bicycle accommodations for connections to existing pedestrian or bicycle routes? Yes No

k. Will the proposed action (for commercial or industrial projects only) generate new or additional demand for energy? Yes No
 If Yes:
 i. Estimate annual electricity demand during operation of the proposed action: _____
 ii. Anticipated sources/suppliers of electricity for the project (e.g., on-site combustion, on-site renewable, via grid/local utility, or other): _____
 iii. Will the proposed action require a new, or an upgrade, to an existing substation? Yes No

l. Hours of operation. Answer all items which apply.
 i. During Construction:
 • Monday - Friday: _____
 • Saturday: _____
 • Sunday: _____
 • Holidays: _____
 ii. During Operations:
 • Monday - Friday: _____
 • Saturday: _____
 • Sunday: _____
 • Holidays: _____

m. Will the proposed action produce noise that will exceed existing ambient noise levels during construction, operation, or both? Yes No
 If yes:
 i. Provide details including sources, time of day and duration:

ii. Will the proposed action remove existing natural barriers that could act as a noise barrier or screen? Yes No
 Describe: _____

n. Will the proposed action have outdoor lighting? Yes No
 If yes:
 i. Describe source(s), location(s), height of fixture(s), direction/aim, and proximity to nearest occupied structures:

ii. Will proposed action remove existing natural barriers that could act as a light barrier or screen? Yes No
 Describe: _____

o. Does the proposed action have the potential to produce odors for more than one hour per day? Yes No
 If Yes, describe possible sources, potential frequency and duration of odor emissions, and proximity to nearest occupied structures: _____

p. Will the proposed action include any bulk storage of petroleum (combined capacity of over 1,100 gallons) or chemical products 185 gallons in above ground storage or any amount in underground storage? Yes No
 If Yes:
 i. Product(s) to be stored _____
 ii. Volume(s) _____ per unit time _____ (e.g., month, year)
 iii. Generally, describe the proposed storage facilities: _____

q. Will the proposed action (commercial, industrial and recreational projects only) use pesticides (i.e., herbicides, insecticides) during construction or operation? Yes No
 If Yes:
 i. Describe proposed treatment(s):

ii. Will the proposed action use Integrated Pest Management Practices? Yes No

r. Will the proposed action (commercial or industrial projects only) involve or require the management or disposal of solid waste (excluding hazardous materials)? Yes No
 If Yes:
 i. Describe any solid waste(s) to be generated during construction or operation of the facility:
 • Construction: _____ tons per _____ (unit of time)
 • Operation : _____ tons per _____ (unit of time)
 ii. Describe any proposals for on-site minimization, recycling or reuse of materials to avoid disposal as solid waste:
 • Construction: _____

 • Operation: _____

 iii. Proposed disposal methods/facilities for solid waste generated on-site:
 • Construction: _____

 • Operation: _____

s. Does the proposed action include construction or modification of a solid waste management facility? Yes No
 If Yes:
 i. Type of management or handling of waste proposed for the site (e.g., recycling or transfer station, composting, landfill, or other disposal activities): _____
 ii. Anticipated rate of disposal/processing:
 • _____ Tons/month, if transfer or other non-combustion/thermal treatment, or
 • _____ Tons/hour, if combustion or thermal treatment
 iii. If landfill, anticipated site life: _____ years

t. Will the proposed action at the site involve the commercial generation, treatment, storage, or disposal of hazardous waste? Yes No
 If Yes:
 i. Name(s) of all hazardous wastes or constituents to be generated, handled or managed at facility: _____

 ii. Generally describe processes or activities involving hazardous wastes or constituents: _____

 iii. Specify amount to be handled or generated _____ tons/month
 iv. Describe any proposals for on-site minimization, recycling or reuse of hazardous constituents: _____

 v. Will any hazardous wastes be disposed at an existing offsite hazardous waste facility? Yes No
 If Yes: provide name and location of facility: _____

 If No: describe proposed management of any hazardous wastes which will not be sent to a hazardous waste facility:

E. Site and Setting of Proposed Action

E.1. Land uses on and surrounding the project site

a. Existing land uses.
 i. Check all uses that occur on, adjoining and near the project site.
 Urban Industrial Commercial Residential (suburban) Rural (non-farm)
 Forest Agriculture Aquatic Other (specify): _____
 ii. If mix of uses, generally describe:

b. Land uses and covertypes on the project site.

Land use or Covertypes	Current Acreage	Acreage After Project Completion	Change (Acres +/-)
• Roads, buildings, and other paved or impervious surfaces			
• Forested			
• Meadows, grasslands or brushlands (non-agricultural, including abandoned agricultural)			
• Agricultural (includes active orchards, field, greenhouse etc.)			
• Surface water features (lakes, ponds, streams, rivers, etc.)			
• Wetlands (freshwater or tidal)			
• Non-vegetated (bare rock, earth or fill)			
• Other Describe: _____ _____			

c. Is the project site presently used by members of the community for public recreation? Yes No
i. If Yes: explain: _____

d. Are there any facilities serving children, the elderly, people with disabilities (e.g., schools, hospitals, licensed day care centers, or group homes) within 1500 feet of the project site? Yes No
If Yes,
i. Identify Facilities:

e. Does the project site contain an existing dam? Yes No
If Yes:
i. Dimensions of the dam and impoundment:

- Dam height: _____ feet
- Dam length: _____ feet
- Surface area: _____ acres
- Volume impounded: _____ gallons OR acre-feet

ii. Dam's existing hazard classification: _____
iii. Provide date and summarize results of last inspection:

f. Has the project site ever been used as a municipal, commercial or industrial solid waste management facility, or does the project site adjoin property which is now, or was at one time, used as a solid waste management facility? Yes No
If Yes:
i. Has the facility been formally closed? Yes No

- If yes, cite sources/documentation: _____

ii. Describe the location of the project site relative to the boundaries of the solid waste management facility:

iii. Describe any development constraints due to the prior solid waste activities: _____

g. Have hazardous wastes been generated, treated and/or disposed of at the site, or does the project site adjoin property which is now or was at one time used to commercially treat, store and/or dispose of hazardous waste? Yes No
If Yes:
i. Describe waste(s) handled and waste management activities, including approximate time when activities occurred:

h. Potential contamination history. Has there been a reported spill at the proposed project site, or have any remedial actions been conducted at or adjacent to the proposed site? Yes No
If Yes:
i. Is any portion of the site listed on the NYSDEC Spills Incidents database or Environmental Site Remediation database? Check all that apply: Yes No
 Yes – Spills Incidents database Provide DEC ID number(s): _____
 Yes – Environmental Site Remediation database Provide DEC ID number(s): _____
 Neither database
ii. If site has been subject of RCRA corrective activities, describe control measures: _____

iii. Is the project within 2000 feet of any site in the NYSDEC Environmental Site Remediation database? Yes No
If yes, provide DEC ID number(s): _____
iv. If yes to (i), (ii) or (iii) above, describe current status of site(s):

v. Is the project site subject to an institutional control limiting property uses? Yes No

- If yes, DEC site ID number: _____
- Describe the type of institutional control (e.g., deed restriction or easement): _____
- Describe any use limitations: _____
- Describe any engineering controls: _____
- Will the project affect the institutional or engineering controls in place? Yes No
- Explain: _____

E.2. Natural Resources On or Near Project Site

a. What is the average depth to bedrock on the project site? _____ feet

b. Are there bedrock outcroppings on the project site? Yes No
 If Yes, what proportion of the site is comprised of bedrock outcroppings? _____%

c. Predominant soil type(s) present on project site: _____ %
 _____ %
 _____ %

d. What is the average depth to the water table on the project site? Average: _____ feet

e. Drainage status of project site soils: Well Drained: _____ % of site
 Moderately Well Drained: _____ % of site
 Poorly Drained _____ % of site

f. Approximate proportion of proposed action site with slopes: 0-10%: _____ % of site
 10-15%: _____ % of site
 15% or greater: _____ % of site
*Based on the NRCS Web Soil Survey and are subject to change

g. Are there any unique geologic features on the project site? Yes No
 If Yes, describe: _____

h. Surface water features.

i. Does any portion of the project site contain wetlands or other waterbodies (including streams, rivers, ponds or lakes)? Yes No

ii. Do any wetlands or other waterbodies adjoin the project site? Yes No
 If Yes to either *i* or *ii*, continue. If No, skip to E.2.i.

iii. Are any of the wetlands or waterbodies within or adjoining the project site regulated by any federal, state or local agency? Yes No

iv. For each identified regulated wetland and waterbody on the project site, provide the following information:

- Streams: Name _____ Classification _____
- Lakes or Ponds: Name _____ Classification _____
- Wetlands: Name _____ Approximate Size _____
- Wetland No. (if regulated by DEC) _____

v. Are any of the above water bodies listed in the most recent compilation of NYS water quality-impaired waterbodies? Yes No
 If yes, name of impaired water body/bodies and basis for listing as impaired: _____

i. Is the project site in a designated Floodway? Yes No

j. Is the project site in the 100-year Floodplain? Yes No

k. Is the project site in the 500-year Floodplain? Yes No

l. Is the project site located over, or immediately adjoining, a primary, principal or sole source aquifer? Yes No
 If Yes:
 i. Name of aquifer: _____

m. Identify the predominant wildlife species that occupy or use the project site: _____ _____ _____	
n. Does the project site contain a designated significant natural community? <input type="checkbox"/> Yes <input type="checkbox"/> No If Yes:	
i. Describe the habitat/community (composition, function, and basis for designation): _____ _____	
ii. Source(s) of description or evaluation: _____	
iii. Extent of community/habitat:	
<ul style="list-style-type: none"> • Currently: _____ acres • Following completion of project as proposed: _____ acres • Gain or loss (indicate + or -): _____ acres 	
o. Does project site contain any species of plant or animal that is listed by the federal government or NYS as endangered or threatened, or does it contain any areas identified as habitat for an endangered or threatened species? <input type="checkbox"/> Yes <input type="checkbox"/> No	
If Yes:	
i. Species and listing (endangered or threatened): _____ <div style="text-align: center;">(Threatened and endangered species study to be performed)</div>	
p. Does the project site contain any species of plant or animal that is listed by NYS as rare, or as a species of special concern? <input type="checkbox"/> Yes <input type="checkbox"/> No	
If Yes:	
i. Species and listing: _____ _____	
q. Is the project site or adjoining area currently used for hunting, trapping, fishing or shell fishing? <input type="checkbox"/> Yes <input type="checkbox"/> No If yes, give a brief description of how the proposed action may affect that use: _____ _____	
E.3. Designated Public Resources On or Near Project Site	
a. Is the project site, or any portion of it, located in a designated agricultural district certified pursuant to Agriculture and Markets Law, Article 25-AA, Section 303 and 304? <input type="checkbox"/> Yes <input type="checkbox"/> No If Yes, provide county plus district name/number: _____	
<div style="font-size: small; text-align: right;">Fields auto populated by the EAF Mapper. Saratoga County records do not outline the parcel as being within an agricultural district</div>	
b. Are agricultural lands consisting of highly productive soils present? <input type="checkbox"/> Yes <input type="checkbox"/> No i. If Yes: acreage(s) on project site? _____ ii. Source(s) of soil rating(s): _____	
c. Does the project site contain all or part of, or is it substantially contiguous to, a registered National Natural Landmark? <input type="checkbox"/> Yes <input type="checkbox"/> No If Yes:	
i. Nature of the natural landmark: <input type="checkbox"/> Biological Community <input type="checkbox"/> Geological Feature ii. Provide brief description of landmark, including values behind designation and approximate size/extent: _____ _____	
d. Is the project site located in or does it adjoin a state listed Critical Environmental Area? <input type="checkbox"/> Yes <input type="checkbox"/> No If Yes:	
i. CEA name: _____ ii. Basis for designation: _____ iii. Designating agency and date: _____	

e. Does the project site contain, or is it substantially contiguous to, a building, archaeological site, or district which is listed on the National or State Register of Historic Places, or that has been determined by the Commissioner of the NYS Office of Parks, Recreation and Historic Preservation to be eligible for listing on the State Register of Historic Places?	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
If Yes:	
<i>i.</i> Nature of historic/archaeological resource: <input type="checkbox"/> Archaeological Site <input type="checkbox"/> Historic Building or District	
<i>ii.</i> Name: _____	
<i>iii.</i> Brief description of attributes on which listing is based: _____	
f. Is the project site, or any portion of it, located in or adjacent to an area designated as sensitive for archaeological sites on the NY State Historic Preservation Office (SHPO) archaeological site inventory?	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No
g. Have additional archaeological or historic site(s) or resources been identified on the project site?	
If Yes:	
<i>i.</i> Describe possible resource(s): _____	
<i>ii.</i> Basis for identification: _____	
h. Is the project site within five miles of any officially designated and publicly accessible federal, state, or local scenic or aesthetic resource?	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
If Yes:	
<i>i.</i> Identify resource: _____	
<i>ii.</i> Nature of, or basis for, designation (e.g., established highway overlook, state or local park, state historic trail or scenic byway, etc.): _____	
<i>iii.</i> Distance between project and resource: _____ miles.	
i. Is the project site located within a designated river corridor under the Wild, Scenic and Recreational Rivers Program 6 NYCRR 666?	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
If Yes:	
<i>i.</i> Identify the name of the river and its designation: _____	
<i>ii.</i> Is the activity consistent with development restrictions contained in 6NYCRR Part 666?	
<input type="checkbox"/> Yes <input type="checkbox"/> No	

F. Additional Information

Attach any additional information which may be needed to clarify your project.


If you have identified any adverse impacts which could be associated with your proposal, please describe those impacts plus any measures which you propose to avoid or minimize them.

G. Verification

I certify that the information provided is true to the best of my knowledge.

Applicant/Sponsor Name Saratoga Landmarks LLC Date 12/02/2025

Signature  Title Applicant

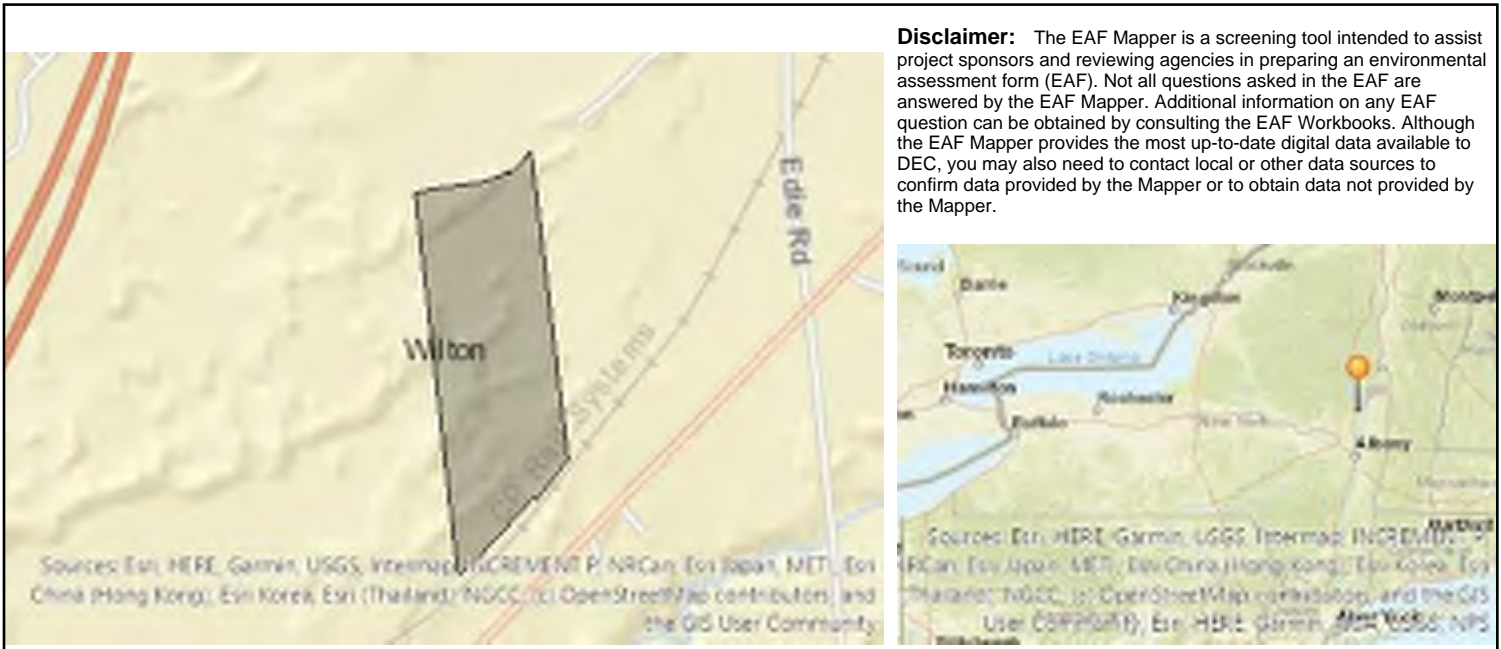

B.i.i [Coastal or Waterfront Area]	No
B.i.ii [Local Waterfront Revitalization Area]	No
C.2.b. [Special Planning District]	Yes - Digital mapping data are not available for all Special Planning Districts. Refer to EAF Workbook.
C.2.b. [Special Planning District - Name]	NYS Heritage Areas: Mohawk Valley Heritage Corridor
E.1.h [DEC Spills or Remediation Site - Potential Contamination History]	Digital mapping data are not available or are incomplete. Refer to EAF Workbook.
E.1.h.i [DEC Spills or Remediation Site - Listed]	Digital mapping data are not available or are incomplete. Refer to EAF Workbook.
E.1.h.i [DEC Spills or Remediation Site - Environmental Site Remediation Database]	Digital mapping data are not available or are incomplete. Refer to EAF Workbook.
E.1.h.iii [Within 2,000' of DEC Remediation Site]	No
E.2.g [Unique Geologic Features]	No
E.2.h.i [Surface Water Features]	Yes - Digital mapping information on local, New York State, and federal wetlands and waterbodies is known to be incomplete. Refer to the EAF Workbook.
E.2.h.ii [Surface Water Features]	Yes - Digital mapping information on local, New York State, and federal wetlands and waterbodies is known to be incomplete. Refer to the EAF Workbook.
E.2.h.iii [Surface Water Features]	Yes - Digital mapping information on local, New York State, and federal wetlands and waterbodies is known to be incomplete. Refer to the EAF Workbook.
E.2.h.iv [Surface Water Features - Wetlands Name]	Federal Waters
E.2.h.v [Impaired Water Bodies]	No
E.2.i. [Floodway]	Digital mapping data are not available or are incomplete. Refer to EAF Workbook.

E.2.j. [100 Year Floodplain]	Digital mapping data are not available or are incomplete. Refer to EAF Workbook.
E.2.k. [500 Year Floodplain]	Digital mapping data are not available or are incomplete. Refer to EAF Workbook.
E.2.l. [Aquifers]	Yes
E.2.l. [Aquifer Names]	Principal Aquifer
E.2.n. [Natural Communities]	Yes
E.2.n.i [Natural Communities - Name]	Red Maple-Hardwood Swamp, Appalachian Oak-Pine Forest
E.2.n.i [Natural Communities - Acres]	44.13, 985.35
E.2.o. [Endangered or Threatened Species]	Yes
E.2.o. [Endangered or Threatened Species - Name]	Frosted Elfin, Karner Blue
E.2.p. [Rare Plants or Animals]	No
E.3.a. [Agricultural District]	Yes
E.3.a. [Agricultural District]	SARA001
E.3.c. [National Natural Landmark]	No
E.3.d [Critical Environmental Area]	No
E.3.e. [National or State Register of Historic Places or State Eligible Sites]	Digital mapping data are not available or are incomplete. Refer to EAF Workbook.
E.3.f. [Archeological Sites]	Yes
E.3.i. [Designated River Corridor]	No



Appendix M:

Stormwater Management Practice Operation & Maintenance Manual



STORMWATER MANAGEMENT PRACTICE OPERATION & MAINTAINENCE MANUAL



**Bullard Lane
Conservation
Residential Subdivision**
Town of Wilton, Saratoga County

PREPARED FOR:
Saratoga Landworks, LLC



Bullard Lane Conservation Residential Subdivision Operation & Maintenance Manual

Table of Contents

1.0 INTRODUCTION..... 4

2.0 PROJECT DESCRIPTION & INFORMATION 4

3.0 SMP SPECIFICS 4

3.1 FILTRATION BIORETENTION 4

3.2 CASCADE UNIT HYDRODYNAMIC SEPARATOR..... ERROR! BOOKMARK NOT DEFINED.

4.0 INSPECTIONS & MAINTENANCE 5

APPENDICIES

Appendix A: Project SMP Map

- Site Location Map
- SMP Identification Map

Appendix B: SMP Maintenance Guidance

- NYSDEC Infiltration Basin Maintenance Guidance
- NYSDEC Infiltration Trench Maintenance Guidance

Appendix C: Sample Annual Inspection Report

Appendix D: Final Stamped Project Plans



1.0 Introduction

The purpose of this manual is to provide guidance for the long-term maintenance and operation for the Stormwater Management Practices (SMP's) located within the Bullard Lane Conservation Residential Subdivision. This manual serves as guidance to Saratoga Landworks, LLC, the project owner/developer and the Town of Wilton who will own and maintain the SMP's located within this development.

This manual is intended to serve as a guideline, and source of information regarding the SMP's located within this development. Per section 3.5 of the 2025 NYS Stormwater Design Manual - The responsibility for implementation of long-term operation and maintenance of a post-construction stormwater management practice shall be vested with a responsible party by means of a legally binding and enforceable mechanism, such as a maintenance agreement, deed covenant or other legal measure. This mechanism shall protect the practice from neglect, adverse alteration and/or unauthorized removal.

Proper routine maintenance is crucial to ensure the long-term functionality, and integrity of the SMP's. Beyond the basic maintenance requirements outlined in this manual, consultation of NYSDEC maintenance guidelines may be utilized.

2.0 Project Description & Information

The proposed Bullard Lane Conservation Residential Subdivision project is located along Bullard Lane in the Town of Wilton, NY. The project involves the construction of a residential subdivision that includes (25) new single-family residential homes. In order to collect, treat, and mitigate the stormwater runoff from new impervious surfaces, (2) separate Stormwater Management Practices were designed in accordance with the NYSDEC 2025 Stormwater Management Design Manual standards. The following SMP's exist within the project area:

- (1) Stormwater Infiltration Basin (I-2)
- (1) Stormwater Infiltration Trench (I-1)

A Schematic of the SMP's as they are situated within the project area is included in Appendix A of this Manual.

3.0 SMP Specifics

As previously mentioned, the Bullard Lane Conservation Residential Subdivision consists of (2) SMP's that were designed in accordance with the NYSDEC 2025 Stormwater Management Design Manual. This section of the manual will provide specific maintenance procedures, and guidance for each individual practice.

3.1 Stormwater Infiltration Basin

The Bullard Lane Conservation Residential Subdivision includes a Stormwater Infiltration Basin. The Infiltration Basin is located in the northeastern portion of the project parcel. A schematic of the SMP locations relative to the project area can be found in Appendix A of this report. The maintenance guidelines for the Stormwater Infiltration Basin follows section 12.2.9 of the NYSDEC Stormwater Management Design Manual.



The Stormwater Infiltration Basin is pretreated via a forebay. The forebay should be inspected on a routine basis and following severe rainfall events for evidence of accumulated debris and sediment. The forebay shall be maintained/cleaned as necessary to prolong the life of the infiltration basin.

The Stormwater Infiltration Basin should be inspected/maintained at least 2 times a year to ensure the practice survived the winter season. Debris cleanout and dewatering inspection should occur monthly. Inspection of inlets and outlets should occur at least once per year with sediment cleanout and aggregate repairs as needed.

3.2 Stormwater Infiltration Trench

The project development includes a Stormwater Infiltration Trench. The Infiltration Trench is located in the northwestern corner of the project parcel. Refer to the schematic in Appendix A of this report. The maintenance guidelines for the Stormwater Infiltration Trench follows section 12.2.9 of the NYSDEC Stormwater Management Design Manual.

The Stormwater Infiltration Trench is pretreated via grass filter strips. The grass swales shall be maintained as necessary to prolong the life of the infiltration trench.

The Stormwater Infiltration Trench should be inspected/maintained at least 2 times a year to ensure the practice survived the winter season. Debris cleanout and dewatering inspection should occur monthly. Inspection of the grass swale inlets should occur at least once per year with sediment cleanout and lawn repair as needed.

4.0 Inspections & Maintenance

Per section 12.1.2 in the 2025 NYSWDM, SMP inspections can be classified into (3) different levels.

- Level 1 inspections can be conducted by property owners, managers and municipal maintenance staff. These inspections are typically only visual and require a limited amount of stormwater knowledge or training. Level 1 Inspections are the most common and are intended to identify minor maintenance issues early and keep up with routine maintenance tasks. They should be conducted at least annually for all practices and supplemented with additional visits after large storms, winter salting and sanding, or other seasonal changes. Issues that may arise during a level 1 inspection may trigger a level 2 inspection.
- Level 2 inspections shall be conducted by trained personnel or municipal staff. Level 2 inspections can result from structural damage to a practice, excessive ponding in a practice, or other issued that may require repair.
- Level 3 inspections shall be conducted by qualified individuals such as professional engineers or landscape architects.

A project specific sample annual Level 1 inspection report has been included in Appendix C of this manual.

Further information regarding maintenance recommendations the project SMP's can be found in the July 31, 2024 edition of the NYS Stormwater Management Design Manual. Or the stormwater construction toolbox found at:




<https://dec.ny.gov/environmental-protection/water/water-quality/stormwater/construction-stormwater-toolbox>

Appendix A
Project SMP Maps



SITE LOCATION MAP



PRELIMINARY / NOT FOR CONSTRUCTION

UNAUTHORIZED ALTERATION OR
ADDITION TO THIS DOCUMENT
IS A VIOLATION OF THE
NYS EDUCATION LAW.
COPYRIGHT LANSING
ENGINEERING, PC.

BULLARD LANE RESIDENTIAL SUBDIVISION BULLARD LANE, TOWN OF WILTON, SARATOGA COUNTY, NEW YORK



**LANSING
ENGINEERING**


2452 STATE ROUTE 9 SUITE 301
MALTA, NY 12020
(518) 899-5243

CIVIL - TRANSPORTATION - ENVIRONMENTAL - LAND SURVEYING


SITE LOCATION MAP

PROJ. NO: 1061.01
SCALE: AS SHOWN
DATE: 2/03/2025

SLM-1
SHEET 1 OF 1

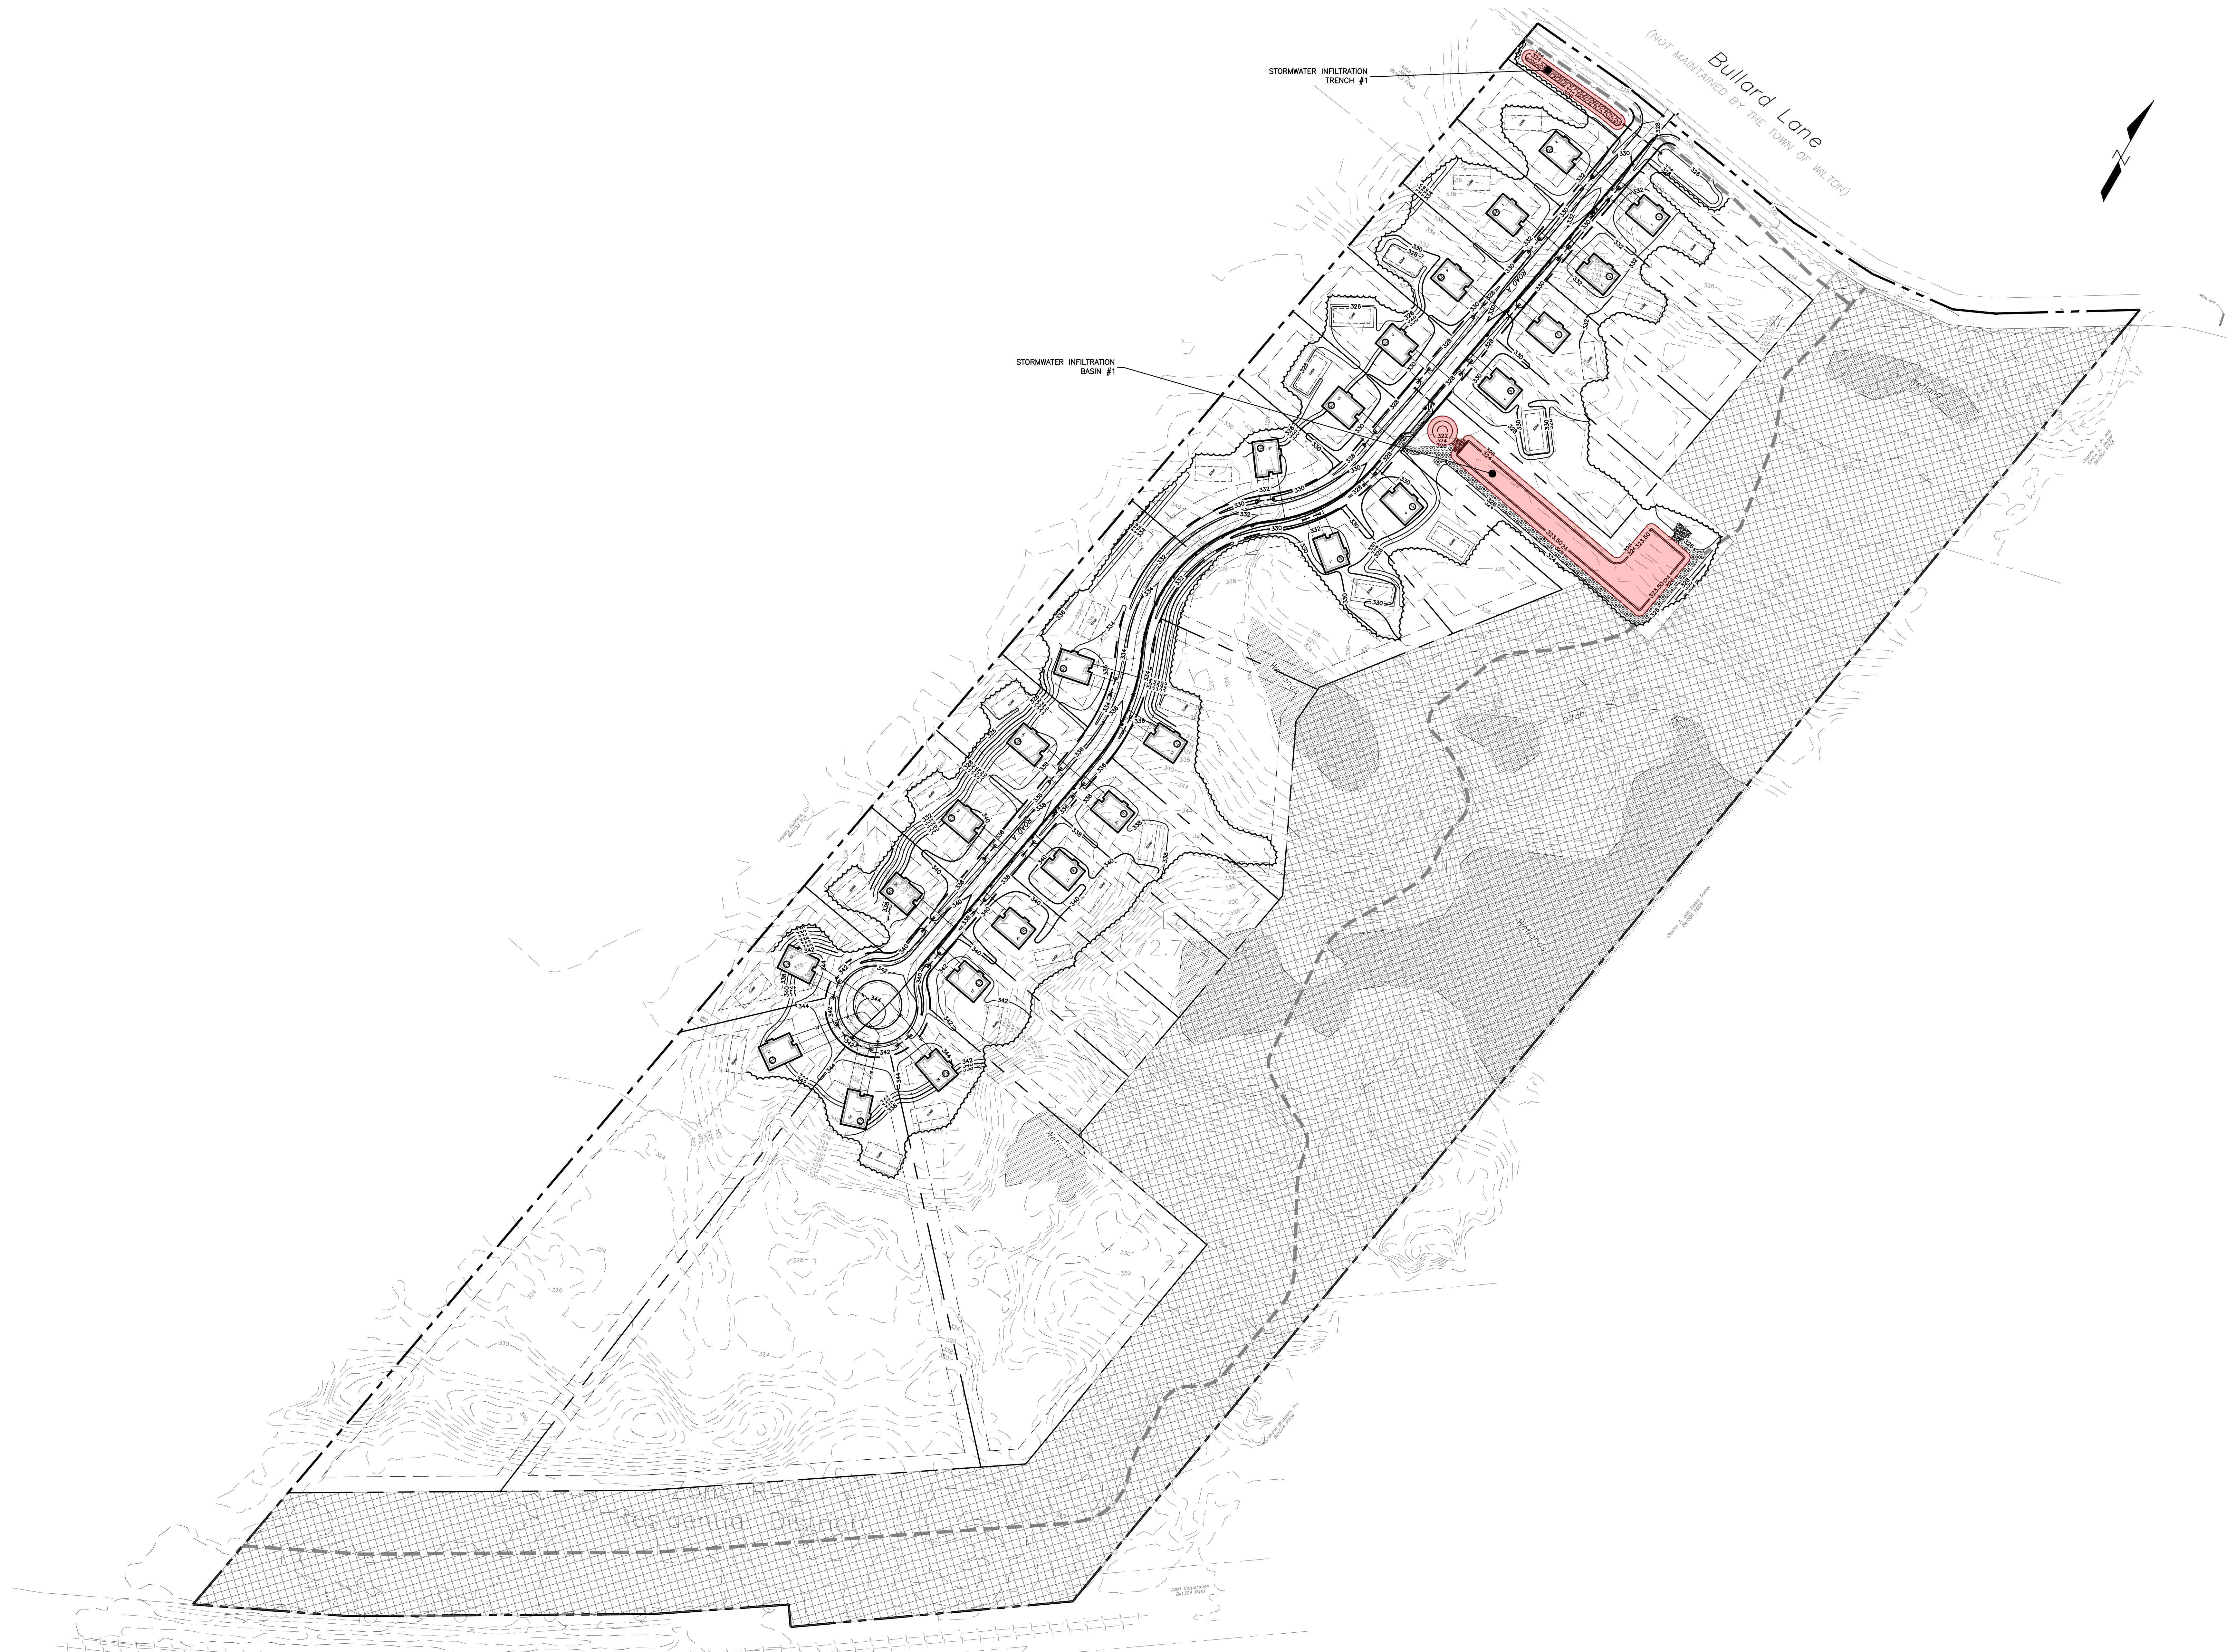

SMP SCHEMATIC



LANSING
ENGINEERING

1000 WEST 10TH STREET
WALTON, NY 12580
(518) 888-8848

PRELIMINARY / NOT FOR CONSTRUCTION

DATE: _____
REVISIONS: _____
DESCRIPTION: _____

BULLARD LANE RESIDENTIAL SUBDIVISION
BULLARD LANE, TOWN OF WILTON, SARATOGA COUNTY, NEW YORK

CIVIL, TRANSPORTATION, ENVIRONMENTAL, LAND SURVEYING

UNAUTHORIZED
REPRODUCTION,
COPYING, OR
DISSEMINATION
OF THIS DOCUMENT
WITHOUT THE
WRITTEN
CONSENT OF
LANSING ENGINEERING, P.C.




Appendix B
SMP Maintenance Guidance

PW 4. Pond Outlet

Description: The pond's outlet enables the ponded water to discharge to downstream drainage systems or stream channels. The outlet is often at the base of the dam/embankment on the downstream side. Inspection of this point can help prevent flooding of the pond and upstream drainage systems and prevent pond failure at a weak point of a pond's containment system.

Instruction: Examine the outlet of the pipe on the downstream side of the dam/embankment where it empties into a stream, channel, or drainage system. Consult the table below for possible problems.

Table 2.10.4 PW Pond Outlet

Problem (Check if Present)	Follow-Up Actions
 <ul style="list-style-type: none"> <input type="checkbox"/> The pond outlet is clogged with sediment, trash, debris, vegetation, or is eroding, caving in, slumping, or falling apart. 	<ul style="list-style-type: none"> <input type="checkbox"/> If there is a minor blockage, remove the debris or vegetation to allow free flow of water. <input type="checkbox"/> Remove any accumulated trash at the outlet. <input type="checkbox"/> Outlet: <hr/> <ul style="list-style-type: none"> <input type="checkbox"/> Kick-Out to Level 2 Inspection: <input type="checkbox"/> If the area at the outlet cannot be easily accessed or if the blockage is substantial, a Level 2 Inspection is warranted. <input type="checkbox"/> Erosion at and downstream of the outfall should be evaluated by a qualified professional. <input type="checkbox"/> Any structural problems, such as broken pipes, structures falling into the stream, or holes or tunnels around the outfall pipe, should be evaluated by a Level 2 Inspector and will require repair by a qualified contractor. <input type="checkbox"/> The pool of water at the outlet pipe is discolored, has an odor, or has excessive algae or vegetative growth.

2.11. Infiltration

Areas of Infiltration

Key areas to inspect for Infiltration include the following:

- IN 1. Drainage Area
- IN 2. Inlets
- IN 3. Infiltration Area
- IN 4. Outlets

Note: The category of Infiltration includes:

- Infiltration Trench – Long, narrow infiltration practice, usually with small gravel at the surface and a reservoir of larger gravel or stone beneath
- Infiltration Basin – Larger practice, usually covered with grass and highly permeable soil beneath
- Dry Well – Small pit filled with stone or gravel, or precast concrete chamber surrounded by stone that receives and stores runoff to enable it to infiltrate into the underlying ground.



Figure 2.11.1 Key Areas for Level 1 Inspection of Infiltration Practice

Infiltration Level 1 Inspection




The Level 1 Inspection focuses on the Drainage Area (IN1), Inlets (IN2), Infiltration Area (IN3), and Outlets (IN4). The purpose of an infiltration practice is to temporarily store collected runoff so that it can percolate into the underlying soil. Using this practice is dependent on having a good on-site soil that is capable of infiltrating the amount of runoff generated by the drainage area. The Level 1 Inspection should be conducted at least twice a year, especially in early spring, to ensure that the practice has survived the winter, particularly if there has been a significant amount of snow.

IN 1. Drainage Area

Description: The drainage area conveys runoff to and is uphill from the Infiltration cell. When it rains, water runs off and flows to the Infiltration cell and soaks into its underlying layers.

Instruction: Look for both pervious and impervious areas that are uphill from the Infiltration cell. Consult **Table 11.1.1** below.

Table 11.1.1 IN Drainage Area

Problem (Check if Present)		Follow-Up Actions
	<input type="checkbox"/> Bare soil, erosion of the ground (rills washing out the dirt)	<input type="checkbox"/> Seed and straw areas of bare soil to establish vegetation. <input type="checkbox"/> Fill in erosion areas with soil, compact, and seed and straw to get vegetation established. <input type="checkbox"/> If a rill or small channel is forming, try to redirect water flowing to this area by creating a small berm or adding topsoil to areas that are heavily compacted. <input type="checkbox"/> Other:
<input type="checkbox"/> For Dry Wells: Leaves, sticks, or other debris in gutters and downspouts		<input type="checkbox"/> Kick-Out to Level 2 Inspection: Large areas of soil have been eroded, or larger channels are forming. May require rerouting of flow paths. <input type="checkbox"/> Remove all debris by hand. <input type="checkbox"/> Other:
	<input type="checkbox"/> Piles of grass clippings, mulch, dirt, salt, or other materials	<input type="checkbox"/> Remove or cover piles of grass clippings, mulch, dirt, etc. <input type="checkbox"/> Other:
	<input type="checkbox"/> Open containers of oil, grease, paint, or other substances	<input type="checkbox"/> Cover or properly dispose of materials; consult your local solid waste authority for guidance on materials that may be toxic or hazardous. <input type="checkbox"/> Other:


IN 2. Inlets

Description: The inlets to an Infiltration practice are where water flows into the cell. Depending on the design, inlets can be:

- *Curb cuts or openings* in a parking lot or roadway
- *Downspouts* that deliver runoff directly from a rooftop to the Infiltration practice
- *Pipes or ditches* that carry water into the Infiltration practice from the drainage area
- *Flow directly over the land surface* (known as “sheetflow”), sometimes across a strip of rock or stone

Instruction: Look for all the places where water flows into the Infiltration practice. Consult **Table 11.1.2** below for possible problems.

Table 11.1.2 IN Inlets

Problem (Check if Present)	Follow-Up Actions
 <p><input type="checkbox"/> Inlets are collecting grit and debris or grass/weeds are growing. Some water may not be getting into the Infiltration practice.</p>	<p><input type="checkbox"/> Use a flat shovel to remove grit and debris (especially at curb inlets or openings). Parking lots generate fine grit that will accumulate at these spots.</p> <p><input type="checkbox"/> Pull out clumps of growing grass or weeds and scoop out the soil or grit that the plants are growing in.</p> <p><input type="checkbox"/> Remove any grass clippings, leaves, sticks, and other debris that is collecting at inlets.</p> <p><input type="checkbox"/> For pipes and ditches, remove sediment and debris that is partially blocking the pipe or ditch opening where it enters the Infiltration practice.</p> <p><input type="checkbox"/> Dispose of all material properly in an area where it will not re-enter the practice.</p> <p><input type="checkbox"/> Other:</p> <hr/> <p><input type="checkbox"/> Kick-Out to Level 2 Inspection: Inlets are blocked to the extent that most of the water does not seem to be entering the Infiltration practice.</p>
<p><input type="checkbox"/> Some or all of the inlets are eroding so that rills, gullies, and other erosion is present, or there is bare dirt that is washing into the Infiltration practice.</p>	<p><input type="checkbox"/> For small areas of erosion, smooth out the eroded part and apply rock or stone (e.g., river cobble) to prevent further erosion. Usually, filter fabric is placed under the rock or stone.</p> <p><input type="checkbox"/> In some cases, reseeding and applying erosion-control matting can be used to prevent further erosion. Some of these materials may be available at a garden center, but it may be best to consult a landscape contractor.</p> <p><input type="checkbox"/> Other:</p> <hr/> <p><input type="checkbox"/> Kick-Out to Level 2 Inspection: Erosion is occurring at most of the inlets and it looks like there is too much water that is concentrating at these points. The inlet design may have to be modified.</p>

IN 3. Infiltration Area

Description: The infiltration area is the area that collects water and allows it to seep into the underlying soil. Some infiltration areas also have a vertical perforated pipe called an *observation well*, which is used to view the water level in the infiltration practice after a storm. If the infiltration practice is working properly, the water in the observation well should be completely drained down within 2 to 3 days of a storm. Depending on the design, the infiltration area can be covered with grass, gravel, or stone.

Instruction: Examine the surface of the infiltration area and the observation well. Consult **Table 11.1.3** below for possible problems. Note: The following Problem and Follow-Up Actions apply to infiltration practice pretreatment areas also.

Table 11.1.3 IN Infiltration Area






Problem (Check if Present)	Follow-Up Actions
 <p><input type="checkbox"/> For grass-covered Infiltration practices: grass has grown very tall, (Photo credit: Stormwater Maintenance, LLC)</p>	<p><input type="checkbox"/> Mow infiltration area at least twice per year.</p> <p><input type="checkbox"/> Other:</p>
 <p><input type="checkbox"/> For grass-covered Infiltration practices: sparse vegetation cover or bare spots</p>	<p><input type="checkbox"/> Add topsoil (as needed), grass seed, straw, and water during the growing season to re-establish consistent grass coverage.</p> <p><input type="checkbox"/> Other:</p> <p><input type="checkbox"/> Kick-Out to Level 2 Inspection: Sparse vegetation cover can be a sign that the infiltration area is not infiltrating at the proper rate and water is standing too long after a storm. The surface may be saturated or squishy, and the conditions do not enable grass to grow. This situation should be evaluated by a Level 2 Inspection and likely corrected by a qualified contractor.</p>
<p><input type="checkbox"/> Minor areas of sediment, grit, trash, or other debris are accumulating on the surface.</p>	<p><input type="checkbox"/> Use a shovel to scoop out minor areas of sediment or grit, especially in the spring after winter sanding materials may wash in and accumulate. Dispose of the material where it cannot re-enter the Infiltration practice.</p> <p><input type="checkbox"/> If removing the material creates a hole or low area, rake the surface smooth and level.</p> <p><input type="checkbox"/> Remove trash, debris, and other undesirable materials.</p> <p><input type="checkbox"/> Other:</p> <p><input type="checkbox"/> Kick-Out to Level 2 Inspection: Sediment has accumulated more than 2-inches deep and covers 25% or more of the surface of the Infiltration area.</p>

Table 11.1.3 IN Infiltration Area


Problem (Check if Present)	Follow-Up Actions
 <ul style="list-style-type: none"> <input type="checkbox"/> There is erosion on the surface; water seems to be carving out rills as it flows across the surface of the Infiltration area or sinkholes are forming in certain areas. 	<ul style="list-style-type: none"> <input type="checkbox"/> For minor areas of erosion, try filling the eroded areas with clean topsoil, sand, or stone (whatever the existing cover is). <input type="checkbox"/> If the problem recurs, you may have to use larger stone (e.g., river cobble) to fill in problem areas. <input type="checkbox"/> Other: <hr/> <ul style="list-style-type: none"> <input type="checkbox"/> Kick-Out to Level 2 Inspection: The problem persists or the erosion is more than 3-inches deep and seems to be an issue with how water enters and moves through the infiltration area. <input type="checkbox"/> Kick-Out to Level 2 Inspection: The problem does not seem to be caused by flowing water but a collapse or sinking of the surface (e.g., "sinkhole") due to some underground problem.
 <ul style="list-style-type: none"> <input type="checkbox"/> Observation well is damaged or cap is missing 	<ul style="list-style-type: none"> <input type="checkbox"/> Kick-Out to Level 2 Inspection: Requires replacing pipes or caps.
 <ul style="list-style-type: none"> <input type="checkbox"/> Water still visible in the observation well more than 72 hours after a rain storm. The Infiltration practice does not appear to be draining properly. 	<ul style="list-style-type: none"> <input type="checkbox"/> Kick-Out to Level 2 Inspection: This is generally a serious problem, and it will be necessary to activate a Level 2 Inspection.

IN 4. Outlets

Description: Outlets are where water exits the surface of the infiltration area during larger storms when the underground infiltration reservoir fills up and the excess water needs somewhere to go. Note that not all infiltration practices will have an identifiable outlet if the design is for all the water to infiltrate into the ground. Outlets may be a berm, stone weir, or pipe.

Instruction: Locate and inspect all outlets. Consult **Table 2.11.4** below for possible problems.

Table 2.11.4 IN Outlets

Problem (Check if Present)	Follow-Up Actions
 <ul style="list-style-type: none"> <input type="checkbox"/> Outlet obstructed with sediment, debris, trash, etc. 	<ul style="list-style-type: none"> <input type="checkbox"/> Remove the debris and dispose of it where it cannot re-enter the infiltration area. <input type="checkbox"/> Other: <hr/> <ul style="list-style-type: none"> <input type="checkbox"/> Kick-Out to Level 2 Inspection: Outlet is completely obstructed; there is too much material to remove by hand or with simple hand tools.
<ul style="list-style-type: none"> <input type="checkbox"/> Rills or gullies are forming at outlet. 	<ul style="list-style-type: none"> <input type="checkbox"/> For minor rills, fill in with soil, compact, and seed and straw to establish vegetation. <input type="checkbox"/> Other: <hr/> <ul style="list-style-type: none"> <input type="checkbox"/> Kick-Out to Level 2 Inspection: Rills are more than 2" to 3" deep and require more than just hand raking and re-seeding.

Appendix C
Sample Annual Inspection Report

ANNUAL POST CONSTRUCTION SMP MAINTANINENCE INSPECTION REPORT

Project Name: Bullard Lane Conservation Residential Subdivision

Project Address: Bullard Lane, Wilton, NY 12866

Date of NOT: TBD

Inspector's Name/Title: TBD

NYR#: NYR#

Date and Time: x

Temperature: xx°F

Ambient Conditions: x

Soil Conditions: x

PROJECT SMP INFORMATION

The Bullard Lane Conservation Residential Subdivision consists of an open swale stormwater conveyance system with (1) Stormwater Infiltration Basin and (1) Stormwater Infiltration Trench for stormwater mitigation/treatment. The practices are listed below;

- (1) Stormwater Infiltration Basin (I-2)
- (1) Stormwater Infiltration Trench (I-1)

The inspection checklists below contain project specific operation & maintenance inspection items per guidance from the July 31, 2024 edition of the NYSDEC Stormwater Design Manual. Each project stormwater practice is outlined with specific inspection items to be investigated, upon investigation corrective actions may be recommended.

INSPECTION CHECKLIST

Stormwater Infiltration Basin Post Construction Inspection Checklist					
SMP Element	Inspection Item	Yes	No	N/A	Corrective Action
Upstream Contributing Drainage Area	Excessive Trash/Debris	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Remove & properly dispose
	Evidence of erosion	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Stabilize with seed and mulch. Erosion stabilization may be warranted.
Pretreatment Forebay	High level of floatable solids such as trash, lawn debris etc.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Consult contractor to remove debris from forebay.
	High level of sediment in the permanent pool of the forebay. Maximum 75% capacity.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Consult contractor to excavate sediment build up from permanent pool of forebay.
Infiltration Basin	Excessive Trash/Debris	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Remove & properly dispose
	Overgrown Vegetation	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Mow overgrown vegetation and remove spoils from basin area
	Evidence of excessive ponding, odors	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Consult the engineer immediately for recommendations.
	Evidence of erosion & undermining	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Backfill area, see, mulch and consider matting with erosion blanket.

Rip-rap Emergency Spillway	Spillway overgrown, full of sediment, washed away	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Mow, clear vegetation or consult engineer for replacement recommendations.
	Access road is overgrown or inaccessible	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Consult landscaper/contractor to repair or restore access to roadway. Consult final plans for installation specifications.
Overall Practice	Evidence of oil/chemical accumulation, odor, algae, color or pollution	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Consult engineer immediately for proper investigation & spill reportage procedure.
	Fences/signage is inadequate	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Repair and replace. Consult final plans for fence & signage location, and type.
	Trash in the pool	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Remove and properly dispose

Stormwater Infiltration Trench Post Construction Inspection Checklist					
SMP Element	Inspection Item	Yes	No	N/A	<u>Corrective Action</u>
Upstream Contributing Drainage Area	Excessive Trash/Debris	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Remove & properly dispose
	Evidence of erosion	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Stabilize with seed and mulch. Erosion stabilization may be warranted.
Pretreatment Grass Filter Strips	High level of floatable solids such as trash, lawn debris etc.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Remove & properly dispose of trash and debris.
	High level of sediment in the in the grass filter strip area.	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Consult contractor to excavate sediment build up and repair grass lawn as necessary.
Infiltration Trench	Excessive Trash/Debris	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Remove & properly dispose
	Overgrown Vegetation	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Mow overgrown vegetation and remove spoils from basin area
	Evidence of excessive ponding, odors	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Consult the engineer immediately for recommendations.
Overall Practice	Evidence of oil/chemical accumulation, odor, algae, color or pollution	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Consult engineer immediately for proper investigation & spill reportage procedure.
	Fences/signage is inadequate	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Repair and replace. Consult final plans for fence & signage location, and type.
	Trash in the trench area	<input type="checkbox"/>	<input type="checkbox"/>	<input type="checkbox"/>	Remove and properly dispose

CERTIFICATION

Lansing Engineering Qualified Inspector Signature: _____

Date: _____





Appendix D
Final Stamped Project Plans
